


KELLOGG-DRISCOLL

HANDY-STILES

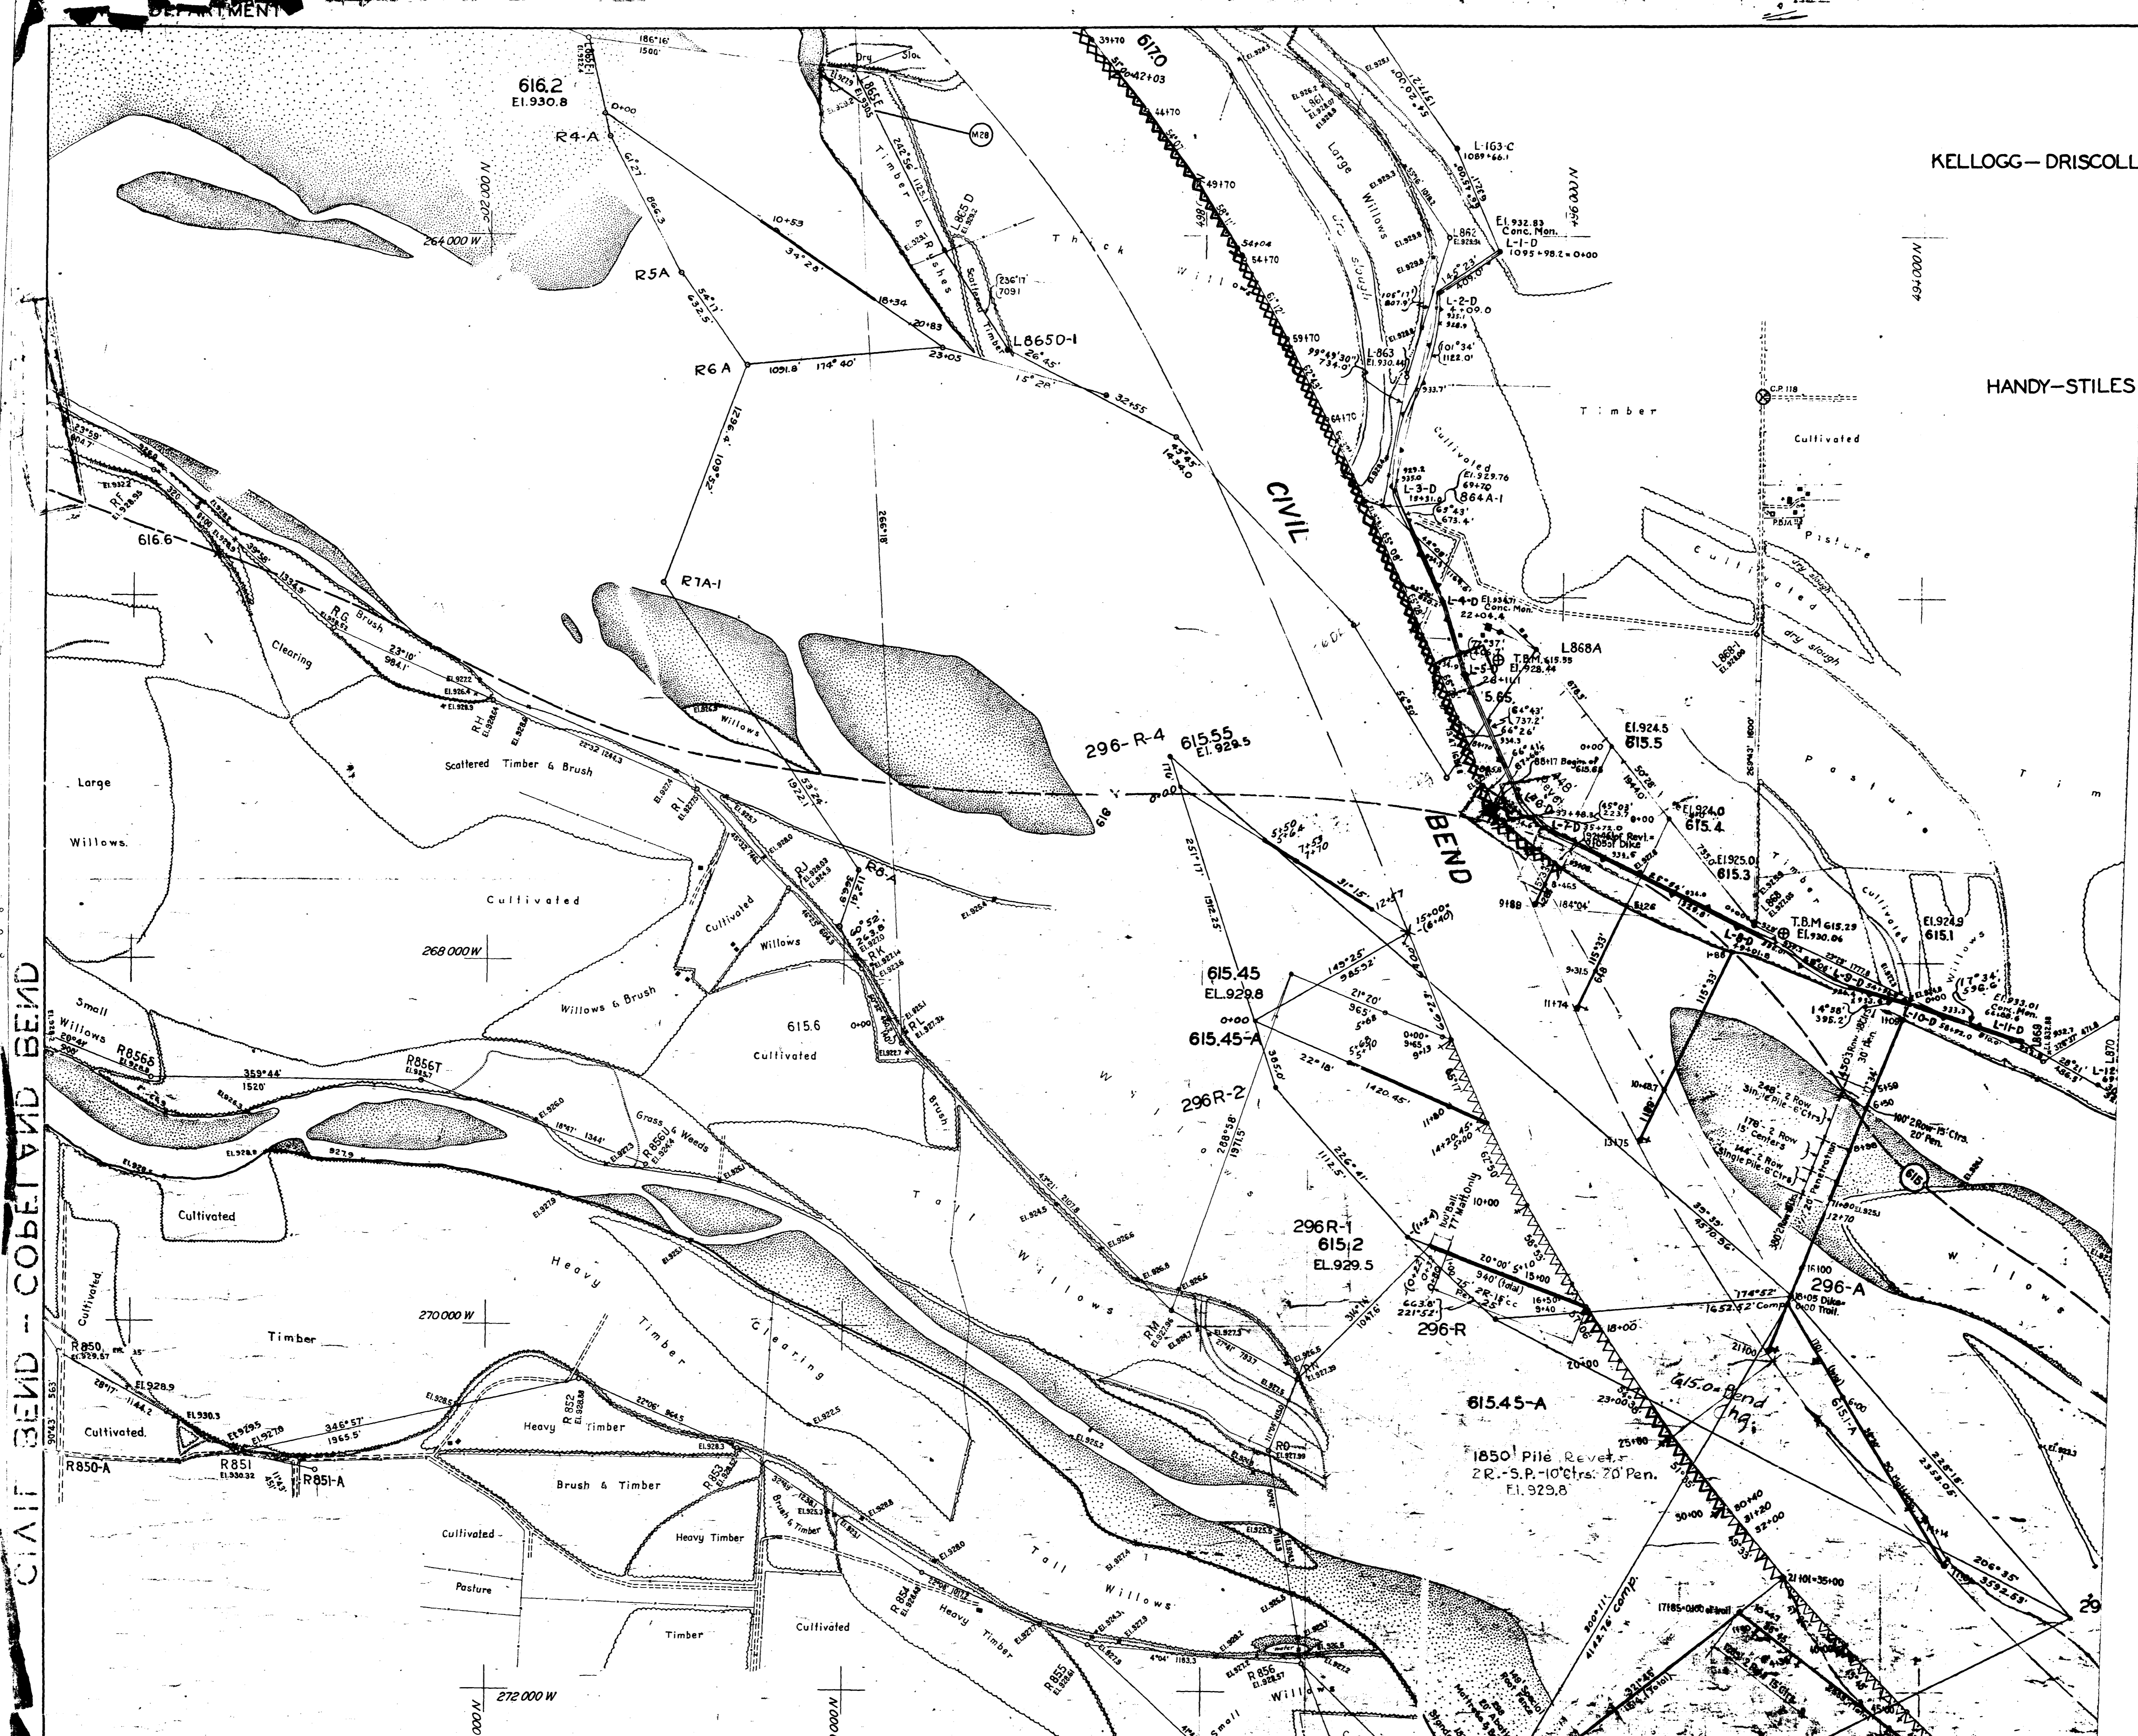

CONTRACTOR: M.A. WOGAN
 CIVIL BEND - COPELAND BEND CONTRACT NO. W643 eng-56

STRUCTURE	NUMBER	LENGTH	AZIMUTH	STRENGTH	30' PENETRATION	ELEVATION ABOVE M.S.L.	MARKER CLUMP	M.L.W.	ALLOT. NO.
REVELMENT	615.65	L.B. 448'				924.5	932.1	917.9	7017
DIKE	615.5	L.B. 284'	115° 33'	3 ROW-18' CTRS.	284'	924.0	932.0	917.7	7017
DIKE	615.4	L.B. 648'	115° 33'	3 ROW-18' CTRS.	648'	924.0	932.0	917.6	7017
DIKE	615.3	L.B. 1189'	115° 33'	3 ROW-18' CTRS.	1189'	925.0	930.0	917.4	7017
DIKE	615.1	L.B. 1991'	111° 34'	SEE DIKE	SEE DIKE	924.9	930.0	917.2	7017
DIKE	614.7	L.B. 1665'	103° 38'	SEE DIKE	STA. 30154 TO STA. 36101	924.0	930.0	916.5	7017
TRAIL	614.7-A	L.B. 3590'	35° 16'	SEE DIKE	MAXIMUM UP TO 30'	924.0	930.0	916.3	7017
DIKE	614.7-B	L.B. 315'	100° 17'	3 ROW-18' CTRS.	STA. 28100 TO STA. 35190	924.0	930.0	916.3	7017
DIKE	614.9	R.B. 1614'	321° 45'	SEE DIKE	STA. 6136 TO STA. 21101	924.8	930.0	916.9	7017
TRAIL	614.9-A	R.B. 2539'	36° 45'	SEE DIKE	STA. 12103 TO STA. 25139	924.8	930.0	916.9	7017
TRAIL	615.1-A	L.B. 1701'	58° 30'	SEE DIKE	STA. 6100 TO STA. 17104	924.9	930.0	917.2	7017

Revised: May 26, 1936; showing recession of Marker Clumps on Trail Dike, 615.1-A, at Stations 1114, 614.5+14 & 214.

REVISIONS:
 Aug. 1934 showing Revelment 615.65 L.B. & Dikes 615.5, 615.4, 615.3, 615.1, 614.7-A, 614.7-B, L.B. and 614.9, 614.9-A, R.B. authorized for construction.
 Oct. 23, 1934 showing change in strength of Dike 615.1 L.B. to conform to letter of even date.
 Oct. 31, 1934 showing change in layout of Dike 614.7 L.B., also Dike 615.1-A L.B. authorized for construction.
 Nov. 19, 1934 showing elevation of Dikes 615.3 & 615.1 L.B. changed to conform to letter of even date.
 Feb. 20, 1935 showing elevation of Dikes 614.7-A & 614.7-B L.B. changed to conform to letter of even date.
 March 18, 1935 showing elevation of Dikes 614.7-A & 614.7-B L.B. changed to conform to letter of even date.
 March 29, 1935 showing strength for Dike 614.7 L.B. changed to conform to letter of even date.
 April 4, 1935 to show change in length, strength & elevation of Dike 614.9 R.B. and change in elevation of Dike 615.1-A L.B.
 April 18, 1935 showing elevation of Dike 614.9-A R.B. changed to conform to letter of even date.
 Aug. 14, 1935 showing penetration of Dike 615.1-A L.B. changed to conform to letter of even date.
 Oct. 21, 1935 showing penetration of Dike 614.7-A L.B. changed to conform to letter of even date.
 May 15, 1936 showing recession of Revelment 615.65 L.B. from sta. 82165 to sta. 88417 to conform to letter of even date.

CONTRACTOR: M.A. WOGAN
 COPELAND BEND CONTRACT NO. W643 eng-55

STRUCTURE	NUMBER	LENGTH	AZIMUTH	STRENGTH	30' PENETRATION	ELEVATION ABOVE M.S.L.	MARKER CLUMP	M.L.W.	ALLOT. NO.
REVELMENT	613.4	R.B. 41070'				915.3	915.3	7018	
DIKE	612.6	L.B. 3448'	71° 20'	SEE DIKE	STA. 31132 TO STA. 34175	923.5	928.0	914.5	7018

* Includes 1110' Pile Revelment from sta. -45176) to sta. -27140) Elevation = 927.0

REVISIONS:
 Aug. 10, 1934 showing Revelment 613.4 R.B. & Dike 612.6 L.B. authorized for construction.
 Aug. 20, 1934 to show changed alignment and length of Revelment 613.4 R.B. & changed length of Dike 612.6 L.B.
 Sept. 19, 1934 to show changed alignment of Revelment 613.4 R.B. to conform with letter of even date.
 Oct. 15, 1934, showing changed strength for Dike 612.6 L.B. to conform to letter of even date.
 April 3, 1935 showing 3633' of additional treatment authorized for construction of Mile 613.4 R.B.
 April 19, 1935 showing changed alignment of Revelment 613.4 R.B. from sta. 0100 to sta. -136191); also Standard Revelment changed to Pile Revelment from sta. -45175) to sta. -261483).
 Mar. 24, 1936 showing recession of Revelment 613.4 R.B. sta. -136191) to sta. -136190) rescinded.

COPELAND BEND HIRED LAB

STRUCTURE	NUMBER	LENGTH	AZIMUTH	STRENGTH	30' PENETRATION	ELEVATION
ABATIS	614.9	R.B. 450'	321° 45'			

REVISIONS:
 April 5, 1935 to show Abatis 614.9 R.B. authorized for construction.

N E B R A S K

COPELAND BEND HIRED LAB

276 000 W
