General Land Office • Original Field Notes

Book Number

74

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.

Compd

Vol. 6 R. 6 E.

Contract No 210.

Descriptive List Completed

Field Notes of the Subdivision lines of Township 21 North, of Range 6 East of the 6th Principal Meridian in the Territory of Nebraska. as surveyed by Isaac C. Stuck Deputy Surveyor under his Contract bearing date the 19th day of June 1857. No 210

Subdivision Commenced August 1st 1857.

Subdivision Completed August 3rd 1857. 3rd

Ok Lina

b

Names and duties of Assistants

John Farnham	Compassman
Harman Lanforsuck	Chainman
Frank McKeana	Chainman
Bushnell B. Loomis	Chainman
Thos C. Jones	Chainman
Frank Hill	Axeman
James Quinn	Axeman
George Ocklin	Flagman

c

Township 21 N. Range 6 East

6	43	5	33	4	23	3	16	2	8	1
43		42		33		24		15		7
7	42	8	32	9	23	10	14	11	7	12
41		40		32		22		14		6
18	40	17	31	16	22	15	13	14	6	13
39		38		30		21		12		5
19	38	20	29	21	20	22	12	23	4	24
37		36		28		19		11		3
30	36	29	28	28	18	27	10	26	3	25
35		34		27		17		10		2
31	34	32	26	33	17	34	9	35	2	36

UNITED STATES OF AMERICA,
TERRITORY OF Nebraska

I, John Farnham do solemnly swear that I will well and truly perform the duties of Compassman according to instructions given me, and to the best of my skill and ability.

John Farnum

Subscribed and sworn to before me this Sixteenth day of July A. D. 1857

~~Justice of the Peace~~

John C. Funk Notary Public

UNITED STATES OF AMERICA,
TERRITORY OF Nebraska

I, Harman Lanfersieck do solemnly swear that I will execute the duties of chain carrier; that I will level the chain upon uneven ground, and plumb the tally pins whether by sticking or dropping the same; that I will report the true distance to all notable objects; and the true length of all lines that I assist in measuring according to the best of my skill and ability.

Hamen Lanfersieck

Subscribed and sworn to before me this 16th day of July A. D. 1857

~~Justice of the Peace~~

John C. Funk Notary Public

UNITED STATES OF AMERICA,
TERRITORY OF Nebraska

I, Frank McKenna do solemnly swear that I will execute the duties of chain carrier; that I will level the chain upon uneven ground, and plumb the tally pins, whether by picking or dropping the same; that I will report the true distance to all notable objects; and the true length of all lines that I assist in measuring, to the best of my skill and ability.

Frank McKenna

Subscribed and sworn to before me this 16th day of July A. D. 1857

Johnle Funk ~~Justice of the Peace~~ Notary Public

UNITED STATES OF AMERICA,
TERRITORY OF Nebraska

I, Bushnell B. Loomis do solemnly swear that I will execute the duties of chain carrier; that I will level the chain upon uneven ground, and plumb the tally pins whether by picking or dropping the same; that I will report the true distance to all notable objects; and the true length of all lines that I assist in measuring according to the best of my skill and ability.

Bushnell B. Loomis

Subscribed and sworn to before me this 16th day of July A. D. 1857

~~Justice of the Peace~~

Johnle Funk Notary Public

UNITED STATES OF AMERICA,
TERRITORY OF Nebraska

I, Thos C Jones do solemnly Swear
I will execute the duties of chain carrier; that I will level the
upon uneven ground, and plumb the tally pins, whether by
ing or dropping the same; that I will report the true distance
notable objects; and the true length of all lines that I assist in
uring, to the best of my skill and ability.

Thomas C Jones

Subscribed and sworn to before me this 16th day
July A. D. 185 7
John C. Funk ~~Justice of the Peace~~ Notary Public

UNITED STATES OF AMERICA,
TERRITORY OF

I, George W. Cocklin do solemnly Swear
that I will execute ~~the duties of chain carrier; that I will level the~~ the
chain ~~upon uneven ground, and plumb the tally pins, whether by~~
~~lifting or dropping the same; that I will report the true distance~~ Flagm
~~to all notable objects; and the true length of all lines that I assist in~~
~~measuring,~~ to the best of my skill and ability.

George W. Cocklin

Subscribed and sworn to before me this 16th day
of July A. D. 185 7
John C. Funk ~~Justice of the Peace~~ Notary Public

UNITED STATES OF AMERICA,
TERRITORY OF Nebraska

F. R. Hill do solemnly Swear
will well and truly perform the duties of Axe man
ing to instructions given me, and to the best of my skill and

F. R. Hill

bscribed and sworn to before me this 10th day
July A. D. 1857

~~Justice of the Peace~~
John C. Lusk, Notary Public

UNITED STATES OF AMERICA,
TERRITORY OF Nebraska

James Quinn do solemnly Swear
ill well and truly perform the duties of Axeman
g to instructions given me, and to the best of my skill and

James Quinn

bscribed and sworn to before me this 10th
July A. D. 1857

~~Justice of the Peace~~
John C. Lusk Notary Public

1

Township 21 N R 6 East of 6th P. M.

To determine the proper adjustment of my Compass for subdividing this Township I commence at the Corner to Townships 20 & 21 N. Range 6 & 7 East, and run North on a blank line along the East boundary of Sect. 36.

Variation 14°.00' East

39.94 To a point 26 links East of quarter Sect Corner.

79.83 To a point 52 links East Of the Corner to Sects. 25 and 36. To retrace this line or run parallel thereto my Compass must be adjusted to a Variation of 14°.22' East

Subdivision Commenced August 1st 1857

Township 21 N. R. 6 E 6th P. M.

From the corner to Sections 35 and 36 on the South boundary of the Township and on the 5th Standard Parallel North I run N

North between Sections 35 and 36.

Variation 14°. 22' East.

40.00 Set a post in mound with trench and pits, as per instructions for a quarter Section Corner.

80.00 Set a post in mound with trench and pits as per instructions for Corner to Sections 25. 26. 35 and 36.

Roling prairie Soil 2nd Rate.

East on Random line between Sects 25 and 36.

Variation 14°. 22' East.

40.00 Set temporary quarter Sect Corner

79.68. Intersected the East boundary of the Township at Post, the corner to Sections 25 & 36. from which

Township 21 N. R 6 E 6th P. M.

Corner I run

West on true Line between Sections 25 and 36.

Variation 14° 22' East

39.84 Set a Post in Mound with Trench and Pits as per Instructions for a quarter Section Cor.

79.68 The Corner to Sections 25. 26. 35 & 36.

Land Rolling, Soil 1st Rate.

North between Section 25 & 26.

Variation 14° 40' East

40.00 Set a Post in Mound with trench and Pits as per Instructions for a quarter Section Corner

80.00 Set a Post in Mound with Trench and Pits as per instructions for Corner to Sections 23. 24. 25 & 26.

Land Rolling, Soil 2nd Rate

East on Random Line between Sections 24 and 25.

Township 21 N R 6 E 6th P.M.

Variation 14° 30' East

40.00 Set a Post for a Temporary quarter Section Corner

80.34 Intersected the East boundary of the Township 151 links North of Corner to Sections 24 and 25. from which Corner I run West on true Line between Sections 24 and 25.

Variation 13° 25' East

40.17 Set a Post in Mound with trench and Pits as per instructions for a quarter Section Corner

80.34 The Corner to Sections 23. 24. 25 & 26. Land Rolling, Soil 2d Rate

---

North between Section 23 & 24.

Variation 13° 05' East

40.00 Set a Post in Mound with Trench and Pits as per instructions for a quarter Section Corner

80.00 Set a Post in Mound with the

Township 21 N R 6 E 6th P.M.

Trenches and Pits as per instructions for Corner to Sections 13. 14. 23 & 24. Land Rolling, Soil 2d Rate.

East on Random Line between Sections 13 & 24.

Variation 13° 30' East

40.00 Set a Post for a temporary quarter Section Corner

80.47 Intersected the East boundary of the Township 79 links North of Corner to Sections 13 & 24. from which Corner I run West on true Line between Sections 13 & 24.

Variation 12° 56' East

40.24 Set a Post in Mound with the Trench and Pits as per instructions for a quarter Section Corner

80.47 The Corner to Sections 13. 14. 23 & 24. Land Rolling, Soil 1st Rate

Township 21 N.

North between Sections 13 & 14

Variation 12° 28' East

40.00 Set a Post in Mound with trench and Pits as per instructions for a quarter Section Corner

67.50 Ravine 10 lks, wide Runs S.W.

80.00 Set a Post in Mound with trench and Pits as per instructions for Corner to Sections 11. 12. 13 and 14.

Land Rolling, Soil 2d Rate

East on Random Line between Sections 12 & 13.

Variation 13° East

40.00 Set a Post for a temporary the Quarter Section Corner

73.00 Ravine Runs South

80.50 Intersected East boundary of Township 97 links North of Corner to Sections 12 & 13. from which Corner I run

West on true Line between

Range 6th East of 6th P.M.

Sections 12 and 13.

Variation 12° 18' East

40.25 Set a Post in Mound with trench and Pits as per instructions for a quarter Section Corner

80.50 The Corner to Sections 11. 12. 13 & 14.

Land Rolling, Soil 2d Rate

North between Sections 11 & 12

Variation 12° 40' East

40.00 Set a Post in Mound with trench and Pits as per instructions for a quarter Section Corner

80.00 Set a Post in Mound with trench and Pits as per instructions for Corner to Sections 1. 2. 11. and 12.

Land Rolling, Soil 2d Rate

East on Random Line between Sections 1. and 12.

Variation 12° 50' East

Township 21 N.

40.00 Set a Post for a temporary quarter Section Corner

80.98 Intersected the East boundary of Township 133 links North of Corner to Sections 1. and 12. From which Corner I run West on true Line between Sections 1. and 12.

Variation 11° 53' East

40.49 Set a Post in Mound with the trench and Pits as per instruction for a quarter Section Corner

80.98 The Corner to Sections 1. 2. 11. & 12. Land Rolling, Soil 2d Rate.

North on Random Line between Sections 1. and 2.

Variation 11° East.

40.00 Set temporary quarter Sect Cor.

55.42 Creek 10 links wide runs West, a few trees on the banks.

Range 6 E. 6th Pm

79.92 Intersected North boundary of the Township 87 links East of Corner to Sects 1 & 2 from which Corner I run South on true line between Sects 1 & 2

Variation 11° 37' East.

39.92 Set a post in mound with trench & pits as per instruction for a quarter Sect Cor.

79.92 The Corner to Sects 1. 2. 11 & 12. Rolling prairie Land. Soil 2nd Rate, Timber Burr oak & Cottonwood.

North between Sections 34 & 35.

Variation 13° 15' East

40.00 Set a Post in Mound with trench and Pits as per instruction, for a quarter Section Corner

80.00 Set a Post in Mound with trench and Pits as per instructions for Corner to Sections 26. 27. 34. & 35. Land Rolling, Soil 2d Rate

Township 21 N

East on Random Line between
Sections 26 and 35.
Variation 13° East

40.00 Set a Post for a temporary
quarter Section Corner

73.00 Intersect West Point Road bears N & S.

79.35 Intersected N. & S. Line 255 lks
South of Corner to Sections 25.
26. 35. and 36. from which
Corner I run
West on true line between
Sections 26 and 35.
Variation 11° 12' East

39.67 Set a Post in Mound with
trench and Pits as instructed for a quarter
Section Corner

79.35 The Corner to Sections 26. 27. 34 & 35.
Land level and Rolling. Soil 1st Rate

North between Sections 26 & 27.
Variation 13° 42' East

Range 6 E. 6th P.M.

40.00 Set a Post in Mound with
trench and Pits as instructed for a quarter
Section Corner

80.00 Set a Post in Mound with
trench and Pits as instructed for Corner
to Sections 22. 23. 26 & 27.
Land Rolling Soil 1st Rate

East on Random Line between
Sections 23 and 26.
Variation 12° 45' East

40.00 Set Post for a temporary
quarter Section Corner

80.04 Intersected N. and S. Line
57 links North of Corner to
Sections 23. 24. 25 & 26.
from which Corner I run
West on true Line between
Sections 23 & 26.
Variation 12° 20' East

40.02 Set Post in Mound with

Township 21 N.

Trench and Pits, as per instructions, for a quarter Section Corner

80.04 The Corner To Sections 22. 23. 26 & 27.
Land Rolling Prairie, Soil 2d Rate

North between Sections 22 & 23.
Variation 12° 34' East

40.00 Set a Post in Mound with Trench and Pits, as per instructions, for a quarter Section Corner

80.00 Set a Post in Mound with Trench and Pits, as per instructions, for Corner to Sections 14. 15. 22 and 23.
Land level & Rolling, Soil 2d Rate

East on Random Line between Sections 14 and 23.
Variation 12° 30' East

40.00 Set a Post for a temporary quarter Section Corner

80.20 Intersected N. and S. Line 112.4 North of Corner To Sections 13. 14.

Range 6 E 6th P.M.

23 and 24. from which Corner I run
West on True Line between Sections 14 and 23.
Variation 11° 42' East

40.00 Set a Post in Mound with Trench and Pits, as per instructions, for a quarter Section Corner

80.20 ~~Set a~~ The Corner To Sections 14. 15. 22 & 23.
Lands Rolling, Soil 2d Rate

North between Sections 14 & 15.
Variation 12° 44' East

36.00 Intersect West Point Road.

40.00 Set a Post in Mound with Trench and Pits, as per instructions, for a quarter Section Corner

80.00 Set a Post in Mound with Trench and Pits, as per instructions, for Corner To Sections 10. 11. 14 & 15.
Lands Rolling, Soil 1st Rate.

Township 21 N.

East on Random Line between
Sections 11 and 14.
Variation 12° East

5.39 Marine Rocks N. W.
29.00 Marine Rocks S. W.
40.00 Set a Post for a temporary quarter
Section Corner
79.30 Intersected N. & S. Line 19 links
North of Corner to Sections 11. 12.
13 and 14. from which Corner
I. run
West on true Line between Sections 11. & 14.
Variation 11° 52' East
39.65 Set a Post in Mound with the
trench and Pits as per instructions for a quarter
Section Corner
79.30 The Corner to Sections 10. 11. 14 & 15.
Land Rolling. Soil 1st Rate.

North between Sections 10. & 11.
Variation 12° 30' East

R 6 E 6th P.M.

40.00 Set a Post in Mound with
French and Pits as per instructions for a quarter
Section Corner
80.00 Set a Post in Mound with
French and Pits as per instructions for Corner
to Sections 2. 3. 10 & 11.
Land Rolling. Soil 2d Rate

East on Random Line between
Sections 2 and 11.
Variation 12° 40' East
40.00 Set a Post for a temporary
quarter Section Corner
80.29 Intersected N. and S. Line
142 links North of Corner to
Sections 1. 2. 11 and 12. from
which Corner I run
West on true Line between
Sections 2 and 11.
Variation 11° 39' East
40.1[illegible] Set a Post in Mound with the

Township 21 N

trench and Pits as per instruction for a quarter
Section Corner
80.39 The Corner to Sections 2. 3. 10 & 11.
Land Rolling, Soil 2d Rate.

North on Random Line between
Sections 2 and 3.
Variation 12° East.
40.00 Set temporary quarter Sect Cor.
79.71 Intersected North boundary of Township
140 links West of Corner to Sects 2 & 3.
from which Corner True
South on true line between Sects 2 & 3.
Variation 11° East.
39.71 Set a post in mound with trench & pits
as per Instructions for a quarter Sect Cor.
79.71 The Corner to Sects 2. 3. 10 & 11.
Roling prime, Soil 2nd Rate.
August 1st 1857

Range 6 E 6th P.M.

North between Sections 33 & 34.
Variation 13° 30' East
40.00 Set Post in mound with
trench and Pits as per instruction for a quarter
~~Section Corner~~
50.75 Creek 6 links wide runs S.E.
80.00 Set Post in mound with
trench and Pits as per instruction for Corner to
Sections 27. 28. 33. & 34.
Land Rolling. Soil 1st Rate.

East on Random between
Sections 27 & 34.
Variation 13° East
40.00 Set a Post for a temporary
quarter Section Corner
* 47.50 Elkhorn Riva 300 lks wide by Measurement runs S.E.
69.80 Enter March bears N. & S.
73.80 Leave March bears N. & S.
80.80 Intersected N. & S. Line 56 links
North of Corner to Sections

Township 18 21 N

26. 27. 34 and 35. from which
Corner I run
West on true line between Sections
27 and 34.
Variation 12° 36' East
40.40 Set a Post in Mound with Trench
and Pits as per instructions for a quarter Section Cor.
80.80 Set a Post in Mound with a
Trench and Pits as per instructions for Corner to
Sections 27. 28. 33. & 34.
Land River Bottom level. Soil 1st Rate.

North between Sections 27 & 28.
Variation 13° East
4.00 Set a Post in Mound with Trench
and Pits as per instructions for a quarter Section Corner
48.50 Elkhorn River 300 links wide by Measurement Runs N.E.
Trees skirting North bank
70.00 Elkhorn River 300 links wide by measurement Runs N.W.
Skirted with Willows on North Side
80.00 Set a Post in Mound with Trench

Range 19 6 E 6th P.M.

and Pits as per instructions for Corner to Sections
21. 22. 27 and 28.
Land level Bottom Soil 1st Rate.
Timber Cottonwood & Willows.

East on Random Line between
Sections 22 and 27.
Variation 12° 40' East by measurements.
12.75 Elkhorn River 350 links wide
Runs S.W. Timber Skirted on both Sides
40.00 Set a Post for a temporary
Quarter Section Corner.
44.01 Entered Lake bears S.E. and N.W.
51.71 Leave Lake bears S.E. & N.W.
79.90 Intersected N. and S. Line
at Post to Sections 22. 23. 26.
and 27. from which Corner
I run
West on true line between
Sections 22 and 27.
Variation 12° 40' East
39.95 ~~39.85~~ Set a Post in Mound with

Township 21 N.

Trench and Pits as per instructions for a quarter Section Corner

79.90 The Corner to Sections 21. 22. 27 & 28.
Land level Bottom, Soil 1st Rate.
Timber Cottonwood & Willows.

North Between Sections 21 & 22.

Variation 11° 34' East

40.00 On slope of bank of Elkhorn. I therefore Set a post in mound with trench and pits as per Instructions. 100 links East of true Corner as a witness to the Same.

40.30 Elk horn Creek. 340 links by measurement wide runs N. E.

44.00 Enter timber bears N. E & S. W.

47.00 Leave timber and Enter prairie bears N. E & N. W.

80.00 Set a post in mound with trench and pits as per instructions for Corner to Sects. 15. 16. 21. & 22.
Level bottom. Soil 1st Rate.
Timber Cottonwood & Willows. —
Undergrowth Same & Vines

Range 6 E 6th P. M.

East on Random line between Sects. 15 & 22.
Variation 12° 40' East

12.00 Enter marsh bears N. W. & S. E.

13.00 Leave marsh bears N. W & S. E. & Enter Willows & Cottonwood bearing N. W. & S. E.

28.00 Leave Willows & Cottonwood & Enter prairie bearing N. W & S. E.

40.00 Set temporary quarter Sect Cor.

45.00 Enter Slough bears N. W & S. E.

51.40 Leave Slough bears N. W & S. E.

80.38 Intersected the N & S line 70 links North of Corner to Sects. 14. 15. 22 & 23 from which Corner I run West on true line between Sects. 15 & 22
Variation 12° 10' East.

40.19 Set a post in mound with trench & pit as per instructions for a quarter Sect Cor.

80.38 The Corner to Sects. 15. 16. 21 & 22.
West of Slough level bottom. East of Same Rolling prairie. Soil 1st Rate —
Timber Cottonwood & Willows

Township 21 N.

North between Sects 15 & 16

Variation 12°. 24' East.

15.00 Elk horn Creek. 300 links wide by measurement runs S.W.

and Enter timber bears with Creek.

26.00 Elk horn Creek 200 links wide by measurement runs S.E.

32.00 Leave timber bears S.E. & N.W.

40.00 Set post in mound with trench & pits as per instructions for 1/4 Sect Cor.

46.98 Elk horn Creek 240 links wide by measurement runs N.W.

and Enter timber bears with Creek.

56.00 Elk horn Creek 200 links wide by measurement runs East.

60.80 Elk horn Creek 240 links wide by measurement runs West.

66.00 leave timber bears S.E. & N.W.

80.00 Set a post in mound with trench & pits as per instructions for Corner to Sects 9. 10. 15 & 16.

Level bottom. Soil 1st Rate.

Timber Cottonwood & Willows.

East on Random line between Sects 10 & 15

Variation 12° East.

16.00 Enter timber bears N & S.

22.00 Leave timber bears N.W. & S.W.

Range 6 E. 6th P.M.

22.95 Elk horn Creek 210 links wide by measurement, runs S.W.

40.00 Set temporary quarter Sect Cor.

54.00 Slough 800 links wide bears S.E. & N.W.

72.80 a Road bears S.E. & N.W.

80.67 Intersected the N & S line 25 links North of Corner to Sects 10. 11. 14 & 15. from which Corner I run

West on true line between Sects 10 & 15

Variation 11° 49' East.

40.34 Set a post in mound with trench & pits as per instructions for a quarter Sect Cor.

80.67 the Corner to Sects 9. 10. 15 & 16.

Land West of Slough level bottom. East of same Rolling prairie. Soil 1st Rate.

Timber Cottonwood & Willows

North between Sections 9 & 10.

Variation 12° 40' East

6.00 Enter timber N. W. and S. E.

10.00 Right Bank of Elk Horn River runs S. E. and leave timber bears E & W.

Township 2 N.

19.70 Right Bank of Elk Horn again, runs S.W. = Line passes through a bend

40.00 Set a Post in Mound with Trench and Pits as per instructions for a quarter Section Corner

80.00 Set a Post in Mound with Trench and Pits as per instructions for Corner to Sections 3. 4. 9 and 10.

Land level Bottom, Soil 1st Rate.

Timber Cottonwood & Wills.

East on Random Line between Sections 3 and 10.

Variation 12° East

30.50 Elkhorn River 300 lks wide by measurement runs S.W. a few trees skirting the Banks

40.00 Set a Post for a temporary quarter Section Corner

63.00 Circular Road 2 chains in diam.

70.63 Road bears North & South

80.38 Intersected N. & S. Line 31. links South of Corner to Sections 2. 3. 10 and 11. from which Corner I run

Range 6 E. 6th P.M.

West on true Line between Sections 3 and 10.

Variation 12° 13' East

40.19 Set a Post in Mound with Trench and Pits as per instructions for a quarter Section Corner

80.38 The Corner to Sections 3. 4. 9 & 10.

Land level Bottom, Soil 1st Rate

Timber Cottonwood & Willows.

North on Random line between Sections 3. & 4.

Variation 11° 30' East

37.05 Elk horn Creek 210 links wide by measurement runs N.E.

40.20 39.50 Enter timber bears with River or Creek.

40.00 Set temporary quarter Sect Cor.

57.70 Elk horn Creek 260 links wide by measurement runs S.W.

79.28 Intersected North boundary of Township 59 links West of Corner to Sects 3 & 4 from which Corner I run South on true line between Sects 3 & 4

Variation 11° 05' East.

39.28 Set a post for a quarter Sect Corner.

Township 21 N.

from which a
Cottonwood 20in dia bears N 56¾° E. 116 links dist
a Cottonwood 22in dia bears N 20¾° W. 82 links dist
79.28 The Corner to Sect, 3. 4. 9 & 10.
Level bottom Soil 1st Rate.
Timber Cottonwood & Willows. undergrowth
Same & Vines

North between Sections 32 & 33.
Variation 13° 30' East
40.00 Set a Post in Mound with
Trench and Pits as instructing for a quarter
Section Corner
73.14 Raising 10 lks wide runs East
76.90 do 10 lks wide runs N.W.
78.00 do 10 lks wide runs N E.
80.00 Set a Post in Mound with the
trench and Pits as instructing for Corner to
Sections 28. 29. 32 and 33.
Land Rolling Prairie, Soil 1st Rate

Range 6 E. 6th P. M.

East on Random Line
between Sections 28 & 33.
Variation 12° 40 East
4.00 Raising 10 lks wide runs N.E.
40.00 Set a Post for a temporary
quarter Section Corner.
80.10 Intersected N. and S. Line
61 links North of Corner
to Sections 27, 28, 33 & 34.
From which Corner I run
West on true Line between
Sections 28 and 33.
Variation 12° 14' East
40.05 Set a Post in Mound with
Trench and Pits as instructing for a Quarter
Section Corner
80.10 The Corner to Sections 28. 29. 32
and 33.
Land Rolling Prairie
Soil 1st Rate

Township 21 N.

North between Sections 28 & 29

Variation 13° East

40.00 Set a Post in Mound with trench and Pits as per instructions for a quarter Section Corner

54.00 Ravine 40 lks. wide runs N. E.

80.00 Set a Post in Mound with trench and Pits as per instructions for Corner to Sections 20. 21. 28 and 29.

Land Rolling Prairie, Soil 1st Rate

East on Random Line between Sections 21 and 28.

Variation 12° 10' East

5.00 Ravine 10 lks wide runs S. E.

40.00 Creek 30 links wide runs N. E.

Set a Post for temporary Quarter Section Corner 100. links West of true temporary quarter Sect Cor.

42.50 Elkhorn River 300 links wide runs S. W. and Enter timber bears with Creek

Range 6 E. 6th P. M.

62.85 Elkhorn River 230 lks. w. runs N. W.

68.00 Leave timber S. E. & N. W.

80.42 Intersected the N. and S. Line 25 links North of Corner to Sections 21. 22 27 & 28. from which Cor. I run

West on true Line between Sections 21 & 28.

Variation 12° East

41.21 Set a witness Post in Mound with trench and Pits as per instructions for quarter Section Corner 100. links West of true Corner (in Creek)

80.42 The Corner to Sections 20. 21. 28 and 29.

Land West of River Rolling do East of same level Bottom

Soil 1st Rate.

Timber Cottonwood & Willows

North between Sections 20 & 21.

Township 21 N.

Variation 11° 10' East

3.30 Creek 10 lks wide runs S.E.

40.00 Set a Post in Mound with trench and Pits as per instruction for a quarter Section Corner

80.00 Set a Post in Mound with trench and Pits as per instruction for Corner to Sections 16. 17. 20 & 21.

Land Rolling Prairie Soil 1st Rate.

East on Random Line between Sections 16 & 21.

Variation 12° East

40.00 Set a Post for a temporary quarter Section Corner

52.80 Elkhorn River 190 lks wide runs S.E. and Enter timber bears with River

56.75 Leave timber runs North & South

80.06 Intersected N. & S. Line 45 links North of Corner to Sections 15. 16. 21 and 22.

Range 6 E. 6th P.M.

From which Corner I run West on true Line between Sections 16 & 21.

Variation 11° 41' East

40.03 Set a post in mound with trench & pits as per instruction for a quarter Sect Cor.

80.06 The Corner to Sects 16. 17. 20 & 21. West of River Rolling. East of same level. Soil 1st Rate.

Timber Cottonwood & Willows — undergrowth. Same & vines

North between Sects 16 & 17.

Variation 12° 15' East

40.00 Set a post in mound with trench & pits as per instruction for quarter Sect Cor.

80.00 Set a post in mound with trench & pits as per instruction for Cor to Sects. 16. 17. 20 & 21.

Land level. Soil 1st Rate.

Township 21 N.

East on Random line between Sects 9 & 16.
Variation 12°.30' East

40.00 Set temporary quarter Sect Cor.
49.00 Crk. 30 links wide runs N. E.
80.06 Intersected N and S line 15 links North of Corner to Sects. 9. 10. 15 & 16. from which Corner I run.
West on true line between Sects 9 & 16.
Variation 12°.23' East

40.03 Set a post in mound with trench & pits as per instructions for quarter Sect Cor.
80.06 The Corner to Sects. 8. 9. 16 & 17
Land level. Soil 1st Rate.

North between Sects 8 & 9.
Variation 12°.20' East

30.00 Ravine runs N. E.
40.00 Set a post in mound with trench & pits as per Instructions for a quarter Sect Cor
80.00 Set a post in mound, with trench &

Range 6 E. 6th P.M.

pits as per instructions for Corner to Sects 4. 5. 8 & 9.
Land level. Soil 1st Rate.

East on a Random line between Sects 4 & 9.
Variation 12°.30' East

40.00 Set temporary quarter Sect Cor.
79.08 Intersected the N & S line 20 links South of Corner to Sects. 3. 4. 9 & 10. from which Corner I run
West on true line between Sects 4 & 9.
Variation 12°.38' East

39.54 Set a post in mound with trench & pits as per instructions for a quarter Sect Cor.
79.08 The Corner to Sects 4. 5. 8 & 9.
Land level. Soil 1st Rate.

North on Random line between Sects 4 & 5.
Variation 12°.30' East

40.00 Set temporary quarter Sect Cor.
78.22 Intersected North boundary of Township

Township 21 N

84 links East of Corner to Sects 4 & 5
from which Corner I run
South on true line between Sects 4 & 5
Variation 13°.06 East.

38.22 Set a post in mound with trench & pits
as per instructions for a quarter Sect Cor.

78.22 The Corner to Sects 4. 5. 8 & 9.
Land level. Soil 1st Rate.
August 3rd 1857

North between Sects 31 and 32.
Variation 13°.30' East.

40.00 Set a post in mound with trench & pits
as per instructions for a quarter Sect Cor.

72.50 a Ravine runs S.E.

80.00 Set a post in mound with trench and
pits as per instructions for ~~a quarter~~
~~Sect~~ Cor. to Sec. 29. 30. 31 & 32
Land Roling. Soil 1st Rate.

East on Random line between Sect 29 & 32.

Range 6 E 6th P. M.

Variation 12°.40' East.

40.00 Set temporary quarter Sect Cor.

50.80 Ravine runs S.W.

80.20 Intersected the N and S. line 67
links North of Corner to Sects.
28. 29. 32 & 33. from which Corner I run
West on true line between Sects 29 & 32.
Variation 12°.11' East.

40.10 Set a post in mound with trench &
pits as per instructions for a quarter
Sect Cor.

80.20 the Corner to Sects. 29. 30. 31. & 32
Land Roling. Soil 1st Rate.

West on Random line between Sect 30 & 31.
Variation 12°.15 East

14.50 Ravine runs S.W.

40.00 Set temporary quarter Sect Cor.

78.42 Intersected west boundary 38 links
South of Cor. to Sects 30 & 31 from
which Corner I run.

Township 21 N.

East on true line between Sects 30 & 31.
Variation 11°59' East.

38.42 Set a post in mound with trench & pits as per instructions for a quarter sect Cor.

~~78.42~~ The Cor to Sects. 29. 30. 31. & 32.
Land Rolling Soil 1st Rate

North between Sects 29 & 30.
Variation 13° East.

18.80 Ravine runs S. E.

40.00 Set a post in mound with trench and pits as pr. instructions for a quarter sect Cor.

80.00 Set a post in mound with trench & pits as pr. instructions for Corner to Sects. 19. 20. 29 & 30.
Land Rolling. Soil 1st Rate

East on Random line between Sects 20 & 29
Variation 12°15' East.

14.00 Ravine runs S. E.

Range 6 E. 6th P. M.

20.20 Same Ravine runs S. W.

22.50 Same Ravine runs S. E.

40.00 Set temporary quarter Sect Cor.

80.54 Intersected the S & S line 43 links North of Corner to Sects. 20. 21. 28 & 29. from which Corner Drum

West on true line between Sects 20 & 29
Variation 11°57' East.

40.27 Set a post in mound with trench and pits as pr. instructions for a Quarter Sect Cor.

80.54 The Cor. to Sects. 19. 20. 29. & 30
Land Rolling. Soil 1st Rate.

West on Random line between Sects 19 & 30
Variation 12° East.

37.20 Ravine runs S. W.

40.00 Set temporary quarter Sect Cor.

77.22 Intersected West boundary 26 links North of Corner to Sects. 19 & 30 from which Corner Drum

Township 21 N.

East on true line betwn Sects 19 & 30.
Variation 12°. 11' East.

37.22 Set a post in mound with trench & pits as per instructions for a quarter Sect Cor

77.22 The Corner to Sects 19. 20. 29 & 30.
Land Rolling. Soil 1st Rate.

North between Sects 19 & 20
Variation 11° 10' East.

40.00 Set a post in mound with trench & pits as pr. instructions for a quarter Sect Cor.

80.00 Set a post in mound with trench & pits as pr. instructions for Corner to Sect 17. 18. 19 & 20.
Land Rolling. Soil 1st Rate.

East on Random line betwn Sects 17 & 20
Variation 12° 50' East.

11.80 Ravine runs S.E.
13.00 Same Ravine S.W.

Range 6 E 6th P.M.

13.50 Same Ravine runs S.E.
22.00 Same Ravine runs S.W.
40.00 Set temporary quarter Sect Cor.
80.68 Intersected N and S line 70 links North of Corner to Sects. 16. 17. 20 & 21 from which Cor Drum.
West on true line betwn Sects. 17 & 20.
Variation 12° 20' East.

40.34 Set a post in mound with trench and pits as pr. instructions for quarter Sect Cor.

80.68 The Corner to Sects. 17. 18. 19 & 20
Land Rolling. Soil 1st Rate.

West on Random line betwn Sects 18 & 19.
Variation 12° East.

40.00 Set temporary quarter Sect Cor.
77.83 Intersected West boundary. 122 links North of Corner to Sects 18 & 19. from which Corner Drum.
East on true line betwn Sects 18 & 19.

Township 21 N.

Variation 12° 52' East.

37.83 Set a post in mound with trench & pits as per instructions for a quarter Sect Cor.

77.83 The Corner to Sects. 17. 18. 19 & 20.
Rolling prairie. Soil 1st Rate.

North between Sects 17 & 18.
Variation 12° East.

40.00 Set a post in mound with trench & pits as per instructions for a quarter Sect Cor.

80.00 Set a post in mound with trench & pits as per Instructions for Corner to Sects. 7. 8. 17 & 18.
Sand Rolling Soil 1st Rate.

East on Random line between Sects 8 & 17
Variation 12° 30' East.

40.00 Set temporary quarter Sect Cor.

79.75 Intersected N & S line 66 links South of Corner to Sect 8. 9. 16 & 17. from which Corner I run.
West on true line between Sects. 8 & 17.

Range 6 E. 6th P. M.

Variation 12° 58' East

39.88 Set a post in mound with trench & pits as per instructions for a quarter Sect Cor.

79.75 The Corner to Sect 7. 8. 17 & 18.
Land Rolling. Soil 1st Rate.

West on Random line between Sects. 7 & 18
Variation 12° 50' East.

33.25 Narrow cross N.W.

40.00 Set temporary quarter Sect Cor.

79.90 Intersected West boundary 45 links North of Cor. to Sect 7 & 18. from which Corner I run.
East on true line between Sects. 7 & 18
Variation 13° 09' East.

39.90 Set a post in mound with trench and pits as per instructions for a quarter Sect Cor.

79.90 The Cor to Sects 7. 8. 17 & 18.
Sand Rolling. Soil 1st Rate.

Township 21 N.

North between Sects 7 & 8.
Variation 12° 15' East

18.50 Ravine runs N.E.
40.00 Set a post in mound with trench & pits as per instructions for a quarter Sect Cor.
41.00 a deep ravine runs N.E.
80.00 Set a post in mound with trench & pits as per instructions for Corner to Sects 7. 8. 17 & 18.
Land Roling. Soil 1st Rate.

East on Random line between Sects 5 & 8.
Variation 13° East.

40.00 Set temporary quarter Sect Cor.
79.22 Intersected N & S line 16 links North of Corner to Sects 4. 5. 8 & 9. from which Corner I run
West on true line between Sects 5 & 8.
Variation 12° 53' East
39.61 Set a post in mound with trench & pits as per instructions for a quarter Section Corner.

Range 6 E. 6th Pr.

79.22. The Corner to Sects 5. 6. 7 & 8.
Land level. Soil 1st Rate

West on Random line between Sects 6 & 7.
Variation 13° East.

40.00 Set temporary quarter Sect Cor.
69.00 Ravine runs N.E.
80.83. Intersected West boundary at Corner to Sects 6 & 7. from which Corner I run.
East on true line between Sects 6 & 7.
Variation 13° East.

40.83 Set post in mound with trench & pits as per instructions for a quarter Sect Cor.
80.83 The Corner to Sects 5. 6. 7 & 8.
Land Roling. Soil 1st Rate.

North on Random line between Sects 5 & 6.
Variation 12° 50' East.

40.00 Set temporary quarter Sect Cor

Township 21 N

77.86 Intersected North boundary 152 links East of Corner to Sects 5 & 6. from which Cor. I[illegible]
18.50 South on true line between Sects 5 & 6.
40.00 Variation 13°55' East.
37.86 Set a post in mound with trench & pits
41.00 as per instructions for a quarter Sect Cor
80.00 77.86 The Corner to Sects. 5. 6. 7 & 8.
Land Roling. Soil 1st Rate,
August 3rd 1857.

General Description

Land in this township generally
40.00 1st quality, with a very large
79.2[illegible] proportion of bottom land along
the Elk horn River.
There is considerable timber on the
Elkhorn, consisting principally of
Cottonwood, and Willow, with an
39.61 occasional Burr oak, it is large
and make Excellent Rails or how

Range 6 E. 6th P.M.

logs.
Elk Horn is a noble stream
from 200 to 500 links wide, slow
Current, and Sandy bottom.
and can be forded with teams
at every half or 3/4 of mile.
the water is generally 4 ft deep
at its usual level. There are
no settlements in this Township

List of Names.

a list of the names of the individuals employed
to assist in running measuring, or marking the
lines and Corners described in the foregoing field notes 1857
of Township 21 North, Range 6 East of 6th P.M. Shewing 1857
the respective capacities in which they acted.

John Farnham Compassman,
Harman Lauforsieck Chainman
Frank McKenna Chainman
Bushnell B. Loomis Chainman
Thos C. Jones Chainman
F. R. Hile ageman
James Quinn ageman
George Cockling Flagman

How did you obtain width of Elkhorn
Notes not headed —
Timber not described
What part of Elkhorn is 2 lks wide — see G. D.

Ex'd Nov 2nd 1857

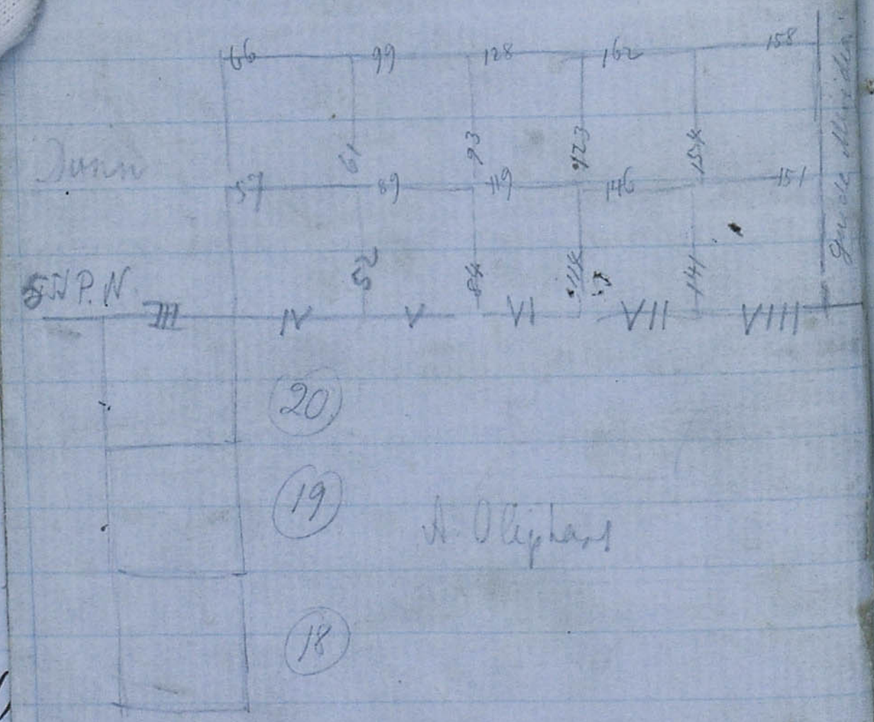

1850
40.00
41.00
80.00
40.00
79.2
39.6

22

Compd Descriptive List
Contract No. 210 Completed

Field Notes

of the Subdivision lines of Township 22 North, of Range 6 East of the 6th Principal Meridian in the Territory of Nebraska as Surveyed by Isaac C. Stuck Deputy Surveyor under his Contract dated 19th day of June 1857. — No. 210

Subdivision Commenced. August 4th 1857
Subdivision Completed August 7th 1857

all Right

Names & duties of Assistants

John Farnham Compassman
Harman Lanfersick Chainman
Frank McKenna Chainman
Bushnell B. Loomis Chainman
Thos C Jones Chainman
Frank Hill Axeman
James Quinn Axeman
George Cocklin Flagman.

Township 22 N. Range 6 East

6	38	5	27	4	20	3	13	2	7	1
37		36		27		20		12		6
7	36	8	26	9	19	10	12	11	6	12
35		34		25		19		11		5
18	33	17	25	16	18	15	11	14	5	13
33		32		24		17		10		4
19	32	20	23	21	17	22	10	23	4	24
31		30		23		16		9		3
30	30	29	22	28	15	27	9	26	3	25
29		29		21		14		8		2
31	28	32	21	33	14	34	8	35	2	36

Township 22 N. R. 6 E. of 6th P.M.

To determine the proper adjustment of my Compass for subdividing this Township I commence at the Corner to Township 21 & 22 N R. 6 & 7 East, and run North on a blank line along the East boundary of Sect 36.

Variation 12° 30' East,

40.01 To a point 2 links West of quarter Sect Cor.

79.96 To a point 5 links West of Corner to Sect. 25 & 36. To retrace this line or run parallel thereto my Compass must be adjusted to a Variation of 12° 28' E.

Subdivision Commenced August 4th 1857

From the Corner to Sect. 1. 2. 35 & 36. on the South boundary of the Township I run

2/52 Township 22 N R 6 E 6th P M

North between Sects. 35 & 36.

Variation 12° 28' East.

40.00 Set a post in mound with trench & pits as pr. instructions for quarter Sect Cor.

80.00 Set post in mound with trench & pits as pr Instructions for Corner to Sects. 25. 26. 35. & 36.

Very Roling prairie. Soil 2nd Rate.

East on Random line between Sects 25 & 36.

Variation 12° East.

40.00 Set temporary quarter Sect Corner.

79.76 Intersected East boundary of Township 48 links South, of Corner to Sects 25 and 36. from which Corner Iron

West on true line between Sects 25 and 36

Variation 12° 20' East

39.88 Set post in mound with trench & pits as pr Instructions for a quarter Sect Cor.

79.76 The Cor to Sects. 25. 26. 35. & 36.

Roling prairie Soil 2nd Rate.

Township 22 N R 6 E 6th P M

3/53

North between Sects. 25 and 26.

Variation 13° 28' East.

40.00 Set post in mound with trench & pits as pr. Instructions for a quarter Sect Cor.

80.00 Set post in mound with trench & pits as pr. instructions for Corner to Sects 23. 24. 25 & 26.

Roling prairie. Soil 1st Rate

East on Random line between Sects 24 & 25.

Variation 12° East.

40.00 Set temporary quarter Sect Cor.

79.49 Intersected East boundary of Township 97 links South of Corner to Sects 24 & 25. from which Corner Iron

West on true line between Sects 24 & 25

Variation 12° 47' East.

39.75 Set post in mound with trench & pits as pr instructions for a quarter Sect Cor.

79.49 The Corner to Sects 23. 24. 25 & 26.

Roling prairie. Soil 2nd Rate.

Township 22 N R 6 E 6th P M

North between Sects 23 & 24

Variation 14° 05' East,

40.00 Set post in mound with trench & pits as pr Instructions for a quarter Sect Cor

80.00 Set post in mound with trench & pits as pr Instructions for Corner to Sects 13. 14. 23 & 24

Roling prairie. Soil 2nd Rate,

East on Random line between Sects. 13 & 24.

Variation 12° East.

40.00 Set temporary quarter Sect Cor.

79.16 Intersected East boundary of Township 141 links South of Corner to Sects 13 & 24. from which Corner Iron

West on true line between Sects 13 & 24

Variation 13° East.

39.58 Set post in mound with trench & pits as pr. instructions for quarter Sect Cor.

79.16 The Corner to Sects. 13. 14. 23. and 24.

Roling prairie. Soil 2nd Rate.

Township 22 N R 6 E 6th P M

North between Sects 13 and 14.

Variation 13°. 55' East.

40.00 Set post in mound with trench & pits as pr instructions for quarter Sect Cor.

80.00 Set post in mound with trench & pits as pr instructions for Corner to Sects 11. 12. 13 & 14.

Roling prairie. Soil Sandy & 2nd Rate,

East on Random line between Sects 12 & 13

Variation 12° East,

40.00 Set temporary quarter Sect Cor.

79.11 Intersected East boundary 50 links South. of Corner to Sects 12. & 13 from which Cor Iron

West on true line between Sects 12 & 13.

Variation 12°. 21' East.

39.56 Set post in mound with trench & pits as pr instructions for quarter Sect Cor.

79.11 The Corner to Sects 11. 12. 13. & 14.

Roling prairie. Soil 2nd Rate.

6/56

Township 22 N R 6 E 6th P M

North between Sects 11 and 12.

Variation 13° 20' East.

12.00 Raring 20 links wide runs N.W.

4 40.00 Set post in mound with trench and pits as pr instruction for quarter Sect Cor.

8 80.00 Set post in mound with trench & pits as pr. instructions for Corner to Sects 1. 2. 11. & 12.

Rolling prairie. Soil 1st Rate.

East on Random line between Sects 1 and 12.

Variation 12° East.

4 40.00 Set temporary quarter Sect Cor.

7 79.03 Intersected East boundary 12 links South of Corner to Sects 1 & 12. from which Cor I run West on true line between Sects 1 & 12.

Variation 12.05 East.

3 39.52 Set post in mound with trench & pits as pr instructions for quarter Sect Cor.

7 79.03 The Corner to Sects. 1, 2. 11 & 12.

Rolling prairie Soil 1st Rate,

7/57

Township 22 N R 6 E 6th P M

North on Random line between Sects 1 and 2.

Variation 13° East.

40.00 Set temporary quarter Sect Cor.

79.40 Intersected North boundary 61 links East of Corner to Sects 1 and 2 from which Cor I run South on true line between Sects 1 & 2

Variation 13.26 East

39 40 Drove charred stake, Set post and raised Mound with trench & pits as pr Instructions for quarter Sect Cor.

79 40 The Corner to Sects 1. 2. 11 & 12

Land gently rolling prairie Soil 1st Rate

8-58

Township 22 N R 6 E 6th P M

North between Sects 34 and 35.

Variation 12°.40' East.

14.30 Ravine runs N.E.

40.00 Set post in mound with trench & pits as pr instructions for quarter Sect Cor.

49.00 Road bears N.W & S.E.

80.00 Set post in mound with trench & pits as pr. Instructions for Corner to Sects 26. 27. 34 and 35.

Rolling prairie. Soil 1st Rate.

East on Random line between Sects 26. & 35

Variation 12°.40 East.

40.00 Set temporary quarter Sect Cor.

79.03 Intersected N & S line 161 links South of Corner to Sect. 25. 26. 35 & 36. from which Corner I run

West on true line between Sects 26 & 35

Variation 13°.49' East

79.52 Set post in mound with trench and pits as pr Instructions for a quarter Sect Cor.

59

Township 22 N R 6 E 6th P M

79.03 The Corner to Sects 26. 27. 34 & 35.

Land hilly. Soil 2nd Rate.

North between Sects. 26 and 27.

Variation 14° East

25.30 Ravine runs N.W.

40.00 Set post in mound with trench and pits, as pr instructions for quarter Sect Cor.

80.00 Set post in mound with trench and pits as pr. instructions for Cor to Sects. 22. 23. 26 & 27

Land mostly level. Soil 1st Rate.

East on Random line between Sects 23 & 26.

Variation 13°.40 East.

40.00 Set temporary quarter Sect Cor.

46.50 deep ravine runs N.E.

79.30 Intersected the N & S line 64 links South of the Corner to Sects 23. 24. 25 & 26. from which Corner I run.

10/60

Township 22 N R 6 E 6th P M

West on true line between Sects 23 and 26.

Variation 14.07 East

39.65 Set post in mound with trench and pits as pr instructions for quarter Sect Cor.

79.30 The Cor to Sects 22. 23. 26 and 27.

Land hilly. Soil 2nd Rate.

North between Sects. 22 and 23.

Variation 14° 15' East.

40.00 Set post in mound with trench and pits as pr instructions for a quarter Sect Cor.

80.00 Set post in mound with trench and pits as pr instructions for Cor to Sects. 14. 15. 22. & 23.

Land Rolling prairie. Soil 1st Rate.

East on Random line between Sects. 14 and 23.

Variation 14° East.

40.00 Set temporary quarter Sect Cor.

79.52 Intersected N and S line 88 links North of Corner to Sects. 13. 14. 23 & 24 from which Cor. Iron

11-61

Township 22 N R 6 E 6th P M

West on true line between Sects 14 & 23.

Variation 13° 22' East.

39.76 Set post in mound with trench & pits as pr instructions for quarter Sect Cor.

79.52 The Cor to Sects. 14. 15. 22 & 23.

Land hilly. Soil 2nd Rate.

North between Sects 14 and 15.

Variation 13° 05' East.

10.00 Ravine runs N.W.

40.00 Set post in mound with trench & pits as pr instructions for quarter Sect Cor.

80.00 Set post in mound with trench and pits as pr instructions for Cor to Sects 10. 11. 14 & 15.

Land Rolling. Soil 2nd Rate.

East on Random line between Sects 11 & 14

Variation 13° 30' East.

40.00 Set temporary quarter Sect Cor.

79.45 Intersected N and S line 28 links North

12-62

Township 22 N R 6 E 6th P M

of Corner to Sects 11. 12. 13 and 14. from which Cor I run.

West on true line between Sects 11 and 14

Variation 13° 18' East

39.73 Set post in mound with trench and pits as pr instructions for a quarter Sect Cor.

79.45 The Cor to Sects 10. 11. 14 & 15.

Land Roling prairie. Soil 2nd Rate.

North between Sects 10 and 11.

Variation 12° 43' East.

40.00 Set post in mound with trench and pits as pr. Instructions for a quarter Sect Cor.

80.00 Set post in mound with trench and pits as pr instructions for Cor to Sects 2. 3. 10 & 11.

Land Roling prairie. Soil 1st Rate.

East on Random line between Sects 2 & 11

Variation 13° 30' East.

40.00 Set temporary quarter Sect Cor.

79.02 Intersected N & S line 91 links

13-63

Township 22 N R 6 E 6th P M

North of Cor to Sects 1. 2. 11 & 12 from which Corner I run

West on true line between Sects 2 & 11

Variation 12.51 E.

39.51 drove Charred Stake. Set post and raised mound with trench & pits as pr instructions for quarter Sect Cor.

79.02 The Corner to Sects 2. 3. 10 & 11.

Gently roling prairie land. Soil 1st Rate.

North on Random line between Sects 2 & 3

Variation 13° 30' East.

40.00 Set temporary quarter Sect Cor

79.49 Intersected North boundary 70 links

East of Corner to Sects 2 & 3. from which Corner I run

South on true line between Sects 2 & 3

Variation 14° E.

39.49 drove charred stake. Set post and raised mound with trench & pits. as pr instructions for quarter Sect Cor.

79.49 The Cor to Sects 2. 3. 10 & 11

14-64

Township 22 N R 6 E 6th P. M.

August 5th 1857

North between Sects. 33 and 34.

Variation 12°.50' East.

0,60 Leave timber bearing E & W.

1,00 Slough 50 links wide bears E & W.

1,50 Enter prairie bearing E & W.

34,80 Elkhorn Creek. 240 links wide by measurement runs S.E. and Enter timber bears with Creek

40,00 Set a post for a quarter Sect Cor. from which a Cottonwood 20in dia bears N 28½ E. 17 links dist a Cottonwood 23in dia bears S 72° W. 28 links dist.

61,50 Elkhorn Creek. 300 links wide by measurement runs S.W.

66,00 Leave timber bears E & W.

80,00 Set post in mound with trench and pits as pr. Instructions for Corner to Sects 27. 28. 33 & 34.

Level bottom Soil 1st Rate.

Timber Cottonwood & Willows.

East on Random line between Sects 27 & 34

Variation 13°.47' East.

40,00 Set temporary quarter Sect Cor.

41,00 Elk horn Creek 600 links wide by measurement runs a little South of East.

15-65

Township 22 N R 6 E 6th P. M.

55.70 Steam Saw mill 3 Chains South on Townsite of West point.

60.00 Road bear N & S.

80 17 Intersected N and S line at Corner to Sects. 26. 27. 34 & 35 from which Corner I run.

West on true line between Sects 27 & 34

Variation 13°.47' East.

40 09 Set post in mound with trench and pits as pr. instructions for a quarter Sect Cor.

80 17 The Cor. to Sects. 27. 28. 33 & 34.

Level bottom. Soil 1st Rate.

North between Sects 27 & 28.

Variation 13°.50' East.

19 00 Enter Slough bearing E & W.

22 00 Leave Slough bearing E & W.

40 00 Set post in mound with trench and pits as pr. instructions for quarter Sect Cor.

48 00 Slough 2 chains wide bears E & W.

16-66

Township 22 N R 6 E 6th P M

80.00 Set post in mound with trench and pits as pr. instruction for Corner to Sects 21. 22. 27 & 28.
Level bottom. Soil 1st Rate.

East on Random line between Sects. 22 & 27.
Variation 13°. 30' East.

9.30 Elkhorn Creek 340 links wide runs South a few trees skirting its banks.
40.00 Set temporary quarter Sect Cor.
56.00 Road bears N and S.
80.40 Intersected N and S line at Corner to Sects. 22. 23. 26 & 27. from which Cor. I run
Westerly true line between Sects 22 & 27.
Variation 13°. 30' East.
40.20 Set post in mound with trench and pits as pr instruction for a quarter Sect Cor.
80.40 The Corner to Sects 21. 22. 27 & 28.
Level bottom. Soil 1st Rate.
Timber

17-67

Township 22 N R 6 E 6th P M

North between Sects 21 and 22.
Variation 13°. 55' East.

16.61 To bend of Elk Horn Creek runs S. E.
25.00 Leave bend runs S. W. line dont Cross Creek.
40.00 Set post in mound with trench and pits as pr instructions for quarter Sect Corner.
65.00 Enter timber bears E & W.
66.00 Slough 200 links wide bears E & W. now dry by measurement.
68.15 Elkhorn Creek runs S. E. 230 links wide and leave timber bears E & W.
80.00 Set post in mound with trench and pits as pr instructions for Corner to Sects. 15. 16. 21. & 22.
Level bottom. Soil 1st Rate;
Timber Cottonwood & willows

East on Random line between Sects 15 & 22.
Variation 13°. 30' East.

40.00 Set temporary quarter Sect Cor.
43.00 Road bears N & S.
80.80 Intersected N and S line 21 links

Township 22 N R 6 E 6th P M

North of Corner to Sects 14. 15. 22 & 23 from which Corner I run
West on true line between Sects 15 and 22.
Variation 13° 21' East.

40.40 Set post in mound with trench and pits as pr instruction for quarter Sect Cor.
80.80 The Corner to Sects. 14. 15. 22 & 23.
West of Road level bottom, East of same Rolling. Soil 1st Rate.

North between Sects 15 and 16.
Variation 12° 30' East.

7.50 Plum Creek 50 links wide runs N.W.
40.00 Set post in mound with trench and pits as pr instructions for a quarter Sect Cor.
77.40 Same Creek 30 links wide runs S.E.
80.00 Set post in mound with trench and pits as pr instructions for Corner to Sects 9. 10. 15 & 16.
Level bottom Soil 1st Rate.

Township 22 N R 6 E 6th P M

East on Random line between Sects 10 & 15
Variation 13° 30' East.

15.40 Road bears N and S.
40.00 Set temporary quarter Sect Cor.
80.10 Intersected N and S line 153 links north of Corner to Sects. 10. 11. 14 & 15. from which Corner I run
West on true line between Sects 10 & 15
Variation 12° 25' East

40.05 Set post in mound with trench and pits as pr instructions for quarter Sect Cor.
80.10 The Corner to Sects 9. 10. 15 & 16.
Rolling prairie Soil 1st Rate.

North between Sects 9 & 10
Variation 12° 31' East.

5.63 Creek 20 links wide runs West.
14.60 ~~Plum~~ Creek 30 links wide runs S.W.
18.00 Plum Creek 30 links wide runs S.E.
32.00 Road bears N.W. & S.E.
40.00 Set post in mound with trench and pits as pr instructions for quarter Sect Cor.

459/62

Township 22 N R 6 E 6th P M

80.00 Set post in mound with trench and pits as pr. Instruction for Corner to Sects 3. 4. 9 & 10.
Level bottom Soil 1st Rate.

East on Random line between Sects 3 & 10.
Variation 12° 30' East.

40.00 Set post for temporary quarter Sect Cor.

80.10 Intersected N and S line 77 links North of Corner to Sects 2. 3. 10 & 11. from which Corner I run West on true line between Sects 3 & 10
Variation 11° 57' East.

40.05 Set post in mound with trench & pits. as pr. instruction for a quarter Sect Cor.

80.10 The Cor to Sects 3. 4. 9 & 10.
Rolling prairie. Soil 1st Rate.

North on Random line between Sects 3 & 4
Variation 14° East.

Township 22 N R 6 E 6th P M

40.00 Set temporary quarter Sect Cor.

79.05 Intersected North boundary 40 links West of Corner to Sects 3 & 4 from which Corner I run South on true line between Sects 3 & 4
Variation 13° 43' East.

39.05 drove charred stake Set post and raised mound with trench & pits as pr. instruction for quarter Sect Cor.

79.05 The Corner to Sects 3. 4. 9 & 10.
gently rolling prairie. Land. Soil 1st Rate.

North between Sects 32 and 33.
Variation 12° 40' East.

40.00 Set post in mound with trench and pits as pr instructions for quarter Sect Cor.

80.00 Set post in mound with trench and pits as pr instructions for Cor to Sects 28. 29 32 & 33.
Rolling prairie. Soil 1st Rate.

East on Random line between Sects 28 & 33
Variation 13° 40' East.

Township 22 N R 6 E 6th P M

40.00 Set temporary quarter Sect Corner,
79.92 Intersected N and S line 36 links
North of Cor to Sect. 27. 28. 33 & 34
from which Cor I run
West on true line between Sect. 28 & 33
Variation 13° 25' East.
39.96 Set post in mound with trench and pits
as pr instructions for quarter Sect Cor.
79.92 The Cor to Sect 28. 29. 32 & 33
Land level. Soil 1st Rate.

North between Sect. 28 & 29.
Variation 14° East.
40.00 Set post in mound with trench and pits
as pr instructions for quarter Sect Cor.
80.00 Set post in mound with trench &
pits as pr. instructions for Corner
to Sect. 20. 21. 28 & 29.
Land level. Soil 1st Rate.

Township 22 N R 6 E 6th P M

East on Random line between Sect. 21 & 28.
Variation 13° 50' East.
40.00 Set temporary quarter Sect Cor.
80.87 Intersected N and S line 178 links
North of Corner to Sect. 21. 22. 27 & 28
from which Corner I run
West on true line between Sect. 21 & 28
Variation 12° 34' East.
40.44 Set post in mound with trench and
pits as pr Instructions for quarter Sect
Cor.
80.87 The Corner to Sect 20. 21. 28 & 29.
Land level Soil 1st Rate.

North between Sect. 20 & 21
Variation 13° 40' East.
40.00 Set post in mound with trench & pits
as pr instructions for quarter Sect Cor.
52.00 Slough 200 links wide bears E & W.
55.00 Entire timber bears E & W.
73.40 Leave timber bears E & W.
74.30 Slough 140 links wide bears E & W.

Township 22 N R 6 E 6th P M

80.00 Set post in mound with trench & pits as pr. Instructions for quarter Sect Cor.
Level bottom. Soil 1st Rate.
Timber Buroak & walnut.

East on Random line between Sects 16 & 21.
Variation 13° 30' East

38.45 Elk horn Creek 310 links wide by measurement runs S. E. a few trees on East bank.
42.00 Set temporary witness to quarter Sect Cor.
74.25 Plum Creek 25 links wide runs S. E.
80.96 Intersected N and S line 162 links North of Corner to Sects. 15. 16. 21 & 22. from which Corner I run
West on true line between Sects 16 & 21.
Variation 12° 21' East.
43.08 Set a post in mound with trench and pit, ~~260 links West of true~~ Corner. as a witness to the same,
80.96 The Corner to Sect. 16. 17. 20 & 21
Level bottom. Soil 1st Rate.
Timber Buroak & Walnut

Township 22 N R 6 E 6th P M

North between Sects 16 & 17.
Variation 13° East.

13.00 Elk horn Creek 200 links wide by measurement runs N. E. and Entire timber bearing with stream
33.85 Elk horn Creek 230 links wide by measurement runs S. W. and leave timber bearing with Creek.
40.00 Set post in mound with trench & pits as pr. instructions for quarter Sect Cor.
69.80 Elk horn Creek 340 links wide by measurement runs S. E.
80.00 Set post in Mound with trench & pits as pr instructions for Corner to Sects 8. 9 16 & 17.
Level bottom, Soil 1st Rate.
Timber Cottonwood & Willows.

East on Random line between Sects 9 & 16.
Variation 12° 15' East.

40.00 Set temporary quarter Sect Cor.
78.55 Plum Creek 30 links wide runs S. E.

26-76

Township 22 N R 6 E 6th P M

80.18 Intersected N and S line 74 links South of Corner to Sect. 9. 10. 15 & 16. from which Corner I run West on true line between Sects 9 & 16.

Variation 12° 47' East.

40.09 Set post in mound with trench and pits as pr instructions for quarter Sect Cor.

80.18 The Corner to Sects. 8. 9. 16 & 17. Very slightly rolling prairie. Soil 1st Rate.

North between Sects 8 & 9.

Variation 12° 15' East

40.00 Set post in mound with trench and pits as pr instructions for quarter Sect Cor.

80.00 Set post in mound with trench and pits as pr instructions for Corner to Sects. 4. 5. 8 & 9.

Level Bottom. Soil 1st Rate.

27-77

Township 22 N R 6 E 6th P M

East on Random line between Sects 4 & 9.

Variation 12° 45' East.

25.00 House stands about 6 chs. North.

27.80 Road bears NW & SE.

39.88 Plum Creek 25 links wide runs SE.

41.00 Set temporary witness to quarter Sect Cor.

80.18 Intersected N & S line 37 links South of Corner to Sects 3, 4, 9 & 10. from which Corner I run West on true line between Sects 4 & 9.

Variation 13° 01' East

39.09 Set a post in mound with trench & pits as pr instructions 100 links East of true Corner as a witness to the same.

80.18 The Corner to Sects. 4. 5. 8 & 9 West of Creek Rolling. East of same level. Soil 1st Rate.

North on Random line between Sects 4 & 5

Variation 12° 30' East.

40.00 Set temporary quarter Sect Corner.

Township 33 N R 6 E 6th P M

79.88 Intersected North boundary 132 links East of Corner to Sects 4 & 5. from which Corner I run
South on true line between Sects 4 & 5
Variation 13° 27' East.

39.88 Set post in mound with trench & pits as per instructions for quarter Sect Cor.

79.88 the Corner to Sects 4. 5. 8 & 9.
Rolling prairie. Soil 1st Rate.
august 6th 1857

North between Sects 31 & 32.
Variation 12° 50' East

40.00 Set post in mound with trench and pits as per Instructions for a quarter Sect Cor.

80.00 Set post in mound with trench & pits as per Instructions for Corner to Sect, 29. 30. 31 & 32.
Land Rolling Soil 1st Rate.

Township 33 N R 6 E 6th P M

East on Random line between Sects 29 & 32
Variation 13° East.

40.00 Set temporary quarter Sect Cor.

57.50 Ravine runs N. E.

79.83 Intersected N and S line 10 links South of Corner to Sects. 28. 29. 32 & 33. from which Corner I run.
West on true line between Sects 29 & 32.
Variation 13° 04' East.

39.92. Set post in mound with trench and pits as per Instructions for a quarter Sect Cor.

79.83 The Corner to Sects. 29. 30. 31. & 32.
Land Rolling. Soil 1st Rate.

West on Random line between Sects 30 & 31
Variation 13° East.

40.00 Set temporary quarter Sect Cor.

80.03 Intersected West boundary 136 links South of Corner to Sects 30 & 31 from which Cor. I run.
East on true line between Sects. 30 & 31.
Variation 12° 02' East.

Township 22 N R 6 E 6th P M

40.03 Set post in mound with trench & pits
as pr Instructions for a quarter Sect Cor.
80.03 The Corner to Sects 29. 30. 31 & 32,
Land Rolling, Soil 1st Rate.

North between Sects 29 & 30.
Variation 13° 30' East.
40.00 Set post in mound with trench & pits
as pr. Instructions for quarter Sect Cor.
80.00 Set post in mound with trench & pits
as pr instructions for Corner to Sect
19. 20. 29 & 30.
Roling prairie. Soil 1st Rate,

East on Random line between Sects 20 & 29
Variation 13° 10' East
1.50 Ravine runs S.E.
40.00 Set temporary quarter Sect Cor.
79.32 Intersected N & S line 42 lin ks North
of Corner to Sects. 20. 21. 28 & 29. from
which Cor. Iron

Township 22 N R 6 E 6th P M

West on true line between Sects 20 & 29.
Variation 12° 52' East.
39.66 Set post in mound with trench and pits
as pr instructions for quarter Sect Cor.
79.32 The Corner to Sects. 19. 20. 29 & 30.
Land Roling. Soil 1st Rate.

West on Random line between Sects 19 & 30.
Variation 12° 15' East.
40.00 Set temporary quarter Sect Cor.
50.50 Ravine runs S.W.
79.08 Intersected west boundary 15 lin ks
South of Corner to Sects 19 & 30
from which Corner Iron.
East on true line between Sects 19 & 30
Variation 11° 47' East.
39.08 Set post in mound with trench & pits
as pr instructions for quarter Sect Cor.
79.08 The Corner to Sects. 19. 20. 29 & 30.
Land Rolling Soil 1st Rate,

Township 22 N R 6 E 6th P M

North between Sects 19 & 20.
Variation 13° 30' East

0.55 Ravine runs N. E.
40.00 Set post in mound with trench & pits as pr instructions for quarter Sect Cor.
80.00 Set post in mound with trench & pits as pr instructions for Corner to Sects 17. 18 19 & 20.
Land Rolling. Soil 1st Rate.

East on Random line between Sects 17 & 20
Variation 12° 30' East.
40.00 Set temporary quarter Sect Cor.
80.17 Intersected N and S line 82 links north of Corner to Sect. 16. 17. 20 & 21. from which Corner Brass V West on true line between Sect 17 & 20
Variation 11° 55' East.
40.00 Set post in mound with trench & pits as pr instructions for quarter Sect Cor.

Township 22 N R 6 E 6th P M

80.17 The Cor to Sects. 17. 18, 19. & 20
Roling prairie Soil 1st Rate,

West on Random line between Sects 18 & 19
Variation 12° East.
40.00 Set temporary quarter Sect Cor.
77.80 Intersected West boundary 48 links South of Corner to Sects 18 & 19 from which Cor Brass
East on true line between Sects 18 & 19
Variation 11° 40' East.
37.80 Set post in mound with trench & pits as pr instructions for quarter Sect Cor.
77.80 The Corner to Sects. 17. 18. 19 & 20.
Land Roling. Soil 1st Rate,

North between Sects 17 & 18.
Variation 11° 23' East.
40.00 Set post in mound with trench & pits as pr instructions for quarter Sect Corner.

Township 22 N R 6 E 6th P M

56.00 Enter timber bearing S E & N W.
56.80 Elkhorn Creek 200 links wide runs S.E.
60.00 Leave timber bearing S.E. & N.W.
80.00 Set post in mound with trench & pits as pr instructions for Corner to Sects. 7. 8. 17 & 18.
Level bottom. Soil 1st Rate.
Timber. Cottonwood. Buraak & willows

East on Random line between Sects 8 & 17.
Variation 12° East.

40.00 Set temporary quarter Sect Cor.
66.00 Intersect Left bank of Elk horn Creek runs N.E.
72.00 Intersect Left bank again runs S.E. line passes through bend but dont Cross.
80.00 Intersected N and S line 11 links South of Corner to Sects. 8. 9. 16 & 17. from which Corner I run
West on true line between Sects 8 & 17
Variation 12°.05 East

Township 22 N R 6 E 6th P M

40.00 Set post in mound with trench & pits as pr instructions for quarter Sect Corner.
80.00 The Corner to Sects. 7. 8. 17. & 18.
Level bottom. Soil 1st Rate.

West on Random line between Sects 7 & 18
Variation 12°.30 East.

3.00 Enter timber bearing N & S.
14.50 Elkhorn Creek 300 links wide runs S.W.
38.00 Leave timber bears N W & S.E.
40.00 Set temporary quarter Sect Cor.
79.88 Intersected West boundary 129 links South of Corner to Sects 7 & 18 from which Corner I run.
387/55
East on true line between Sects 7 & 18.
Variation 11°35 East.
39.88 Set post in mound with trench & pits as pr Instructions for a Quarter Sect Corner.

Township 22 N R 6 E 6th P M

79.88 The Corner to Sects 7. 8. 17 & 18.
East of Creek level bottom, West of Same
Rolling, Soil 1st Rate.
Timber Bur Oak & Cottonwood &
Willows Undergrowth Same & vines

North between Sects 7 & 8.
Variation 12°. 30' East,
12.00 Elk horn Creek 210 links wide runs S.W.
28.90 Elk horn Creek 220 links wide runs N.E.
a few trees on Either bank where the
line Crosses,
40.00 Set post in Mound with trench & pits
as per instructions for quarter Sect Cor.
80.00 Set post in mound, with trench & pits
as per instructions for Corner to Sects.
5. 6. 7 & 8.
Level bottom. Soil 1st Rate,
Timber Oak. Elm. & Cottonwood

East on Random line between Sects 5 & 8
Variation 12° East.

Township 22 N R 6 E 6th P M

40.00 Set temporary quarter Sect Corner,
73.00 Enter Slough bearing N.W. & S.E.
78.00 Leave Slough bearing N.W. & S.E.
79.84 Intersected N. and S. line 27 links
South of Corner to Sects. 4. 5. 8 & 9.
from which Corner I run.
East on true line between Sects 5 & 8.
Variation 12°. 11' East.
39.92 Set post in mound with trench & pits
as per instruction for quarter Sect Cor.
79.84 The Corner to Sects 5. 6. 7 & 8.
Level bottom. Soil 1st Rate.

West on Random line between Sects 6 & 7.
Variation 12°. 30' East,
31.00 Elk horn Creek 210 links wide runs S.W. &
Enter Willows & a few Cottonwood
40.00 Set temporary quarter Sect Cor.
43.00 Leave Willows & Cottonwood bearing S.W. & N.E.
80.00 Intersected West boundary 8 links North
of Corner to Sects 6 & 7. from which Corner
I run

Township 22 N R 6 E 6th P M

East on true line between Sects 6 & 7.
Variation 12° 33' East.

40.06 Set post in mound with trench & pits as per instructions for quarter Sect Corner.

80.06 The Corner to Sects. 5. 6. 7 & 8.
Level bottom. Soil 1st Rate.

North on Random line between Sects 5 & 6.
Variation 13° 30' East.

40.00 Set temporary quarter Sect Cor.

42.50 Enter Slough bearing E & W.

47.50 Leave Slough bearing E & W.

79.75 Intersected North boundary at Corner to Sects 5 & 6. from which Corner I run

South on true line between Sects 5 & 6.
Variation 13° 30' East.

39.75 Set post in mound with trench & pits as per instructions for quarter Sect Cor.

79.75 The Corner to Sects 5. 6. 7 & 8.
Level bottom. Soil 1st Rate

Township 22 N. Range 6 E 6th P.M.

General description

Land in this Township of first and second rate, there is a large quantity of bottom land along the Elkhorn, all of first quality.—
Timber on Elk horn Mostly Cottonwood, and Willow, and some Bur oak, the Former large and straight the last, Scrubby & Small,
Elk Horn River is a fine stream, from 200 to 400 links wide 4 ft deep and Sandy bottom, the banks are from 6 to 12 ft high and are seldom overflowed.
There are several settlements in this Township & a Steam Saw Mill building near the South boundary.

List of Names.

a list of names of the individuals employed to assist in running measuring or marking the lines and corners described in the foregoing field notes of Township No. 22 North of Range 6 East of the 6th Principal Meridian Nebraska Territory shewing the respective capacities in which they acted,

John Farnham Compassman
Harman Lanforsick Chainman
Frank McKenna Chainman
Brehnell B. Loomis Chainman
Thos C Jones Chainman
F. R. Hile axeman
James Quinn Axeman
Geo Cocklin Flagman

Contract No. 185

Field Notes of the Subdivision lines of Township Number Twenty three North of Range number Six East of the Sixth Principal Meridian, in the Territory of Nebraska

Surveyed by Bernard D Holbrook U S. Deputy Surveyor under his contract Number 185 dated 20 May A D 1857

Subdivision commenced August 18th completed August 20th A D 1857

Rcd Nov 19th 1857

A list of the names of the individuals employed to assist in running measuring and marking the lines and corners described in the following Field Notes of Township Number Twenty Three North of Base line of Range Number Six East of the Fifth Principal Meridian Showing the respective capacities in which they acted

Christian G Stutzman	Chainman
William A Cox	Chainman
Levi Van Amum	Chainman
William S McCrea	Chainman
Gustavus A Hess	Axeman
Nelson W Thompson	Axeman
Charles M Cocklin	Axeman
Wallace Walcott	Axeman
Warren S Simpson	Flagman
Norman B Colbrook	Flagman
John G Clopper	Compassman

Township 23 N. Range 6 East

6	33	5	24	4	18	3	12	2	6	1
32		31		29		17		12		6
7	31	8	23	9	17	10	11	11	5	12
30		30		22		16		10		5
18	29	17	22	16	16	15	10	14	4	13
29		28		21		15		9		4
19	28	20	21	21	15	22	9	23	3	24
27		26		20		14		8		3
30	21	29	20	28	14	27	8	26	2	25
25		25		19		13		7		2
31	24	32	19	33	13	34	7	35	1	36

Township 23 N Range 6 E. 6th Principal Meridian

To determine the proper adjustment of My Compass for subdividing this Township. I commence at the corner to Townships 22 and 23 N Range 6 and 7 East and run North on a blank line along the East line of Section 36

Variation 12° 30' East

3996 To a point 36 links East of the quarter Section corner

7997 To a point 70 links East of the corner to Sections 25 and 36

To retrace this line or run parallel to My Compass must be adjusted to a variation of

13° 00' East

Subdivision commenced August 18th AD 1857

From the corner to Sections 1 and 2, 35 and 36 on the south boundary of the Township. I run North between Sections 35 and 36

Variation 13° 00' East

4000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

8000 Drove a chained stake and set a post in Mound with trench and pits as per

Township 23 N Range 6 E 5th Principal Meridian

instructions for corner to Sections 25, 26, 35 and 36
Rolling Prairie Sandy soil 2nd rate

East on a random line between Sections 25 and 36
Variation 12° 30' East

4000 set a post for temporary quarter Section corner
7980 Intersected the East boundary of Township 85 links North of the corner to Sections 25 and 36 from which corner I run West on a true line between Sections 25 and 36
Variation 11° 54' East
3990 Dug a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
7980 The corner to Sections 25, 26, 35 and 36
Rolling Prairie Sandy soil 2nd rate

North between Sections 25 and 26
Variation 13° 15' East
4000 Dug a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8000 Dug a chained stake and set a post in Mound with trench and pits as per

Township 23 N Range 6 E 5th Principal Meridian

instructions for corner to Sections 23, 24, 25 and 26
Rolling Prairie Sandy soil 2nd rate

East on a random line between Sections 24 and 25
Variation 12° 15' East
4000 set a post for temporary quarter Section corner
7980 Intersected the East boundary of the Township 10 links North of the corner to Sections 24 and 25 from which corner I run West on a true line between Sections 24 and 25
Variation 12° 11' East
3990 Dug a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
7980 The corner to Sections 25, 26, 23 and 24
Rolling Prairie Sandy soil 2nd rate

North between Sections 23 and 24
Variation 13° 0' East
4000 Dug a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

Township 23 N Range 6 E 6th Principal Meridian

8000 Dug a chained stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 13, 14, 23 and 24
Rolling Prairie Sandy soil 2nd rate

East on a random line between Sections 13 and 24
Variation 12° 30' East

4000 set a post for temporary quarter Section corner
7940 Intersected the East boundary of Township at the corner to Sections 13 and 24 from which corner I run West on a true line between Sections 13 and 24
Variation 12° 30' East

3970 Dug a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
7940 The corner to Sections 13, 14, 23 and 24
Rolling Prairie Sandy soil 2nd rate

North between Sections 13 and 14
Variation 13° 20' East

4000 Dug a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

Township 23 N Range 6 E 6th Principal Meridian

8000 Dug a chained stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 11, 12, 13 and 14
Rolling Prairie Sandy soil 2nd rate

East on a random line between Sections 12 and 13
Variation 12° 30' East

4000 set a post for temporary quarter Section corner
7960 Intersected the East boundary of Township 152 links South of the corner to Sections 12 and 13 from which corner I run West on a true line between Sections 12 and 13
Variation 13° 31' East

3980 Dug a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
7960 The corner to Sections 11, 12, 13 and 14
Rolling Prairie Sandy soil 2nd rate

North between Sections 11 and 12
Variation 14° 00' East

4000 Dug a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

8000 Dove a chaned stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 1, 2, 11 and 12
Rolling Prairie Sandy Soil 2nd rate

East on a random line between Sections 1 and 12
Variation 12° 40' East
4000 set a post for temporary quarter Section corner
8020 Intersected the East boundary of Township 15 links South of corner to Sections 1 and 12 from which corner I run West on a true line between Sections 1 and 12
Variation 12° 46' East
4010 Dove a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8020 The corner to Sections 1, 2, 11 and 12
Rolling Prairie Sandy Soil 2nd rate

North on a random line between Sections 1 and 2
Variation 13° 00' East
4000 set a post for temporary quarter Section corner
8000 Intersected the north boundary of Township at the

corner to Sections 1 and 2 from which corner I run South on a true line between Sections 1 and 2
Variation 13° 00' East
4000 Dove a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8000 The corner to Sections 1, 2, 11 and 12
Rolling Prairie Sandy Soil 2nd rate

North between Sections 34 and 35
Variation 13° 00' East
4000 set a post in a Mound with trench and pits for quarter Section corner as per instructions
8000 Dove a chaned stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 26, 27, 34 and 35
Rolling Prairie Sandy soil 2nd rate

East on a random line between Sections 26 and 35
Variation 12° 30' East
4000 set a post for temporary quarter Section corner

Township 23 N Range 6 E 6th Principal Meridian

8052 Intersected the N and S line at corner to Sections 25, 26, 35 and 36 from which corner I run West on a true line between Sections 26 and 35

Variation 12° 30' East

4026 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

8052 The corner to Sections 26, 27, 34 and 35
Rolling Prairie Sandy Soil 2nd rate

North between Sections 26 and 27

Variation 12° 30' East

4000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

4830 Small stream 8 links wide course S.W.

8000 Drove a chained stake and set a post in Mound with trench and pits as per instructions for corner to sections 22, 23, 26 and 27
Rolling Prairie Sandy Soil 2nd rate

East on a random line between Sections 23 and 26

Variation 12° 30' East

Township 23 N Range 6 E 6th Principal Meridian

1516 Stream 6 links wide course S.W.

4000 Set a post for temporary quarter section corner

8032 Intersected the N and S line 66 links South of corner to Sections 23, 24, 25 and 26 from which corner I run West on a true line between Sections 23 and 26

Variation 12° 58' East

4016 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

8032 The corner to sections 22, 23, 26 and 27
Rolling Prairie Sandy Soil 2nd rate

North between Sections 22 and 23

Variation 13° 00' East

4000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

8000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 14, 15, 22 and 23
Rolling Prairie Sandy Soil 2nd rate

East on a random line between sections 14 and 23

Variation 13° 00' East

Township 23 N Range 6 E 6th Principal Meridian

3520	Stream 3 links wide course S W.
4000	set a post for temporary quarter section corner
8040	Intersected the N and S line 18 links south of corner to Sections 13.14.23 and 24 from which corner I run west on a true line between sections 14 and 23
	Variation 13°08' East
4020	Drove a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter section corner
8040	The corner to sections 14.15.22 and 23
	Rolling Prairie Sandy soil 2nd rate

North between Sections 14 and 15

Variation 13°00' East

4000	Drove a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter section corner
8000	Drove a chaned stake and set a post in a Mound with trench and pits as per instructions for corner to sections 10.11.14 and 15
	Rolling Prairie Sandy soil 2nd rate

East on a random line between Sections 11 and 14

Township 23 N Range 6 E 6th Principal Meridian

Variation 13°00' East

4000	set a post for temporary quarter section corner
4100	wide marshy bottom course S.E. 2 feet deep
6500	~~[illegible]~~ leave marsh
8080	Intersected the N and S line 12 links north of corner to Sections 11.12.13 and 14 from which corner I run west on a true line between Sections 11 and 14
	Variation 13°54' East
4040	Drove a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter section corner
8080	The corner to sections 10.11.14 and 15
	Land level wet Bottom 1st rate soil

North between Sections 10 and 11

Variation 13°00' East

4000	Drove a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter section corner
5000	low marshy bottom 2 feet deep course S.E. 200 chs wide
8000	Drove a chaned stake and set a post in a Mound with trench and pits as per instructions for corner to sections 2.3.10 and 11
	Land low and wet-Level. Soil 1st rate

Township 23 N Range 4 E 6th Principal Meridian

East on a random line between Sections 2 and 11
Variation 13°00' East

4000 set a post for temporary quarter Section corner
5000 Marshy bottom course S.E. 500 chs wide
8096 Intersects the N and S line at the corner to sections 1, 2, 11 and 12 from which corner I run West on a true line between Sections 2 and 11
Variation 13°00' East
4048 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8096 The corner to sections 2, 3, 10 and 11
Low wet Bottom, Land Level. Soil 1st rate

North on a random line between Sections 2 and 3
Variation 13°00' East
2400 leave the Slough course S.E.
4000 set a post for temporary quarter Section corner
8070 Intersect the North boundary of Township 68 links west of corner to Sections 2 and 3 from which corner I run South on a true line between Sections 2 and 3

Township 23 N Range 4 E 6th Principal Meridian

Variation 12°31' East
4070 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8070 The corner to sections 2, 3, 10 and 11
Rolling Prairie Sandy soil 2nd rate
August 18th 1857

North between Sections 33 and 34
Variation 13°45' East
4000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for corner to sections 27, 28, 33 and 34
Level Bottom Land 1st rate clay loam Soil

East on a random line between Sections 27 and 34
Variation 13°00' East
3050 crossed a Lake 5 feet deep 160 links wide no current
4000 set a post for temporary quarter Section corner
7950 Intersect the N and S line at the corner to Sections

Township 23 N Range 6 E 6th Principal Meridian

26, 27, 34 and 35 from which corner I run West on a true line between Sections 27 and 34

Variation 13° 00' East

3975 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

7950 The corner to sections 27, 28, 33 and 34

Level Bottom Land Soil 1st rate clay loam

North between sections 27 and 28

Variation 13° 15' East

4000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

8000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 21, 22, 27 and 28

Land Rolling Sandy Soil 2nd rate

East on a random line between Sections 22 and 27

Variation 13° 00' East

4000 set a post for temporary quarter section corner

7980 Intersected the N and S line 66 links North of corner

Township 23 N Range 6 E 6th Principal Meridian

to Sections 22, 23, 26 and 27 from which corner I run West on a true line between Sections 22 and 27

Variation 12° 32' East

3990 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

7980 The corner to sections 21, 22, 27 and 28

Rolling Prairie Sandy soil 2nd rate

North between sections 21 and 22

Variation 13° 15' East

4000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

8000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 15, 16, 21 and 22

Rolling Prairie Sandy soil 2nd rate

East on a random line between Sections 15 and 22

Variation 12° 30' East

4000 at a post for temporary quarter section corner

8030 Intersected the N and S line 6 links North of corner to

sections 14, 15, 22 and 23 from which corner I run West
on a true line between Sections 15 and 22
Variation 12° 29' East
4015 Drove a chaned stake and set a post in a Mound with trench and pits as
as per instructions for quarter Section corner
8030 The corner to Sections 15, 16, 21 and 22
Rolling Prairie Sandy Soil 2nd rate

North between Sections 15 and 16
Variation 12° 30' East
4000 Drove a chaned stake and set a post in a Mound with trench and pits as
per instructions for quarter Section corner
8000 Drove a chaned stake and set a post in a Mound with trench and pits as per
instructions for corner to Sections 9, 10, 15 and 16
Sand ~~rough and~~ broken soil 2nd rate

East on a random line between Sections 10 and 15
Variation 12° 30' East
4000 set a post for temporary quarter Section corner
7994 Intersected the S and S line 30 links North of corner

to Sections 10, 11, 14 and 15 from which corner I run West
on a true line between Sections 10 and 15
Variation 12° 17' East
3997 Drove a chaned stake and set a post in a Mound with trench and pits as
per instructions for quarter Section corner
7994 The corner to Sections 9, 10, 15 and 16
Rolling Prairie Sandy soil 2nd rate

North between Sections 9 and 10
Variation 12° 30' East
4000 Drove a chaned stake and set a post in a Mound with trench and pits as
per instructions for quarter Section corner
8000 Drove a chaned stake and set a post in a Mound with trench and pits as
per instructions for corner to Sections 3, 4, 9 and 10
Sand gently rolling soil 1st and 2nd rate

East on a random line between Sections 3 and 10
Variation 12° 00' East
4000 set a post for temporary quarter Section corner
7992 Intersected the S and S line 32 links North of corner to

Sections 2, 3, 10 and 11 from which corner I run west
on a true line between Sections 3 and 10
Variation 11°46' East
3996 Drove a chaned stake and set a post in a Mound with trench and pits as
per instructions for quarter Section corner
7992 The corner to Sections 3, 4, 9 and 10
Land Hilly 2nd rate Sandy soil

North on a random line between Sections 3 and 4
Variation 12°45' East
4000 set a post for temporary quarter Section corner
8030 Intersected the North boundary of Township 52 links
East of corner to Sections 3 and 4 from which corner I run
South on a true line between Sections 3 and 4
Variation 13°07' East
4030 Drove a chaned stake and set a post in a Mound with trench and pits
as per instructions for quarter Section corner
8030 The corner to Sections 3, 4, 9 and 10
South of 40 links Land rolling sandy soil 2nd rate
North of 40 links Land high and level 2nd rate soil

North between Sections 32 and 33
Variation 13°00' East
3400 Plum creek 25 links wide course S.E. 3 feet deep
4000 Drove a chaned stake and set a post in a Mound as
per instructions for quarter Section corner
8000 Drove a chaned stake and set a post in a Mound as per
instructions for corner to Sections 28, 29, 32 and 33
Rolling Prairie Sandy soil 2nd rate

East on a random line between Sections 28 and 33
Variation 12°30' East
4000 set a post for temporary quarter Section corner
8046 Intersected the N and S line 50 links north of corner to
Sections 27, 28, 33 and 34 from which corner I run
west on a true line between Sections 28 and 33
Variation 12°09' East
4023 Drove a chaned stake and set a post in a Mound with trench and pits as
per instructions for quarter Section corner
8046 The corner to Sections 28, 29, 32 and 33
Rolling Prairie Sandy soil 2nd rate

North between Sections 28 and 29

Variation 12°45' East

4000 Gen a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

8000 Gen a chained stake and set a post in a Mound with trench and pits as per instructions for corner to sections 20, 21, 28 and 29

Rolling Prairie Sandy soil 2nd rate

East on a random line between Sections 28 and 21

Variation 13°00' East

4000 set a post for temporary quarter Section corner

8008 Intersected the N and S line 7 links north of corner to Sections 21, 22, 27 and 28 from which corner I run West on a true line between sections 28 and 21

Variation 12°57' East

4004 Gen a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

8008 The corner to sections 20, 21, 28 and 29

High rolling Prairie Sandy soil 2nd rate

North between Sections 20 and 21

Variation 12°45' East

4000 Gen a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

8000 Gen a chained stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 16, 17, 20 and 21

Rolling Prairie Sandy soil 2nd rate

East on a random line between sections 16 and 21

Variation 12°00' East

4000 set a post for temporary quarter Section corner

7980 Intersected the N and S line at the corner to Sections 15, 16, 21 and 22 from which corner I run West on a true line between Sections 16 and 21

Variation 12°01' East

3990 Gen a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

7980 The corner to sections 16, 17, 20 and 21

Rolling Prairie Sandy soil 2nd rate

Township 23 N Range 6 E 6th Principal Meridian

North between Sections 16 and 17

Variation 13°00' East

4000 Done a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

8000 Done a chaned stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 8, 9, 16 and 17

Rolling Prairie Sandy Soil 2nd rate

East on a random line between Sections 9 and 16

Variation 12°30' East

4000 set a post for temporary quarter Section corner

8020 Intersected the N and S line 56 links North of corner to Sections 9, 10, 15 and 16 from which corner I run West on a true line between Sections 9 and 16

Variation 12°09' East

4010 Done a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

8020 The corner to Sections 8, 9, 16 and 17

Rolling Prairie Sandy Soil 2nd rate

Township 23 N Range 6 E 6th Principal Meridian

North between Sections 8 and 9

Variation 13°00' East

4000 Done a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

8000 Done a chaned stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 4, 5, 8 and 9

High rolling Prairie Sandy soil 2nd rate

East on a random line between Sections 4 and 9

Variation 12°30' East

4000 set a post for temporary quarter Section corner

8020 Intersected the N and S line 64 links North of corner to Sections 3, 4, 9 and 10 from which corner I run West on a true line between Sections 4 and 9

Variation 12°03' East

4010 Done a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

8020 The corner to Sections 4, 5, 8 and 9

Rolling Prairie Sandy soil 2nd rate

North on a random line between Sections 4 and 5
Variation 13°00' East

4000 set a post for temporary quarter section corner
8020 Intersected the North boundary of Township 20 links
west of corner to Sections 4 and 5 from which corner
I run South on a true line between Sections 4 and 5
Variation 12°51' East
4020 Drove a chained stake and set a post in a Mound with trench and pits
as per instructions for quarter Section corner
8020 The corner to Sections 4, 5, 8 and 9
Rolling Prairie Sandy Soil 2nd rate
August 19th 1857

North between Sections 31 and 32
Variation 13°00' East
350 Elk Horn bottom course S.E. and N.W.
3800 Enter Plum creek bottom course S.E. and N.W.
4000 Drove a chained stake and set a post in Mound with trench and pits
as per instructions for quarter Section corner
8000 Drove a chained stake and set a post in a Mound with trench and pits as per

instructions for corner to Sections 29, 30, 31 and 32
Upland Rolling 2nd rate soil, bottom land level Soil 1st rate clay loam

---

East on a random line between Sections 29 and 32
Variation 12°30' East
4000 set a post for temporary quarter section corner
5000 Plum creek 25 links wide 5 feet deep course S.E.
8060 Intersected the N and S line at the corner to Sections
28, 29, 32 and 33 from which corner I run West on a
true line between Sections 29 and 32
Variations 12°30' East
4030 Drove a chained stake and set a post in a Mound with trench and pits
as per instructions for quarter Section corner
8060 The corner to Sections 29, 30, 31 and 32
~~Upland and bottom~~ Gently Rolling Surface Soil 1st rate clay loam

---

West on a random line between Sections 30 and 31
Variation 12°30' East
1800 leave bottom to Plum creek bears N.E. & S.W.
4000 set a post for temporary quarter section corner

Township 23 N Range 6 E 6th Principal Meridian

7920	Intersected the west boundary of Township 12 links South of corner to Sections 30 and 31 from which corner I run East on a true line between Sections 30 and 31
	Variation 12° 25' East
3920	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
7920	The corner to Sections 29, 30, 31 and 32
	Land Level 2nd rate soil

North between Sections 29 and 30

Variation 12° 30' East

4000	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8000	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 19, 20, 29 and 30
	Rolling Prairie soil 1st rate clay loam

East on a random line between Sections 20 and 29

Variation 12° 30' East

250	Plum creek 5 feet deep 25 links wide course S swift current

Township 23 N Range 6 E 6th Principal Meridian

2100	leave Plum creek bottom course N and S.
4000	set a post for temporary quarter Section corner
8060	Intersected the N and S line at the corner to Sections 20, 21, 28 and 29 from which corner I run west on a true line between Sections 20 and 29
	Variation 12° 30' East
4030	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8060	The corner to Sections 19, 20, 29 and 30
	Land level 1st rate soil clay loam bottom

West on a random line between Sections 19 and 30

Variation 12° 30' East

3700	Bluff course N W and S. E.
4000	set a post for temporary quarter Section corner
7950	Intersected the west boundary of Township 72 links South of corner to Sections 19 and 30 from which corner I run East on a true line between Sections 19 and 30
	Variation 11° 59' East
3950	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner

7950 The corner to Sections 19, 20, 29 and 30
High rolling Prairie Sandy Soil 2nd rate

North between Sections 19 and 30
Variation 12° 00' East

500 Plum creek 20 links wide course S.E.
4000 Drive a chained stake and set a post with trench and pits in a Mound as per instructions for quarter Section corner
8000 Drive a chained stake and set a post with trench and pits in a Mound as per instructions for corner to Sections 17, 18, 19 and 20
Rolling Prairie Sandy Soil 2nd rate

East on a random line between Sections 17 and 20
Variation 12° 30' East

2400 leave bottom course N W.
4000 set a post for temporary quarter Section corner
8076 Intersected the N and S line 24 links north of corner to Sections 16, 17, 20 and 21 from which corner Pecan bears on a true line between Sections 17 and 20
Variation 12° 20' East

4038 Drive a chained stake and set a post with trench and pits in a Mound as per instructions for quarter Section corner
8076 The corner to Sections 17, 18, 19 and 20
Level Land 1st and 2nd rate Soil Sandy

West on a random line between Sections 18 and 19
Variation 12° 00' East

4000 set a post for temporary quarter Section corner
6200 Plum creek 15 links wide course S.E.
7980 Intersected the west boundary of Township at corner to Sections 18 and 19 from which corner Pecan bears East on a true line between sections 18 and 19
Variation 12° 00' East
3980 Drive a chained stake and set a post with trench and pits in a Mound as per instructions for quarter Section corner
7980 The corner to Sections 17, 18, 19 and 20
Level bottom Land Soil 1st rate clay loam

North between sections 17 and 18
Variation 12° 00' East

Township 23 N Range 6 E 6th Principal Meridian

4000	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8000	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 7, 8, 17 and 18
	Rolling Prairie Sandy Soil 2nd rate
	East on a random line between Sections 8 and 17
	Variation 12° 36' East
4000	set a post for temporary quarter Section corner
8002	Intersected the North Bdy line 16 links South of corner to Sections 8, 9, 16 and 17 from which corner North West on a true line between Sections 8 and 17
	Variation 12° 37' East
4000	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8002	The corner to Sections 7, 8, 17 and 18
	Rolling Prairie sandy soil 2nd rate
	West on a random line between Sections 7 and 18
	Variation 12° 30' East

Township 23 N Range 6 E 6th Principal Meridian

4000	set a post for temporary quarter Section corner
7950	Intersected the west boundary of Township 16 links South of corner to Sections 7 and 18 from which corner North East on a true line between Sections 7 and 18
	Variation 12° 23' East
3950	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
7950	The corner to Sections 7, 8, 17 and 18
	Rolling Prairie Sandy Soil 2nd rate
	North between Sections 7 and 8
	Variation 13° 0' East
4000	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8000	Drove a chained stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 5, 6, 7 and 8
	Rolling Prairie Sandy Soil 2nd rate
	East on a random line between Sections 5 and 8
	Variation 12° 30' East

Township 23 N Range 6 E 6th Principal Meridian

4000	set a post for temporary quarter Section corner
8030	Intersected the N and S line 66 links North of corner to Sections 4, 5, 8 and 9 from which corner I run West on a true line between Sections 5 and 8
	Variation 12° 02' East
4015	Drew a chained stake and set a post in a Mound with trench and pits as per instructions for quarter Section corner
8030	The corner to Sections 5, 6, 7 and 8
	Rolling Prairie Sandy Soil 2nd rate

West on a random line between Sections 6 and 7

Variation 13° 00' East

4000	set a post for temporary quarter Section corner
7950	Intersected the west boundary of Township 60 links South of corner to Sections 6 and 7 from which corner I run West on a true line between Sections 6 and 7
	Variation 13° 26' East
3950	Drew a chained stake and set a post in Mound with trench and pits as per instructions for quarter Section corner
7950	The corner to sections 5, 6, 7 and 8
	Rolling Prairie Sandy Soil 2nd rate

Township 23 N Range 6 E 6th Principal Meridian

North on a random line between Sections 5 and 6

Variation 12° 15' East

4000	set a post for temporary quarter Section corner
7990	Intersected the north boundary of Township 80 links East of corner to Sections 5 and 6 from which corner I run South on a true line between Sections 5 and 6
	Variation 12° 22' East
3990	Drew a chained stake and set a post in Mound with trench and pits as per instructions for quarter Section corner
7990	The corner to Sections 5, 6, 7 and 8
	Rolling Prairie Sandy Soil 2nd rate

August 20th 1857

General Description

This Township contains no timber and is badly watered, and the quality of the soil is generally poor. There is a bottom above a mile wide on Plum creek in the South west part of the Township, which is good and rich land

No Settlements in this Township

Prairie Dog city in the S.E. quarter of Section 30

A list of the names of the individuals Employed to assist in running Measuring and Marking the lines and corners described in the fregoing Field Notes of Township Number Twenty Three North of the Base line of Range Six East of the Sixth Principal Meridian

Showing the respective capacities in which they acted

Christian G Stutzman	Chainman
William A Cox	Chainman
Levi Van Arnum	Chainman
William S McCrea	Chainman
Gustavus A Hess	Axeman
Nelson W Thompson	Axeman
Charles M Cochlin	Axeman
Wallace Wolcott	Axeman
Warren G Simpson	Flagman
Norman B Holbrook	Flagman
John G Clossper	Compassman

Field Notes
of the Subdivision
lines of Fractional
Township Number

Twenty Four
North of
Range Number
Six
East of the Sixth P.M.
executed by John Y Cloppers
Deputy Surveyor under
Special instructions
dated the 5th day of
June A.D. 1838

Commenced July 26th AD 1838
completed July 26th AD 1838

Township 24 North Range 6 East 6th P. M.

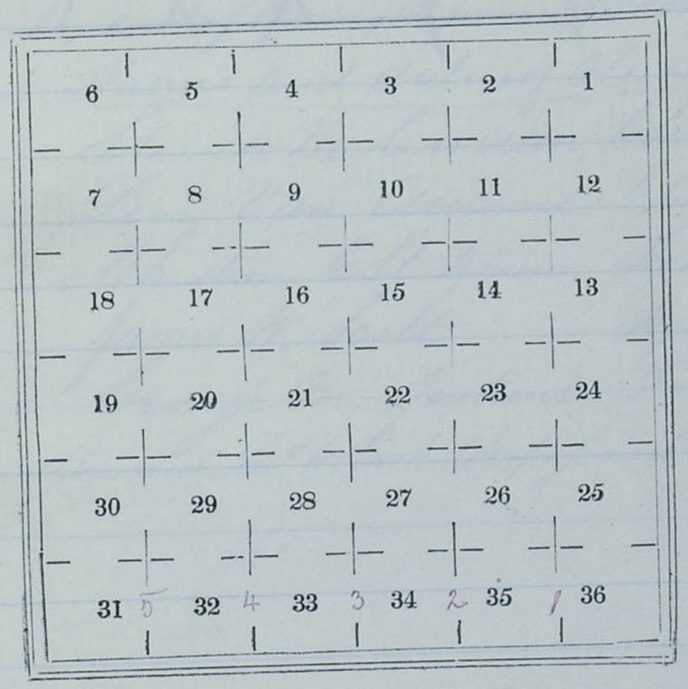

T. 24 N. of R. 6 E. of 6th Prin. Mer.

~~A list of the names of the persons employed to assist in running the subdivision lines of~~
F.l ~~township twenty four North of range six east of the sixth principal meridian~~

Names and duties of Assistants.

Sterritt M Curran, Chainman
Levi Van Arnum Chainman
Christian G Stutzman Axeman
James W. Scott Axeman
George M. Jenkins Flagman
Bernard D. Holbrook Compassman

~~In order~~ To determine the proper adjustment of my compass for Subdividing this township I ~~Start~~ commence at the ~~South~~ corner to townships 23 & 24 N. R 6 & 7 E. and run, ~~East corner of Section thirty six~~ ~~and run~~ North on a blank line along the East boundary of Sec 36

Variation 11° 00' East

40.03 to a point 14 links East of Quarter Section corner

73.10 to a point 30 links East of corner to Fractional Sections 31 & 36

My compass must therefore be adjusted to a variation of ~~10° 58'~~ 11° 13' E.

Subdivision commenced July 26th 1858.

From the corner to Secs 1. 2. 35 & 36 on the south boundary of the Township, I run

[illegible]

North between Sections 35 & 36

Variation ~~10° 58'~~ 11° 13' East

40.00 Drove a charred stake and set a post in mound with trench and pits as per instructions for Quarter Section Corner,

72.80 Intersected South boundary of Omaha Reserve, Drove a charred stake and

set a post in mound with trench and pits as pr. instructions for corner to Fractional Sections 35 & 36. Land rolling, soil 2nd rate

The nearest corner on the reserve line being in sight I run East ~~on a true line~~ between the Omaha reservation and Section 36

Variation 11° 06' East

22.00 to a corner on the South boundary of the Omaha reservation

Surface rolling, soil 2nd rate

North between Sections 34 and 35

Variation 10° 58' East

40.00 Drove a charred stake and set a post in mound with trench and pits as per instructions for Quarter Section corner

73.60 Intersected the South boundary of the Omaha reservation

Drove a charred stake and set

a post in mound with trench and
pits as per instructions for co
ner to sections 34 and 35
Land rolling. Soil 2nd rate prairie

The nearest corner on the South
boundary of the Omaha Reserve
being in sight From
West ~~on a true line~~ between
the Omaha Reserve and Section 34
Variation 11°08' East
17.50 to corner on South boundary of
the Omaha Reserve
Land level, soil good prairie

North between Sections 33 and 3
Variation 11°00' East
40.00 Drove a charred stake and set a
post in mound with trench and pi
as per instructions for quarter section
corner.

Intersected the South boundary of Omaha Reserve
73.10 Drove a charred stake and set a
post in mound with trench and pits
as per instructions for corner to Fractional Sections 33 + 34
Surface rolling soil 2nd rate prairie

A corner on the reserve line being in
sight From East ~~on true line~~
Variation 11°00' East
8.56 to nearest corner on line of reserve
Surface rolling soil 2nd rate

North between Sections 32 and 33
Variation 11°00 East
40.00 Drove a charred stake and set a post
in Mound with trench and pits as per
instructions for quarter Section corner
Intersected South boundary of Omaha Reserve
73.80 Drove a charred stake and
set a post in mound with trench and
pits as per instructions for corner
to fractional sections 32 and 33

T 24 N R 6 E 6th Principal Meridian

Surface rolling soil 2nd rate

The nearest corner on the south boundary of the Omaha reserve being in sight I run

East ~~on a true line~~ between the Omaha reserve and Section 33

Variation 11°00' East

15.20 ~~To a~~ corner on line of reserve

Sandy rolling surface soil 2nd rate

North between Sections 31 and 32

Variation 11°00' East

40.00 Drove a charred stake and set a post in mound with trench and pits as per instructions for quarter section corner

74.40 Intersected the south boundary of the Omaha reserve, ~~at a point 3.20 chains east of the nearest corner~~

Drove a charred stake and set a post in mound with trench and pits as per instructions for

T 24 N R 6 E 6th Principal Meridian

corner to fractional sections 31 and 32

Sandy rolling surface soil 2nd rate

A corner on the reserve line being in sight I run West ~~on a true line~~ between the Omaha reservation and Section 31

Variation 11°00' East

3.20 to a corner on the south boundary of Omaha reservation

Surface rolling soil 2nd rate

July 26th 1838

F 24 N R 6 E 6th Principal Meridian

General Description

The average of land in this township is of medium quality No streams were crossed on line and no bottom land or timber

(+ Insert list here)

We hereby certify that we assisted John Y. Clopper deputy surveyor in surveying the subdivision lines in Township twenty four north of Ranges Six, Seven and Eight East of the Sixth Principal Meridian and that the said townships have been in all respects to the best of our knowledge and belief well and faithfully surveyed and the boundary monuments planted according to instructions furnish-

+ A list of the names of the individuals employed to assist in running, measuring or marking the lines and corners described in the foregoing field notes of Township No 24 North of the base line of Range No 6 East of the 6th Principal Meridian, showing the respective capacities in which they acted.

Sterritt, M. Curran, Chainman
Jerr. Van Arnum. Chainman
Christian G. Stutzman, Axeman
James, W. Scott. Axeman
George, M. Jenkins. Flagman
Bernard D Holbrook. Compassman

ed by the Surveyor General

Christian G. Stutzman, Axeman
James W. Scott Axeman
Levi Van Arnum Chainman
Sterrill McCurran Chainman
George W Jenkins Flagman
Bernard D Holbrook Compassman

Subscribed and sworn to by the above named persons before me a Notary Public in and for the County of Douglas Nebraska Territory the 30th day of July A.D. 1858

William E Moore
Notary Public

I John Y Clopper deputy Surveyor do solemnly swear that in pur-
mance of Special instructions
issued by John Calhoun Surveyor of the Public lands of the United States in the Territories of Kansas and Nebraska, and in strict conformity to the laws of the United States and the Special

instructions aforesaid,
(they being dated the 5 day
of June AD 1858) I have
faithfully surveyed the
subdivision lines of Township
twenty four North of ranges
Six Seven and Eight East of
the Sixth Principal Meridian
in the Territory of Nebraska
And do further solemnly swear
that the foregoing are the
true and original field
notes of said survey

John G. Clapper
Deputy Surv

Sworn to and Subscribed
before me this 30th Day of
July AD 1858.

William E Moor
Notary Public

Surveyor General's Office
Nebraska City

September 22nd AD 1858

The foregoing Field Notes of the survey
of Fractional Township Twenty Four
North of Ranges Six Seven and Eight
East of the Sixth Principal Meridian in
Nebraska Territory, executed by John G.
Clapper, Deputy Surveyor under special instruc-
tions dated the 5th day of June AD 1858
for the month of July AD. 1858.
Having been critically examined the
necessary corrections and explanations
made the said Field Notes, and the survey
they describe are hereby approved

Ward B. Burnett
Surveyor General.

General Land Office • Original Field Notes

Book Number

74

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.
