General Land Office • Original Field Notes

Book Number

89

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.

Descriptive List Completed May 18th 59.

Vol. 6 R. 8 E.

Contract No. 210.

Field Notes of the Subdivision lines of Township 21 North of Range 8 East of the 6th Principal Meridian in the Territory of Nebraska, as Surveyed by Isaac C. Stuck Deputy Surveyor under his Contract bearing date the 19th day of June 1857.

No. 210 -

Subdivision Commenced Sept 5 1857

Subdivision Completed, Sept. 8th 1857

Cok.

b

Names and duties of Assistants

John Farnham Chainman
Harman Lanforsieck Chainman
Frank McKenna Chainman
Bushnell B. Loomis Chainman
Thos. C. Jones Chainman
Frank Hill Axeman
James Quinn Axeman
George Cocklin Flagman

c

Township 21 N. Range 8 East

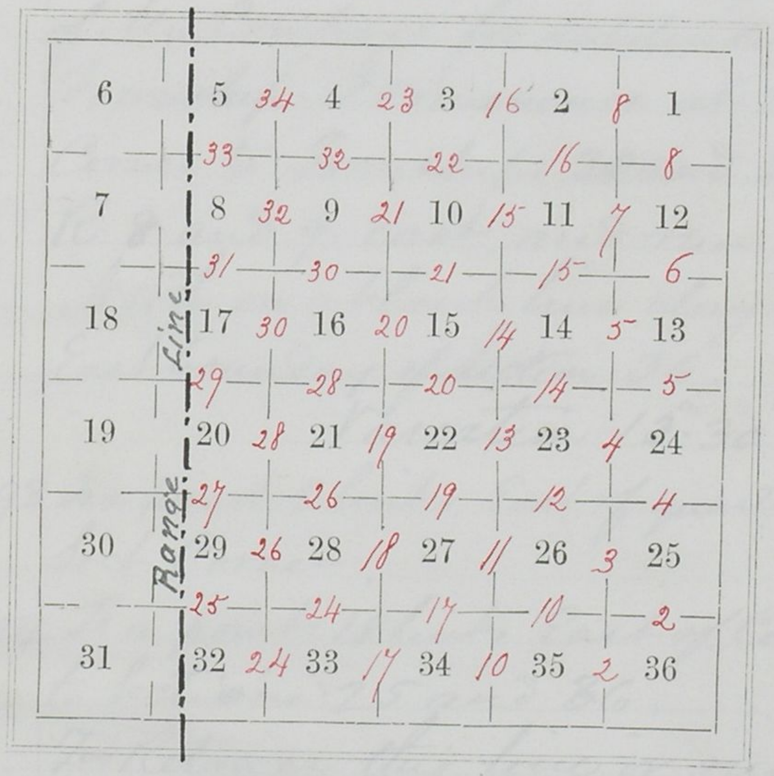

Township 21 N. R 8 East of 6 P.M.

To determine the proper adjustment of My Compass for subdividing this Township. I commence at the Corner to Townships 20 and 21 N R 8 and 9 East, and run North on a blank line along the East boundary of Section 36.

Variation 13°. 30′ E.

39.98 To a point 8 links East of quarter Sect Corner.

80.04 To a point 18 links East of Corner to Sections 25 and 36.

To Retrace this line or run parallel thereto, my Compass must be adjusted to a Variation of 13°. 38′ East.

Subdivision Commenced, Sept 17th 1857

Township 21 N. R 8 E. 6th P.M.

From the Corner to Sections 35 and 36. on the South boundary of the Township I run North between Sections 35 and 36

Variation 13°.38' East

40.00 Set a post for quarter Sect Corner and raised Mound with trench as per instructions

55.50 Ravine or Branch 8 links wide runs N.W.

80.00 Set a post for corner to Sections 25. 26. 35 and 36. and raised mound, with trench as per instructions Prairie Roling. Soil 1st Rate,

---

East on a Random line between Sect 25 and 36

Variation 13°.38' East

40.00 Set a post for a temporary quarter Section Corner

80.03 Intersected East boundary of Township 53 links North of Corner to Sects

Township 21 N. R. 8 E 6th P.M.

25 and 36, from which Corner I run

West on a true line between Sects 25 and 36.

Variation 13°.15' East

40.02 Set a post, and raised mound, with trench and pits as per instructions for a quarter Sect Cor,

80.03 the Corner to Sects. 25. 26. 35 & 36. Roling prairie Soil 1st Rate,

---

North between Sects 25 and 26.

Variation 13°.30' East

28.50 a Creek 10 links wide runs S.W.

40.00 Set a post, and raised mound, with trench and pits as per instructions for a quarter Sect Corner,

80.00 Set a post, and raised mound with trench and pits, as per instructions for Corner to Sects. 23. 24. 25 and 26.

Roling prairie land. Soil 1st Rate,

Township 21 N.

East on a Random line between Sects 24 & 25
Variation 13°.15' East.

40.00 Set a post for a temporary quarter Sect Corner

79.62 Intersected the N and S line 8 links South of the Corner to Sects. 24 and 25. from which Corner I run West on a true line between Sects 24 & 25
Variation 13°.18' East

39.81 Set a post in mound, with trench and pits as per instructions for a quarter Sect Corner

79.62 The Corner to Sects 23. 24. 25 and 26. Roling prairie land. Soil 1st Rate.

North between Sects 23 and 24
Variation 13°.40' East.

40.00 Set a post in mound with trench and pits as per instructions for quarter Sect Cor.

43.75 a Ravine runs N.W.

44.75 a Ravine runs S.W.

Range 8 E. 6th P. Mer.

80.00 Set a post in mound, with trench and pits as per instructions for Corner to Sects 13. 14. 23 & 24 Roling prairie land. Soil 1st Rate.

East on a Random line between Sects 13 and 24
Variation 13°.20' East

40.00 Set a post for temporary quarter Sect Cor.

80.28 Intersected East boundary of Township 140 links North of Corner to Sects 13 & 24 from which corner I run West on a true line between Sects 13 & 24
Variation 12°.20' East

40.14 Set a post in mound with trench and pits as per instructions for a quarter Section Corner

80.28 The Corner to Sects 13. 14. 23 and 24 Roling prairie land Soil 1st Rate

---

North between Sects 13 and 14
Variation 12°.30' East

40.00 Set a post in mound with trench and pits as per instructions for a quarter Section Corner

Township 21 N.

80.00 Corner on Left bank of Logan Creek Course S.W. I set a post in mound with trench and pits as per instructions 95 links East for a witness to the true Corner, to Sections 11. 12. 13 and 14.
Land Roling praire, Soil 1st Rate, a few Scattering trees on North ½ of this mile. —

East on a Random line between Sects 12 & 13
Variation 13° 20' East

00.95 Witness Corner
40.00 Set a post for temporary quarter Sect Cor.
80.93 Intersect East boundary of Township 206 links North of Corner to Sects 12 & 13 from which Corner I run West on a true line between Sects 12 & 13
Variation 11° 52' East
40.47 Set a post in Mound with trench and pits as per instruction for a quarter Sect Corner
80.93 the Corner to Sects 11. 12. 13 & 14

Range 8 E. 6th P.M.

Land very Roling Soil 1st Rate,

North from witness Cor between Sects. 11 & 12.
Variation 11° 15' East.

3.00 Offset 95 links West and get on true line
~~19.00~~ 19.80 Logan Creek 40 links wide, runs S.W.
~~23.00~~ 22.75 Logan Creek 50 links wide runs N.E.
40.00 Set a post in mound with trench and pits as per instructions 50 links East of point for true Cor, for a witness Corner to the Same,
~~40.30~~ 40.10 Logan Creek 40 links wide runs S.W. soon turns N.W.
~~63.50~~ 63.25 Logan Creek 50 links wide runs N.E.
70.00 touch bend on East side of Creek, Runs S.E. to line thence S.W.
80.00 Set a post in mound, with trench and pits as per instruction for Corner to Sections 1. 2. 11 & 12.
Land level bottom. Soil 1st Rate,

Township 21 N. R 8 E 6th P.M.

East on a Random line between Sections 1 and 12.

Variation 12° East

8.75 ~~9.00~~ Logan Creek 50 links wide runs N.W.

15.24 ~~54~~ Logan Creek 60 links wide runs S.E.

80.25 Intersected East boundary 80 links North of Corner to Sects 1 and 12 from which Corner I run

West on a true line between Sects 1 and 12

Variation 11°26' East.

40.13 Set a post in mound with trench and pits, ash instruction for a quarter Sect Corner

80.25 The Corner to Sects 1. 2. 11 and 12

West ½ mile level bottom, East half Roling, Soil 1st Rate.

North on a Random line between Sects 1 and 2

Variation 11°45' East.

4.95 ~~5.20~~ Logan Creek 50 links wide runs S.W.

40.00 Set temporary quarter Sect Cor.

80.00 Intersected North boundary 39 links

Township 21 N. R 8 E. 6th P.M.

East of Cor to Sects 1 and 2.

From which Cor I run

South on true line between Sects 1 and 2.

Variation 12°02' East.

40.00 Drove Charred Stake. Set post and raised mound with trench & pits, as pr Instruction for Quarter Section Corner

80.00 The Corner to Sects 1. 2. 11 & 12.

Level bottom Land,

Soil 1st Rate.

A few trees occasionally mark the Course of this Creek,

Township 21 N

North between Sects 34 and 35
Variation 13° 38' East

6.80 ~~7.00~~ Logan Creek 40 links wide runs S.E.
18.70 ~~19.00~~ Logan creek 60 links wide runs S.W.
29.75 ~~30.00~~ Logan creek 50 links wide runs N.E.
40.00 Set a post in mound with trench and pits as per instructions for a quarter Sect Corner,
69.70 ~~70~~ Logan creek 60 links wide runs S.W.
81.70 ~~72.00~~ Logan creek 60 links wide runs N.E.
79.80 ~~80.00~~ Logan Creek 60 links wide runs N.W.
80.00 The Corner to Sects 26. 27. 34 and 35 falls in Logan Creek runs N.W. I set a post in mound with trench and pits as instructions 70 links South of true point for a witness Corner to the same, Land level bottom Soil 1st Rate.

East from witness Corner between Sects. 34 and 35.
Variation 13° 15' East
3.00 Offset north 70 links to Random line on bank of Creek between Sects 26 & 35

Range 8 E. 6th P.M.

Thence East on Random line between Sects 26. & 35

38.00 Creek 15 links wide runs N.W. and leave bottom.
40.00 Set post for a temporary quarter Sect Cor.
65.50 Ravine 8 links wide runs S.W.
80.02 Intersected N and S line at Corner to Sects 25. 26. 35 and 36. from which Corner I run West on true line between Sects 26 & 35
Variation 13° 15' East
40.01 Set a post in Mound with trench and pits as per instructions for a quarter Sect Cor.
80.02 The point for Cor to Sects 26. 27. 34 & 35 Land level bottom & Rolling prairie Soil 1st Rate.

North between Sects 26 and 27.
Variation 13° 30' East
00.15 Leave Logan Creek runs N.W.
~~of Logan Creek runs S.W.~~
4.25 ~~50~~ Logan Creek 50 links wide runs N.E.

Township 21 N.

7.80 ~~800~~ Logan Creek 40 links wide runs West.
13.30 ~~1400~~ Logan Creek 40 links wide runs a little East of South,
18.65 ~~1900~~ Logan Creek 70 links wide runs S.W.
22.80 ~~2300~~ Logan Creek 40 links wide runs S.E.
40.00 Corner in Logan Creek runs West
Set a post in mound with trench and pits, as by instructions 40 links South of true Corner as a witness to the same.
45.70 ~~4600~~ Logan Creek 60 links wide runs S.E.
71.75 ~~7200~~ Logan Creek 50 links wide runs S.W.
80.00 Set a post in mound with trench and pits, as by instructions for Corner to Sects 22.23 26 & 27.
Land level bottom. Soil 1st Rate,

East on a Random line between Sects 23 and 26.
Variation 13° 20' East
14.80 ~~1500~~ Logan Creek 40 links wide, runs S.E.
20.50 Pass through a bend of Logan Creek
Comes from N.E. and runs N.W.

Range 8 E. 6th P.M.

40.00 Set a post for a temporary quarter Sect Corner,
80.06 Intersected N and S line at Corner to Sects 23.24.25 and 26. from which Corner I run
West on a true line between Sects 23 & 26.
Variation 13° 20' East.
40.03 Set a post in mound, with trench and pits, as by instructions for a quarter Sect Corner
80.06 The Corner to Sects 22.23.26 & 27
Land Roling & level bottom
Soil 1st Rate,

North between Sects 22 and 23
Variation 13° 30' East.
40.00 Set a post in mound with trench and pits, as by instructions for a quarter Sect Corner,
80.00 Set a post in mound with trench and pits, as by instructions for Corner to Sects 14.15.22 & 23.
Land level bottom Soil 1st Rate.

Township 21 N.

East on a Random line between Sects 14 & 23
Variation 13°.10' East.

39.~~20~~00 Logan Creek 40 links wide runs S. E.,
40.00 Set a temporary quarter Sect Corner.
80.95 Intersected N & S line 11 links North of Corner to Sects 13.14.23 and 24. from which Corner Drum

West on true line between Sects 14 and 23.
Variation 13°.05' East.

40.48 Set a post in mound with trench and pits as per instructions for a quarter Sect Cor.
80.95 The Corner to Sects 14.15.22.& 23
Land level bottom: Soil 1st Rate.
Sept 6th 1857

North between Sects 14 and 15.
Variation 12°.20' East.

40.00 Set a post in mound with trench and pits as per instructions for a quarter Sect Corner
80.00 Set a post in mound with trench and pits as per instructions for Corner to Sects 10.11.14 & 15
Land level bottom Soil 1st Rate.

Range 8 E. 6th P.M.,

East on a Random line between Sects 11 & 14
Variation 12° East.

40.00 Set temporary quarter Sect Corner.
43.00 Entre Pond bears N & S. about 8 chs long
47.00 leave Pond bears N & S. about 4 ft dist.
80.~~60~~40 Logan Creek 40 links wide runs S. W.
80.95 intersected N and S line at true Corner to Sects 11.12.13.14, from which Corner Drum

West on a true line between Sects 11 & 14
Variation 12° East

40.48 Set a post in mound with trench and pits as per instructions for a quarter Sect Corner,
80.95 the Corner to Sects 10.11.14 & 15.
Land level bottom Soil 1st Rate.

North between Sects 10 & 11
Variation 10°.45' East

40.00 Set a post in mound with trench and pits as per instructions for a quarter Sect Corner
80.00 Set a post in mound, with trench and pits

Township 21 N.

as per instructions
for Corner to Sects 2.3.10 & 11.
Land Roling. Soil 1st Rate.

East on Random line between Sects 2 & 11
Variation 12°.05' East.

40.00 Set temporary quarter Sect Cor.
78.70 ~~79.00~~ Logan Creek 60 links wide runs S.E.
80.00 Intersected N and S line at Corner to Sects 1. 2. 11 & 12 from which Corner
~~Irun We~~

West on true line between Sects 2 & 11
Variation 12°.05' East.

40.00 Set post in mound with trench and pits as per instructions for a quarter Sect Corner,
80.00 the Corner to Sects 2.3.10 & 11.
Land level. Soil 1st Rate.

North on a Random line between Sects 2 & 3
Variation 11°.45' East,

40.00 Set temporary quarter Sect Cor,

Range 8 E. 6th P.M.

81.75 Intersected North boundary 219 links East of Corner to Sects 2 & 3. from which Corner
I run
South on true line between Sects 2 & 3.
Variation 13°.19' East,

41.75 drove Charred Stake Set post and raised mound with trench & pits as per instructions for quarter Sect Cor
81.75 The Cor to Sects 2.3.10 & 11.
Rolling prairie Land. Soil 1st Rate.

North between Sects. 33 and 34
Variation 11°.25' East.

40.00 Set post in mound with trench and pits as per instructions for a quarter Sect Corner,
80.00 Set post in mound with trench & pits as per instructions for Corner to Sects 27.28.33.& 34
Land level. Soil 1st Rate.

East on Random line between Sects 27 & 34
Variation 13°.20' East.

40.00 Set temporary quarter Sect Corner,

Township 21 N.

67.~~80~~ 45 Crek Logan 70 links wide runs S.E.
75.~~50~~ 05 Logan Creek 90 links wide runs N.W.
80.04 Intersected N & S line 70 links north
of true Corner to Sects 26.27.34 & 35
from which Corner I run
West on true line between Sects 27 & 34
Variation 12°.50' East.
40.02 Set post in mound with trench and
pits as per instructions for quarter Sect Corner.
80.04 The Corner to Sects 27.28.33 & 34
Land level Crek bottom Soil 1st Rate

North between Sect 27 & 28
Vaiation 11°.15' East.
40.00 Set post in mound with trench & pits as per
instructions for a quarter Sect Corner
80.00 Set post in mound with trench & pits as per
instructions for Corner to Sects 21.22.27 & 28
Land Roling & level Soil 1st Rate.

Range 8 E. 6th P.M.

East on Random line between Sects 22 & 27
Variation 12°.35' East
40.00 Set temporary quarter Sect Cor.
79.56 Intersected N & S line 277 links
North of Corner to Sects 22.23.26 & 27
from which Corner I run
West on true line between Sects 22 & 27
Variation 10°.36' East
39.78 Set a post in mound with trench & pits
as per instructions for a quarter Sect Corner
79.56 The Corner to Sects 21.22.27 & 28
Land level. Soil 1st Rate.

North between Sections 21 & 22
Variation 12°.29' East
40.00 Set Post in Mound with Trench
& Pits for as per instructions Quarter Section Corner
80.00 Set Post in Mound with trench
and Pits as per instructions for Cor. to Sections 15.16.21 & 22
Land level. Soil 1st Rate

Township 21 N.

East on Random Line between Sections 15 & 22.

Variation 10° 35' East

40.00 Set Temporary Quarter Section Cor.

80.03 Intersected N & S. Line 130 links North of Cor. to Sections 14, 15, 22 & 23. from which Corner I run West on true Line between Sections 15 & 22.

Variation 9° 39' East

40.02 Set Post in Mound with trench and Pits as instructions for Quarter Section Corner

80.03 The Corner to Sections 10, 16, 21 and 15, 22.

Land level. Soil 1st Rate.

North between Sections 15 & 16.

Variation 12° 33' East

40.00 Set Post in Mound with trench and Pits as instructions for Quarter Section Cor.

Range 8 E. 6th P.M.

80.00 Set Post in Mound with trench and Pits as instructions for Corner to Sections 9, 10, 15 & 16.

Land Rolling. Soil 1st Rate.

East on Random Line between Sections 10 & 15.

Variation 9° 50' East.

40.00 Set temporary Quarter Section Corner

79.41 Intersected N & S. Line 16 links South of Corner to Sections 10, 11, 14 & 15. from which Cor. I run West on true Line between Sections 15 & 22.

Variation 9° 57' East

39.71 Set Post in Mound with trench and Pits as instructions for a Quarter Section Cor.

79.41 The Corner to Sections 9, 10, 15 & 16.

Land Rolling and level. Soil 1st Rate.

North between Sections 9 & 10.

Variation 12° 00 East

Township 21 N.

40.00 Set Post in Mound with trench and Pits as prescribed now for Quarter Section Cor.

80.00 Set Post in Mound with trench and Pits as per instructions for Corner to Sections 3.4.9 & 10

Land Rolling. Soil 1st Rate.

East on Random Line between Sections 3 & 10.

Variation 10° 00 East

40.00 Set temporary Quarter Section Cor.

80.35 Intersected N & S. Line 108 links North of Corner to Sections 2.3.10 & 11. from which Corner Bears West on true Line between Sections 3 & 10

Variation 9° 14' East

40.18 Set Post in Mound with trench and Pits as per instructions for Quarter Section Cor.

80.35 The Corner to Sections 3.4.9 & 10

Land Rolling and level. Soil 1st Rate.

Range 8 E. 6th P.M.

North on Random Line between Sections 3 & 4.

Variation 12° East.

40.00 Set temporary quarter Sect Cor.

78.62 Intersected North boundary ~~252 links West of Corner to Sect~~ 3 & 4 from which Corner Bears South on true line between Sect. 3 & 4

Variation 10° 27' East

38.62 drove Charred stake. Set post and raised mound with trench & pits as per instructions for Quarter Sect Cor.

78.62 The Corner to Sect. 3.4.9 & 10.

Rolling prairie Land Soil 1st Rate.

Sept 7th 1857

Township 21 N.

North between Sections 32 & 33.
Variation 11° 20' East

40.00 Set Post in Mound with trench and Pits as per instructions for Quarter Section Cor.

80.00 Set Post in Mound with trench and Pits as per instructions for Cor. to Sections 28. 29. 32 & 33.
Land Roling. Soil 1st Rate.

East on Random Line between Sections 28 & 33.
Variation 11° 15' East

5.40 Branch 10 links wide runs S.E.

40.00 Set temporary Quarter Section

80.67 Intersected N & S line 61 links North of Corner to Sects 27. 28. 33 & 34 from which Corner I run
West on true line between Sects 28 & 33
Variation 10° 49' East

40.34 Set post in mound with trench & pits as per instructions for quarter Sect Corner

Range 8 E. 6th P.M.

80.67 the Corner to Sects 28. 29. 32 & 33.
Land gently Roling. Soil 1st Rate

West on a Random line between Sects 29 & 32.
Variation 11° 15' East.

34.85 Ravine 10 links wide runs N.E.

40.00 Set temporary quarter Sect Cor.

58.26 Intersected West boundary 7 links South of Corner to Sects 29 & 32 from which Corner I run
East on true line between Sects 29 & 32
Variation 11° 11' East

18.26 drove charred stake. Set post and raised mound with trench & pits as per instructions for quarter Sect Cor.

58.26 The Corner to Sects. 28. 29. 32 & 33.
Land gently roling prairie. Soil 1st Rate.

Township 21 N.

North between Sections 28 & 29.
Va 11° E.

8.00 Varins N. E.

9.00 Varins N. E.

29.00 Varins N. W.

40.00 Set Post in Mound with trench and Pits as per instructions for quarter Section Corner

80.00 Set Post in Mound with trench and Pits as per instructions for Cor. to Sections 20. 21. 28 & 29.
Land level. Soil 1st Rate.

East on Random Line between Sections 21 & 28.
Va 10° 45' E.

40.00 Set Temporary Quarter Section Corner.

80.20 Intersected N & S. Line 130 Links South of Cor. to Sections 21. 22. 27 & 28.
From which Corner I run
West on a True Line between Sections 3 & 10
Va 11° 41' E.

40.00 Set Post in Mound with trench and Pits as per instructions for Quarter Section Corner

Range 8 E. 6th P. M.

80.20 The Cor. to Sections 20. 21. 28 & 29.
Land Level. Soil 1st Rate.

West on a Random Line between Sections 20 & 29.
Va 11° 15 East.

40.00 Set temporary quarter Sect Cor.

59.04 Intersected West boundary 89 Links North of Corner to Sects 20 & 29. from which Corner I run
East on true line between Sects 20 & 29
Variation 12° 0' East

19.04 Drove Charred Stake. Set post and raised mound with trench & pits. as per instructions for quarter Sect Cor.

59.04 The Corner to Sects 20. 21. 28 & 29.
Rolling prairie Land, Soil 1st Rate.

Township 21 N.

North between Sections 20 & 21.
Va 11° 51' E.

24.00 Varies N. E.

40.00 Set Post in Mound with trench and Pits as per instructions for Quarter Section Corner

80.00 Set Post in Mound with trench and Pits as per instructions for Corner to Sections 16.17.20 & 21
Lands Rolling Soil 1st Rate.

East on Random Line between Sections 16 & 21.
Va 11° 10' E.

40.00 Set temporary Quarter Section Corner

79.30 Intersected N. & S. Line 56 links South of Corner to Sections 15.16.21 & 22 from which Corner I run
W.
West on a true line between Sections 16 & 21
Va 11° 34' E.

39.65 Set Post in Mound with trench and Pits as per instructions for Quarter Section Cor.

Range 8 E. 6th P.M.

79.30 The Corner to Sections 16.17.20 & 21.
Land level. Soil 1st Rate.

West on a Random Line between Sections 17 & 20.
Variation 11° 15' East.

40.00 Set temporary quarter Sect Cor.

59.10 Intersected West boundary 96 links North of Cor to Sects 17 & 20 from which Cor. I run
East on true line between Sects 17 & 20.
Variation 12° 11' East.

19.10 drove Charred stake. Set post, and raised Mound with trench & pits as per instructions for quarter Sect Cor.

59.10 The Cor to Sects 16.17.20 & 21
Rolling prairie Land. Soil 1st Rate.

Township 21 N.

North between Sections 16 & 17.
Va 12° East

40.00 Set a Post in Mound with trench and Pits as per Instructions for a quarter Section Corner.

80.00 Set a Post in Mound with trench and Pits as per Instructions for Corner to Sections 8, 9, 16 and 17.
Land Rolling Prairie, 1st Rate.

East on Random Line between Sections 9 and 16.
Variation 11° 40' East

40.00 Set Post for a temporary quarter Section Corner

79.30 Intersected N. and S. Line 63 links North of the Corner to Sections 9, 10, 15 and 16. from which Corner I run
West on a true Line between

Range 8 E. 6th P.M.

Sections 9 and 16.
Variation 11° 13' East

39.65 Set a Post in Mound with trench and Pits as per Instructions for a quarter Section Corner.

79.30 The Corner to Sections 8, 9, 16 and 17.
Land Rolling Prairie, 1st Rate

West on Random Line between Sections 8 and 17.
Variation 11° 15' East

40.00 Set temporary quarter Sect Cor.

58.57 Intersected West boundary 118 links North of Cor to Sects 8 & 17 from which Cor I run
East on true line between Sects 8 & 17
Variation 12° 23' East

18.57 drove Chained stake. set post. and raised mound with trench & pits as per Instructions for quarter Sect Cor.

Township 21 N.

58.57 The Cor to Sect. 8. 9. 16 & 17.
Rolling prairie Land. Soil 1st Rate.

North between Sections 8 & 9.
Variation 12° 30' East

40.00 Set a Post in Mound with trench and Pits as per Instructions for a quarter Section Corner

80.00 Set a Post in Mound with trench and Pits as per Instructions for Corner to Sections 4. 5. 8. & 9.
Land Rolling Prairie, 1st Rate.

East on a Random Line between Sections 4 and 9.
Variation 11° 10' East

40.00 Set a Post for temporary quarter Section Corner.

80.19 Intersected N. and S. Line 40 links South of the Corner to Sections 3. 4. 9 and 10.

Range 8 E. 6th P.M.

from which Corner I run West on a true Line between Sections 4 and 9.
Variation 11° 27' East

40.05 Set a Post in Mound with trench and Pits as per Instructions for a quarter Section Corner

80.19 The Corner to Sections 4. 5. 8. & 9.
Land Rolling Prairie, 1st Rate

West on Random Line between Sections 5 and 8.
Variation 11° 15' East

40.00 Set temporary quarter Sect Cor.

56.87 Intersected West boundary 122 links North of Cor to Sects 5 & 8 from which Cor I run
East on true line between Sects 5 & 8
Variation 12° 28' East.

11.87 drove chained stake. Set post and raised mound with trench & pits as per instructions

Township 21 N.

for quarter Sect Cor.
56.87 The for to Sects 4. 5. 8 & 9.
Rolling prairie Land. Soil 1st Rate

North on Random line
between Sections 4 and 5.
Variation 10° 30' East
40.00 Set temporary quarter Sect Cor.
78.87 Intersected North boundary of
Township 10 links East of Cor
to Sects 4 & 5 from which Cor.
Drum.
South on true line between Sects 4 & 5.
Variation 10° 34' East
38.87 drove chained stake set post and
raised mound with trench & put
as pr instructions for quarter Sect
Cor.
78.87 The Corner to Sects 4. 5. 8 & 9

Range 8 E. 6th P. M.

Sept 8th 1857

General Description.

Land in this Township Rolling
prairie with a large portion of
Bottom Land along Logan Creek.
Generally of first Quality.
There is considerable timber on Logan
Creek Mostly Cottonwood and Bur
Oak. also Willow. but it is generally
small and not of good quality.
Logan Creek is a Sluggish stream
from 50 to 80 links wide. muddy
and miry Bottom. Steep banks
which are very even and regular
(giving it the appearance of a canal)
1 to 1½ ft deep.

Township 21 N. R 8 E 6th P.M.

List of Names.

A list of the individuals employed to assist in running measuring, or marking the lines and corners described in the foregoing field notes of Township No. 21 North of Range 8 East of the 6th Principal Meridian in Nebraska Territory, showing the respective capacities in which they acted,

John Farnham	Compassman
Thomas Langsdick	Chainman
Frank McKenna	Chainman
Bushnell B. Lonnis	Chainman
Thos C. Jones	Chainman
F. R. Hill	Axeman
James Dunn	Axeman
George Cocklin	Flagman

The Notes of each line must be complete in itself — Sec 11+1
How does Logan Creek run N W on one bank + S W on the other — + what is the wid of Creek —

11+14 How did you get through a March 4 ft deep?

Compd

2

(Descriptive List

Contract No 210 Completed)

Field notes of the Subdivision Lines of Township 22 North of Range 8 East of the 6th Principal Meridian in the Territory of Nebraska as Surveyed by Isaac C. Stuck Deputy Surveyor, under his Contract bearing Date the 19th day of June — 1857 No. 210 —

(No 210)

{Contract No 210}

Subdivision Commenced Sept 17th 1857
Subdivision Completed, Sept 19th 1857

Correct
Van

OK X

Names and duties of Assistants

John Farnham Compassman.
Harman Lanforsick Chainman
Frank McKenna Chainman
Bushnell B. Loomis Chainman
Thos C. Jones Chainman
Frank R. Hill Axeman
Samuel Lucius Axeman.
George Cocklin Flagman.

Township 22 N. Range 8 East

6	5	30	4	20	3	14	2	7	1
	30		29		20		14		7
7	8	28	9	19	10	13	11	6	12
	28		27		19		12		5
18	17	26	16	18	15	12	14	5	13
	26		25		18		11		4
19	20	25	21	17	22	10	23	4	24
	24		23		17		10		3
30	29	23	28	16	27	9	26	3	25
	22		22		16		8		2
31	32	21	33	15	34	8	35	1	36

Township 22 N. Range 8 East of 6th

To determine the proper adjustment of my Compass for subdividing this Township I commence at the Corner to Townships 21 & 22 N Ranges 8 & 9 East, and run

North, on a blank line along the East boundary of Sect 36.

Variation 12° East.

9.91 To a point 10 links East of quarter Sect Cor.

9.89 To a point 16 links East of Corner to Sects 25 & 36.

To retrace this line, or run parallel thereto my Compass must be adjusted to a Variation 12° 07' East.

Subdivision Commenced, Sept 17th 1857

From the Corner to Sects 1. 2. 35 & 36. on South boundary of Township I run

North between Sections 35 and 36.

Variation 12° 07' East.

40.00 drove charred stake. set post and raised mound

Township 22 N. R 8 E of 6th P. M.

with trench and pits as pr instructions for quarter Sect Cor.

80.00 drove chained stake, set post and raised mound with trench and pits as pr instruction for Corner to Sect, 25. 26. 35 & 36.

Level bottom land. Soil 1st Rate,

East on Random line between Sects 25 & 36,

Variation 12°. 07' East

21.00 Logan Creek 80 links wide runs S. E. a grove of timber on Creek about 20 chains South of where the Line Crosses.

40.00 Set temporary quarter Sect Cor.

80.54 Intersected East boundary 129 links North of Corner to Sects 25 & 36. from which Corner I run

West on true line between Sects 25 & 36.

Variation 11°. 12' East

40.27 drove chained stake, set post and raised mound with trench & pits. as pr instruction

Township 22 N. R 8 E. 6th P. M.

for quarter Sect Cor.

80.54 The Cor to Sects 25. 26. 35 & 36.

West half level bottom. East half rolling prairie Land. Soil 1st Rate,

---

North between Sects 25 & 26.

Variation 11°. 50' East

38.00 Pass 10 links west of land in — Logan Creek running S. W. & S. E.

40.00 drove chained stake, set post and raised mound with trench & pits. as pr instructions for quarter Sect Cor.

75.60 Logan Creek 50 links wide runs S. E.

80.00 drove chained stake. set post and raised mound with trench & pits as pr instruction, for Corner to Sects 23. 24. 25. 26.

Level bottom, Soil 1st Rate, no timber on Creek.

East on Random line between Sects 24 & 25.

Township 22 N. R 8 E. 6th P. M.

Variation 11° 50' East

13.75 Logan Creek 140 links wide on line runs a little North of East

23.20 Logan Creek 50 links wide runs S. E.

27.00 Logan Creek 50 links wide runs N. E.

31.10 Logan Creek 50 links wide runs S. E.

39.60 Touch Left bank of Logan Creek runs S. E.

40.00 Set temporary quarter Sect Cor.

80.80 Intersected East boundary of Township ~~170 links North of Corner to Sects 24 & 25~~ 55/100 from which Corner I run West on true line between Sects 24 & 25

Variation 10° 37' East

40.40 drove chained stake set post and raised mound with trench & pits as prinstruction for quarter Sect. Cor

80.80 The for to Sects 23. 24. 25 & 26. West half level bottom, East half Rolling prairie Land. Soil 1st Rate.

Township 22 N. R 8 E 6th P. M.

North between Sects 23 & 24.

Variation 10° 30' East

40.00 drove chained stake, set post and raised mound with trench and pits as pr instruction for quarter Sect Cor.

80.00 drove chained stake set post and raised mound with trench & pits as pr instruction for Corner to Sects 13. 14. 23 & 24. Level bottom Land Soil 1st Rate.

East on Random line between Sects 13 & 24

Variation 10° 30' East.

40.00 Set temporary quarter Sect Cor.

80.22 Intersected East boundary 34 links North of Corner to Sects 13 & 24 from which Corner I run

West on true line between Sects 13 & 24

Variation 10° 15' East.

40.11 drove chained stake set post, and raised mound with trench & pits, as pr instruction for quarter Sect Cor.

Township 22 N. R. 8 E. 6th P.M.

80.22 The Cor to Sects 13. 14. 23 & 24,
Very gently Rolling prairie. Soil 1st Rate.

North between Sects 13 & 14.
Variation 10° 50' East.

40.00 drove chained stake set post and raised mound with trench & pits as pr instruction for quarter Sect Cor.

80.00 drove chained stake set post and raised mound with trench & pits as pr instruction for Corner to Sects 13. 12. 13 & 14,
South half level bottom, North half rolling Soil 1st Rate.

East on Random line between Sects 12 & 13.
Variation 10° 30' East

40.00 Set temporary quarter Sect Cor.

80.32 Intersected East boundary 40 links South of Cor to Sects 12 & 13 from which Corner I run

Township 22 N. R. 8 E. 6th P.M.

West on true line between Sects 12 & 13
Variation 10° 47' East.

40.16 drove chained stake set post and raised mound with trench & pits, as pr instruction for quarter Sect Cor.

80.32 The Cor to Sects 11. 12. 13 & 14,
Gently Rolling prairie. Soil 1st Rate,

North between Sects 11 & 12
Variation 10° 40' East.

40.00 drove chained stake set post and raised mound with trench and pits as pr instructions for quarter Sect Cor.

49.60 Indian trail bears N. E. & S. W.

80.00 drove chained stake set post and raised mound with trench & pits as pr instructions for Cor to Sects 1. 2. 11 & 12.
Gently Rolling prairie. Land. Soil 1st Rate,

Township 22 N. R. 8 E 6th P. M.

East on Random line between Sects 1 & 12.

Variation 10°45' East.

2.00 Indian trail bears N & S.

40.00 Set temporary quarter Sect Cor.

79.55 Intersected East boundary at Corner to Sects 1 and 12. from which Cor I run West on true line between Sects 1 & 12

Variation 10°45' East

39.78 drove charred stake, Set post and raised mound with trench & pits as pr instruction for quarter Sect Cor

79.55 The Cor to Sects. 1. 2. 11 & 12.

Gently rolling prairie Land. Soil 1st Rate

North on Random line between Sects 1 & 2

Variation 11°18' East

40.00 Set temporary quarter Sect Cor.

79.32 Intersected North boundary at Corner to Sects 1 & 2 from which Corner I run.

Township 22. N. R 8 E 6th P. M.

South on true line between Sects 1 & 2,

Variation 11°18' East

39.32 drove charred stake set post and raised mound with trench & pits as pr instructions for quarter Sect Cor.

79.32 The Corner to Sects 1. 2. 11 & 12.

Gently Rolling prairie Land. Soil 1st Rate

North between Sects. 34 and 35.

Variation 11°50' East.

40.00 drove charred stake. Set post and raised mound with trench & pits as pr instructions for quarter Sect Cor.

80.00 drove charred stake set post and raised mound with trench & pits as pr instructions for Cor to Sects 26. 27. 34 and 35.

Gently Rolling prairie Land Soil 1st Rate.

East on Random line between Sects 26 & 35.

Variation 11°50' East

Township 22 N R 8 E 6th P.M.

40.00 Set temporary quarter Sect Cor.

80.16 Intersected A & S line 129 links north of Corner to Sect, 25.26.35 & 36. from which Cor I run

West on true line between Sect, 26 & 35

Variation 10° 55' East

40.08 drove chained stake. Set post and raised mound with trench & pits, as pr instructions for quarter Sect Cor.

80.16 The Cor to Sect, 26.27.34 & 35

Level bottom Land. Soil 1st Rate.

North between Sects 26 & 27

Variation 10° 57' East

40.00 drove chained stake. set post and raised mound with trench & pits as pr instructions for quarter sect Cor

80.00 drove chained stake. Set post and raised mound with trench & pits as pr instructions for Cor to Sect, 22.23.26 & 27

Township 22 N. R 8 E 6th P.M.

Level bottom, and Rolling prairie Land.

Soil 1st Rate.

East on Random line between Sect, 23 & 26.

Variation 11° 10' East

40.00 Set temporary quarter Sect Cor.

73.27 Logan Creek 50 links wide runs South

80.25 Intersected A and S line at Cor to Sect 23.24.25 and 26, from which Cor I run

West on true line between Sect, 23 & 26.

Variation 11° 10' East

40.13 drove chained stake. Set post and raised mound with trench & pits as pr instructions for quarter Sect Cor

80.25 The Cor to Sects 22.23.26 & 27.

Level bottom Land Soil 1st Rate

North between Sects 22 & 23.

Variation 10° 20' East

37.85 Indian trail bears SW & NE.

40.00 Drove chained stake. Set post. and raised mound with trench & pits as pr instructions for quarter Sect Cor

11/54

Township 22 N. R 8 E 6th P.M.

80.00 Drove chained stake set post and raised mound with trench & pits, as pr instruction, for Cor to Sects 14. 15. 22 & 23.

Level bottom Land, Soil 1st Rate

East on Random line between Sects 14 & 23.

Variation 11° 10' East

7.20 Indian trail bears S.W. & N.E.

29.81 Logan Creek 50 links wide runs S.E.

40.00 Set temporary quarter Sect Cor.

50.77 Logan Creek 50 links wide runs North.

55.74 Logan Creek 50 links wide runs South.

61.50 Logan Creek 50 links wide runs N.E.

67.00 Logan Creek 50 links wide runs S.W.

80.03 Intersected N and S line 13 links north of Cor to Sects. 13. 14. 23 & 24 from which Cor Firm

West on true line between Sect 14 & 23.

Variation 11° 04' East

40.02 drove chained stake. Set post and raised mound with trench & pits, as pr instructions for quarter Sect Cor.

39/

12/55

Township 22 N. R 8 E. 6th P.M.

80.03 The Cor to Sects 14. 15. 22 & 23.

Level bottom Land Soil 1st Rate

North between Sects 14 & 15.

Variation 10° 45' East

40.00 drove chained stake. Set post and raised mound with trench & pits as pr instruction for quarter Sect Cor.

80.00 drove chained stake set post and raised mound with trench & pits as pr instruction for Cor to Sects 10. 11. 14 & 15.

Level bottom Land Soil 1st Rate.

East on Random line between Sect 11 & 14.

Variation 11° 10' East

20.00 Logan Creek 50 links wide runs S.E.

40.00 Set temporary quarter Sect Corner.

80.00 Intersected N and S line 81 links South of Cor to Sects 11. 12. 13 & 14, from which Corner I run

24/321

Township 22 N. R 8 E. 6th P.M.

West on true line between Sects 11 & 14
11° 45' East

40.00 drove chained stakes set post and raised mound with trench & pits as pr instructions for quarter Sect Cor.

80.00 The Corner to Sects 10. 11. 14 & 15.
Level bottom Land. Soil 1st Rate.

North between Sects 10 & 11.
Variation 10° 35' East

40.00 drove chained stake set post and raised mound with trench & pits as pr instructions for quarter Sect Cor.

76.83 Logan Creek 50 links wide runs N. E.

80.00 drove chained stake set post and raised mound with trench & pits as pr instructions for Cor to Sects 2. 3. 10 & 11.
Level bottom Land. Soil 1st Rate.

Township 22 N. R 8 E. 6th P.M.

East on Random line between Sects 2 & 11.
Variation 11° 30' East

40.00 Set temporary quarter Sect Cor.

79.06 Intersected A and S line at Cor to Sects 1. 2. 11 & 12. from which Cor I run
West on true line between Sects 2 & 11
Variation 11° 30' East

39.53 Drove chained stakes, set post and raised mound with trench & pits as pr instructions for quarter Sect Cor.

79.06 The Cor to Sects 2. 3. 10 & 11.
Level bottom Land. Soil 1st Rate.

North on Random line between Sects 2 & 3
Variation 12° East

2.43 Logan Creek 50 links wide runs S. W.

40.00 Set temporary quarter Sect post.

53.50 Creek 8 links wide runs N. E.

60.50 Same Creek 8 links wide runs S. W.

62.50 Same Creek 8 links wide runs S. E.

79.40

Township 22 N R 8 E 6th P.M.

79.40 Intersected North boundary 69 links East of Cor to Sect 2 & 3 from which Cor Trees South on true line between Sect 2 & 3.

Variation 12°.29 East.

39.40 Drove chained stake set post and raised mound with trench & pits as pr instruction for quarter Sect Cor

79.40 The Cor to Sect 2.3.10 & 11.

Level bottom Land. Soil 1st Rate.

Sept 18 1857

North between Sects 33 & 34

Variation 11°.45 East

40.00 Drove chained Stake. Set post and raised mound with trench and pits, as pr instructions for quarter Sect Cor.

77.00 Indian Trail bears S.W. & N.E.

80.00 Drove chained stake. Set post and raised mound with trench & pits as pr instructions for Cor to Sect 27.28.33 & 34.

Level, Bottom. and very Slightly rolling prairie.

Soil 1st Rate.

Township 22 N. R 8 E 6th P.M.

East on Random line between Sects 27 & 34.

Variation 11° East

3.50 Indian trail bears N & S.

40.00 Set temporary quarter Sect Cor

79.48 Intersected N and S line 49 links South of Cor to Sect. 26.27.34 & 35 from which Cor Trees

West on true line between Sect 27 & 34

Variation 11°.21 East.

39.74 Drove chained stake. Set post and raised mound with trench and pits as pr instructions for Quarter Sect Cor.

79.48 The Cor to Sects 27.28.33. & 34.

Gently Rolling prairie. Soil 1st Rate.

North between Sects 27 & 28

Variation 11°.15 East

40.00 Drove chained stake. Set post and raised mound with trench & pits as pr instructions for quarter Sect Cor.

80.00 Drove chained stake set post and raised mound with trench & pits as pr instructions for Cor to Sect 21.22.27 & 28.

Township 22 N. R 8 E 6th Pm

East on Random line between Sect. 22 & 27

Variation 11° 30' East

40.00 Set temporary quarter Sect Cor

61.50 Indian trail bears N & S.

79.25 Intersected N and S line 6 links North of Cor to Sects. 22. 23. 26 & 27. From which Cor Brass

West on true line between Sect. 22 & 27

Variation 11° 27' East

39.63 drove chained stake. Set post and raised mound with trench and pits as pr instruction for quarter Sect Cor.

79.25 The Cor to Sect. 21. 22. 27 & 28.

Level bottom and Rolling prairie. Soil 1st Rate

North between Sect. 21 & 22.

Variation 11° 13 East

40.00 Drove chained stake. set post and raised mound with trench & pits as pr instruction, for quarter Sect Cor.

80.00 Drove chained stake. Set post and raised mound with trench & pits as pr instruction for Cor to Sects 15. 16. 21 & 22

Rolling prairie Land, Soil 1st Rate

Township 22. N. R 8 E 6th P. M.

East on Random line between Sect. 15 & 22.

Variation 11° East

40.00 Set temporary quarter Sect Cor

79.53 Intersected N and S line 65 links south of Cor to Sects. 14. 15. 22 & 23. from which Cor Brass

West on true line between Sect. 15 & 22

Variation 11° 28' East

39.77 drove chained stake. set post and raised mound with trench and pits as pr instruction for quarter Sect Cor.

79.53 The Cor to Sects 15. 16. 21 & 22.

East half level bottom. West half Rolling prairie Land. Soil 1st Rate

---

North between Sects 15 & 16.

Variation 13° East

40.00 drove chained stake set post and raised mound with trench and pits as pr instruction for quarter Sect Cor

80.00 drove chained stake. set post and raised mound with trench & pits as pr instruction for Cor to Sects 9. 10. 15 & 16.

Rolling prairie Land Soil 1st Rate.

19/62

Township 22 N. R 8 E 6th P.M.

East on Random line between Sects 10 & 15

Variation 11° 10' East.

342/50

40.00 Set temporary quarter Sect Cor.

80.00 Intersected N and S line 114 links South of Cor to Sects 10. 11. 14 & 15. from which Cor I run

West on true line between Sects 10 & 15

Variation 11° 59' East.

40.00 drove charred stake set post and raised mound with trench & pits as pr instruction for quarter Sect Cor.

80.00 The Cor to Sects 9. 10. 15 & 16.

Level bottom & Rolling prairie Land Soil 1st Rate

North between Sects 9 & 10.

Variation 12° 20' East

40.00 Drove charred stake set post and raised mound with trench & pits as pr instruction for quarter Sect Cor.

80.00 Drove charred stake set post and raised mound with trench & pits as pr instruction for Cor to Sects 3. 4. 9 & 10.

Rolling prairie Land Soil 1st Rate

20/63

Township 22 N. R 8 E 6th P.M.

East on Random line between Sects 3 & 10

Variation 12° East.

40.00 Set temporary quarter Sect Cor.

77.88 Logan Creek 50 links wide runs South

80.96 Intersected N and S line 62 links North of Cor to Sects 2. 3. 10 & 11. from which Cor I run

West on true line between Sects 3 & 10.

Variation 11° 33' East

186/27

40.48 drove charred stake. set post and raised mound with trench & pits as pr instructions for quarter Sect Cor

80.96 The Cor to Sects 3. 4. 9 & 10.

East half level bottom West half Rolling prairie Land Soil 1st Rate.

North on Random line between Sects 3 & 4

Variation 12° 30' East.

39.50 Creek 3 links wide runs S.E.

40.00 Set temporary quarter Sect Cor.

40.50 Same Creek 3 links wide runs N.W.

45.10 Same Creek 3 links wide runs N.E.

~~49.04~~

Township 22 N. R 8 E 6th P.M.

79.04 Intersected North boundary at Corner to Sects 3 & 4 from which Cor I run
South on true line between Sects 3 & 4
Variation 12° 30' East
39.04 drove charred stake set post and raised mound with trench and pits as pr instructions for quarter sect Cor
79.04 The Cor to Sects 3. 4. 9 & 10.
Rolling prairie Land. Soil Rate.

North between Sects 32 & 33
Variation 12° 52 East
13.00 Indian trail bears N E & S W
40.00 drove charred stake set post and raised mound with trench and pits as pr instructions for quarter Sect Cor.
80.00 Drove charred stake set post and raised mound with trench & pits as pr instructions for Cor to Sects 28. 29. 32 & 33.
Gently Rolling prairie. Soil Rate.

Township 22 N R 8 E 6th P.M.

East on Random line between Sects 28 & 33.
Variation 11° 45' East
40.00 Set temporary quarter Sect Cor.
80.00 Intersected N and S line at Cor to Sects 27. 28. 33. & 34 from which Cor I run
West on true line between Sects 28 & 33
Variation 11° 45' East
40.00 drove charred stake set post and raised mound with trench & pits as pr instructions for quarter Sect Cor.
80.00 The Cor to Sects 28. 29. 32 & 33
Gently rolling prairie Land Soil Rate.

West on Random line between Sects 29 & 32
Variation 11° 45' East
40.00 Set temporary quarter Sect Cor
57.92 Intersected West boundary at Cor to Sects 29 & 32 from which Cor I run
East on true line between Sects 29 & 32
Variation 11° 45' East
17.92 drove charred stake set post and raised mound with trench & pits as pr instructions for

Township 22 N. R 8 E. 6th P.M.

57.92 The Cor to Sects 28. 29. 32 & 33.
Gently Rolling prairie. Soil 1st Rate

North between Sects 28 & 29
Variation 12° East

40.00 drove chaned stake set post, and raised mound with trench and pits as pr instruction for quarter Sect Cor.
80.00 Drove chaned stake set post and raised mound with trench and pits as pr instruction for Corner to Sects 20. 21. 28 & 29.
Gently Rolling prairie Land. Soil 1st Rate.

East on Random line between Sects 21 & 28
Variation 11° 45' East
40.00 Set temporary quarter Sect Cor.
80.56. Intersected N and S line 29 links North of Corner to Sects. 21. 22. 27 & 28. from which Corner Bears
West on true line between Sects 21 & 28
Variation 11° 33' East

Township 22 N. R 8 E. 6th P.M.

40.28. drove chaned stake set post and raised mound with trench and pits, as pr instruction for quarter Sect Cor.
80.56. The Cor to Sects 20. 21. 28 & 29.
Gently Rolling prairie Land. Soil 1st Rate.

West on Random line between Sect 20 & 29
Variation 11° 45' East
40.00 Set temporary quarter Sect Cor.
57.70 Intersected West boundary 49 links North of Cor to Sects 20 & 29. from which Cor Bears
East on true line between Sects 20 & 29
Variation 12° 14' East
17.70 drove chaned stake set post and raised mound with trench and pits as pr instruction for Quarter Sect Cor
57.70 The Cor to Sects. 20. 21. 28 & 29.
Gently Rolling prairie. Soil 1st Rate.

25/68

Township 22 N. R 8 E 6th P.M.

North between Sects 20 & 21
Variation 12° East.

4.00 drove chained stake set post and raised mound with trench and pits as pr instructions for quarter Sect Cor.

8.00 drove chained stake set post and raised mound with trench and pits as pr instructions for Cor to Sect. 16. 17. 20 & 21.

Gently Rolling prairie Land. Soil 1st Rate.

East on Random line between Sects 16 & 21
Variation 11° 30' East.

4.00 Set temporary quarter Sect Cor.

8.00 Intersected A and S line 26.7 links South of Corner to Sects. 15. 16. 21 & 22, from which Cor Form

West on true line between Sects 16 & 21
Variation 13° 24' East

4.00 drove chained stake set post and raised mound with trench and pits as pr instructions for quarter Sect Cor.

80/7.14/1.54

26/69

Township 22 N. R 8 E 6th P.M.

8.00 The Cor to Sects. 16. 17. 20 & 21.

Gently Rolling prairie Land. Soil 1st Rate.

West on Random line between Sects 17 & 20.
Variation 12° 15' East

4.00 Set temporary quarter Sect Cor.

58.90 Intersected West boundary at Cor. to Sects 17 & 20. from which Cor Form

East on true line between Sects 17. & 20
Variation 12° 15' East

18.90 drove chained stake set post and raised mound with trench and pits as pr instructions for quarter sect Cor

58.90 The Cor to Sects. 16. 17. 20 & 21.

Gently Rolling prairie Land. Soil 1st Rate.

North between Sects 16 & 17.
Variation 13° 10' East.

4.00 drove chained stake set post and raised mound with trench and pits as pr instructions for quarter Sect Cor.

Township 22 N. R 8 E 6th Pm.

80.00 drove chained stake, set post and raised mound with trench and pits as pr instructions for Cor to Sects 8.9.16 & 17

Rolling prairie Land Soil 1st Rate

East on Random line between Sects 9 & 16.

Variation 13°.25 East

11.30 Branch 5 links wide runs S. E.

12.20 Same Branch 5 links wide runs N. E.

14.70 Same Branch 5 links wide runs S. E.

40.00 Set temporary Quarter Sect Cor

80.00 Intersected N and S line 53 links North of Cor to Sects 9.10.15 & 16. from which Cor I run

~~West on true line between Sects 9 & 16~~

Variation 13°.02 East

40.00 drove chained stake set post and raised mound with trench and pits as pr instructions for quarter Sect Cor.

80.00 The Cor to Sects 8.9.16 & 17.

Gently Rolling prairie Land. Soil 1st Rate.

159/23

Township 22 N. R 8 E 6th Pm.

West on Random line between Sects 8 & 17

Variation 12°.15 East.

35.00 Branch 5 links wide runs N. E.

40.00 Set temporary quarter Sect Cor.

58.40 Intersected West boundary 128 links South of Corner to Sects 8 & 17. from which Cor I run

East on true line between Sects 8 & 17

Variation 11°.30 East

18.40 Drove chained stake, set post, and raised mound with trench and pits as pr instructions for quarter Sect Cor.

58.40 The Cor to Sects 8.9.16 & 17

Rolling prairie Land. Soil 1st Rate,

North between Sects 8 & 9.

Variation 11°.45 East

12.50 Branch 5 links runs East.

40.00 drove chained stake set post and raised mound with trench and pits as pr instructions for quarter Sect Cor.

29/72

Township 22 N. R 8 E. 6th P.M.

80.00 drove chained stake set post and raised mound with trench and pit as pr instruction for Cor to Sect. 4. 5. 8 & 9.
Rolling prairie Land. Soil 1st Rate

East on Random line between Sects 4 & 9
Variation 13° East

31.00 Creek 5 links wide runs S.E.
40.00 Set temporary quarter Sect Cor.
65.00 Same Creek 5 links wide runs N.E.
80.00 Intersected N and S line at Corner to Sects. 3, 4, 9 & 10 from which Cor I run
West on true line between Sects 4 & 9
Variation 13° East
40.00 drove chained stake, set post and raised mound with trench and pit as pr instructions for quarter Sect Cor
80.00 The Cor to Sects 4. 5. 8 & 9.
Rolling prairie Land. Soil 1st Rate.

30/73

Township 22 N. R 8 E 6th P.M.

West on Random line between Sects 5 & 8.
Variation 12° East
40.00 Set temporary quarter Sect Cor.
58.90 Intersected west boundary 35 links north of Cor to Sects 5 & 8. from which Cor I run
East on true line between Sects 5 & 8
Variation 12° 20' East.
18.90 drove chained stake set post and raised mound with trench and pit as pr instruction for quarter Sect Cor
58.90. The Cor to Sects. 4. 5. 8 & 9.
Rolling prairie Land. Soil 1st Rate

North on Random line between Sects 4 & 5
Variation 12° East
40.00 Set temporary quarter Sect Cor.
70.30 Branch 5 links wide runs East
80.16 Intersected North boundary at Corner to Sects 4 and 5. from which Cor I run

Township 22 N. R 8 E. 6th P.M.

South on true line between Sects 4 & 5
Variation 12° East
40.16 drove chained stake. Set post and raised mound with trench and pits as per instruction for quarter sect Cor
80.16 The for to Sects 4. 5. 8 & 9.
Rolling prairie Land. Soil 1st Rate,
Sept 19th 1857

General Description

Land in this township mostly 1st Rate, well situated for farming and grazing purposes.
Not timber worth mentioning except in Section 36, and here it is confined entirely to the Creek bottoms,
Logan Creek is a never failing stream from 50 to 80 links wide and from

Township 22 N. R 8 E. 6th P.M.

4 to 10 feet deep, slow current and banks from 10 to 15 feet high, it looks more — a work of Art than of Nature, owing to its regular width, and evenness of Banks. No Coal or other mineral was discovered, though a very great change in the Magnetic Variation was remarked, particularly on the 4th tier
There are 2 settlements in Section 36.

List of Names.

A List of the names of the individuals employed to assist in running measuring, or marking the lines and corners described in the foregoing field notes of Township 22 North, of Range 8 East of the 6th P.M. Shewing the respective Capacities in which they acted

John Farnham Compassman
Harman Lanforsieck Chainman
Frank McKenna Chainman

Township 22 N. R 8 E 6th P.M.

Bushnell B. Loomis Chainman
Thos C Jones Chainman
F. R. Hill Axeman
James Quinn Axeman
George Cocklin Flagman.

We hereby Certify that we assisted Isaac C. Stuck Deputy Surveyor in subdividing Townships twenty one and twenty two North of Ranges four five six seven & Eight East, and Townships Eighteen Nineteen and twenty North, of Range three East of the 6th Principal Meridian in the Territory of Nebraska and that said Townships have in all respects to the best of our knowledge & belief been well and faithfully surveyed and the boundary monuments planted according to instructions furnished by the Surveyor General,

Township 22 N. R 8 E. 6th P.M.

John Farmers Compassman
Frank McKenna Chainman
T C Jones Chainman
H. H. Lanfersieck Chainman
Bushnell B. Loomis Chainman
James Quinn Axeman
F. R. Hill Axeman
George Cocklin Flagman

Subscribed and sworn to by the above named persons before me, a Probate Judge in and for Douglas County Nebraska Territory. this the 21st day of September A. D. 1857.

Clinton Briggs
Probate Judge

I Isaac C. Stuck deputy Surveyor do solemnly swear that in pursuance of a contract with John Calhoun Surveyor of the Public Lands of the Territories United States in the territories of Kansas and Nebraska, bearing date, the 19th day of June 1857 and in strict conformity to

the Laws of the United states and the instructions furnished by the said Surveyor General, I have faithfully surveyed the subdivision lines of Townships twenty One and twenty two North, of Ranges four, five, Six Seven, and Eighth East and Townships Eighteen, Nineteen and twenty North of Range three East of the 6th Principal Meridian in the Territory of Nebraska, and do further solemnly swear that the foregoing are the true and Original field notes of such survey

Isaac C. Stuck
Deputy Surveyor

Subscribed by said Isaac C. Stuck deputy surveyor, and sworn to before me, a Probate Judge in and for the County of Douglas and Territory of Nebraska, this the 21st day of September A. D. 1857. Clinton Briggs
Probate Judge

Surveyor Generals office
Lecompton K.T. 10 Dec 1857.

The foregoing transcript of the field notes of the survey of the subdivision lines of Townships Twenty one and Twenty two North of Ranges Four, Five, Six, Seven, and Eight East and Townships Eighteen nineteen and Twenty North of Range Three East of the Sixth Principal meridian in the Territory of Nebraska executed by Isaac C. Stuck DS under his contract No 210 dated the 19th day of June 1857 during the months of August and September 1857 having been critically examined the necessary corrections and alterations made the said field notes and the surveys they describe are hereby approved

J Calhoun

Field Notes of the Subdivision lines of
Township number Twenty three North of
Range number Eight East of the Sixth
Principal Meridian in the
Territory of Nebraska

Surveyed by Bernard D Holbrook
U. S. Deputy Surveyor under his
Contract number 185 dated 20
May AD 1857

Subdivision commenced August
25th completed August
27th AD 1857

Rec'd Nov 20th 1857

A list of the names of the individuals Employ-
-ed to assist in running Measuring and Marking
the lines and corners described in the following
Field Notes of Township Number Twenty Three
North of the Base Line of Range Number Eight
East of the Sixth Principal Meridian
Showing the respective capacities in which they act

Christian G Stutzman	Chainman
William A Cox	Chainman
Levi Van Arnum	Chainman
William S McCrea	Chainman
Gustavus A Hess	Axeman
Nelson W Thompson	Axeman
Charles M Cocklin	Axeman
Wallace Walcott	Axeman
Warren G Simpson	Flagman
Norman B Holbrook	Flagman
John Y. Clopper	Compassman

Township 23 N. Range 8 East

6	5	29	4	21	3	15	2	8	1
	29		28		20		14		7
7	8	28	9	20	10	13	11	7	12
	27		26		19		13		6
18	17	26	16	19	15	12	14	6	13
	25		25		18		12		5
19	20	24	21	18	22	11	23	4	24
	24		23		17		10		3
30	29	23	28	17	27	10	26	3	25
	22		22		16		9		2
31	32	21	33	15	34	9	35	1	36

Township 23 N Range 8 E. Sixth Principal Meridian

To determine the proper adjustment of my Compass for Subdividing this Township, I commenced at the corner to Townships 22 and 23 N Range 7 and 8 East, and run North on a blank line along the East boundary of section 36

Variation 11° 45' East

39.94 To quarter section corner

80.04 To corner to sections 25 and 36.

This being the proper adjustment of my Compass, I commenced at the corner to sections 1, and 2, 35 and 36 on the south boundary of the Township subdivision commenced August 25th A.D. 1857

North between sections 35 and 36

Variation 11° 45' East

40.00 Drove a charred stake and set a post in Mound with trench and pits as per instructions for quarter section corner

Township 23 N Range 8 E. Sixth Principal Meridian

80.00 Bore a chared stake and set a post in a Mound with trench and pits as per instructions for corner to Sections 25, 26, 35 and 36

Land level Soil 1st rate clay loam

East on a random line between sections 25 and 36

Variation 11° 15' East

40.00 set a post for temporary quarter section corner

80.50 Intersected the East boundary of the Township 40 North of the corner to sections 25 and 36. from which corner I run West on a true line between sections 25 and 36

Variation 10° 58' East

40.25 Bore a chared stake and set a post in Mound with trench and pits as per instructions for quarter section corner

80.50 The corner to sections 25, 26, 35 and 36

Low level land 1st rate Soil clay loam

Township 23 N Range 8 E. Sixth Principal Meridian

North between sections 25 and 26

Variation 11° 30' East

30.00 Middle creek 75 links wide runs S W

35.00 Middle creek 75 links wide runs S E

40.00 Bore a chared stake and set a post in Mound as per instructions for quarter section corner

40.50 Middle creek 75 links wide runs S. W.

50.00 Middle creek 75 links wide runs S. E.

59.00 Middle creek 75 links wide runs S. W.

75.00 Middle creek 75 links wide runs S. E.

77.50 Middle creek 75 links wide runs S W

80.00 Bore a chared stake and set a post in Mound with trench and pits as per instructions for corner to sections 23, 24, 25 and 26

Low level land. Soil 1st rate clay loam

East on a random line between sections 24 and 25

Variation 11° 30' East

6.00 Middle creek 75 links wide course South

15.00 Middle creek 75 links wide course North

Township 23 N Range 8 E. Sixth Principal Meridian

24.00	touched north bank of Middle creek
35.00	crossed Middle creek 75 links wide. runs S
40.00	set a post for temporary quarter section corner
80.10	Intersected the East boundary of the Township 40 links south of the corner to sections 24 and 25. from which corner I run West on a true line between sections 24 and 25
	Variation 11° 47' East
40.05	Drove a charred stake and set a post in Mound with trench and pits as per instructions for quarter section corner
80.10	The corner to sections 23, 24, 25 and 26 low level bottom land 1st rate clay loam

North between sections 23 and 24

Variation 11° 30' East

35.00	Middle creek 80 links wide course S. E.
40.00	Drove a charred stake and set a post in Mound with trench and pits as per instructions for quarter section corner
44.00	Middle creek 80 links wide course West

Township 23 N Range 8 E. Sixth Principal Meridian

60.00	Middle creek 75 links wide course S. E.
63.00	Middle creek 75 links wide course N
64.00	Middle creek 75 links wide course S. E.
80.00	Drove a charred stake and set a post in Mound with trench and pits as per instructions for ~~quarter section corner~~ corner to sects 13, 14, 23 & 24 Low level bottom land 1st rate clay loam

East on random line between sections 13 and 24

Variation 12° East

40.00	set a post for temporary quarter section corner
80.40	Intersected the East boundary of the Township 30 links south of the corner to sections 13 and 24 from which corner I run West on a true line between sections 13 and 24
	Variation ~~11° 47'~~ 12° 13' East
40.30	Drove a charred stake and set a post in Mound with trench and pits as per instructions for quarter section corner
80.60	The corner to sections 13, 14, 23 and 24 Bottom land 1st rate clay loam

Township 23 N Range 8 E Sixth Principal Meridian

North between sections 13 and 14

Variation 11° East

40.00 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner

80.00 Drove a chained stake and set a post in Mound with trench and pits as per instructions for corner to sections 11, 12, 13 and 14

Bottom land 1st rate soil clay loam

East on a random line between sections 12 and 13

Variation 12° 10' East

40.00 Set a post for temporary quarter section corner

80.18 Intersected the East boundary of the Township at the corner to sections 12 and 13 from which corner I run West on a true line between sections 12 and 13

Variation 12° 10' East

4009 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner

Township 23 N Range 8 E Sixth Principal Meridian

8018 The corner to Sections 11, 12, 13 and 14

Bottom Land Soil 1st rate clay loam

North between Sections 11 and 12

Variation 11° East

4000 Drove a chained stake set a post in Mound with trench and pits as per instructions for quarter section corner

8000 Drove a chained stake and set a post in Mound with trench and pits as per instructions for corner to Sections 1, 2, 11 and 12

Low Bottom land Soil 1st rate clay loam

East on a random line between sections 1 and 12

Variation 12° 15' East

4000 Set a post for temporary quarter section corner

7990 Intersected the East boundary of the Township at the corner to sections 1 and 12 from which corner I run West on a true line between Sections 1 and 12

Township 23 N Range 8 E. Sixth Principal Meridian

Variation 12° 15' East

3995 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner

7990 The corner to sections 1, 2, 11 and 12

level Bottom land soil 1st rate clay loam

North on a random line between sections 1 and 2

Variation 12° 15' East

40.00 set a post for temporary quarter section corner

80.16 Intersected the North boundary of the Township 26 links East of the corner to sections 1 and 2 from which corner I run South on a true line between sections 1 and 2

Variation 12° 24' East

40.16 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

80.16 The corner to sections 1, 2, 11 and 12

Bottom, level land 1st rate. soil clay loam

Township 23 N Range 8 E. Sixth Principal Meridian

North between sections 34 and 35

Variation 12° East

40.00 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner

80.00 Drove a chained stake and set a post in Mound with trench and pits as per instructions for corner to sections 26, 27, 34 and 35.

Low level Bottom Sand soil 1st rate clay loam

East on a random line between sections 26 and 35

Variation 11° 15' East

40.00 set a post for temporary quarter section corner

53.75 crossed Middle creek 75 links wide runs S.

58.00 crossed Middle creek 75 links wide runs S

66.00 crossed Middle creek 75 links wide runs S.

80.12 Intersected the N and S line at the corner to sections 25, 26, 35 and 36 from which corner I run West on a true line between sections 26 and 35

Township 23 N Range 8 E Sixth Principal Meridian

Variation 11° 15' East

40.06 Drove a chained stake and set a post in Mound with trench and pits
as per instructions for quarter section corner
80.12 The corner to sections 26, 27, 34 and 35.
Bottom land level soil 1st rate clay loam

North between sections 26 and 27

Variation 12° East

40.00 Drove a chained stake and set a post in Mound with trench and pits
as per instructions for quarter section corner
80.00 Drove a chained stake and set a post in Mound with trench and pits
as per instructions for corner to sections
22, 23, 26 and 27
Low Bottom land soil 1st rate clay loam

East on a random line between sections
23 and 26.

Variation 12° 15' East

40.00 set a post for temporary quarter section corner
79.90 Intersected the N and S line 48 link
North of the corner to sections 23, 24, 25 and 26

Township 23 N Range 8 E, Sixth Principal Meridian

from which corner I run West on a true
line between sections 23 and 26

Variation 11° 54' East

39.95 Drove a chained stake and set a post in Mound with trench and pits
as per instructions for quarter section corner
79.90 The corner to sections 22, 23, 26 and 27
Low level land soil 1st rate clay loam

North between sections 22 and 23

Variation 12° East

40.00 Drove a chained stake and set a post in Mound with trench and pits
as per instructions for quarter section corner
80.00 Drove a chained stake and set a post in Mound with trench and pits
as per instructions for corner to sections
14, 15, 22 and 23.
Low level bottom land soil 1st rate clay loam

East on a random line between sections
14 and 23

Variation 12° East

40.00 set a post for temporary quarter section corner

Township 23 N Range 8 E. Sixth Principal Meridian

5040 crossed Middle creek 50 links wide, runs S.E.
5450 crossed Middle creek 55 links wide, runs S.E.
5950 crossed Middle creek 50 links wide course S.E.
6650 small stream 6 link wide course S.E.
80.20 Intersected the N and S line 34 links north of the corner to sections 13, 14, 23 and 24 from which corner I run West on a true line between sections 14 and 23

Variation 11°45' East

40.10 Drove a chaned stake and set a post in Mound with trench and pits as per instructions for quarter section corner
80.20 The corner to sections 14, 15, 22 and 23
low bottom land soil 1st rate clay loam

North between sections 14 and 15

Variation 11° 15' East

40.00 Drove a chaned stake set a post in Mound with trench and pits as per instructions for quarter section corner
80.00 Drove a chaned stake and set a post in Mound with trench and pits as per instructions for corner to sections 10, 11, 14 and 15

Township 23 N Range 8 E. Sixth Principal Meridian

low level land 1st rate. soil clay loam

East on a random line between sections 11 and 14

Variation 12° East

36.00 Middle creek 75 links wide course south
40.00 ~~Pointed~~ for temporary quarter section corner
80.30 Intersected the N and S line 20 links south of the corner to sections 11, 12, 13 and 14 from which corner I run West on a true line between sections 11 and 14

Variation 12°09' East

40.15 Drove a chaned stake and set a post in mound with trench and pits for quarter section corner as per instructions
80.30 The corner to sections 10, 11, 14 and 15
Bottom Sand land soil 1st rate clay loam

North between sections 10 and 11

Variation 11° East

4000 Drove a chaned stake and set a post in Mound with trench and pits as per instructions for quarter section corner

Township 23 N Range 8 E. Sixth Principal Meridian

80.00 Drove a chained stake and set a post in Mound with trench and pits as per instructions for corner to sections 2, 3, 10 and 11
Low bottom land Soil 1st rate clay loam

East on a random line between sections 2 and 11

Variation 12°. East

25 00 Middle creek 75 links wide course N and S
40 00 set a post for temporary quarter section corner
70.00 Lake 5.00 chs wide. Miry and full of Bullrushes N + S
80.10 Intersected the N and S line 30 link South of the corner to sections 1, 2, 11 and 12 from which corner I run West on a true line between sections 2 and 11

Variation 12° 13' East

40 05 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter Section corner
80.10 The corner to Sections 2, 3, 10 and 11
level Low bottom land Soil 1st rate clay loam

Township 23 N Range 8 E. Sixth Principal Meridian

North on a random line between sections 2 and 3

Variation 11° 45' East

21.50 Middle creek 75 links wide course East
40 00 set a post for temporary quarter section corner
80 24 Intersected the North boundary of the Township 10 links East of the corner to sections 2 and 3. from which corner I run south on a true line between sections 2 and 3

Variation 11° 49' East

40 24 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter Section corner
80 24 The corner to Sections 2, 3, 10 and 11
level Low bottom land Soil 1st rate clay loam

August 23th 1857

North between sections 33 and 34

Variation 11° 45' East

40.00 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner
80.00 Drove a chained stake. set a post in a Mound with trench and pits

Township 23 N Range 8 E. Sixth Principal Meridian

as per instructions for corners to sections 27, 28
33 and 34
Land rolling Prairie Soil 2nd rate sandy Soil

East on a random line between sections
27 and 34
Variation 12° 15' East
10.00 stream 20 link wide course south East
40.00 set a post for temporary quarter section corner
80.04 Intersected the N and S line 38 link North
of the corner to sections 26, 27, 34 and 35
from which corner I run West on a true
line between sections 27 and 34
Variation 12° East
40.02 Bore a chained stake and set a post in Mound with trench and pits
as per instructions for quarter section corner
80.04 The corner to sections 27, 28, 33 and 34
Land West of 50 chains rolling Prairie 2nd rate
sandy soil, East of 50 chains low level Bottom
1st rate clay loam

Township 23 N Range 8 E. Sixth Principal Meridian

North between sections 27 and 28
Variation 12° East
14.10 creek 20 links wide course south East
24.50 leave Bottom land
40.00 Bore a chained stake and set a post in Mound with trench and pits
as per instructions for quarter section corner
80.00 Bore a chained stake and set a post in Mound with trench and pits
as per instructions for corners to sections 21, 22, 27 and 28
South 1/2 level Bottom land Soil 1st rate clay loam
North 1/2 rolling Prairie soil 2nd rate sandy

East on a random line between sections 22 and 27
Variation 12° East
40.00 set a post for temporary quarter section corner
79.96 Intersected the N and S line at the corner to
sections 22, 23, 26 and 27 from which corner I run
West on a true line between sections 22 and 27
Variation 12° East
39.98 Bore a chained stake and set a post in Mound with trench and pits
as per instructions for quarter section corner
79.96 The corner to sections 21, 22, 27 and 28

Township 23 N Range 8 E. Sixth Principal Meridian

Land rolling Prairie 2nd rate sandy soil

North between sections 21 and 22

Variation 12° East

40.00 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner

80.00 Drove a chained stake and set a post in Mound with trench and pits as per instructions for corner to sections 15, 16, 21 and 22.

Land rolling Prairie 2nd rate sandy soil

East on a random line between sections 15 and 22

Variation 12° East

40.00 set a post for temporary quarter section corner

79.80 Intersected the N and S line 56 links south of corner to sections 14, 15, 22, and 23 from which corner I run West on a true line between sections 15 and 22

Variation 12° 24' East

39.90 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner

79.80 The corner to sections 15, 16, 21 and 22

Land rolling Prairie 2nd rate sandy soil

Township 23 N Range 8 E Sixth Principal Meridian

North between sections 15 and 16

Variation 12° 15' East

40.00 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner

80.00 Drove a chained stake and set a post in Mound with trench and pits as per instructions for corner to sections 9, 10, 15 and 16

Land rolling Prairie Sandy soil 2nd rate

East on a random line between sections 10 and 15

Variation 13° 15' East

40.00 set a post for temporary quarter section corner

79.92 Intersected the N and S line 40 links south of corner to sections 10, 11, 14 and 15 from which corner I run West on a true line between sections 10 and 15

Variation 13° 32' East

39.96 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner

79.92 The corner to sections 9, 10, 15 and 16

Land rolling Prairie Sandy soil 2nd rate

Township 23 N Range 8 E Sixth Principal Meridian

North between sections 9 and 10

Variation 12° 38' East

4000 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner

8000 Drove a chained stake and set a post in Mound with trench and pits as per instructions for corner to sections 3, 4, 9 and 10

Land rolling Prairie Sandy Soil 2nd rate

East on a random line between sections 3 and 10

Variation 12° 30' East

4000 set a post for temporary quarter section corner

8020 Intersected the N and S line 4 links south of corner to sections 2, 3, 10 and 11 from which corner I run West on a true line between sections 3 and 10

Variation 12° 32' East

4010 Drove a chained stake and set a post in Mound with trench and pits as per instructions for quarter section corner

8020 The corner to sections 3, 4, 9 and 10

Land rolling Prairie Sandy Soil 2nd rate

Township 23 N Range 8 E Sixth Principal Meridian

North on a random line between sections 3 and 4

Variation 12° 15' East

4000 set a post for temporary quarter section corner

8012 Intersected the North boundary of Township 10 links West of the corner to sections 3 and 4 from which corner I run South on a true line between sections 3 and 4

Variation 12° 04' East

4012 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

8012 The corner to sections 3, 4, 9 and 10

Land rolling Prairie Sandy Soil 2nd rate

North between sections 32 and 33

Variation 12° 10' East

4000 Drove a chained stake and set a post in a Mound with trench and pits as per instructions for quarter section corner

8000 Drove a chained stake and set a post in Mound with trench and pits as per instructions for corner to sections 28, 29, 32 and 33

Land rolling Prairie Sandy Soil 2nd rate

Township 23 N Range 8 E. Sixth Principal Meridian

East on a random line between sections 28 and 33
Variation 11°56' East

3700 small stream 3 links wide course North East
4000 set a post for temporary quarter section corner
7960 Intersected the N and S line at the corner to sections 27, 28, 33 and 34 from which corner I run West on a true line between sections 28 and 33
Variation 11°56 East
3980 Drove a charred stake and set a post in Mound with trench and pits as per instructions for quarter section corner
7960 The corner to sections 28, 29, 32 and 33
Land level bottom 1st rate Clay loam

West on a random line between sections 29 and 32
Variation 13° East

4000 set a post for temporary quarter section corner
5960 Intersected the West boundary of the Township 20 link North of the corner to sections 29 and 32 from which corner I run East on a true line between sections 29 and 32
Variation 13° 09' East

Township 23 N Range 8 E. Sixth Principal Meridian

1960 Drove a charred stake and set a post in Mound with trench and pits as per instructions for quarter section corner
5960 The corner to Sections 28, 29, 32 and 33
Land rolling Prairie Sandy Soil 2nd rate

North on line between sections 28 and 29
Variation 12° 36' East

4000 Drove a charred stake and set a post in Mound with trench and pits as per instructions for quarter section corner
8000 Drove a charred stake and set a post in Mound with trench and pits as per instructions for corner to sections 20, 21, 28 and 29
Land rolling Prairie Sandy Soil 2nd rate

East on a random line between sections 21 and 28
Variation 13° East

1300 Small stream 5 links wide course South East
4000 set a post for temporary quarter section corner
8006 Intersected the N and S line 62 links south of corner to sections 21, 22, 27 and 28, from which corner I run West on a true line between sections 21 and 28
Variation 13°, 27' East

Township 23 N Range 8 E Sixth Principal Meridian

40.03	Drove a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter section corner
80.06	The corner to Sections 20, 21, 28 and 29 Land rolling Prairie Sandy Soil 2nd rate

West on a random line between sections 20 and 29
Variation 13° 30' East

40.00	Set a post for temporary quarter section corner
60.06	Intersected the West boundary of Township 14 links North of the corner to sections 20 and 29 from which corner Run East on a true line between sections 20 and 29

Variation 13° 36' East

20.06	Drove a chaned stake and set a post in Mound with trench and pits as per instructions for quarter Section corner
60.06	The corner to Sections 20, 21, 28 and 29 Land rolling Prairie Sandy soil 2nd rate

North between sections 20 and 21
Variation 12° 30' East

12.00	Small stream 5 links wide course South East

Township 23 N Range 8 E Sixth Principal Meridian

40.00	Drove a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter section corner
80.00	Drove a chaned stake and set a post in Mound with trench and pits as per instructions for corner to sections 16, 17, 20 and 21 Land rolling Prairie Sandy Soil 2nd rate

East on a random line between Sections 16 and 21
Variation 12° 30' East

40.00	set a post for temporary quarter section corner
79.92	Intersected the N and S line at the corner to sections 15, 16, 21 and 22, from which corner Run West on a true line between sections 16 and 21

Variation 12° 36' East

39.96	Drove a chaned stake and set a post in Mound with trench and pits as per instructions for quarter Section corner
79.92	The corner to sections 16, 17, 20 and 21 Land rolling Prairie Sandy Soil 2nd rate

West on a random line between sections 17 and 20
Variation 13° 45' East

35.00	Small stream 20 links wide course South

Township 23 N Range 8 E. Sixth Principal Meridian

40 00	set a post for temporary quarter section corner
60 32	Intersected the West boundary of Township 40 links North of the corner to sections 17 and 20 from which corner I run East on a true line between Sections 17 and 20
	Variation 11° 02' East
20 32	Dove a chaned stake and set a post in Mound with trench and pits as per instructions for quarter section corner
60 32	The corner to Sections 16, 17, 20 and 21 Land rolling Prairie Sandy Soil 2nd rate
	August 26th 1857
	North between Sections 16 and 17
	Variation 13° East
40 00	Dove a chaned stake and set a post in Mound with trench and pits as per instructions for quarter section corner
80 00	Dove a chaned stake and set a post in Mound with trench and pits as per instructions for corner to sections 8, 9, 16 and 17 Land rolling Prairie Sandy Soil 2nd rate
	East on a random line between Sections 9 and 16
	Variation 12° East

Township 23 N Range 8 E. Sixth Principal Meridian

40 00	set a post for temporary quarter section corner
79 82	Intersected the N and S line at the corner to sections 9, 10, 15 and 16, from which corner I run West on a true line between sections 9 and 16
	Variation 12° East
39 91	Dove a chaned stake and set a post in a Mound with trench and pits as per instructions for quarter section corner
79 82	The corner to sections 8, 9, 16 and 17 Land rolling Prairie Sandy Soil 2nd rate
	West on a random line between sections 8 and 17
	Variation 14° East
30 00	Small stream 5 links wide course South West
40 00	set a post for temporary quarter section corner
45 00	Stream 2 links wide course South
59 96	Intersected the West boundary of Township 4 links south of the corner to sections 8 and 17 from which corner I run East on a true line between Sections 8 and 17
	Variation 13° 58' East
19 96	Dove a chaned stake and set a post in a Mound with trench and pits

Township 23 N Range 8 E. Sixth Principal Meridian

as per instructions for quarter section corner
5996 The corner to Sections 8, 9, 16 and 17
Land rolling Prairie Sandy Soil 2nd rate

North between Sections 8 and 9
Variation 14° 15' East
1000 Struck Bottom Land
4000 Drove a chained stake and set a post in Mound with trench and pits
as per instructions for quarter Section corner
8000 Drove a chained stake and set a post in Mound with trench and pits
as per instructions for corner to sections 4, 5, 8 and 9
Large Bottom Land Soil 1st rate Clay loam

East on a random line between sections 4 and 9
Variation 12° East
4000 set a post for temporary quarter section corner
7986 Intersected the Ra's line 10 link North of the corner to sections 3, 4, 9 and 10 from which corner I run West on a true line between Sections 4 and 9

Township 23 N Range 8 E. Sixth Principal Meridian

Variation 11° 56' East
39.93 Drove a chained stake and set a post in Mound with trench and pits
as per instructions for quarter section corner
7986 The corner to Sections 4, 5, 8 and 9
Land Bottom Land 1st rate Clay loam

West on a random line between Sections 5 and 8
Variation 14° East
4000 set a post for temporary quarter section corner
5980 Intersected the West boundary of Township 12 links North of the corner to Sections 5 and 8 from which corner I run East on a true line between sections 5 and 8
Variation 14° 05' East
1980 Drove a chained stake and set a post in a Mound with trench and pits
as per instructions for quarter section corner
5980 The corner to sections 4, 5, 8 and 9
Large Bottom Land Soil 1st rate Clay loam

North between sections 4 and 5 on a Random line
Variation 13° 10' East

Township 23 N Range 8 E Sixth Principal Meridian

4000 set a post for temporary quarter section corner
80.14 Intersected the North boundary of Township
12 link West of the corner to sections 4
and 5 from which corner I run South
on a true line between sections 4 and 5
Variation 12° 55' East
with trench and pits
4014 Drove a chaned stake and set a post in Mound
as per instructions for quarter section corner
8014 The corner to sections 4, 5, 8 and 9
Bottom land 1st rate Clay loam
August 27th 1857

Township 23 N Range 8 E sixth Principal Meridian

General Description

This Township has in the East part some very excellent farming Land Middle creek is a deep rapid stream with a few scattering trees along its banks. The Bottom Lands on each side of the stream are wide and of excellent quality. There is no timber in the Township for farming purposes except a Grove of 8 or 10 acres in Section 34 The south Western part of the Township is generally hilly and the soil of poor quality

No Settlements

A List of the names of the individuals employed to assist in Running measuring or marking the lines and corners described in the foregoing Field Notes of Township No. 23 North of the Base line of Range No. 8 East of the 6th Principal Meridian, Showing the respective capacities in which they acted

Christian G Stutzman Chainman
William A Cox Chainman
Levi Van Arnum Chainman
William S McCrea Chainman
Gustavus A Hess Axeman
Nelson W Thompson Axeman
Charles M Cocklin Axeman
Wallace Wolcott Axeman
Warren G Simpson Flagman
Norman B Holbrook Flagman
John G Clopper Compassman

We hereby certify that we assisted Bernard D. Holbrook Deputy Surveyor in subdividing Township number twenty three north of Ranges Number ~~[illegible]~~ four five six, seven and Eight east of the Sixth principal meridian and that said townships have been in all respects to the best of our knowledge and belief well and faithfully surveyed and the boundary monuments planted according to the instructions furnished by the Surveyor General

John Y. Clopper Compassman
Christian G. Hutzman Chainman
William A Cox Chainman
Levi Van Arnum Chainman
William F. McCrea Chainman
Gustavus A Hess Axeman
Nelson W Thompson Axeman
Charles M Cocklin Axeman

Wallace Wolcott Axeman
Warren E Simpson Flagman
Norman B Holbrook Flagman

Subscribed and Sworn to by the above named Persons before me a Notary Public in and for the County of Douglas in the Territory of Nebraska this twelfth day of September 1857

A S McMorgan

I, Bernard D. Holbrook deputy Surveyor do Solemnly Swear that in pursuance of a contract with John Calhoun Surveyor of the public lands of the United States in the Territories of Kansas and Nebraska bearing date the day of May 1857 and in strict conformity to the laws of the United States and the instructions furnished by the Surveyor General I have faithfully Surveyed the Subdivision lines of Township Number Twenty three North of the Base line, of Ranges number four, five six seven and eight East of the Sixth Principal Meridian in the territory of Nebraska and do further Solemnly Swear that the foregoing are the true and original field notes of such Survey

Bernard D. Holbrook
Deputy Surveyor

Subscribed by said Bernard D. Holbrook deputy Surveyor and Sworn to before me a Notary Public in and for Douglas County in the Territory of Nebraska this day of 1857

A. W. Morgan

Surveyor Generals Office
~~Lecompton K.T. 28 Jan 1858~~

The foregoing field notes of the survey of the subdivision lines of Township Twenty Three North of Ranges Four Five Six Seven and eight East of the Sixth Principal Meridian in the Territory of Nebraska executed by Bernard O Holbrook DS under his contract No 185 dated 20th May 1857. during the month of August 1857. having been critically examined the necessary corrections and alterations being made the said field notes and the surveys they describe are hereby approved

J Calhoun
Surveyor Genl

38/122

Notary Public's Certificate not dated

Under Instructions of June 5th 1858.

Survey of the

Subdivisional lines of

Fractional Townships

24 N. of Ranges 6. 7. & 8. East of the 6th Principal Meridian N.T.

Executed by

John Y. Clapper D.S.

under

Instructions dated the 5th day of June 1858.

I John Y. Clopper having been appointed a deputy surveyor of the lands of the United States in Nebraska Territory do solemnly swear that I will well and faithfully and to the best of my skill and ability execute the duties confided to me pursuant to ~~a contract with~~ instructions from John Calhoun Surveyor General of public lands in Nebraska Territory bearing date the 5th day of June AD 1838 according to the laws of the United States and the instructions furnished me by the said Surveyor General

John Y. Clopper
Deputy Surveyor

Sworn to and subscribed before me this 18th day of July AD 1838

William E Moore
Notary Public

We Levi Van Arnum and Sterritt M. Curran do solemnly swear that we will well and faithfully execute the duties of chain carriers that we will level the chain on uneven ground and plumb the tally pins whether by sticking or dropping the same, that we will report the true distance of all notable objects and the true length of all lines that we assist in measuring to the best of our skill and ability

Levi Van Arnum
Sterritt M. Curran

Sworn to and subscribed before me this 18th day of July AD 1838

William E Moore
Notary Public

We Christian G. Stutzman and James W. Scott do solemnly swear that we will well and truly perform the duties of Fireman to the best of our skill and ability and according to instructions given us

Christian G. Stutzman
James W. Scott

Sworn to and subscribed before me this 18th day of July AD 1858

William E. Moore
Notary Public

I George W. Jenkins do solemnly swear that I will well and truly perform the duties of flagman according to instructions given me and to the best of my skill and ability

George W. Jenkins

Sworn to and subscribed before me this 18th day of July AD 1858

William E. Moore

I, Bernard D. Holbrook do solemnly swear that I will well and faithfully perform the duties of Compagnman according to directions given me and to the best of my skill and ability

Bernard D. Holbrook

Sworn to and subscribed before me this 18th day of July AD 1858

William E. Moore
Notary Public

Field Notes of the Subdivision lines of Fractional Township number Twenty four North of Range Eight East of the 6th principal Meridian in the Territory of Nebraska. by John B Clopper. Deputy Surveyor under Special instructions. dated the 5th day of June A D 1858.

Commenced July 24th 1858.
Completed July 24th 1858.

Corrd by Crowd & Tony
Sept 21st

Names and duties of Assistants.

Sterrett, M. Curran.	Chainman
Levi. Van Arnum	Chainman
Christian. G. Stutzman	Axeman
James. W. Scott	Axeman
George. W. Jenkins	Flagman
Bernard. D. Holbrook	Compassman

Township 24 North Range 8 East 6th P. M.

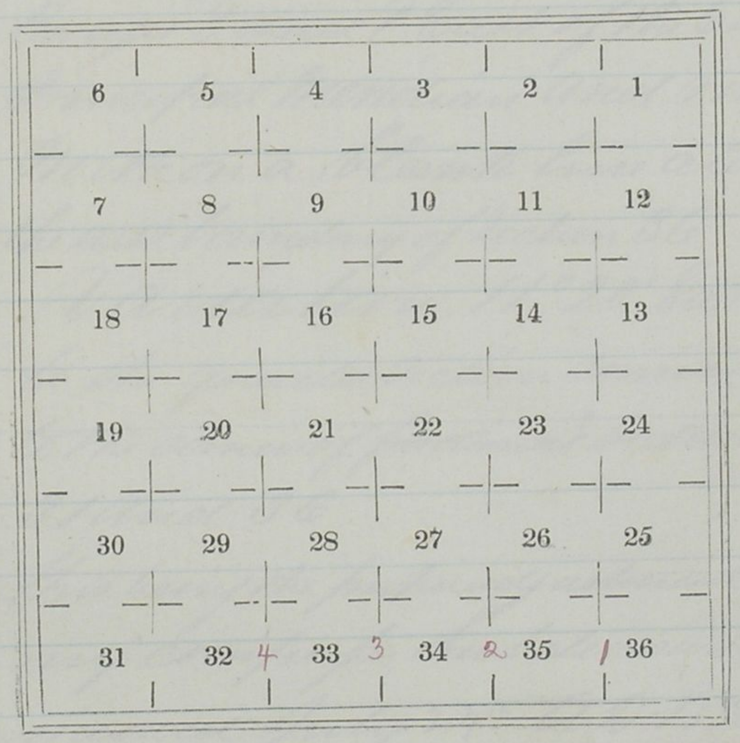

6	5	4	3	2	1
7	8	9	10	11	12
18	17	16	15	14	13
19	20	21	22	23	24
30	29	28	27	26	25
31	32 4	33 3	34 2	35 1	36

T 24 N R 8 E 6th Principal Meridian

To determine the proper adjustment of my compass for subdividing this Township I commenced at the corner to Townships 23 and 24 north and Ranges 8 and 9 East of the 6th Principal Meridian and run North on a blank line along the east boundary of Section 36

Variation 11° 20' East

40,02 to the quarter section corner

72,20 to the corner of fractional sections 31 and 36

This being the proper adjustment of my compass Subdivision commenced July 24th AD 1838

North between sections 35 and 36

Variation 11° 20' East

40,00 Drove a chenced stake and set a post in mound with trench and pits as per instructions for quarter section corner

T 24 N R 8 E 6th Principal Meridian

72.30 Intersected the south boundary of Omaha reserve Drove a charred stake and set a post in mound with trench and pits as per instructions for corner to fractional sections 35 and 36

Surface rolling soil 2nd rate

East between Omaha reserve and Section 36.

Variation 11° 20' East

28.40 to a corner on reserve line

Surface rolling soil 2nd rate

North on a line between sections 34 and 35.

Variation 11° 20' East

40.00 Drove a charred stake and set a post in mound with trench and pits as per instructions for quarter section corner

T 24 N R 8 E 6th Principal Meridian

72.10 Intersected South boundary of Omaha reserve, Drove a charred stake and set a post in mound with trench and pits as per instructions for corner to fractional sections 34 and 35.

Surface rolling soil 2nd rate

East between Section 35 and Omaha Reserve

Variation 11° 18 East

18.16 To the nearest corner on Omaha reserve line

Surface hilly soil 3rd rate

North between Sections 33 and 34

Variation 11° 20' East

40.00 Drove a charred stake and set a post in mound with trench and pits as per instructions for quarter section corner.

T. 24 N. R. 8 E. 6th Principal Meridian

72.00 Intersected the South boundary of the Omaha Reserve, Drove a charred stake and set a post in mound with trench and pits as per instructions for corner to fractional sections 33 and 34
Land gently rolling soil 2nd rate

East between Section 34 and the Omaha Reserve
Variation 11° 10' East
10.15 To nearest corner on line of Omaha Reserve
Land, rolling surface, soil 2nd rate

North between Sections 32 and 33
Variation 11° 20' East.
40.00 Drove a charred stake and set a post in mound with trench and pits as per instructions for quarter section corner
72.06 Intersected the South boundary of the Omaha Reserve. Drove a charred

T. 24 N. R. 8 E. 6th Principal Meridian

stake and set a post in mound with pits and trench as per instructions for corner to fractional sections 32 and 33.
Surface rolling soil 2nd rate

East between the Omaha Reserve and section 33
Variation 11° 20' East
15.70 To nearest corner on line of Omaha reserve
Surface rolling soil 2nd rate
July 24th 1858

North between sections 31 and 32
Variation 11° 20' East
40.00 Drove a charred stake and set a post in mound with pits and trench as per instructions for quarter section corner
71.94 Intersected South boundary of Omaha Reserve line. Drove a charred stake and set a post in mound with trench and pits as per instructions for corner to fractional sections 31 and 32
Surface rolling soil 2nd rate

T. 24 N R 8 E 6th Principal Meridian

West between Omaha Reserve and section 31.

Variation 11° 20' East

13.07 to nearest corner on Omaha reserve line

Surface rolling Soil 2nd rate

July 24th 1838

General Description

The Soil of this Township is below the common average there is some good land along Middle Creek (a stream not crossed on line) but it is without timber or other inducements to settlers, No settlements in this Township

Field Notes of the subdivision lines of fractional Township number Twenty four north of Range number Eight East of the 6th principal Meridian in the Territory of Nebraska by John Y. Clopper deputy Surveyor under special instructions dated the day of A.D. 1838

Commenced July 24th 1838

Completed July 24th 1838

A list of the names of the individuals employed to assist in running, measuring or marking the subdivision lines in fractional township twenty four North of Range number Eight East of the 6th Principal Meridian Showing the respective capacities in which they acted

Sterrett McCunan Chainman
Levi Van Amum Chainman
Christian G Stutzman Axeman
James W Scott Axeman
George W Jenkins Flagman
Bernard D Holbrook Compassman

General Land Office • Original Field Notes

Book Number

89

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.
