General Land Office • Original Field Notes

Book Number

131

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.

Base line in Range 4. E

Chains	
	To determine the broken adjustment of

Index Diagram

Field Notes of T. 1. S. Rs. 4. 5. 6. 7 & 8 are in this Book but not indexed. belonging to Kansas.

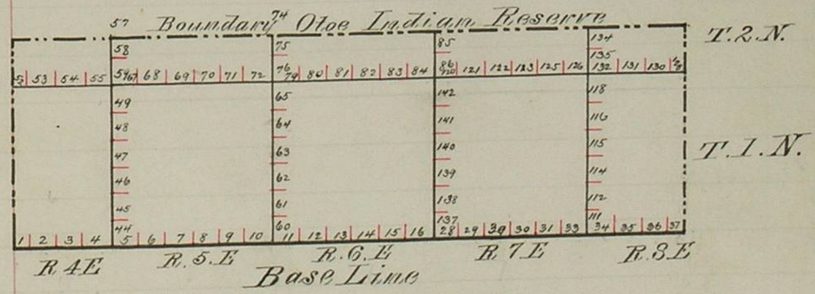

Base line in Range 4. E

Chains		
		To determine the proper adjustment of my compass for the retracing and re-establishment of the Base line I commenced at the cor. to sec. 32 and 33 T. 1 N. R. 4 E.
		East on South boundary sec. 33 Va. 11° 30' E
39	96	to a point 10 lks N. of the 1/4 sec. cor. limestone
45	51	to a point 14 lks N. of the limestone cor. on the West boundary of the Otoe Indian Reserve
79	9	to a point 22 lks N. of the limestone cor. to sec. 33 and 34. to retrace this line or run parallel thereto my compass must be adjusted to A. Va. 11° 21' E

Base line in Range 4. E.

Chains		
		East on the S. boundary sec. 33 from the limestone cor. the W. Boundary of the otoe Indian reserve Va. 11°21' E
14	57	set Sandstone 17 x 9 x 6 in 8 in in ground marked 1/16 for 1/16 sec. cor.
34	57	the Limestone cor. to sec. 33 and 34 still standing as planted

Base line in Range 4. E.

Chains		
		Easton S. boundary Sec. 34 Va. 11°21' E
20	00	set Sandstone 18×9×4 in 8 in in ground marked M6 for M6 Sec. cor.
40	00	the Limestone Pt Sec. cor. standing as planted
60	00	set Sandstone 18×10×5 in 8 in in ground marked M6 for M6 Sec. cor.
71	73	the Sandstone Cor. to Sec. 3 T. 1. S. R. 4. E.
80	00	the limestone Cor. to Sec. 34 and 35 still standing as planted.

Base line in Range 4. E.

Chains		
		Easton. S. boundary Sec. 35 Va. 11°21' E
20	00	set Sandstone 18×9×6 in 8 in in ground marked M6 for M6 Sec. cor.
31	65	the Sandstone Pt Sec. cor. for N. boundary Sec. 2 T. 1. S. R 4 E
40	00	the limestone Pt Sec. cor. still standing as planted
60	00	set Sandstone 18×9×4 in 8 in in ground marked M6 for M6 Sec. cor.
71	56	the Sandstone Cor. to Sec. 1 and 2 T. 1. S. R. 4 E
80	00	the limestone Cor. to Sec. 35 and 36 still standing as planted.

Base line in Range 4. E. 6th P.M.

Chains		
		East on S. boundary sec. 36. Va. 11°21' E
20	00	set Sandstone 19×10×4 in 8 in in ground marked 1/16 for 1/16 sec. cor.
31	45	the sandstone 1/4 sec. cor. on N. boundary sec. 1. T. 1 S. R. 4 E. standing as planted
40	00	the limestone 1/4 sec. cor.
60	00	set Sandstone 18×10×5 in 8 in in ground marked 1/16 for 1/16 sec. cor.
71	30	the limestone cor. to Township 1 Ranges 4 and 5 E. South of the Base line
80	00	the limestone cor. to Township 1 North Ranges 4 and 5 E. marked with 6 notches and R 5 on East side 6 notches and R 4 on West side 6 notches and T. 1 on North side

Base line in Range 5. E.

Chains		
		East on S. boundary sec. sec. 31 Va. 11°26' E
20	00	set Sandstone 19×10×6 in 8 in in ground marked 1/16 for 1/16 sec. cor.
31	29	the sandstone cor. on N. boundary sec. 6 T. 1 S. R. 5 E.
40	00	the limestone 1/4 sec. cor. standing as planted
60	00	set Sandstone 18×10×5 in 8 in in ground marked 1/16 for 1/16 sec. cor.
71	33	the limestone cor. to sec. 5 and 6 T. 1 S. R. 5 E
80	00	the limestone cor. to sec. 31 and 32 still standing as planted

Base line in Range 5. E.

Chains		
		East on S. boundary Sec. 32 Va. 11°25' E
20	00	Set limestone 19x10x3 in 8 in in ground marked M6 for M6 Sec. cor.
31	41	the limestone 1/4 Sec. cor. on N. boundary Sec. 5 T. 1 S. R. 5 E.
40	00	~~Set limestone~~ the limestone 1/4 Sec. cor. still standing as planted
60	00	set ~~L~~ limestone 20x10x3 in 8 in in ground marked M6 for M6 Sec. cor.
71	35	the limestone cor. to Sec. 4 and 5 T. 1 S. R. 5. E. 6th P.M.
80	00	the limestone cor. to Sec. 32 and 33 still standing as planted

August 4th 1873

Base line in Range 5. E.

Chains		
		East on S. boundary Sec. 33. Va. 11°27' E
20	00	Set ~~L~~ limestone 17x10x6 in 8 in in ground marked M6 for M6 Sec. cor.
31	26	the 1/4 Sec. cor. (limestone) on the N. line Sec. 4 T. 1 S. R. 5 E.
40	00	the limestone 1/4 Sec. cor. as planted
~~60~~	~~00~~	~~Set~~ limestone 19x10x5 in 8 in in ground marked M6 for M6 Sec. cor.
71	30	the limestone cor. to Sec. 3 and 4 T. 1 S. R. 5. E.
80	00	the limestone cor. to Sec. 33 and 34 standing as planted

Base line in Range 5. E.

East on S. Boundary Sec. 34
Va. 11°34' E

20 00	set limestone 17x9x5 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
31 18	the limestone 1/4 Sec. Cor. on N. bound Sec. 3 T. 1. S. R. 5. E.
40 00	the limestone 1/4 Sec. Cor. as planted
60 00	set limestone 19x10x4 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
71 22	the limestone Cor. to Sec. 2 and 3 T. 1 S. R. 5. E.
80 00	the limestone Cor. to Sec. 34 and 35 still standing as planted.

Base line in Range 5. E.

Chains

East on S. Boundary Sec. 35
Va. 11°35' E

20 00	set limestone 19x10x4 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
30 51	the limestone 1/4 Sec. Cor. on the N. line Sec. 2 T. 1. S. R. 5. E.
40 00	the limestone 1/4 Sec. Cor. as planted
60 00	set limestone 17x9x4 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
69 72	the limestone Cor. to Sec. 1 and 2 T. 1 S. R. 5. E.
80 00	the limestone Cor. to Sec. 35 and 36 marked with 3 notches on W. edge and 1 notch on East edge. still standing as planted

Base line in Range 5. E.

Chains		
		East on S. boundary sec. 36 Va. 11°41' E
20	00	set limestone 19x10x4 in 8 in in ground marked 1/16 for 1/16 sec. cor.
29	34	the limestone 1/4 sec. cor. on N. line of sec. 1 T. 1 S. R. 5 E.
40	00	the limestone 1/4 sec. cor. as planted
60	00	set limestone 17x9x4 in 8 in in ground marked 1/16 for 1/16 sec. cor.
69	20	the limestone cor. to Township 1. S. Ranges 5 and 6. E. no marks on it
80	00	the limestone cor. to Townships 1. N. Ranges 5 and 6. E. marked with 6 notches and R 5 on the West side, 6 notches and R 6 on the East side 6 notches and T 1 on the N. side standing on the East side of drum bearing N. E.

Base line in Range 6. E.

Chains		
		East on S. boundary sec. 31 Va. 11°41' E
20	00	set limestone 19x10x3 in 8 in in ground marked 1/16 for 1/16 sec. cor.
28	70	the 1/4 sec. cor. (limestone) on the N. line sec. 6 T. 1 S. R. 6. E.
40	00	the limestone 1/4 sec. cor. as planted
68	00	set limestone 18x9x4 in 8 in in ground marked 1/16 for 1/16 sec. cor.
68	68	the limestone cor. to sec. 5 and 6 T. 1 S. R. 6. E.
80	00	the limestone cor. to sec. 31 and 32 stile standing as planted.

August 5th 1878

Base line in Range 6. E

Chains	
	East on S. boundary sec. 32 Va. 11°38' E
20 00	set limestone 20x10x3 in 8 in in ground marked 1/16 for 1/16 sec. cor.
27 85	the limestone 1/4 sec. cor. on the N. line sec. 5 T. 1 S. R. 6. E.
40 00	the limestone 1/4 sec. cor. as planted
60 00	set limestone 19x10x4 in 8 in in ground marked 1/16 for 1/16 sec. cor.
67 72	the limestone cor. to sec. 4 and 5 T. 1 S. R. 6. E. as planted
80 00	the limestone cor. to sec. 32 and 33 still standing as planted. No marks on the stone.

Base line in Range 6. E.

Chains	
	East on S. boundary sec. 33 Va. 11°33' E
20 00	set limestone 19x10x5 in 8 in in ground marked 1/16 for 1/16 sec. cor.
27 68	the limestone 1/4 sec. cor. on the N. boundary sec. 4 T. 1 S. R. 6. E.
40 00	the limestone 1/4 sec. cor. as planted
60 00	set limestone 18x9x5 in 8 in in ground marked 1/16 for 1/16 sec. cor.
67 70	the limestone cor. to sec. 3 and 4 T. 1 S. R. 6. E. as planted No marks on stone
80 00	the cor. to sec. 33 and 34 still standing as planted with 3 notches on E and W. edges very indistinct (limestone)

Base line in Range 6. E.

Chains	
	East on S. boundary Sec. 34 Va. 11°29' E
20 00	set limestone 18x9x4 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
27 55	the limestone 1/4 Sec. Cor. on the N. boundary Sec. 3 T. 1 S. R. 6 E. as planted
40 00	the limestone 1/4 Sec. Cor. as planted
60 00	set limestone 19x10x6 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
67 48	the limestone Cor. to Sec. 2 and 3 T. 1 S. R. 6 E. as planted no marks on it
80 00	the limestone Cor. to Sec. 34 and 35 as planted no visible marks on it

Base line in Range 6. E.

Chains	
	East on S. boundary Sec. 35 Va. 11°18' E
20 00	set limestone 17x10x5 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
27 30	the limestone 1/4 Sec. Cor. on the N. boundary Sec. 2 T. 1 S. R. 6 E. no marks
40 00	the limestone 1/4 Sec. Cor. as planted no marks
60 00	set limestone 18x10x4 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
67 28	the limestone Cor. to Sec. 1 and 2 T. 1 S. R. 6 E. as planted no visible marks
80 00	the limestone Cor. to Sec. 35 and 36 as planted no visible marks to be seen

Base line in Range 6. E.

East on S. boundary Sec. 36
Va. 10°. 39' E

2000 Set limestone 19×10×4 in 8 in in ground
marked 1/16 for 1/16 sec. cor.

2671 the limestone 1/4 sec. cor. on N. boundary
sec. 1 T. 1 S. R. 6 E. as planted no marks

4000 the limestone 1/4 sec. cor. as planted
no visible marks

6000 Set limestone 18×9×6 in 8 in in ground
marked 1/16 for 1/16 sec. cor.

6673 the limestone (large) cor. to Townships
1 S. Ranges 6 and 7. E. thus are no
visible marks on the stone standing

8000 the limestone cor. to Townships 1
N. Ranges 6 and 7. E. marked with
6 notches and R 6. on W. side 6 notches
and R 7 on East side and 6 notches
and T 1 on North side. still
standing as planted

August 6th 1873

List of Names

A list of the names of the individuals
employed to assist in running
measuring and marking the lines
and corners described in the fore-
going field notes of the Retracing of the
Base Line in Ranges 4. 5 & 6. East of
~~N. M. R. 4 E.~~ 6th P. M. showing
the respective capacities in
which they acted

W. H. Chain chainman
G. W. Warren chainman
P. P. Ryndus Flagman
O. Kinney moundman

We hereby certify that we assisted W. T. Hull Deputy Surveyor in Retracing the Base Line between the States of Nebraska and Kansas from the West Boundary of the Otoe and Mo Indian Reserve to the corner to Townships No 1. North of the Base Line of Ranges Nos 6 and 7 East of the 6th Principal Miridean and that said ~~Township~~ Base Line has been in all respects to the best of our knowledge and belief well and faithfully retraced and the Monuments planted according to instructions furnished by the Surveyor General and of dimensions character construction and marking and in the manner as spicifically described in the foregoing field notes

Subscribed and from to before me this 18th day of Nov. 1873.

S. P. Beecher
Notary Public

W.H. Chain Chainman
G.W. Warren Chainman
P.P. Rynders Flagman
J. Kennedy Moundman

I. W. T. Hull Deputy Surveyor do solemnly swear that in pursuance of a joint contract wherein C. F. White and W. T. Hull are joint contractors with E. E. Cunningham Surveyor General for the District of Nebraska and Iowa bearing date the 3d day of July 1873 I have well faithfully and truly in my own proper person and in strict conformity with the instructions furnished by the Surveyor General the Surveying Manual and the Laws of the United States Retraced all those parts or portions of the Base line between the States of Nebraska and ~~Iowa~~ Kansas from the West boundary of the Otoe & Mo Indian Reserve to the corner to Township Nos 1 North of the Base line of Ranges 6 and 7 East of the 6th Principal Meridian as are represented in the foregoing field notes as having been retraced

under my direction and I do further solemnly swear that all the corners of said survey have been established and perpetuated in strict accordance with the Special Instructions of the Surveyor General of demensions. character. construction and marking. and in the manner as specifically described in the foregoing field notes and that the foregoing are the true and original field notes of such survey

W. T. Hull
deputy Surveyor

Subscribed to by the said W. T. Hull deputy Surveyor and sworn to before me a Notary Public in and for Lancaster Co. in the state of Nebraska this 18th day of November A.D. 1873

R P Beecher
Notary Public

Surveyor Generals Office
Plattsmouth. Jan 20th 1874

The foregoing field notes of the Retracing and establishment of 1/16 Sec. corners on the Base line between Nebraska & Kansas from the West Bdry of the Otoe & Missouria Indian Reserve to Cor to T. 1 N. Rs. 6 & 7 E, Executed by Wm. T. Hull, deputy Surveyor under joint Contract No. 78. of July 3d 1873 in the month of August 1873 having been critically examined, the necessary corrections and explanations made the said field notes & the surveys they describe are hereby approved.

E. E. Cunningham
Surveyor General

Field Notes
of the
Survey in Retracing & re establishing
the Base line
from the
Range line in Ranges 6 & 7
East of the 6th Principal Meridian
to the
East boundary of the Otoe & Missouria
Indian Reservation

Executed by
William Harrell
Deputy Surveyor under contract
No 98
Dated July 21st 1875

Survey
Commenced August 13th 1875
Completed August 13. 1875

62

A
List of Names
And
Duties of Assistants

Joseph F. Mitchell	Compassman
Henry R. Dunn	Flagman
Emmett C. Maxwell	Chainmen
Walter H. Taylor	
Richard C. Cook	Rodmen
William F. Haining	

Index Diagram

Base Line in Rs. 7 & 8 E of the 6th P.M.

To determine the proper adjustment of my compass for the Retracing & Reestablishing the Base-line

I commence at the cor to Townships No 1 North R's 6 & 7 East of the 6th P.M. and run

East along the South boundary of Sec 31 T 1 N. R. 7 E

Var 10°50' E

40 04 To a point 7 lks South of the 1/4 Sec cor

80 07 To a point 16 lks South of the cor to Secs 31 & 32

To retrace this line or run parallel thereto my compass must be adjusted to a

Var 10°57' E

24) 213 (9
216

Base line in Range 7 East of the 6th P. M. 11

		From the cor to Township No 1 N. R's 2 & 7 East of the 6th P. M.	5
		From	15
		East along the South boundary of Sec 31	8
		Va 10°57' E	4
20	00	Set post 3 x 3 in x 4 ft 1 ft deep	14
		marked 1/16 Raised mound of earth	6
		2 ft high from 4 pits 12 x 24 x 12 in	12
		deep for 1/16 Sec cor	5
40	00	Limestone 1/4 Sec still standing	7
52	60	Drain S	4
60	00	Set post 3 x 3 in x 4 ft 1 ft deep	14
		marked 1/16 Raised mound of earth 2 ft	8
		high from 4 pits 12 x 24 x 12 in deep for	12
		1/16 Sec cor	3
80	00	Limestone cor to Secs 31 & 32 still	
		standing	11
		Land rolling	
		Soil 2" rate	5
			144

21) 144 (7

Base line in Range 7 East of the 6th P M

East along the South boundary of Sec 32

Va 10°48' E

7 00 Drain S. W.

20 00 Set post 3x3in x 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12x24x12in deep for 1/16 Sec cor

40 00 Limestone 1/4 Sec cor standing

60 00 Set post 3x3x4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12x24x12in deep for 1/16 Sec cor

74 00 Wagon Road N. W. & S. E.

80 00 Limestone Cor to Secs 32 & 33 still standing

Land gently rolling

Soil 2nd rate

Base line in Range 7 East of the 6th P M

East along the South boundary of Sec 33

Va 10°35' E

20 00 Set post 3x3in x 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12x24x12in deep for 1/16 Sec cor

23 00 Drain S. W.

40 00 Sandstone 1/4 Sec cor still standing

60 00 Set post 3x3in x 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12x24x12in deep for 1/16 Sec cor

80 00 Limestone cor to Sec 33 & 34 still standing

Land gently rolling

Soil 2nd rate

East along the South boundary of Sec 34

Va 10°30' E

10 60 Enter Bottom N. E. & S W

20 00 Set post 3x3in x 4 ft 1 ft deep

Base line in Range 7 East of the 6th P.M.

		marked 1/16 Raised mound of earth 2 ft high from 4 pits 12×24×12in deep for 1/16 Sec cor
40	00	Sandstone 1/4 Sec cor still standing
60	00	Set post 3×3in × 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12×24×12in for 1/16 Sec cor
80	00	Lime stone cor to Secs 34 & 35 still standing
		Upland gently rolling Soil 2nd rate
		Bottom level Soil 1st rate

East, along the South boundary of Sec 35

Va 10° 30' E

3	00	Spring Branch 5 lks wide course S. E.

Base line in Range 7 E of the 6th P.M.

16	00	Spring Branch 6 lks wide course S.W.
20	00	Set post 3×3in × 4 ft 1 ft deep marked 1/16 Raised mound of Earth 2 ft high from 4 pits 12×24×12in deep for 1/16 Sec cor
40	00	Sandstone 1/4 Sec cor still standing
56	00	Set post 3×3in × 4 ft 1 ft deep marked W.C. 1/16 Raised mound of earth 2 ft high from 4 pits 12×24×12in for witness 1/16 Sec cor 4 lks N. of true point for cor
56	20	Right bank of the Big Blue River Course S.W.
60	00	True point for cor falls in River & cannot be established
61	76	Left Bank of Big Blue River course S.W.
74	00	Creek 60 lks wide course S W
80	00	Limestone cor to Secs 35 & 36 still standing
		Land gently rolling Soil 2nd rate

Base line in Range 7 East of the 6th PM

East along the South boundary of Sec 36

Va 10° 50 E

10 00 Geare Bottom N & S.

20 00 Set post 3 x 3in x 4 ft 1 ft deep marked M Raised mound of earth 2 ft high from 4 pits 12 x 24 x 12in deep for M Sec Cor

40 00 Limestone 1/4 Sec Cor still standing

57 00 Wagon Road N & S.

60 00 Set post 3 x 3in x 4 ft 1 ft deep marked M Raised mound of earth 2 ft high from 4 pits 12 x 24 x 12in deep for M Sec Cor

80 00 Limestone Cor to Township No 1 N. Rs 7 & 8 E. still standing

Uplands gently rolling

Soil 2nd rate

Bottom level

Soil 1st rate

Base line in R. 8. East of the 6th PM

East along the South boundary of Sec 31. T. No 1 N R 8. E

Va 10° 30' E

20 00 Set post 3 x 3in x 4 ft 1 ft deep marked M Raised mound of earth 2 ft high from 4 pits 12 x 24 x 12in deep for M Sec Cor

40 00 Lime-stone 1/4 Sec Cor still standing

60 00 Set post 3 x 3in x 4 ft 1 ft deep marked M Raised mound of earth 2 ft high from 4 pits 12 x 24 x 12in deep for M Sec Cor

65 00 Enter Bottom N.E. & SW

75 00 Creek 35 lks wide Course SW

78 00 Creek 40 lks wide Course N E

80 00 Limestone Cor to Secs 31 & 32 still standing

Lands rolling

Soil 2nd Rate

Bottom lands level &

Soil 1st rate

Base line in R. No 8 East of the 6th P.M.

East along the South boundary of Sec 32

Va 10°22' E

20 00 Set post 3x3in x 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12x24x12in deep for 1/16 Sec cor

40 00 Limestone 1/4 Sec cor still standing

60 00 Set post 3x3in x 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12x24x12in deep for 1/16 Sec cor

80 00 Limestone Cor to Secs 32 + 33 still standing

Land rolling

Soil 2nd rate

Base line in R No 8 East of the 6th PM

East along the South boundary of Sec 33

Va 9°57' E

20 00 Set a Limestone 17x12x4 in for 1/16 Sec cor & Sunk pits 12x24x12in deep

30 00 Creek 30 lks wide course S E

38 00 Same " " " " " N E

40 00 Limestone 1/4 Sec cor still standing

43 00 Same Creek 30 lks wide course S E

46 00 " " " " " " N. E.

51 16 " " " " " " S. E.

60 00 Set post 3x3in x 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12x24x12in for 1/16 Sec cor.

80 00 Not finding cor as described Set post 4x4x4½ ft 1 ft deep Raised mound of earth 2½ ft high from 4 pits 12x24x12in deep for cor to Secs 33 + 34

Land gently rolling Soil 2nd rate

Base line in Range No 8 East of the 6th P.M.

East along the South boundary of Sec 34

Va 10° E

20 00 Set frost 3 x 3 in x 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12 x 24 x 12 in deep for 1/16 Sec cor

40 00 Limestone 1/4 Sec cor still standing.

60 00 Set frost 3 x 3 in x 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12 x 24 x 12 in deep for 1/16 Sec cor

61 82 Intersect East boundary of the Otoe & Missouria Indian Reservation at Limestone Closing cor to fractional Secs 34 T 1 N R 8 East + Sec 3 T 1 S R 8 " E. 6. P.M.

Land rolling

Soil 2nd rate

August 13th 1875

Field Notes of the Base line Rs 7 & 8 E of the 6th P.M.

List of Names

A list of names of the individuals employed to assist in retracing the Base line, Establishing 1/16 section corners, & reestablishing missing corners from the corner to Towns No 1 North Ranges 6 & 7 East of the 6th principal meridian, east to the east boundary of the Otoe & Missouri Indian Reserve 18.18 west of the corner to sections 2 & 3 of Town No 1 South of Range No 8 east. Showing the respective capacities in which they acted

Joseph N Mitchell	Compassman
Monroe R Dunn	Flagman
Emmett C Maxwell	Chainman
Walter W Taylor	Chainman
Richard C Cook	Moundman
William T Haming	Moundman

Field Notes of the Base Line in Rs 7 & 8 E of the 6th P.M.

We hereby certify that we have assisted Wm Maxwell Deputy Surveyor in retracing the Base line, Establishing 1/16 Section corners & reestablishing missing Corners from the Corner to Town No 1 North of Ranges Nos 6 & 7 East of the 6th principal meridian East to the East boundary of the Otoe & Missouri Indian Reserve 18.18 west of the corner to sections 34 & 35 of Town No 1 North of Range No 8 East and that the said work has been in all respect to the best of our knowledge & belief well & faithfully Executed & the boundary monuments planted according to the instructions furnished by the Surveyor General

Joseph S. Mitchell Compassman
Monroe R Dunn Flagman
Emmett C Maxwell Chainman
Walter W Taylor Chainman
Richard C. Cook Mounduan
William Trainin Mounduan

Subscribed & sworn to by the above named persons before me a Notary Public for the County of Gage State of Nebraska this 1st day of September 1875

C R Steddard
Notary Public for Gage County

of Dimensions character, construction & marking, & in the manner as specifically described in the foregoing field notes

Field Notes of the Base Line bet Rs 7 & 8 E of the 6th PM

I Wm Maxwell deputy surveyor do solemnly swear that in pursuance of a contract with John R Clark Surveyor of the public lands of the United States in the states of Nebraska ~~and Kansas~~ bearing date the 21st day of July 1875 and in strict conformity to the laws of the United States and the instructions furnished by the said Surveyor General, I have faithfully retraced the base line, established the section corners, and reestablished missing corners, from the corner to Towns 1 North, Ranges 6 & 7 East of the 6th principal Meridian, East to the East boundary of the Otoe and Missouri Indian Reserve 18.18 chains West of corner to sections 34 and 35 of Town 1 North of Range No 8 East. And that said work has been in all respects to the best of my knowledge & belief well & faithfully executed according to the instructions received from

the surveyor General
Wm Maxwell
Deputy Surveyor
Subscribed to by the said William Maxwell & sworn to before me a Notary Public for the County of Gage State of Nebraska this 1st day of September 1875
C. R. Stoddard
Notary Public
for Gage County

If dimensions, character, construction & marking of the manner as specifically described in the foregoing field notes

Surveyor Generals Office
Plattsmouth Neb Dec. 14th 1875.

The foregoing field notes of the survey of the Retracing and Reestablishing the Base Line from Range Line between Ranges 6 and 7 East, to the East Boundary of the Otoe and Missouri Indian in the States of Nebraska and Kansas, executed by Wm Maxwell, under his contract of the 20th day of July 1875 in the month of Aug. 1875 having been criticaly examined, the necessary corrections and explanations made, the said field notes and the Surveys they describe are hereby approved.

Jno. R. Clark
Surveyor General.

Ex. F. Sch

2 copies | T.B. Jan 10 | " " Jan 14

44

Field Notes
of
The Survey of the Exterior Lines
of
Townships 1 and 2 N. Ranges 4 and 5 East and Township No. 2 N. R. 6 East. of 6th P. M.
within the Otoe & Missouri Indian Reserve
in the
State of Nebraska

Executed by
Wm T. Hull, under jt Contract No. 78. of July 3d 1873
wherein C. F. White & Wm T. Hull are jt contractors

Survey

Commenced July 20th 1873
Completed July 31st 1873

List of Names
a list of the names and duties of assistants

W. H. Chain	Chainman
G. W. Warren	"
P. P. Rynders	Flagman
O. Kinney	Moundman

Plat S.S.

Township-line between Ranges 4 and 5 T. 1. N.

Chains		
		Survey commenced July 20th 1873
		From the cor. to Townships 1 N. Ranges 4 & 5 East ~~[illegible]~~ on the Base line Trun North on range line between Sec. 31 and 36 Va. 11°.21' E
20	00	Set sandstone 18×10×5 in 8 in in ground marked 1/16 for 1/16 sec. cor.
30	55	old Military road between Leavenworth and Fort Kearney bears N.W. and S.E.
36	50	drain bears S.W.
40	00	Set sandstone 17×10×6 in 8 in. in ground marked 1/4 for 1/4 sec. cor.
60	00	Set sandstone 16×12×5 in 8 in in ground marked 1/16 for 1/16 sec. cor.
73	25	drain bears S.W.
80	00	Set sandstone 20×10×3 in 8 in in ground marked with 1 notch on S. edge and 5 notches on N. Edge for cor. to Sec. 25. 30. 31 and 36

Land rolling

Soil 1st rate

Township line between Ranges 4 and 5 T. 1 N.

Chains		
		North between sec. 25 and 30
		Va. 11°21' E
18	00	old trail bears E. and W.
20	00	set sandstone 17x10x4 in 8 in in ground
		marked 1/16 for 1/16 sec. cor.
40	00	set sandstone 18x9x5 in 8 in in ground
		marked 1/4 for 1/4 sec. cor.
60	00	set sandstone 18x9x6 in 8 in in ground
		marked 1/16 for 1/16 sec. cor.
80	00	set sandstone 22x10x3 in 8 in in ground
		marked with 2 notches on S. edge and
		4 notches on N. edge for cor. to sec. 19, 20,
		25 and 30
		Land gently rolling
		Soil 1st rate

Township line between Ranges 4 and 5 T. 1 N.

Chains		
		North between sec. 19 and 24
		Va. 11°21' E
16	75	light drain bears W.
20	00	set sandstone 17x9x4 in 8 in in ground
		marked 1/16 for 1/16 sec. cor.
40	00	set sandstone 18x9x5 in 8 in in ground
		marked 1/4 for 1/4 sec. cor.
59	55	drain bears W.
60	00	set sandstone 18x10x4 in 8 in in ground
		marked 1/16 for 1/16 sec. cor.
65	50	drain bears S.W.
80	00	set sandstone 20x10x5 in 8 in in ground
		marked with 3 notches on the N and
		S. edges for cor. to sec. 13, 18, 24 and 19
		Land rolling
		Soil 1st rate

Township line between Ranges 4 and 5 S. 1. W.

Chains		
		North between Sec. 13 and 18
		Va. 11°. 21' E
6	00	old Road or trail bears E. and W.
20	00	Set Sandstone 18x9x4 in 8 in in ground
		marked 1/16 for 1/16 Sec. cor.
40	00	Set Sandstone 20x9x4 in 8 in in ground
		marked 1/4 for 1/4 Sec. cor.
60	00	Set Sandstone 18x9x6 in 8 in in ground
		marked 1/16 for 1/16 Sec. cor.
67	70	drain bears S. N. E.
80	00	Set Sandstone 20x9x4 in 8 in in ground
		marked with 4 notches on S. Edge and
		2 notches on W. Edge for cor. to Sec. 7
		12. 13 and 18
		Land rolling
		Soil 1st rate

Township line between Ranges 4 & 5 S. 1. W.

Chains		
		North between Sec. 7 and 12
		Va. 11°. 21' E
20	00	Set Sandstone 18x10x4 in 8 in in ground
		marked 1/16 for 1/16 Sec. cor.
40	00	Set Sandstone 17x10x6 in 8 in in ground
		marked 1/4 ~~for~~ 1/4 Sec. cor.
60	00	Set Sandstone 18x9x5 in 8 in in ground
		marked 1/16 for 1/16 Sec. cor.
80	00	Set Sandstone 20x10x3 in 8 in in ground
		marked with 5 notches on S. Edge
		and 1 notch on N. Edge for cor. to Sec.
		1. 6. 7 and 12
		Land rolling
		Soil 1st rate

Township line between Ranges 4 and 5 S. 1. N.

Chains		
		North between sec. 1 and 6 Va. 11°21' E
9	75	Rynders Branch bears N.W. very thick underbrush.
14	13	cross Branch again bears N.E.
16	00	cross Branch bears N.W.
20	00	set sandstone 18×10×6 in 8 in in ground marked 1/16 for 1/16 sec. cor.
		an oak. N 13.30 W. dist 39 lks 12 in dia: a Walnut 16 in. dia bears N. 32.15 E. 53 lks
20	55	cross branch bears N.E. some light Elm. oak and Walnut timber
22	50	Branch again bears N.W.
23	85	Branch again bears N.E.
24	31	a. White oak blazed on N & S. sides wa 3 notches for a line tree is 15 in dia:
30	00	Branch again bears N.W.
33	20	Branch again bears N E. has very thick underbrush and a few small Elm and oak trees
34	45	deep drain bears S. E.
40	00	set sandstone 18×9×4 in 8 in in ground marked 1/4 for 1/4 sec. cor.

Township line between Ranges 4 & 5 S. 1. N.

Chains		
47	30	~~North~~ Branch again bears N.W. heavey underbrush and a few small Elm Oak. Walnut and cottonwood. it is now dry
50	75	Branch again bears N.E.
60	00	set sandstone 18×9×6 in 8 in in ground marked 1/16 for ~~1/16~~ sec. cor.
80	00	set sandstone 24×6×6 in 12 in. in ground marked with 6 notches on the N. E. S. and W. sides for cor. to Townships 1 and 2 Ranges 4 and 5 East of the 6th P. M.

Land Broken
Soil 1st rate

Township line between Townships 1 and 2 Range 4.

Chains	
	From the cor. to Townships 1 and 2 N.R. 4 and 5 E. I run West on a random line between said Townships
	Va. 11.°21' E
	I set temporary 1/16. 1/4. 1/16 and sec. cor. at every 20.00 40.00 60.00 and 80.00 chains and at 3 Miles 26.82 chs. I intersected West boundary of the Ottoe Indian Reserve 170 links North of a sandstone marked C.C. between Sections 4 and 33. T. 1 & 2 N. Range East
	The correction for the true line will be 51 links South per mile and the course will be
	N. 89° 38' East.

Township line between Townships 1 and 2 Range 4 E.

Chains	
	1 from Secs. 4 & 33. T. 1 & 2 N.R. 4 E. From the closing cor. on the West boundary of the Otoe Indian Reserve I run N 89.38 E on a true line between Sec. 4 and 33.
	Va. 11.°21' E
6.82	set sandstone 17x9x5 in 8 in in ground marked 1/16 for 1/16 sec. cor.
19.75	drain with light brush bears N.E.
26.82	set sandstone 20x10x4 in 8 in in ground marked with 3 notches on the E and West edges for cor. to Sec. 3. 4. 33 and 34
	Land rolling
	Soil 1st rate

Township line between Townships 1 and 2 R. 4 E.

Chains		
		~~East~~ between Sec. 3 and 34 ~~Course~~
		N 89.38 E on a true line
		Va. 11.°21' E
	15 25	heavy drain bears N. light underbrush
	20 00	Set Sandstone 18x9x5 in 8 in in ground
		marked 1/16 for 1/16 Sec. Cor.
	24 50	leave bottom bears N.E.
	40 00	Set Sandstone 19x9x5 in 8 in in ground
		marked 1/4 for 1/4 Sec. Cor.
	60 00	Set Sandstone 17x9x4 in 8 in in ground
		marked 1/16 for 1/16 Sec. Cor.
	80.00	Set Sandstone 20x10x3 in 8 in in ground
		marked with 4 notches on N. edge and
		2 notches on E. edge for cor. to Sec. 2
		3. 34 and 35
		Land gently rolling
		Soil 1st rate

Township line between Townships 1 and 2 R. 4 E.

		~~East~~ between Sec. 2 and 35 ~~Course~~
		N 89.38' E on a true line
		Va. 11.21' E
	20 00	Set Sandstone 17x10x6 in 8 in in ground
		marked 1/16 for 1/16 Sec. Cor.
	40 00	Set Sandstone 18x9x4 in 8 in in ground
		marked 1/4 for 1/4 Sec. Cor.
	60 00	Set Sandstone 18x9x4 in 8 in in ground
		marked 1/16 for 1/16 Sec. Cor.
	63 50	Road between Beatrice and Steel
		City Nebraska bears N. E and S. W.
	80 00	Set Sandstone 20x9x4 in 8 in in ground
		marked with 5 notches on N. edge and
		1 notch on East edge for cor. to Sec.
		1. 2. 35 and 36
		Land gently rolling
		Soil 1st rate

Township line between Townships 1 and 2 R. 4 E

Chains	
	~~East~~ between sec. 1 and 36
	~~course line~~ N 89°.38' E on a true line
	Va 11°.21' E
20 00	set sandstone 18×9×4 in 8 in in ground marked 7/16 for 1/16 sec. cor.
40 00	set sandstone 17×10×4 in 8 in in ground marked 1/4 for 1/4 sec. cor.
60 00	set sandstone 17×9×5 in 8 in in ground marked 1/16 for 1/16 sec. cor.
80 00	The cor. to Townships 1 and 2 Ranges 4 and 5 E.

Land rolling
Soil 1st rate
July 21st. 1873

General Description

This Fractional Township contains a large quantity of good Farming land that is well adapted to growing all kinds of grain. the surface is rolling. and there are very few draws or drain but what can be cultivated.
There is very little timber that being nearly all on the East line of section 1. at this time of the year there is no running water.

Fract. Township 2 N. Ranges 4 & 5 E. 6th P.M.

	Chains	
		From the closing cor to Secs. 19 & 24 T. 2 N R.s. 4 & 5 East on N. B'dry of Reserve Drain
		South on true line between Secs. 19 & 24 Va 10° 45' East
8	98	Set Sandstone 20 x 12 x 3. 8 in. in ground mkd with 2 notches on South - 4 notches on N. Edge for cor to Secs. 19. 20. 25 & 30
		Land gently rolling bot'l 1st rate.

Fract. Township 2 N. Rs. 4 & 5 E 6th PM.

chains		
		South on true line between Secs. 25 & 30. Va. 10° 42' East
6	20	Big Indian Cr. (dry) bears S.E. underbrush Elm & oak trees.
9	25	Same Cr. bears S.W. (dry)
16	00	Same " S.E. thick underbrush no timber
20	00	Set sandstone 17 x 9 x 6. 8 in ground mkd 1/16 for 1/16 Sec cor.
30	50	Drain bears N. E.
40	00	Set sandstone 18 x 9 x 6. 8 in in ground 4 mkd 1/4 for 1/4 Sec cor.
60	00	Set sandstone 18 x 10 x 4. 8 in ground. mkd 1/4 for 1/4. Sec. cor.
71	50	Road bet Beatrice & Steel City N. E. & W.
80	00	Set sandstone 20 x 10 x 3. 8 in ground mkd 1 notch on S. 5 notches on N. Edge for cor Secs. 25. 30. 31 & 36.
		Land broken Soil 1st rate,

Fractional Township 2 N. Rs. 4 & 5 E. 6th PM

chs.		
		South on true line between Secs. 31 & 36. Va 10° 42' East
5	75	Ryan's branch now dry N. E. thick underbrush
9	00	Same S. W.
18	50	Same N. E.
20	00	Set sandstone 18 x 9 x 6. 8 in ground mkd 1/16 for 1/16 Sec cor.
25	45	Same Branch bears N.W. thick underbrush a few small Elm, Walnut & Cottonwood trees.
30	00	Enter level of Bed
32	60	Leave Same
34	00	Branch N. W
40	00	Set sandstone 19 x 10 x 3. 8 in ground mkd 1/4 for 1/4 Sec cor.
56	50	Branch N. E. a few small Elm Oak & Cottonwood trees
60	00	Set sandstone 18 x 9 x 4. 8 in ground mkd 1/16 for 1/16 Sec cor.
63	30	Branch N.W. thick underbrush few small Oaks. Elms & Cottonwood
79	67	The cor to Townships 1 & 2 N. Rs. 4 & 5 East. Land broken soil. 1st rate.

Judity 22nd 1873

Range line between Ranges 5 and 6 E. T. 1 N

Chains		
		Survey commenced Sept 23d 1873
		North between Ranges 5 and 6 E. from the limestone cor. on the Base line. between Sec. 31 and 36. Town 1 N.
		Va. 11°41' E
6	00	drain bears S. E.
20	00	Set limestone 17x9x4 in 8 in in ground marked 1/16 for 1/16 Sec. cor.
40	00	Set limestone 18x9x6 in 8 in in ground marked 1/4 for 1/4 Sec. cor.
41	25	drain bears S. E.
60	00	Set limestone 18x10x4 in 8 in in ground marked 1/16 for 1/16 Sec. cor.
80	00	Set limestone 20x10x3 in 8 in in ground marked with 1 notch on S. edge and 5 notches on N. edge for cor. to Sec. 25. 30 31 and 36.
		Land rolling
		Soil 1st Rate

Range line between Ranges 5 and 6 E. T. 1 N.

Chains

North between Sec. 25 and 30
Va. 11° 41' E

15 50 old trail or Road bears N.E. & S.W.
20 00 set ~~Sandstone~~ lime stone 17x10x6 in 8 in in ground
marked 1/16 for 1/16 Sec. Cor.
40 00 set limestone 18x9x4 in 8 in in ground
marked 1/4 for 1/4 Sec. Cor.
60 00 set limestone 18x10x5 in 8 in in ground
marked 1/16 for 1/16 Sec. Cor.
72 50 Branch nowdry bears N.E. very thick
underbrush.
76 25 Branch bears N.W.
80 00 set Sandstone 20x10x4 in 8 in in ground
marked with 2 notches on S. edge and
4 notches on N. Edge for cor. to Sec. 19.
24. 25 and 30

Land rolling
Soil 1st Rate

Range line between Ranges 5 and 6 E. T. 1 N.

Chains

North between Sec. 19 and 24
Va. 11° 41' E

1 10 Branch. bears N.E. thick brush.
20 00 set ~~Sandstone~~ limestone 17x10x4 in 8 in in ground
marked 1/16 for 1/16 Sec. Cor.
40 00 set limestone 18x10x5 in 8 in in ground
marked 1/4 for 1/4 Sec. Cor.
44 50 entire Creek bottom bears E & W.
45 30 old trail or Road bears E & W.
60 00 set limestone 18x9x5 in 8 in in ground
marked 1/16 for 1/16 Sec. Cor.
61 00 deep drain bears E.
75 25 Big Indian Creek nowdry bears
S.E. timber Elm. Oak. Cottonwood
and Walnut. thick underbrush
80 00 set limestone 19x12x5 in 8 in in ground
marked with 3 notches on N. and S.
edges for cor. to Sec. 13. 18. 19 and 24

Land rolling on S. 1/2
mile and level bottom the balance
Soil 1st Rate

Range line between Ranges 5 and 6 E. T. 1. N.

Chains		
		North between Sec. 13 and 18.
		Va. 11°41' E
20 00		Set limestone 18x9x4 in 8 in in ground
		Marked 1/16 for 1/16 Sec. Cor.
22 00		Have crete bottom bears E. & W.
40 00		Set limestone 17x10x4 in 8 in in ground
		Marked 1/4 for 1/4 Sec. Cor.
60 00		Set limestone 18x9x6 in 8 in in ground
		Marked 1/16 for 1/16 Sec. Cor.
66 50		drain bears E.
80 00		Set limestone 20x10x3 in 8 in in ground
		Marked with 4 notches on S. edge and
		2 notches on north edge for cor. to Sec.
		7. 12. 13 and 18
		Land rolling
		Soil 1st Rate

Range line between Ranges 5 and 6 E. T. 1. N.

Chain		
		North between Sec. 7 and 12
		Va. 11°41' E
20 00		Set limestone 17x10x4 in 8 in in ground
		Marked 1/16 for 1/16 Sec. Cor.
30 00		drain bears E.
40 00		Set limestone 18x9x6 in 8 in in ground
		Marked 1/4 for 1/4 Sec. Cor.
52 75		drain bears E.
60 00		Set limestone 18x10x4 in 8 in in ground
		Marked 1/16 for 1/16 Sec. Cor.
73 25		drain bears S.E.
80 00		Set limestone 20x12x3 in 8 in in ground
		Marked with 5 notches on S. edge and
		1 notch on N. edge for cor. to Sec. 1. 6
		7 and 12.
		Land rolling
		Soil 1st Rate

Range line between Ranges 5 and 6. E. L. 1. N.

chains		
		North between Sec. 1 and 6
		Va. 11°41' E
20	00	set limestone 17×10×4 in 8 in in ground
		marked 1/16 for 1/16 sec. cor
33	75	drain bears E
40	00	set limestone 18×9×5 in 8 in in ground
		marked 1/4 for 1/4 sec. cor.
60	00	set limestone 18×10×4 in 8 in in ground
		marked 1/16 for 1/16 sec. cor.
69	35	Branch. now dry bears S. E. thick
		underbrush. a grove of timber S. E. of
		the line about 8 chains distant
80	00	set limestone 24×12×4 in 80 in in
		ground marked with 6 notches
		on the N. E. S. and W. sides
		for cor. to Townships 1 and 2
		Ranges 5 and 6 E. 6th P. M.
		Land rolling
		Soil 1st rate

Between Townships 1 and 2 N. R. 5 E. 6th P. M.

chains		
		From cor to Towns 1 & 2 N. Ro. 5 & 6 E. I run
		West on a random line between
		Townships 1 and 2 setting temporary
		post for 1/16. 1/4. 1/16 and sec. corners
		at every 20.00. 40.00. 60.00 and
		80.00 chains
		Va. 11°41' E
		and at 6 miles 2 chains and 43 lks to a
~~482.43~~		to a point 251 links South of the cor.
		to Townships 1 and 2 N Ranges 4 and 5
		E. from which cor. I run ~~East on~~
		S. 89.42 E on a true line between
		Towns 1 and 2.
		the corrections per mile being 42
		links S. North per mile
		July 23d 1873

Between Townships 1 and 2 N. R. 5 E. 6th P.M.

Chains		
		East between Sec. 6 and 31. course true S. 89. 42 E. on a true line Va. 11°. 41' E
5	35	Rynders Branch now dry bears N. thick underbush a small grove of timber 12 chains S. of line
22	43	Set Sandstone 18x9x4 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
42	43	Set Sandstone 19x10x5 in 8 in in ground marked 1/4 for 1/4 Sec. Cor.
62	43	Set Sandstone 18x10x6 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
82	43	Set Sandstone 20x10x3 in 8 in in ground marked with 1 notch on W. edge and 5 notches on E. edge for Cor. to Sec. 5. 6 31 and 32.

Land rolling
Soil 1st rate

Between Townships 1 and 2 N. R. 5 E. 6th P.M.

Chains		
		East between Sec. 5 and 32 ~~course~~ true S. 89. 42 E on a true line Va. 11°. 41' E
8	00	drain bears N.
20	00	Set Sandstone 18x10x4 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
40	00	Set Sandstone 18x10x6 in 8 in in ground marked 1/4 for 1/4 Sec. Cor.
54	50	drain bears N.
60	00	Set Sandstone 18x9x5 in 8 in in ground marked 1/16 for 1/16 Sec. Cor.
80	00	Set Sandstone 19x12x6 in 8 in in ground marked with 2 notches on W. edge and 4 notches on E. edge for Cor. to Sec. 4 5, 32 and 33.

Land rolling
Soil 1st rate

Between Townships 1 and 2 N. R. 5 E 6th P.M.

Chains		
		East between Sec. 4 and 33 course line S. 89.42 E on a true line Va. 11°41' E
14	00	drain bears N.
20	00	Set sandstone 18x9x4 in 8 in in ground marked 1/16 for 1/16 Sec. cor.
34	25	drain bears N.
40	00	Set sandstone 19x10x6 in 8 in in ground marked 1/4 for 1/4 Sec. cor.
45	00	enter Creek bottom bears N. & S.
50	65	Big Indian Creek now dry bears S. by E. Elm. Oak. Walnut. Collonwood and Hickory timber light underbrush
51	34	Blazed an oak tree 18 in dia: on the E. and W. sides with 3 notches for a line tree
57	50	old timber road bears N. & S.
60	00	Set sandstone 18x9x6 in 8 in in ground marked 1/16 for 1/16 Sec. cor. also leave Creek bottom bears N. & S.
80	00	Set sandstone 20x10x4 in 8 in in ground marked with 3 notches on E. & W. edges for cor. to Sec. 3. 4. 33 and 34

Land rolling soil 1st rate

Between Townships 1 and 2 N. R. 5. E. 6th P.M.

Chains		
		East between Sec. 3 and 34 course line S. 89.42' E on a true line Va. 11°41' E
	75	drain bears S.
20	00	Set sandstone 17x9x6 in 8 in in ground marked 1/16 for 1/16 Sec. cor.
31	60	drain bears S.
40	00	Set sandstone 18x10x4 in 8 in in ground marked 1/4 for 1/4 Sec. cor.
55	00	drain bears S.
60	00	Set sandstone 18x10x6 in 8 in in ground marked 1/16 for 1/16 Sec. cor.
80	00	Set sandstone 19x10x5 in 8 in in ground marked with 4 notches on W. edge and 2 notches on E. edge for cor. to Sec. 2. 3. 34 and 35

Land rolling
Soil 1st rate

Between Townships 1 and 2 N. R. 5 E. 6th P.M.

Chains		
		East between Sec. 2 and 35 course ~~line~~ S. 89.42 E on a true line Va. 11°41' E
20	00	Set sandstone 17x10x4 in 8 in ing ground marked 1/16 for 1/16 Sec. cor.
23	00	drain bears S. E.
29	75	drain bears S.
37	25	drain bears S. W.
40	00	Set sandstone 19x10x6 in 8 in ing ground marked 1/4 for 1/4 Sec. cor.
60	00	Set sandstone 18x9x6 in 8 in ing ground marked 1/16 for 1/16 Sec. cor.
80	00	Set sandstone 21x10x6 in 8 in ing ground marked with 5 notches on N. edge and 1 notch on E. edge for cor. to Sec. 1, 2, 35 and 36

Land rolling
Soil 1st rate

Between Townships 1 and 2 N. R. 5 E. 6th P.M.

Chains		
		East between Sec. 1 and 36 course S. 89.42 E. on a true line Va. 11°41' E
20	00	Set sandstone 17x10x6 in 8 in ing ground marked 1/16 for 1/16 Sec. cor.
40	00	Set sandstone 18x9x4 in 8 in ing ground marked 1/4 for 1/4 Sec. cor.
51	25	drain bears N. E.
60	00	Set sandstone 17x9x6 in 8 in ing ground marked 1/16 for 1/16 Sec. cor.
77	35	Branch now dry bears S. very thick under brush. Some few small Elm and oak trees.
80	00	The cor. to Townships 1 and 2 N. Ranges 5 and 6 E. 6th P.M.

Land rolling
Soil 1st rate

July 24th 1873

General Description

There is some first-class land in this Township. particularly the bottom land along what is called Big Indian Creek. that is adapted to growing all kinds of grain. the uplands are gently rolling prairie very few of the Hollows or drains but what can be cultivated

The timber consist of Elm. Oak Cottonwood. Walnut and Hickory of which there are some good sized groves. along the Creek.

Fractional Township 2. N. bet. Rs. 5 & 6. East 6th P.M.

	Chains		
			From the closing cor to fractl Sections 19 & 24. T. 2 N. Rs. 5 & 6 E. on N Bdry of Reserve Trim
			South on true line between Secs. 19 & 24. Va 11° 57' E
	2	18	Set Limestone 20×12×6. 9 in ground mkd. 4 Notches on N & 2 Notches on South edge for cor to Secs. 19, 24 25 & 30
			Leaved gently rolling 1st rate.

Fractl Township 2 N. bet. Rs. 5 & 6 E. 6th P.M.

chains		
		South on true line between Secs. 25 & 30. Va. 11° 57' East
6	75	Drain S. E.
9	00	Drain S. W
20	00	Set limestone 18 × 19 × 4. 8 in ground mkd 1/16. for 1/16 Sec cor.
40	00	Set Limestone 20 × 10 × 4. 10 in ground mkd 1/4 for 1/4 Sec cor
60	00	Set limestone 19 × 11. 5. 8 in ground mkd 1/16 for 1/16 Sec cor
80	00	Set limestone 22 × 10 × 3. 10 in ground mkd 1 notch on South & 5 on North Edge for cor to Secs. 25. 30. 31 & 36.
		Land rolling soil 1st rate.

Fractl. Township 2 N. bet. Ranges 5 & 6 E of 6th P.M.

chains		
		South on true line between Secs. 31 & 36 Va. 11° 57' E.
20	00	Set Limestone 17. 6. 9. 8 in ground mkd 1/16 for 1/16 Sec. cor.
40	00	Set Limestone 20 × 9 × 5. 10 in ground mkd 1/4 for 1/4 Sec. cor.
60	00	Set Limestone 18 & 10 × 6. 8 in ground mkd 1/16 for 1/16 Sec cor.
79	25	To the established cor to Secs. 1. 6. 31 & 36 Towns. 1 & 2 N. Rs. 5 & 6. E.
		Land level soil 1st rate.
		July 25th 1873

General Description

This fractional Township contains first rate rolling prairie. suitable for agriculture and stock raising.

Between Townships 1 & 2 N. R. 6 & East 6th P M

chains

In order to establish the corner to Towns. 1 & 2 N. Rs. 6 & 7 East. I commence at the cor to Towns 1. N on the Base line. & Ranges 6 & 7 East and run North, on true line between said Towns.

Va. 10° 39' E

48000 Set Quinstone 22 x 14 x 3. mkd 6 notches on N. S. & W. edge for cor to Towns. 1 & 2 N. Rs. 6 & 7 East.

From this cor. I run Weston Random line between Towns 1 & 2 N Range 6 E.

Va 10° 39' East

Setting temporary corners at every 20. 40. 60 & 80 chs and at 6 miles 1.77. chains to a point 3.16 chains North of cor to Tp. 1 & 2. N. Rs. 5 & 6 East The correction will therefore be, 5 2/3 lks South per mile and the course will be

N. 89° 37' East

Between Townships 1 & 2 N. Range 6 East 6th R.M.

chains		
21		N. 89° 37' East on true line bet. Secs. 6 & 31. Va. 15° 39' East
21	77	Set Limestone 18 x 7 x 4. 8 in ground mkd 1/16 for 1/16 Sec. cor.
41	77	Set Limestone 18 x 8 x 3. 8 in ground mkd 1/4 for gr. Sec cor.
61	77	Set Limestone 17 x 6 x 4. 8 in ground mkd 1/16 for 1/16 sec cor
81	77	Set Limestone 20 x 9 x 4. 8 in ground mkd 1 Notch on West & 4 Notches on East edge for cor to Secs. 5. 6. 31 & 32.
		Land gutty rolling soil 1 Grade.

Between Townships 1 & 2 N Range 6 East 6th R.M.

chains		
		N. 89° 37' East on true line between Secs. 5 & 32 Va. 15° 39' East
20	00	Set Limestone 17 x 6 x 3. 8 in deep mkd 1/16 for 1/16 Sec. cor.
40	00	Set Limestone 18 x 7 x 4. 8 in deep mkd 1/4 for gr Sec cor
55	00	Drain S.E.
60	00	Set Limestone 17 x 5 x 3 - 8 in deep mkd 1/16 for 1/16 Sec cor
80	00	Set Limestone 19 x 9 x 4. 8 in ground mkd 2 Notches on West and 4 Notches on E. Edge for Cor to Secs. 4. 5. 32 & 33
		Land gutty rolling soil 1 Grade.

Between Townships 1 & 2 N. Range 6 E 6th P.M.

chains		
		N. 89° 37' E on true line bet Secs. 4 & 33. Va. 10° 39' E.
20	00	Set Limestone 17 x 7 x 3. 8 in deep mkd 1/16 for 1/16 Sec cor.
28	00	Drain South
40	00	Set Limestone 18 x 7 x 3. 8 in ∫ round mkd 1/4 for 1/4 Sec cor
60	00	Set Limestone 16 x 6 x 3. 8 in deep mkd 1/16 for 1/16 Sec cor.
80	00	Set Limestone 19 x 9 x 5. 8 in deep mkd 3 Notches on East & West edges for cor to Secs. 3. 4. 33 & 34. Enter Bottom

Land undulating Soil & Drift

Between Towns. 1 & 2 N. Range 6 E 6th P.M.

chs		
		N. 89° 37' E on true line between Secs. 3 & 34 Va 10° 39' E
20	00	Set Limestone 15 x 7 x 3. 8 in deep Mkd 1/16 for 1/16 Sec cor
40	00	Set Limestone 17 x 7 x 4. 8 in deep mkd 1/4 for 1/4 Sec cor.
41	00	Cross Lake
60	00	Set Limestone 16 x 6 x 3. 8 in deep mkd 1/16 for 1/16 Sec cor.
80	00	Set Limestone 19 x 9 x 4. 8 in deep mkd 4 Notches on W. & 2 Notches on E edge for cor to Secs 2. & 3 & 10 & 35.

Land undulating prairie Soil & Drift.

Between Townships 1 & 2 N. Range 6 E 6th P.M.

chains

N. 89°37' E on true line bet Secs. 2 & 35
Va. 10°39' E.

20 00 Set limestone 16 × 6 × 3-8 in deep mkd 1/16 for
1/16 Sec cor

38 00 Creek N. E.
40 00 Set Limestone 17 × 7 × 4. 8 in deep mkd 1/4 for
1/4 sec cor

48 00 same Creek S. E.
52 00 same N. E.
60 00 Set Limestone 17 × 6 × 4. 8 in deep mkd 1/16 for
1/16 sec cor

80 00 Set Limestone 18 × 8 × 4 × 8 in deep mkd 1 No
on E and 5 on W. Edge for cor to Secs. 1. 2.
35 & 36.

Land undulating prairie Soil 1st rate

Between Townships 1 & 2 N. Range 6 East. 6th P.M.

chains

N. 89°37' East on true line between Secs. 1 & 36
Va. 10°39' E

18 00 Creek S. E.
20 00 Set limestone 16 × 7 × 4. 8 in deep mkd 1/16 for
1/16 Sec. cor.

23 00 Creek N. E.
40 00 Set Limestone 18 × 8 × 4. 8 in deep mkd 1/4 for
1/4 sec cor.

60 00 Set Limestone 17 × 7 × 5. 8 in deep mkd 1/16 for
1/16 sec. cor.

80 00 The established cor to Towns 1 & 2 N. Rs.
6 & 7. East.

Land undulating Soil 1st rate.

July 27th

General Description

This fractional Town 2 N Range 6 E is
1st rate undulating prairie suitable for
agriculture and stock raising.

Fractional Town. 2 N. Between Ranges 6 & 7 E 6th P M

Chains		
		From the closing cor to Secs. ~~19 & 24~~ 25 & 30. T. 2 N Rs 6 & 7 E on N Bdry of Reserve Iron
		South on true line between Secs. ~~19 & 24~~, 25 & 30 Va 11° 23' E
10	37	Set limestone 18×10×5 - 8 in deep mkd 1/16 for 1/16 sec. cor.
14	85	Sisley creek 30 lks wide bears E thick brush timber all cut off.
30	37	Set Limestone 20×10×6. 8 in deep mkd 1/4 for 1/4 sec cor.
50	37	Set Limestone 18×9×5. 8 in deep mkd 1/16 for 1/16 sec cor, also leave creek bottom bears E & W.
70	37	Set Limestone ~~20~~ 20×10×6. 8 in deep mkd 1 on S. notch 5 on North edge for cor to Secs. 25. 30. 31 & 36
		Land undulating prairie Soil 1st rate,

Fractional Township 2 N Bet Ranges. 6 & 7. E 6th P M

Chains		
		South on true line between Secs. 31 & 36. Va. 11° 39' East
20	00	Set Limestone 18×8×6. 8 in deep mkd 1/16 for 1/16 sec cor
40	00	Set Limestone 18×10×5. 8 in deep mkd 1/4 for 1/4 sec cor.
60	00	Set limestone 17×10×4. 8 in deep mkd 1/16 for 1/16 sec. cor
66	50	Drain bears W.
79	95	To the cor to Townships 1 & 2 N. Rs 6 & 7. E
		Land gently rolling soil 1st rate. July 31st 1873

List of names

A list of the names of the individuals employed to assist in running, measuring and marking the lines and corners described in the foregoing field notes of the Exterior lines of Township Nos. N.R. 5 E. 6 W. P.M. showing the respective capacities in which they acted

W. H. Chair chainman
G. F. Warren chainman
P. P. Rynders Flagman
O. Kinney Moundman

Red) Oath of Assistants does not include Exterior of Tp 1 and 2 R4E. within Reserve.

We hereby certify that we assisted W. T. Hull Deputy Surveyor in Surveying the Exterior Lines of the ~~fractional~~ Township No 112 North of the Base Line of Range No 3, East and Town 2 N. Range 6 East of the 6th Principal Meridian and that said Townships have been in all respects to the best of our knowledge and belief well and faithfully surveyed and the Boundary Monuments planted according to the instructions furnished by the Surveyor General and of dimensions character construction and marking and in the manner as specifically described in the ~~following~~ foregoing field notes.

J. H. Chinn Chainman
G. W. Warren Chainman
P. P. Rynders Flagman
J. Kenney Mountaman

Subscribed and Sworn to before me this 18 day of Nov 1873.

R. S. Beecher
Notary Public

I. W. T. Hull Deputy Surveyor
do solemnly swear that in
pursuance of a joint Con
-tract wherein C. P. White and
W. T. Hull are joint Contractors
with E E Cunningham
Surveyor General for the
District of Nebraska and
Iowa bearing date the 3d
day July 1873
I have well faithfully and
Truly in my own proper per
-son and in strict conformity
with the instructions furnish
-ed by the Surveyor General
the Surveying Manual and
the Laws of the United States
Surveyed all those parts or
portions of the Exterior Lines of the ~~fractional~~ Town
-ship No 142 North ~~of the Base~~
Line of Range No 4 and Town 2 N Range 6 East 3 East of the
6th Principal Mirideau as are
represented in the foregoing

field notes as having been Surv-
-ed under my direction. And I
further solemnly swear that
all the corners of said Survey
have been established and
perpetuated in strict acco-
-dance with the Surveying Ma-
-nual printed instructions and
special instructions of the Sur-
-veyor General of dimensions
character, construction and Ma-
-king and in the Manner as Spec-
-fically described in the fore-
-going field notes and that the
foregoing are the true and
original field notes of such Surv

W. T. Hull
Deputy Surveyor

Subscribed to by the said W. T. Hull
Deputy Surveyor and sworn to bef-
-ore me a Notary Public in and
for Lancaster County in the State of
Nebraska this 18th day ~~[illegible]~~ Nov A D 18

R P Beecher
Notary Public

Surveyor Generals Office
Plattsmouth Jan 20th 1874

The foregoing field notes of the survey
of the Exterior Township Lines of Towns
1 & 2 N. Ranges 4 & 5 E. and Town 2 N.
Range 6 E. of the 6th P.M. in the State
of Nebraska Executed by W. T. Hull
deputy Surveyor under joint Contract
No 78. dated July 3rd 1873 wherein
C. T. White and W. T. Hull are joint
Contractors in the month of July 1873
having been critically examined
the necessary correction and ex-
planation made the said field
notes and the surveys they describe
are hereby approved.

E. E. Cunningham
Surveyor General

Exd Sch. 3 copies made + sent 92

Field Notes

of

PLAT S.S.

The retracing and reestablishment

of

The Township line of

fractl. Township 1 South of the Base line

Between Ranges 4+5, 5+6 and 6 and 7 East of 6th P.M.

in the

State of Kansas

Executed

By W. T. Hull under joint contract No 78 bearing date the 3d day of July 1873 wherein C. F. White and W. T. Hull are joint contractors

Survey

Commenced August 7th 1873

Completed August 15th + 25th 1873

List of Names

of persons who assisted in the ~~survey~~ retracing of this Township line showing the respective capacities of each

W. H. Chain chainman

G. W. Warren chainman

P. P. Rynders Flagman

O. Kinney moundman

Field Notes
of
The retracing and reestablishment
of
The Township line of
Townships & South of the Base line
Between Ranges 4 & 5. 5 & 6. 8 & 17 East of the 6th P. M
in the
State of Kansas

Executed
By W. S. Hull under joint contract No. 78 ~~wherein~~
bearing date the 3d day of July wherein C. F.
White and W. S. Hull are joint contractors

Survey
Surveyed Aug. 7. Aug. 15 & Aug 25th
1872

List of names
of persons who assisted in the retracing
of this Township line showing the
respective capacities of each
W. H. Chain Chainman
G. W. Warren Chainman
P. P. Rynders Flagman
O'Kinney Moundman

Township line between Ranges 4 & 5 T. 1 S.

to determine the proper adjustment of my compass for the retracing and restablishment of this Township line I commenced at the cor. to Sec. 13 and 18. T. 1. S. Rs. 4 & 5 E.,
North between Sec. 13 and 18
Va. 12°.12' E

40	13	to a point 22 lks W. of the limestone ¼ sec. cor.
72	07	to a point 43 lks W. of the limestone cor. on the S. boundary of the old Indian Reserve
79	97	to a point 50 lks W. of the limestone cor. to Sec. 7. 12. 13 and 18. to retrace this line or run parallel thereto my compass must be adjusted to a.

Va. 11. 51' E

Fractional Township 1 S. Rst. Rs. 4 & 5 E 6th P.M.

chains		
		From the closing cor to Secs 13 & 18 on S. Bdry of Reserve
		T. 1 S. Ranges 4 & 5 E. Drum
		North between Secs 13 & 18.
		Va 11° 51' E.
8	06	The limestone cor. to Secs. 7. 12. 13 & 18.
		Land rolling 1st rate

Township line between Ranges 4 and 5 T. 1. S.

		North between sec. 7 and 12
		Va. 11° 51' E
20	00	set Sandstone 19×9×6 in 8 in in ground
		marked 1/16 for 1/16 sec. cor. in the S. E. 1/4
		of sec. 12
40	00	the limestone 1/4 sec. cor.
60	00	set Sandstone 19×10×5 in 8 in in ground
		marked 1/16 for 1/16 sec. cor. in the N. E 1/4
		of sec. 12.
80	00	the limestone cor. to sec. 1. 6. 7 and 12
		Land rolling
		Soil 1st rate

Township line between Ranges 4 and 5 T. 1. S.

North between Sec. 1 and 6.
Va. 11°51' E

20 00 Set Sandstone 18x10x9 in 8 in in ground
marked 1/16 for 1/16 Sec. cor. in the S. E. 1/4
of Sec. 1

40 00 the limestone 1/4 Sec. cor. standing

60 00 Set Sandstone 18x10x4 in 8 in in ground
marked 1/16 for 1/16 Sec. cor. in the N. E. 1/4
of Sec. 1

79 97 intersection Base line at limestone cor.
to Sec. 1 and 6.

Lance rolling
Civil 1st class
Aug 25th 1873

Township line between Ranges 5 and 6 S. T. 1. S

Survey commenced Aug 15th 1873
to determine the proper adjustment of
my compass for the retracing and res-
-tablishment of this Township line
I commenced at the cor. to Sec. 13, 18
19 and 24
North between Sec. 13 and 18
Va. 11°51' E

39 98 to a point 51 lks W. of the 1/4 Sec. cor. limestone

61 70 to a point 73 lks W. of the limestone cor. on
the S. boundary of the Otoe Indian Reserve

79 93 to a point 94 lks W. of the limestone cor.
to Sec 7. 12. 13 and 18. to retrace this
line or run parallel thereto my
compass must be adjusted to a.
Va. 11°11' E

Township 1. S. bet Ranges 5 & 6 E of 6th P.M.

	chains		
			From the closing cor. to Secs 13 & 18, T 1 S. Rs 5 & 6 E on South bdry of Reserve Drain
			North on true line between Secs 13 & 18 Va 11° 11' East
	18	36	The Limestone cor. Secs. 7, 12, 13 & 18 Land undulating prairie soil 1st rate.

Township line between Ranges 5 and 6 T. 1. S.

			North between Sec. 7 and 12 Va. 11° 11' E
		2000	set limestone 18x10x6 in 8 in in ground marked 1/16 for 1/16 sec. cor. in the S. E. 1/4 of sec. 12.
		40 00	The 1/4 sec. cor. limestone
		60 00	set limestone 19x10x5 in 8 in in ground marked 1/16 for 1/16 sec. cor. in the N. E. 1/4 of sec. 12
		80 00	The limestone cor. to Sec. 1. 6. 7 and 12 Land rolling Soil 1st rate

Township line between Ranges 5 and 6 T. 1 S.

North between Sec. 1 and 6

Va. 11° 11' E

20 00 Set limestone 20 x 10 x 5 in 8 in in ground
Marked 1/16 for 1/16 Sec. Cor. in the S. E. 1/4
of Sec. 1.

40 00 The limestone 1/4 Sec. Cor.

60 00 Set limestone 18 x 9 x 5 in 8 in in ground
Marked 1/16 for 1/16 Sec. Cor. in the N. E. 1/4
of Sec. 1.

77 38 The limestone Cor. to Sec. 1 and 6 on
the Base line

Lance Rolling
Civil 1st Rate
Aug. 15th 1873

To determine the proper adjustment of
my compass for the retracing and res-
-tablishment of this Township line I
commenced at the cor. to sec. 13 and 24
18 and 19 between Ranges 6 and 7. T. 1 S.
north between sec. 13 and 18

Va. 11° 15' E

39 89 To a point 54 lks West of the 1/4 sec. cor. stone

62 00 to a point 82 lks W. of the stone cor. on the
S. boundary of the Oloe Indian Reserve

79 95 to a point 100 lks W. of the stone cor. to sec.
7. 12. 13 and 18. To retrace this line
or run parallel thereto my compass
must be adjusted to a.

Va. 10° 28' E

Township 1 S. Between Ranges 6 & 7 E 6th PM

	chains	
		From the closing cor to secs. 13 & 18 Town 1 S. Ranges 6 & 7 E. on the S. Bdry of the Reserve. Dram
		North on true line between secs. 13 & 18. Va 10° 28' E
	18 30	To the Limestone cor to secs. 7. 12. 13 & 18. Land level Soil 1st rate

T. line Between Ranges 6 & 7 T. 1. S.

		North between sec. 7 and 12 Va. 10° 28'
	20 00	set Post 2 x 2 x 4 ft. long 12 in in ground raised mound of earth from pits 18 x 18 x 12 in 2 ft high for 1/16 sec. cor. in S.E 1/4 of sec. 12.
	40 00	The 1/4 sec. cor. limestone still standing
	60 00	set Post 2 x 2 x 4 ft long 12 in in ground raised mound of earth from pits 18 x 18 x 12 in 2 ft high for 1/16 sec. cor. in the N.E. 1/4 of sec. 12
	80 00	The limestone cor. to sec. 1. 6. 7 and 12 still standing
		Land rolling Soil 1st rate

T. line between Ranges 6 and 7. T. 1 S. 6th P. M.

North between Sec. 1 and 6
Va. 10°28' E

20 00 Set Post 2×2×4 ft long 12 in in ground raised mound of earth from pits 18×18×12 2 ft high for 1/16 sec. cor. in the S. E. 1/4 of sec. 6

40 00 the 1/4 sec. cor. limestone now standing

60 00 Set Post 2×2×4 ft long 12 in in ground raised mound of earth from pits 18×18×12 in 2 ft high for 1/16 sec. cor. in the N. E. 1/4 of sec. 1.

78 57 intersected Base line at the limestone Cor. to Sec. 1 and 6.

Land rolling
Soil 1st rate
Aug 7th 1873

Sworn and subscribed to forme this 18 day of Nov 1873.
S. P. Beeche
Notary Public &c.

We hereby certify that we assisted Wm. S. Hull deputy Surveyor in re-tracing the Township line between the Fractional Townships Nos. 1 South of the Base line of Ranges Nos. 4 & 5, 5 & 6, and 6 and 7 east of the 6th Principal meridian and that said lines has been in all respects to the best of our knowledge and belief well and faithfully retraced and the Boundary monuments planted according to the intructions furnished by the Surveyor General and of dimensions character construction and marking and in the manner as specifically described in the foregoing field notes.

W. H. Chain chainman
G. W. Warren chainman
P. P. Randers Flagman
A. Kenny moundman

I W. T. Stull deputy Surveyor do solemnly
swear that in pursuance of a joint
contract wherein C. F. White and
W. T. Stull are joint contractors with
E. E. Cunningham Surveyor General
for the district of Nebraska and Iowa
bearing date the 3d day of July 1873
I have well faithfully and truely in
my own proper person and in strict
conformity with the instructions
furnished by the Surveyor General
and the Laws of the United States Re-
traced all those parts or portions of
the Fractional Township line between
Townships No. 1 South of the Base
line between Ranges Nos. 5 & 6 and 6 East
of the 6th Principal Meridian as are
represented in the foregoing field Notes
as having been Retraced under my
direction and I do further solemnly
swear that all the corners of said
Survey have been established and
perpetuated in strict accordance

with the Special instructions of the Surveyor General of demensions, character, ~~and~~ construction and marking and in the manner as specifically described in the foregoing field Notes and that the foregoing are the true and original field Notes of such Survey

W. T. Hull
Deputy Surveyor

subscribed to by the said W. T. Hull deputy Surveyor and sworn to before me a Notary Public in and for Lancaster Co. ~~State~~ in the State of Nebraska this 18th day of November A.D. 1875

R. R. Beecher
Notary Public

Field Notes of the Survey of the Range line between Ranges No 6, 7 & 8 East of the 6th Principal Meridian, in Township No 1 North.

The Range line between Ranges Nos 7 & 8 E of the 6th P.M. from the North boundary of the Otoe & Missouri Indian Reservation to the South boundary of Township in Township No 2 North

The Township line between Townships Nos 1 & 2 North, from the cor to Townships No 1 & 2 North Ranges 6 & 7 East, to the East boundary of the Otoe & Missouri Indian Reservation

By William Maxwell under contract No 98 bearing date the 24th day of July A.D. 1875

Survey commenced August 4th 1875

Survey completed August 16th 1875

A list of names of the individuals employed to assist in the above named survey, showing the respective capacities in which they acted

Joseph T. Mitchell Compassman
Monroe R. Dunn Flagman
Emmett C. Maxwell Chainman
Walter W. Taylor Chainman
Richard C. Cook Moundman
William T. Haining Moundman

...ng 8 E of the 6th P. M. 17

...to Township No 1 North of 9
...ng 8 East of the 6th P. M.
... I run North between
...31 and 36.
... by Burts improved
...ars.
10°20' East.
...3 in x 4½ ft. 1 ft. deep.
... raised mound of earth
...from four pits 12 x 24 x
...for 1/16 Sec. Cor. 70
...ter E and W.
...om E and W.
...nd comes from the North
...
...t the true point for.
...e creek and the nearest.
...t for witness corner
... East. Pat that point
... x 3 in 4 ft 1 ft deep.
...ed. W. C. ¼ raised 72
...d of earth 2 ft high
... four pits 12 x 24 x 12 in 15
183

Surrey co

Obis
als employ
named
respective
they acte

Jos
Jon
Emme
Walter
Richa
William

Exterior lines of T. N. of R.s 7 and 8 E. of the 6th P. M. 17

From the cor. to Township No. 1 North of Ranges Nos. 7 and 8 East of the 6th P. M. 9
On base line I run North between Sec.s 31 and 36.
Variation by Burts improved Solar Compass.
10° 20' East.

20.00 Set post 3 x 3 in x 4½ ft. 1 ft. deep. marked 1/16. raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep. for 1/16 Sec. Cor.

33.00 Enter Timber E and W.

35.00 Enter Bottom E and W.

37.00 Enter Creek at bend comes from the North and runs S. W.

40.00 Finding that the true point for cor. is in the creek and the nearest suitable point for witness corner being 60 lks East. Dat that point Set post. 3 x 3 in 4 ft 1 ft deep. marked W. C. 1/4 raised mound of earth 2 ft high from four pits 12 x 24 x 12 in 72 15 183

24 183/8 192

Exterior lines of T. No. 1 N. of R's 7 and 8 E. of the 6th P.M.

		for Witness 1/4 Sec. Cor. No trees convenient to mark
43	00	Leave Creek Course S. and N. E. Distance through creek obtained by actual measurement.
44	00	Leave Timber N. E. and S. W.
50	00	Enter cultivated field E. and W.
60	00	Set. post. 3 x 3 in x 4 ft. 1 ft deep. Mrk'd 1/16 raised mound of earth 2 ft high from 4 pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
71	50	Leave field E. and W.
80	00	Set. post. 4 x 4 in x 4 1/2 ft. 1 ft deep. raised mound of earth 2 ft high from four pits 12 x 24 12 in for Cor. to Sec's 25. 30. 31 and 36

Upland rolling Soil 2d rate
Bottom level Soil 1st rate.
Timber Oak, Elm. and Cottonwood very scattering.

North between
Sec.s 25 and 30

Exterior lines of T. 1 N. of R's 7 and 8 E. of the 6th P.M.

		Va 10° 20' East.
5	00	Leave bottom E. and W.
20	00	Set. post. 3 x 3 in x 4 1/2 ft. 1 ft. deep marked 1/16 raised mound of Earth 2 ft. high from 4 pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
40	00	Set. post. 3 x 3 in x 4 1/2 ft. 1 ft. deep. Mark'd 1/4 raised mound of earth 2 ft. high from 4 pits 12 x 24 x 12 in deep for 1/4 Sec Cor.
60	00	Set. post. 3 x 3 in x 4 1/2 ft 1 ft deep. marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
71	00	Enter. Cultivated field E. and W.
80	00	Set. post. 4 x 4 x 4 1/2 ft. 1 ft deep. raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for Cor. to Sec's 24. 25 19 and 30

Exterior lines of T1N of R's 7 and 8 E of the 6th P.M.

		Land gently rolling Soil 2d rate.
		North on a true line between Sec's 19 and 24
		Va 10°20' E
5	.00	Enter Bottom. N E and S.W.
20	.00	Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. marked 1/16 raised mound of earth 2 ft high from four pits 12 x 24 x 12 in deep. for 1/16 Sec Cor.
20	.34	Leave cultivated field E and W.
24	.55	Creek 15 lks wide course. W. scattering timber on margin.
30	.25	Same creek Course East.
35	.00	Same creek course West.
40	.00	Set. post. 3 x 3 in x 4 ft. 1 ft. deep marked 1/4 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/4 Sec. Cor.
60	.00	Set. post. 4 x 4 in x 4½ feet. 1 ft.

Exterior lines of T1N of R's 7 and 8 E of the 6th P.M.

		marked 1/16 raised mound of earth from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
73	.32	Enter Field E and W.
80	.00	Set. post. 4 x 4 in. 4½ ft. 1 ft. deep. raised mound of earth 2 ft high from four pits 12 x 24 x 12 in deep. for Cor to Sec's 13, 24 18 and 19.
		Upland Gently rolling Soil 2d rate. Bottom level. Lost rate.
		Timber on Creek Cottonwood Elm and Walnut.
		North on a true line between Sec's 13 and 18
		Va. 10°20' E
12	.00	Leave bottom N.W. and S.E.
16	.00	Leave field E and W.
20	.00	Set. post. 3 x 3 in x 4½ ft. 1 ft deep. marked 1/16 raised mound of earth 2 ft high from four pits 12 x 24 x 12

Exterior lines of T1 N of R's 7 and 8 E of the 6th P.M.

		deep for 1/16 Sec. Cor.
40.	00	Set. post. 3 x 3 x in 4 1/2 ft. 1 ft deep. marked 1/4 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep. for 1/4 Sec. Cor.
60.	00	Set. post. 3 x 3 in x 4 1/2 ft. 1 ft. deep marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep. for 1/16 Sec. Cor.
72.	00	Spring branch 6 lks wide runs S.W.
80.	00	Set. post. 4 x 4 in x 4 1/2 ft. 1 ft deep. raised mound of earth 2 ft high from 4 pits 12 x 24 x 12 in deep for Cor. to Sec's 12, 13, 7. & 18.
		Upland gently rolling Soil 2d rate.
		Bottom level Soil 1st rate.
		North on a true line between Sec's 7 and 12
		Va 10° 20' E
4.	60	Wagon Road N.W. and S.E.
20.	00	Set. post. 3 x 3 in 4 1/2 ft. 1 ft deep mrk 1/16 raised mound of earth 2 ft high

Exterior lines of T1 N of R's 7 and 8 E of the 6th P.M.

		from four pits 12 x 24 x 12 in deep. for 1/16 Sec. Cor.
40.	00	Set. post. 3 x 3 in 4 1/2 ft 1 ft. deep. marked 1/4 raised mound of earth 2 ft. high from four pits 12 x 24 12 in deep for 1/4 Sec Cor.
60.	00	Set. post. 3 x 3 in x 4 1/2 ft. 1 ft. deep. marked 1/16. raised mound of earth 2 ft. high from four pits 12 x 24 x 12 deep for 1/16 Sec. Cor.
63.	00	Wagon Road. N.E. and S.W.
65.	00	Enter Bottom N.E. and S.W.
70.	00	Enter Timber E and W.
80.	00	Set. post. 4 x 4 x 4 1/2 ft. 1 ft deep. raised mound of earth 2 ft high from four pits 12 x 24 x 12 in deep for Cor to Sec's. 1, 12, 6 7. From the Cor. an Elm. 24 in in diam bears N 45° E 1,00 ch. distant.
		An Elm. 24 in diam brs. S. 20° E 71 lks distant. No other trees convenient to mark
		Upland gently rolling Soil 2d Rate

Exterior lines of T. N. of R's 7 and 8 E of the 6th P.M.

Bottom level Soil 1st Rate.
Timber Cottonwood Elm Oak and Walnut.

North on a true line between
Sec's 1 and 6
Va 10°20' E

7.	60	Creek 40 lks wide Course W.
14.	00	Same Creek Course E
19	00	Same Creek Course W.
20	.00	Set. post 3 x 3 in 4½ ft. 1 ft. deep marked 1/16 raised mound of earth. 2 ft high from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor. Elm. 20 in N 5° W. 15 lks
20.	50	Wagon Road N. W. and S. E.
29.	78	Creek 40 lks wide Course E
31.	30	Same Creek Course S. W.
37.	90	Same Creek Course E.
40.	00	Set. post. 3 x 3 in 4½ ft. 1 ft. deep. marked 1/4 raised mound of earth. 2 ft. high from four pits 12 x 24 x 12 in deep for 1/4 Sec. Cor. No trees convenient to

Exterior lines of T. N. of R's 7 and 8 E of the 6th P.M.

		mark in 3 chs.
43.	00	Creek 40 lks wide runs west.
44.	50	Leave Timber E and W.
60.	00	Set. post. 3 x 3 in 4½ ft. 1 ft. deep. marked 1/16 raised mound of earth. 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
80.	00	Set. post. 5 x 5 in x 5 ft. 2 ft. deep. raised mound of earth. 2½ ft. high from four pits 18 x 24 x 12 in deep. for Cor. to T's No 1 and 2 North of R's 7 and 8 East of the 6th P.M.

Land level Soil 1st rate.
Timber Cottonwood and Elm.

Exterior lines of T. N. of R's 7 and 8 E of the 6th P. M.

Exterior lines of T. N. of R's 7 and 8 E of the 6th P. M.

From the cor. to Towns. Nos. 1 and 2 N. Ranges Nos 7 and 8 E of the 6th P. M.

I run West. on a random line between said Townships.

Va 10° 20' East.

At each 20. 40. 60 and 80 chs. P set. temporary 1/16. 1/4 1/16 and mile corners. and at 5 miles 79. chs and 18 lks. I intersect the Range line 2. 16 chains North. of Cor. to Townships Nos 1 and 2 North Ranges 6 and 7 East. of the 6th P. M.

Therefore my correction back will be 36 lks. South per. mile.

Find Limestone cor to Township still standing as planted. from which cor. I run.

N 89. 45' E on a true line between Sec's 3 and 6.

Va. 10° 20' East.

19. 18 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. marked 1/16, raised mound of.

Exterior lines of T1 N of R's 7 and 8 E of the 6th P. M.

		earth. 2 ft. high from four pits 12 24 x 12 in. deep for 1/16 Sec Cor.
39.	18	Set. post. 3 x 3 in x 4 1/2 ft. 1 ft. deep marked 1/16 raised mound of earth 2 ft high from 4 pits 12 x 24 x 12 in for 1/4 Sec. Cor.
59	18	Set. post. 3 x 3 in 4 1/2 ft. 1 ft. deep mrkd 1/16 raised mound of earth. 2 ft. high from 4 pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
74.	18	Drain N. E.
79.	18	Set post. 4 x 4 in x 4 1/2 ft. 1 ft. deep. raised mound of earth 2 1/2 ft. high from four pits 12 x 24 x 12 in deep. for Cor. to Sec's 5. 6. 31. and 32
		Land gently rolling Soil 2d rate
		N 89°45' E on a true line between Sec.s 5 and 32.
		Va 10°20' East.
20.	00	Set post. 3 x 3 in x 4 1/2 ft. 1 ft. deep.

Exterior lines of T1 N of R's 7 and 8 E of the 6th P. M.

		marked 1/16. raised mound of earth. 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
40.	00	Set. post. 3 x 3 x in x 4 1/2 ft. high marked 1/4 raised mound of earth. 2 ft. high from 4 pits 12 x 24 x 12 in deep for 1/4 Sec. Cor.
48.	00	Wagon Road. N. E. and S. W.
60.	00	Set. post. 3 x 3 in x 4 1/2 ft. 1 ft. deep. marked 1/16 raised mound of earth. 2 ft. high from 4 pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
80.	00	Set. post. 4 x 4 in x 4 1/2 feet. 1 ft. deep. raised mound of earth 2 ft. high from 4 pits 12 x 24 x 12 in deep for Cor. to Sec.s 4. 5. 32. and 33
		Land gently rolling Soil 2d rate.
		N 89°45' E on a true line between Sec's 4 and 33
		Va. 10°20' East.

Exterior lines of T1N. of R's 7 and 8 E of the 6th P.M.

20.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. Marked 1/16. raised mound of earth 2 ft. high from 4 pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.

40.00 Set. post. 3 x 3 in 4½ ft. 1 ft deep. marked 1/4. raised mound of earth. 2 ft. high from 4 pits 12 x 24 x 12 in deep for 1/4 Sec Cor.

60.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep. for 1/16 Sec. Cor.

80.00 Set. post. 4 x 4 in x 4½ ft. 1 ft. deep. raised mound of earth 2 ft. high from 4 pits 12 x 24 x 12 in deep for Cor to Sec's 3 4. 33 and 34

Land gently rolling
Soil 2d rate.

N 89°45' E on a true line between Sec's 3 and 34

Exterior lines of T1N. of R's 7 and 8 E of the 6th P.M.

Va 10°20' East.

20.00 Set. post. 3 x 3 in x 4½ ft. 1 ft deep. marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.

32.00 Drain N.E.

40.00 Set post. 3 x 3 in 4½ ft. 1 ft. deep marked 1/4. raised mound of earth 2 ft. high from 4 pits 12 x 24 x 12 in deep for 1/4 Sec. Cor.

60.00 Set post. 3 x 3 in 4½ ft. 1 ft deep marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.

80.00 Set post. 4 x 4 in x 4½ ft. 1 ft. deep raised mound of earth. 2 ft. high from four pits. 12 x 24 x 12 in deep for Cor to Sec's 2 3 34 and 35.

Land gently rolling Soil 2d rate.

Exterior lines of T. 1 N. of R's 7 and 8 E. of the 6th P. M.

N. 89° 45' E. on a true line between
Sec's 2 and 35.
Va 10° 20' E.

18.00 Drain N. E.
20.00 Set post 3 x 3 in x 4½ ft 1 ft deep
marked 1/16 raised mound of
earth 2 ft. high from 4 pits
12 x 24 x 12 in deep for 1/16 Sec Cor
22.50 Enter bottom. N. W. and S. E.
40.00 Set post 3 x 3 in x 4½ ft. 1 ft. deep
marked 1/4 raised mound of
earth 2 ft. high from 4 pits
12 x 24 x 12 in deep for 1/4 Sec. Cor.
62.00 Big Blue River 3.70 chains wide
Course S. 45° E. Distance obtained
by actual measurement.
80.00 Set post 3 x 3 in 4½ ft. 1 ft. deep
marked 1/16 raised mound of
earth 2 ft. high from 4 pits
12 x 24 x 12 in deep for 1/16 Sec. Cor.
75.00 Wagon Road. N. W. and S. E.
80.00 Set post 4 x 4 in x 4 ft. 1 ft deep.
raised mound of earth. 2 ft.

Exterior lines of T. 1 N. of R's 7 and 8 E. of the 6th P. M.

high from four pits 12 x 24 x 12 in
deep for Cor to Sec's 1. 2. 35
and 36
Upland gritty rolling Soil 2nd rate.
Bottom Alluv. Soil 1st rate.

N. 89° 45' E. on a true line between
Sec. 1 and 36
Va 10° 20' E.

20.00 Set post 3 x 3 in x 4½ ft. 1 ft deep
marked 1/16. raised mound of
earth 2 ft. high from four
pits 12 x 24 x 12 in deep for
1/16 Sec. Cor.
26.00 Leave bottom. N. W. and S. E.
40.00 Set post 3 x 3 in x 4½ ft. 1 ft. deep.
marked 1/4. raised mound of
earth from four pits 12 x 24 x 12
in deep for 1/4 Sec. Cor.
60.00 Set post 3 x 3 in 4 ft. 1 ft deep.
marked 1/16 raised mound of

Exterior lines of Tp 1 N of R's 7 and 8 E of the 6th P.M.

earth 2 ft. high from 4 pits 12 & 24 & 18 in deep for the Sec. Cor.

75.00 Enter bottom. N. and S.

80.00 To the Cor. to Townships Nos 1 and 2 North Ranges 7 and 8 East of the 6th Principal Meridian. Upland gently rolling Soil 2nd rate. Bottom level Soil 1st rate.

August 14th 1875.

Exterior lines of Tps 1 & 2 N of R's 7 and 8 E of the 6th P.M.

From the Cor to Townships Nos. 1 & 2 North of Ranges 7 and 8 E Prin. East on a random line between Frac'l Townships 1 and 2 N of R 8 E.

Va 10° 20' E.

At each 20. 40. 60 and 80 chains Pert. temporary 1/16. 1/4. 1/16 and mile posts. and at 3 miles 5.9.10 chs. failed to find closing Cor. as described. I continued my line East to a distance of four miles and intersected 40 lks South of Cor. to Sec's. 2. 3. 34 and 35. my correction west will therefore be 10 lks N. per mile. and my true course.

S 89° 56' W.

S 89° 56' W on a true line between Sec's 3 and 34

Va 10° 20' E

At 20.34 chs. True point for Cor. to frac'l Sec's 3 and 34 on the East boundary of the Utes and Muscouria Indian Reservation

Exterior lines of T. N. of R's 7 Eq 8 E of the 6th P. M.

I set. Landstone 17 x 17 x 12 mrk'd C.C. sunk pits on the North South Eq West. 12 x 24 x 12 in for. Closing Cor.

19.10 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. marked ¼. raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for ¼ Sec. Cor.

39.10 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. marked 1/16 raised mound of earth 2 ft. high from 4 pits 12 x 24 x 12 in deep. for 1/16 Sec. Cor.

59.10 Set. post. 4 x 4 in x 4½ ft. 1 ft. deep. Raised mound of earth. 2 ft. high from four. pits 12 x 24 x 12 in deep. for Cor to Sec's 3. 4 33 Eq 34

Land rolling Soil 2d rate.

Exterior lines of T. N. of R's 7 Eq 8 E of the 6th P. M.

S 89° 56' W. on a true line between Sec's 4 Eq. 33.

Va 10° 20' E

20.00 Set. post. 3 x 3 in x 4½ ft 1 ft deep. marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec Cor. From this Cor. a lone Oak 12 in in diam bears. N 28° W. 190 lks distant.

40.00 Set. post. 3 x 3 in x 4½ ft 1 ft deep marked ¼ raised mound of earth. 2 ft high from four pits 12 x 24 x 12 in deep for ¼ Sec. Cor.

60.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. marked 1/16 raised mound of earth. 2 ft. high from 4 pits 12 x 24 x 12 in deep. for 1/16 Sec. Cor.

62.00 Enter bottom N. E. Eq S. W.

80.00 Set. post. 4 x 4 in x 4½ ft. 1 ft deep. raised mound of earth

Exterior lines of Tx N of R's 7 Aug 8 E of the 6th P.M.

2 ft. high from four pits 12 x 24 x 12 in deep for Cor. to Sec's 4. 5. 32. Aug 33.
Upland rolling Soil 2d rate.
Bottom level Soil 1st rate.

S. 89°56' W. on a true line between Sec.s 5 Aug 32
Va 10°20' E

15.00 Leave bottom N. Aug S.
20.00 Set. post. 3 x 3 in 4½ ft. 1 ft. deep marked 1/16 raised mound of earth 2 ft. deep from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
40.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep marked 1/4 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/4 Sec. Cor.
60.00 Set. post. 3 x 3 in, 4½ ft. 1 ft. deep marked 1/16 raised mound of earth

Exterior lines of Tx N of R's 7 Aug 8 E of the 6th P.M.

2 ft high from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
80.00 Set. post. 4 x 4 in x 4½ ft. 1 ft. deep. raised mound of earth 2 ft. high from 4 pits 12 x 24 x 12 in deep. for Cor to Sec's. 5. 6. 31 Aug 32.
Upland gently rolling Soil 2d rate
Bottom level. Soil 1st rate.

S 89°56' W on a true line between Sec's. 6 Aug 31
Va. 10°20' E

20.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 12 in deep. for 1/16 Sec. Cor.
40.00 Set. post. 3 x 3 in x 4½ ft. 1 ft deep. marked 1/4. raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/4 Sec Cor.
45.00 Enter Timber N. E. Aug S. W.

Exterior lines of T. N. of R's 7 and 8 E of the 6th P. M.

45	60	Enter bottom N. E. and S. W.
47	60	Creek 20 lks wide course. S. W.
56	58	Same Creek Course N. W.
59	10	Finding that 1/16 cor. Sec. cor. will come in creek. at this point. I mark an Elm. 4 in diam for Witness 1/16 Sec. Cor.. from which An Elm. 15 in. in diam. bears. S 46° W 46 lks dist. An Elm. 10 in in diam bears. N 10 E 32 lks dist.
59	34	Creek 1.06 chs wide Course South distance obtained by actual measurement.
60	00	True point for Cor. falls in creek and can not be established.
61	10	Leave Timber N and S.
80	00	To Cor. to Townships Nos. 1 and 2 North of Ranges Nos. 7. 8. East. of the 6th Principal Meridian. Upland gently rolling Soil 2d rate Bottom level Soil 1st rate. Timber Oak Ash and Elm. Undergrowth same and vines.

Exterior lines of T. N. of R's 7 and 8 E of the 6th P. M.

		From the Closing Cor. on the North boundary of the Otoe and Missouria Indian Reservation to Fractional Sec's 25. and 30. T 2 N of Ranges 7 and 8 E. Drun. South on a true line between Sec's 25 and 30 Va. 10° 20' E
14	80	Spring Branch. 6 lks wide Course N. E.
15	10	Set. post. 3 x 3 x in 4½ ft. 1 ft. deep marked 1/16. raised mound of Earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.
35	10	Set. post. 3 x 3 in x 4½ ft. 1 ft. deep marked 1/4 raised mound of earth 2 ft. high from four pits 12 x 24 12 in for. 1/4 Sec. Cor.
55	10	Set. post. 3 x 3 in x 4½ feet. 1 ft deep marked 1/16 raised mound of earth 2½ high from four pits 12 x 24 x 12 in deep for 1/16 sec Cor.
75	10	Set. post. 4 x 4 in x 4½ ft. 1 ft. deep

Exterior lines of Tx N of R's 7 and 8 E of the 6th P.M.

Raised mound of earth 2 ft. high
from 4 pits 12 x 24 x 12 in deep.
for Cor to Sec's 25. 36. 30 & 31
Land gently rolling Soil 2d rate.

South on a true line between
Sec's. 31 and 36.
Va 10° 20' E.

20.00 Set. post. 3 x 3 in. x 4½ ft. 1 ft. deep.
marked. 1/16 raised mound of earth
2 ft. high. from 4 pits 12 x 24 x 12
in deep. for 1/16 Sec. Cor.

40.00 Set. post. 3 x 3 in. x 4½ ft. 1 ft. deep.
marked. 1/4 raised mound of
earth 2 ft high from four.
pits 12 x 24 x 12 in deep for.
1/4 Sec. Cor.

(copy this)

60.00 Set post 3 x 3 in x 4½ ft 1 ft deep
Marked 1/16 Raised mound of earth
2 ft high from 4 pits 12 x 24 x 12 in deep
for 1/16 Sec Cor

72.00 Enter Bottom N E and S.W.

80.55 So Cor to Townships Nos 1 and 2
North Ranges. Nos 7 and 8 E of
the 6th Principal Meridian

Exterior lines of Tx N of R's 7 and 8 E of the 6th P.M.

Upland gently rolling Soil 2d rate.
Bottom level. Soil 1st rate.
August. 16th 1875.

Exterior lines of T. 1 N. of R's 7 and 8 E of the 6th P.M.

Range line between R's 6 and 7 E of the 6th P.M. of T's 1 N.

From the Cor to Townships No 1 N of Ranges 6 and 7 E of the 6th P.M.
On Base line I run.
North on a true line between Sec's 31 and 36
Va 11° 0' East.

20.00 Let. post. 3 x 3 in x 4 1/2 ft. 1 ft. deep marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec Cor.

40.00 Let post. 3 x 3 in x 4 1/2 ft. 1 ft deep marked 1/4 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/4 Sec Cor.

60.00 Let. post. 3 x 3 in x 4 1/2 ft. 1 ft deep. marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.

80.00 Let. post. 4 x 4 in x 4 1/2 ft. 1 ft deep Raised mound of earth 2 ft.

Range line between Ranges. 6 and 7 E of the 6th P. M. of T. 1 N.

high from four pits 12 x 24 x 12 in deep for Cor to Sec's 25. 30. 31 and 36.
Land gently rolling Soil 2d rate.

North on a true line between
Sec's 25 and 30
Va 11°00' East.

20.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep. for 1/16 Sec Cor.

35.00 Drain N. E.

40.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep marked 1/4 raised mound of earth 2 ft high from four pits 12 x 24 x 12 in deep for 1/4 Sec. Cor.

60.00 Set post. 3 x 3 in x 4½ ft. 1 ft. deep marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep. for 1/16 Sec Cor.

Range line between R's 6 and 7 E of the 6th P. M. T. 1 N.

80.00 Set. post. 4 x 4 in x 4½ ft. 1 ft. deep Raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for Cor to Sec's 19 24, 25 and 30
Land gently rolling Soil 2d rate.

North on a true line between
Sec's 19 and 24
Va 11°00' East.

20.00 Set. post. 3 x 3 in x 4½ ft. 1 ft deep marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/4 Sec Cor.

40.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. marked 1/4 Sec. Cor. raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/4 Sec Cor.

60.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. marked 1/16 raised mound of earth 2 ft. high from four.

Range line between R's 6 and 7 E of the 6th P M T 1 N

pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.

80.00 Set. post. 4 x 4 in x 4½ ft 1 ft. deep Raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for Cor to Sec's 13. 18. 19 and 24

Land gently rolling Soil 2d rate

North on a true line between Sec's 13 and 18

Va 11° 00' E

20.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep. marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec Cor.

40.00 Set. post. 3 x 3 in x 4½ ft. 1 ft deep marked 1/4 Raised mound of earth 2 ft. high from four pits pits 12 x 24 x 12 in deep for 1/4 Sec Cor.

Range line between R's 6 and 7 E of the 6th P M of T 1 N.

55.00 Spring Branch 3 lks wide. NW

Scattering timber on margin.

60.00 Set. post. 3 in x 3 in x 4½ ft. 1 ft. deep marked 1/16 raised mound of earth 2 ft. high from four pits 12 in 24 x 12 in deep for 1/16 Sec. Cor.

80.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep Raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for Cor. to Sec's 7. 12. 13 and 18.

Land gently rolling Soil 2d Rate. Timber Cottonwood Ash and Elm.

North on a true line between Sec's 7 and 12.

Va 11° 30' E

20.00 Set. post. 3 x 3 in x 4½ ft. 1 ft deep marked 1/16 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/16 Sec. Cor.

40.00 Set. post. 3 x 3 in x 4½ ft. 1 ft. deep marked 1/4 raised mound of earth

Range line between R's 6 and 7 E of the 6th P.M. T. 1 N.

		2 ft. high from four. pits 12 x 24 x 12 in deep. for 1/4 Sec. Cor.
60.	00	Set. post. 3 x 3 in x 4 1/2 ft. 1 ft. deep marked 1/4 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/4 Sec. Cor.
80.	00	Set. post. 4 x 4 in x 4 1/2 ft. 1 ft. deep Raised mound of earth 2 ft high from four pits. 12 x 24 x 12 in deep for Cor. to Sec's 1. 6 7 and 12
		Land gently rolling Soil 2d rate.
		North on a true line between Sec's 1 and 6 Var 13°00' East.
10.	00	Drain. West
20.	00	Set. post. 3 x 3 in x 4 1/2 ft. 1 ft. deep marked. 1/4 raised mound of earth two ft. high four pits 12 by x 24 x 12 in deep for 1/4 Sec. Cor.

Range line between R's 6 and 7 E of the 6th P.M. T. 1 N.

40.	00	Set. post. 3 x 3 in x 4 1/2 ft. 1 ft. deep marked 1/4 raised mound of earth 2 ft. high from four pits 12 x 24 x 12 in deep for 1/4 Sec. Cor.
60.	00	Set. post. 3 x 3 in x 4 1/2 ft. 1 ft deep. marked 1/4 raised mound of earth. 2 ft. high from four pits 12 x 24 x 12 in deep for 1/4 Sec Cor.
80.	00	To Cor. to Township 1 and 2 North of Ranges 6 and 7 East. of the 6th Principal Meridian
		Land gently rolling Soil 2d rate
		Aug 16. 1877.

Ex Lines Ts No 1 & 2. N. Rs 7 & 8 E of the 6th P.M.

List of Names

A list of the names of the individuals employed to assist in running measuring & marking the lines and corners of the exterior boundaries of Township No 1 North of the Base line of Range 6 & 7 East of the 6th principal meridian. The Township line between Towns Nos 1 & 2 North of the Base line of Range No 8 East. The range line between sections, 31, 36, 25 & 30 Of Towns No 2 North, & between Ranges Nos 7 & 8 East of the 6th principal meridian. Showing the respective capacities in which they acted

Joseph T Mitchell Compassman
Monroe R. Dunn Flagman
Emmett C Maxwell Chainman
Walter W Taylor Chainman
Richard C Cook Roundman
William T Haining Roundman

Ex Lines Ts No 1 & 2 N. Rs 7 & 8 E of the 6th P. M.

We hereby certify that we have assisted Wm Maxwell Deputy Surveyor in running measuring & marking the lines & corners of the Exterior boundaries of Township No 1 North of the Base line of Range Nos 6 & 7 East of the 6th principal meridian

The Township line between Towns Nos 1 & 2 North of the Base line of Range No 8 East the Range line between Sections 31, 36, 25 & 30 of Towns No 2 North & between Ranges Nos 7 & 8 East of the 6th principal meridian And that the said work has been in all respects to the best of our knowledge & belief well & faithfully executed and the boundary monuments planted according to the instructions furnished by the Surveyor General

Joseph T. Mitchell Compassman
Monroe R Dunn Flagman
Emmett C Maxwell Chainman
Walter Wm Taylor Chainman
Richard C. Cook Moundman
William T Haining Moundman

Examining, characterizing, construction & marking & in the manner as specifically described in the foregoing field notes

Ex Lines Ts No 1+2, Rs 7+8 E of the 6th P M

Subscribed & sworn to by the above named persons before me a Notary Public for the County of Gage State of Nebraska this 1st day of September 1875

C R Stoddard
Notary Public
for Gage County

Ex Lines Ts No 1+2, N, Rs 7+8 E. of the 6th P M,

I Wm Maxwell deputy Surveyor do solemnly swear that in persuance of a contract with John R Clark Surveyor of the public lands in the state of Nebraska bearing date the ~~15th day of August~~ 1875 and in strict conformity to the laws of the United States and the instructions furnished by the said Surveyor General. I have faithfully surveyed the exterior boundaries of Town No 1 North of Range Nos 6+7 east of the 6th principal Meridian. The Township line between Towns Nos 1+2 North of the base line of range No 8 East. The Range line between sections 31, 36, 25, + 30, Of Towns No 2 North + between Ranges Nos 7+8 east of the 6th principal meridian, and that the said lines have been to the best of my knowledge + belief well + faithfully surveyed, and the boundary monuments planted according to the instructions furnished by the Surveyor General.

Wm Maxwell
Deputy Surveyor

Subscribed by said William Maxwell Deputy Surveyor and sworn

of dimensions character construction + marking
and in the manner as specifically
described in the foregoing field notes

Ex Lines T's No 1 & 2. N. Rs 7 & 8 E of the 6th P.M.

to before me a Notary Public for the County of Gage State of Nebraska this 1st day of September 1875

C. R. Stoddard
Notary Public
for Gage County

Surveyor Generals Office

Plattsmouth Neb Dec 14th 1875

The foregoing field Notes of the Survey of the Range line between Ranges 6.7. & 7.8 East of the 6th Principal Meridian in Township No 1 North of the Range line bet Ranges 7 and 8 East from the North boundary of the Otoe & Missouri Indian Reservation to the South Boundary of Township in Township No 2 North of the Township line bet Township No 1 and 2 Ranges 6 and 7 East to the East boundary of the Otoe and Missouri Indian Reservation Executed by Wm Maxwell deputy Surveyor under contract No 98 dated July 24 1875 in in the month of August 1875 having been critically examined the necessary corrections and explanations made the said field Notes and the Survey they describe are hereby approved

Jno. R. Clark
Surveyor General

Field Notes
of the
Range line between Ranges Nos 7 & 8
East of the 6th Principal Meridian
in
Township No 1 South of the
Base line
in the
Otoe & Missouria Indian Reservation
in the
State of Kansas

Executed by
William Maxwell
Deputy Surveyor. Under Contract
No 98
Dated July 24th 1875

Survey

Commenced August 16th 1875
Completed August 16th 1875

A
List of Names
AND
Duties of Assistants

Joseph T. Mitchell	Compassman
Monroe R. Dunn	Flagman
Emmett C. Maxwell	Chainmen
Walter W. Taylor	Chainmen
Richard C. Cook	Moundmen
William T. Haining	Moundmen

Index Diagram

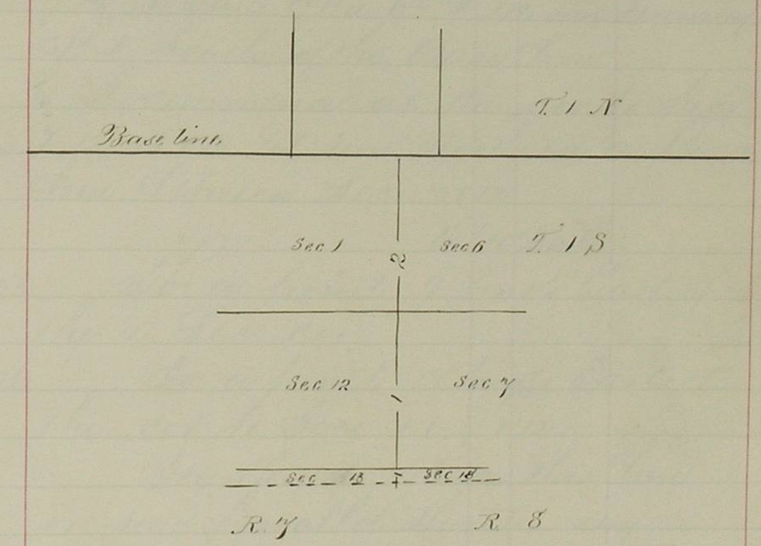

Range Line bet Rs 7 + 8. East of the 6th P.M. T. No 1 S.

To determine the proper adjustment for my compass for the Retracing and reestablishing the Range line between Ranges No 7 and 8 East of the 6th P.M in Township No 1 South of the Base line

I commence at the cor to Secs 7, 12, 13 + 18 and run North on a blank line between Secs 7 + 12

Va 10° 32' E

10 03 To a point 9 links East of the 1/4 Sec cor

80 06 To a point 18 links East of the cor to Secs 1, 6, 7 + 12

Therefore to retrace this line or run parallel thereto, my compass must be adjusted to a

Va 10° 40' E

Range line bet Rs 7 + 8 East of the 6" P.M.S. No 1 S

		From a point 2.37 chs West of a post in mound, marked "1 M." I run North on a true line between fractional Secs 13 & 18
5	58	Find Limestone Sec cor standing
		North on a true line between Secs 7 + 12
		Va 10°40' E
20	00	Set post 3 x 3 in x 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12 x 24 x 12 in deep for 1/16 Sec cor
40	00	Found Limestone 1/4 Sec cor standing
60	00	Set post 3 x 3 in x 4 ft 1 ft deep marked 1/16 Raised mound of earth 2 ft high from 4 pits 12 x 24 x 12 in deep for 1/16 Sec cor
80	00	Found Limestone cor to

Range line bet Rs 7 & 8 East of the 6th P.M. T. No 1 S

Secs 1, 6, 7 & 12 standing
Land rolling
Soil 2nd rate

North on a true line between
Secs 1 & 6
Va 10°40' E
12.00 Enter Bottom E & W.
20.00 Set post 3×3 in × 4 ft 1 ft deep
marked 1/16 Raised mound of
earth 2 ft high from 4 pits 12×24
×12 in deep for 1/16 Sec cor
27.00 Creek 30 lks wide course S.W.
38.70 Leave Bottom E & W
40.00 Limestone 1/4 Sec cor standing
60.00 Set post 3×3 in × 4 ft 1 ft deep
marked 1/16 Raised mound of
earth 2 ft high from 4 pits 12×
24×12 in for 1/16 Sec cor
79.00 Intersect the Base line
2.20 chs West of the 1/16 Sec cor

Range line bet Rs 7 & 8 East of the 6th P.M. T. No 1 S

on South boundary of the S.E. 1/4 of Sec 36
Township No 1 N. R. No 1 East
Not finding cor as described S.
Set post 5×5 in × 5 ft 2 ft deep
Raised mound of earth 2 1/2 ft high
from 3 pits 12×24×12 in deep for closing
cor to Townships No 1 South
Rs 7 & 8 East
Uplands gently rolling
Soil 3rd rate
Bottom Scrub
Soil 1st rate

August 16th 1875

Range line bet Rs 7 & 8 E. T. No 1 S

List of Names

A list of names of the individuals employed to assist in retracing and reestablishing missing corners and establishing 1/16 section corners on Range line between Ranges No 7 & 8 East of Town No 1 South of the Base line, from corner on South boundary of the Otoe and Missouri Indian Reserve to the north boundary of the Township showing the respective capacities in which they acted

Joseph T Mitchell Compassman
Monroe R Dunn Flagman
Emmett C Maxwell Chainman
Walter H Taylor Chainman
Richard C Cook Mounduian
William T Haining Mounduian

Range line bet. Rs 7 & 8 E & No 1 S

We hereby certify that we have assisted Wm Maxwell Deputy Surveyor in retracing & reestablishing missing corners and establishing 1/16 Section corners on Range line between Ranges Nos 7 & 8 East of Town No 1 South of the base line from corner on south boundary of the Otoe & Missouri Indian Reserve, to the north boundary of the Township. And that the said work has been in all respects to the best of our knowledge & belief well & faithfully executed, & the boundary monuments planted according to the instructions furnished by the Surveyor General.

Joseph S. Mitchell Compassman
Moses R Dunn Flagman
Emmett C Maxwell Chainman
Walter Wm Gay Cor Chainman
Richard C. Cook Mounedman
William T Haining Mounedman

Subscribed & sworn to by the above named persons before me a Notary Public for the County of Gage State of Nebraska this 1st day of September 1875

C R Stoddard
Notary Public for Gage Coun

of dimensions character, construction & mastering & established in the manner as specifically described in the foregoing field notes

Range line bet Rs 7 & 8 E. T. No 1 S.

Of dimensions characters, construction & marking and in the manner as specifically described in the foregoing field notes

I William Maxwell Deputy Surveyor do solemnly swear that in pursuance of a contract with John R Clark, Surveyor of the public lands of the United States in the state of Nebraska bearing date the 24th day of July 1875 and in strict conformity to the laws of the United States and the instructions furnished by said Surveyor General, I have faithfully retraced and reestablished missing corners and established 1/16 section corners on Range line between Ranges No 7 & 8 East of Towns No 1 South of Base line, from corner on South boundary of Otoe & Missouri Indian Reserve to the North boundary of the Township and that said line has been in all respects to the best of my knowledge and belief, well and faithfully executed, and the boundary monuments planted according to the instructions furnished by the surveyor General

Wm Maxwell
Deputy Surveyor

Subscribed by said Wm Maxwell
deputy surveyor & sworn to before me
a Notary Public for the County of
Gage State of Nebraska this 1st
day of September 1875

C P Stoddard
Notary Public
for Gage County

Surveyor General's Office
Plattsmouth Neb Dec. 14th 1875

The foregoing field notes of the survey
of the Range line between Ranges 7 and 8,
East. Township 1 South of the Base Line, in
the Otoe and Missouri Indian Reservation
in the State of Kansas, executed by Wm
Maxwell under his Contract of the 24th day
of July 1875, in the month of August 1875
having been critically examined, the necessary
corrections and explanations made, the
said field notes, and the surveys they
describe, are hereby approved.

Jno. F. Clark
Surveyor General.

General Land Office • Original Field Notes

Book Number

131

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.
