General Land Office • Original Field Notes

Book Number

327

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.

35

25-6 Arm

D. Smede

T.25-28
R.6 W.

a

25.

Contract No. 313

Field Notes.
of the
Subdivision lines in Township
25 N. R. 6 W. 6th principal
Meridian Nebraska Territory.
Surveyed by Robert Armstrong,
deputy Surveyor, under joint
contract No 313, dated May
12th 1865, wherein Hackbusch
and Armstrong are joint con-
-tractors,

Survey,
Commenced July 18th 1865,
Completed July 24th 1865,

b

Names and duties of assistants

Merit Howard, Chainman,
Charles Stark, Chainman.
James H Holderby Axeman.
Robert Rabe Flagman,

c

Township 25 S. Range 6 W. 6 P. M.

6	52	5	38	4	28	3	19	2	11	1
51		50		37		27		18		10
7	50	8	37	9	27	10	18	11	9	12
47		48		36		26		17		9
18	47	17	36	16	25	15	17	14	8	13
45		44		35		24		16		7
19	45	20	34	21	23	22	15	23	7	24
42		41		33		22		15		6
30	41	29	31	28	22	27	14	26	5	25
40		39		29		21		13		5
31	39	32	29	33	20	34	12	35	3	36

b

d

I, Merit Howard and Charles Stark do Solemnly Swear (or affirm) that I will faithfully execute the duties of Chain Carrier; that I will level the Chain upon uneven ground, and plumb the tally pins whether by sticking or dropping the same that I will report the true distance to all notable objects, and the true length of all lines that I assist in measuring to the best of my skill and ability

Merit Howard Chainman
Charles Stark Chainman

Subscribed and sworn to by the above named persons, before me a Justice of the

Peace for the County of Cuming
in the Territory of Nebraska
this 15 day of July, 1865
Josiah Mckirahan
Justice of the Peace

I, J. H. Holderby, do Solemnly
Swear (or affirm) that I will
well and truly perform the
duties of Ajrman according
to the instructions given me
and to the best of my Skill
and ability
J H Holderby Ajrman

Subscribed and sworn to by
the above named persons, be-
fore me a Justice of the Peace
for the County of Cuming
in the Territory of Nebraska
this 15th day of July, 1865
Josiah Mckirahan
Justice of the Peace

I, Robert Rabe, do
Solemnly Swear (or affirm)
that I will well and truly
perform the duties of Flag-
man according to instructions
given me, and to the best
of my Skill and ability
Robert Rabe Flagman

Subscribed and sworn to by
the above named persons, be-
fore me a Justice of the Peace
for the County of Cuming
in the Territory of Nebraska
this the 15th day of July, 1865
Josiah Mckirahan
Justice of the Peace

To determine the proper adjustment of my Compass for subdividing this Township I Commence at the corner to Townships 24 and 25 N. R 5 and 6 West, and run North on a blank line along the East Boundary of Section 36.

Va. 13:00' E.

39.97 To a point 12 Lks W. of the ¼ Sec. cor.

79.92 To a point 24 Links W. of the corner to Sections 25 and 36.

To retrace this line or run parallel thereto, my compass must be adjusted to a Variation of 12:50' E.

Subdivision commenced July 18th 1865.

From the corner to Sections 1. 2. 35 and 36. on the South Boundary of the Township. I run North between Sect. 35 and 36.

Va 12:50' E.

11.64 To right bank of Elkhorn River

Townships 25 N. Range 6 W. of 6th P.M.

flows N. 15° E. Soon turns East
water is not too deep to prevent
me from Chaining across.
16.00 Left bank of River Sandy bed and
banks. water 2 feet deep and clear.
average width 160 links. flows
East. ~~after crossing~~ River and enters
Prairie bottom bears S and W.
36.70 A Road bears S.S.E.
40.00 Set a post deposited Charred
Stake raised Mound of earth with pits
as per instructions for 1/4 Sec. Cor.
42.00 Leave bottom and enter upland bears
S. W
80.00 Set a post deposited Charred
Stake raised a Mound of earth
with pits as per instructions for
Cor. to Secs. 25. 26. 35 and 36.
Land bottom Cred Soil 2nd rate
Upland rolling Soil 2nd rate
Timber Cottonwood Oak ash and
Willow Undergrowth Cane and vines

Township 25 N. Range 6 West 6 P.M.

East on a random line between
Secs. 25 and 36.
Va. 12° 50' E.
34.00 A Ravine bears E. E.
40.00 Set post for temporary 1/4 Sec. Cor.
79.80 Intersected East Boundary of
Township 20 Lks N. of Cor to
Secs. 25 and 36, from which
Cor. I run
N. 89° 51' W. on a true line between
Secs. 25 and 36.
Va. 12° 50' E.
39.90 Set a post deposited Charred
Stake and raised a mound
of earth. with pits as per in-
-structions for 1/4 Sec Cor.
79.80 The corner to Secs. 25. 26. 35 and 36,
Land rolling Soil 2nd rate

North between Secs. 25 and 26
Va 12° 50' E.
40.00 Set a post deposited Charred

Township 25 N. Range 6 W. 6th P.M.

Stake raised mound of earth with pits as per instructions for ¼ Sec. Cor.

80.00 Set post deposited Charred Stake raised mound of earth with pits as per instructions for Cor. to Sec. 23. 24. 25 and 26. Land rolling Soil 2nd rate

---

East on a random line between Sec. 24 and 25.
Va 12° 30' E.

26.20 A Ravine bears S.

40.00 Set post for temporary ¼ Sec. Cor.

79.75 Intersected East Boundary of Township 31 Chs N. of Cor. to Secs 24 and 25. from which Cor. I run. N 89° 47' W. on a true line between Secs. 24 and 25.
Va 12° 30' E.

39.87 Set post deposited Charred Stake raised mound of earth with

Township 25 N. Range 6 W. 6th P.M.

pits as per instructions for ¼ Sec. Cor.

79.75 The Cor. to Secs. 23. 24. 25 and 26. Land rolling Soil 2nd rate

---

North between Secs. 23 and 24
Va 12° 30' E.

40.00 Set post deposited Charred Stake raised mound of earth with pits as per instructions for ¼ Sec. Cor.

80.00 Set post deposited Charred Stake raised mound of earth with pits as per instructions Cor. to Secs. 13. 14. 23 and 24. Land rolling Soil 2nd rate

---

East on a random line between Secs. 13 and 24
Va 12° 30' E

40.00 Set post for temporary ¼ Sec. Cor.

79.54 Intersected East Boundary of

Township 25 N. Range 6 W. 6 P.M.

Township 49 Chs N. of the cor. to
Secs 13 and 24. from which
Cor. I run
N. 89° 39' W. on a true line between
Secs 13 and 24.
Va 12° 50' E.

39.77 Set post deposited Charred stake
raised a mound of earth with
pits as per instructions for 1/4
Sec Cor.

79.54 The cor. to Secs. 13. 14. 23 and 24
Land rolling Soil 2nd rate

North between Secs 13 and 14,
Va. 12° 50' E.

40.00 Set post deposited Charred stake
raised mound of earth with pits
as per instructions for 1/4 Sec cor.

80.00 Set post deposited Charred stake
raised mound of earth with pits
as per instructions for cor. to Secs
11. 12. 13 and 14.

Township 25 N. Range 6 W. 6 P.M.

Land rolling Soil 2nd rate

East on a random line between
Secs 12 and 13.
Va 12° 50' E.

40.00 Set post for temporary 1/4 Sec. cor.

79.12 Intersected East Boundary of
Township 60 Chs North of the
Cor. to Secs 12 and 13, from
which cor. I run.
N. 89° 34' W. on a true line between
Secs 12 and 13.
Va 12° 50' E.

39.56 Set post deposited Charred
Stake raised mound of earth
with pits as per instructions
for 1/4 Sec. cor.

79.12 The cor. to Secs 11. 12. 13 and 14
Land rolling Soil 2nd rate

North between Secs 11 and 12
Va 13° 05' E.

Township 25 N. Range 6 W. 6 P.M.

40,00 Set post deposited Charred Stake raised mound of earth with pits as per instructions for 1/4 Sec cor.

80,00 Set post deposited Charred Stake raised mound of earth with pits as per instructions for cor to Sec's. 1. 2. 11 and 12.
Land rolling Soil 2nd rate

East on a random line between Sec's 1 and 12.
Va 12° 30' E.

40,00 Set post for temporary 1/4 Sec cor,

79.34 Intersected East Boundary of Township 44 Lks N. of the Cor. to Sec's 1 and 12 from which cor. I run
N. 89° 41' W. on a true line between Sec's 1 and 12,
Va 12° 50' E.

39.67 Set post deposited Charred Stake raised mound of earth

Township 25 N. Range 6 W. 6 P.M.

with pits as per instructions for 1/4 Sec. cor,

79.34 The cor. to Sec's 1. 2. 11 and 12,
Land rolling Soil 2nd rate

North on a random line between Sec's 1 and 2
Va 13° 05' E.

40,00 Set post for temporary 1/4 Sec cor,

79.47 Intersected North Boundary of Township 50 Lks East of the cor. to Sec's 1 and 2. from which cor. I run,
S 0° 21' E on a true line between Sec's 1 and 2,
Va. 13° 05' E,

39.47 Set post deposited Charred Stake raised mound of earth with pits as per instructions for 1/4 Sec. cor.

79.47 The Cor. to Sec's 1. 2. 11 and 12
Land broken Soil Sandy 3 rate
July 18 to 18, 65

Township 25 N. Range 6 W. 6 P.M.

North between Sec. 34 & 35
Va. 12° 30' E.

6.30 To Elk horn River 250 lks wide by measurment runs East water clear and 2 feet deep. bottom Sandy, Enter Scattering timber on North bank of river bears E & W

39.50 To a Slough 150 lks wide by Meas urement bears S.W. and S.E. Leave Scattering timber on North side of Slough bears S.W. and S.E.

40.00 The point for 1/4 Sec. Cor. in Slough it being impossible to Set permanantly the corner in Slough I therefore at

41.10 Set a post: deposited charred Stake: dig pit north of post for a witness 1/4 Sec. Cor. from which An Ash 11 in. dia. bears S 75 1/2 W. 23 lks dist. No other tree to mark.

77.90 To a Road bears N 60° W. & S 60° E.

80.00 Set post deposited charred Stake

Township 25 N. Range 6 W. 6th P.M.

raised Mound of earth with pits as per instructions for. Cor to Sec. 26. 27. 34 and 35 Land level bottom Soil Mixed Timber. Cottonwood Willow Bur. Oak and Ash.

Cast on a random line between Sec. 26 and 35.
Va. 12° 30' East

2.00 Leave bottom and Enter upland bears N.W and S.E.

36.25 To ravine bears S.

40.00 Set post for temporary 1/4 Sec Cor.

43.00 Ravine bears S.W.

67.00 Ravine bears S.

79.98 Intersected N and S line 43 lks S. of Cor to Sec. 25. 26. 35 and 36 from which corner I run S 89° 42' W on a true line between Sec. 26 and 35.
Va 12° 30' E

Township 26 N. Range 6 W. of 6 P.M.

39.99	Set post deposited chained stake raised mound of earth with pits as per instructions for 1/4 Sec cor.
79.98	The cor. to Sec. 26. 27. 34 and 35 Land broken Soil 2nd rate.

North between Sec. 26 and 27
Va. 13.00 E.

1.00	Lane bottom and enter upland bears N.W and S.E.
40.00	Set post deposited chained stake raised mound of earth with pits as per instructions for 1/4 Sec cor.
42.00	Ravine bears S.E. some timber about 6.00 chains S.E of line
80.00	Set post deposited chained stake raised mound of earth with pits as per instructions for cor to Sec. 22. 23. 26 and 27. Land high rolling prairie Soil 2nd rate

Township 25 N. Range 6 W. 6 P.M.

Cast on a random line between Sec. 23 and 26
Va 13.00 E.

40.00	Set post for temporary 1/4 Sec. cor.
80.12	Intersected N and S line 48 lks S of the cor. to Sec. 23. 24. 25 and 26. from which Cor I ran. S 89° 39' W. on a true line between Sec. 23 and 26

Va 13.00 E.

40.00	Set post deposited chained stake raised mound of earth with pits as per instructions for 1/4 Sec. cor.
80.12	The cor. to Sec. 22. 23. 26 and 27. Land, West 1/2 gently rolling East 1/2 broken Soil 2 rate.

North between Sec. 22 and 23
Va. 13.00 E.

17.00	Ravine bears West.
40.00	Set post deposited chained stake raised mound of earth with pits

Township 25 N. Range 6 W. 6 P.M.

80.00 as per instructions for ¼ Sec. cor.
Set post deposited charred stake
raised mound of earth with pits
as per instructions for cor. to Sec.
14. 15. 22 and 23.
Land rolling prairie Soil 2d rate

Cast on a random line between
Sec. 14 and 23.
Va. 13° 15' E.

11.00 Set post for temporary ¼ Sec. cor.
80.40 Intersected N and S. line 6 lks S.
of the cor. to Sec. 13. 14. 23 and 24
from which cor. I run.
S 89° 57' W on a true line between
Sec. 14 and 23.
Va. 13° 15' E.
40.20 Set post deposited Charred Stake
raised mound of earth with pits
as per instructions for ¼ Sec. Cor.
80.40 The cor. to Sec. 14. 15. 22 and 23.
Land rolling Soil good 2d rate

Township 25 N. Range 6 West of 6th P.M.

North between Sec. 14 and 15—
Va. 13° 00' E.

11.00 Set post deposited charred
Stake raised mound of earth
with pits as per instructions
for ¼ Sec. cor.
80.00 Set post deposited charred stake
raised mound of earth with
pits as per instructions for
Cor. to Sec. 10. 11. 14 and 15—
Land rolling Soil 2d rate

East on a random line between
Sec. 11 and 14.
Va. 13° 10' E.

40.00 Set post for temporary ¼ Sec cor.
79.66 Intersected N and S. line at cor.
to Sec. 11. 12. 13 and 14
from which Cor. I run
West on a true line between Secs
11 and 14.
Va. 13° 10' E.
39.83 Set post deposited Charred Stake

Township 25 N. Range 6 W. of 6 P.M.

raised mound of earth with pits
as per instruction for 1/4 Sec cor.
79.66 The cor. to Secs. 10. 11. 14 and 15
Land rolling Soil 2nd rate

North between Secs. 10 and 11
Va. 13°00' E.
40.00 Set post deposited Charred Stake
raised mound of earth with pits
as per instructions for 1/4 Sec cor.
80.00 Set post deposited Charred Stake
raised mound of earth with pits
as per instructions for cor. to Secs.
2. 3. 10 and 11.
Land rolling Soil 2nd rate

East on a random line between
Secs. 2 and 11
Va. 13°10' East
40.00 Set post for temporary 1/4 Sec. cor.
79.76 Intersected N and S line 13 lks S.
of the cor. to Secs. 1. 2. 11 and 12

Township 25 N. Range 6 W. of 6 P.M.

from which cor. I run
S 89°54' W. on a true line between
Secs. 2 and 11.
Va. 13°10' E.
39.88 Set post deposited Charred Stake
raised mound of earth with pits
as per. instructions for 1/4 Sec. cor.
79.76 The cor. to Secs. 2. 3. 10 and 11.
Land gently rolling surface
broken Soil Sandy poor 2nd rate

North on a random line between
Secs. 2 and 3.
Va. 13°00' E.
40.00 Set post for temporary 1/4 Sec cor
79.74 Intersected N. B. 35 links E.
of the cor. to Secs. 2 and 3.
from which cor. I run
S 0°15' E on a true line between
Secs. 2 and 3.
Va. 13°00' E.
39.74 Set post deposited Charred stake

Township 25 N. Range 6 W. of 6 P.M.

raised a mound of earth with pits as per instructions for ¼ Sec. cor.
79.74 The cor. to Sec's. 2. 3. 10 and 11.
Land rolling Soil Sandy 2nd rate
July 19th 1865

North between Sec's. 33 and 34
Va 12°00' E.

15.00 Leave upland and enter bottom bears N. W and S. E.
26.50 To bend of Elk horn River from N. flows S. E, thence in River - water not too deep to prevent chaining
34.10 Leave River from N. N. E, flows S, enter & cattering timber bears N. N. E. and S. S. W.
40.00 Set post - deposited charred stake 1ft each raised mound, with pits as per instructions for ¼ Sec cor. from with A Cottonwood 36in. dia. bears S 50½ W. 20 lks dist.
42.23 Elk horn River 200 lks wide

Township 25 N. Range 6 W. of 6 P.M.

by measurement runs S. S. E.
46.50 Leave & cattering timber bears E & N. W.
80.00 Set post ~~raised~~ deposited Charred Stake. raised Mound of earth with pits as per instructions for cor to Sec's. 27. 28. 33 and 34
Land. level. South of River Soil Sandy 2nd rate. North side 1st rate Timber. Burr oak & Cottonwood. Under-growth Same plum and grapevines

East on a random line between Sec's 27 and 34
Va 13°00' E.
40.00 Set post for temporary ¼ Sec. cor.
76.40 a Road bears S. E and N. W.
80.00 Intersected N and S line 11 lks E of cor to Sec's 26. 27. 34 & 35 from which cor. I run S 89°.55' W on a true line between Sec's 27 and 34.
Va. 13°.00' E.

Township 25 N. Range 6 W. of 6 Pm.

10.00	Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ Sec cor,
80.00	The cor. to Secs. 27. 28. 33 and 34 Land level Soil 2nd rate

North between Secs. 27 and 28
Va. 13° 00' E.

40.00	Set post deposited Charred Stake raised mound of earth with pits as per instructions for ¼ Sec cor.
72.75	a Road bears S.E. and N.W.
80.00	Set post deposited Charred Stake raised mound of earth with pits as per instructions for. cor. to Secs. 21. 22. 27 and 28. Land level Soil 1st rate.

East on a random line between Secs 22 and 27.
Va 13.00 E.

17.00	Leave bottom and enter upland

Township 25 N. Range 6 West 6 Pm.

	bears E.S.E. and W.N.W.
40.00	Set post for temporary ¼ Sec. cor.
78.10	Ravine bears N.W.
80.20	Intersected N & S line 9 Lks S. of Cor. to Secs. 22, 23. 26 & 27 from which cor. I run, S 89° 36' W. on a true line between Secs 22 and 27.
	Va. 13.00 E.
40.10	Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ Sec cor.
80.20	The cor. to Secs. 21. 22. 27 & 28 Land rolling Soil 2nd rate

North between Secs 21 and 22
Va 12.50 E.

15.00	Leave bottom bears N.W and S.E.
40.00	Set post deposited charred Stake raised mound of earth with pits as per instructions for ¼ Sec. cor.
65.00	Enter timber bears N.E. and S.W.

Township 25 N. Range 6 W. of 6 P.M.

67.00	Spring branch 7 lks wide runs S.W.
68.00	Leave timber bears N.E. and S.W.
78.50	a Drain course W.S.W.
	& Cattering timber on banks
80.10	Set post deposited Chained Stake raised mound of earth with pits for cor to sec as per instructions 15.16.21 & 22 from which An Elm 42 in. dia bears S68½ W. 239 lks dist. An Elm 16 in dia bears S82° E 314 lks Land rolling Soil 2nd rate Timber, Oak and Elm. Undergrowth Same and Vines.

Cast on a sand on line between Sec. 15 and 22

Va. 13°00' E.

1.30	A Drain Course S.W. Scattering Elm trees on banks.
40.00	Set post for temporary ¼ Sec cor.
79.90	Intersected N. and S. line 10 lks

Township 25 N. Range 6 W. of 6 P.M.

South of the cor. to Secs. 14. 15. 22 and 23. from which corner I run,

S 89.56' W. on a true line between Sections 15 and 22.

Va 13:00' E.

39.95	Set post deposited Chained Stake raised Mound of earth with pits as per instructions for ¼ Sec Cor.
79.90	The Cor. to Secs. 15. 16. 21 and 22 Land gently rolling Soil 2nd rate Timber. Principally Elm Undergrowth Same and Vine

North between Secs. 15 and 16.

Va. 13:00' E.

38.50	A Drain Course E. Sam S.
40.00	Set post deposited Chained Stake raised Mound of earth with pits as per instructions for ¼ Sec. Cor.

Township 25 N. Range 6 W. 6 P.M.

80.00 Set post deposited Charred Stake raised Mound of earth with pits as per instructions for Cor. to Sec's. 9. 10. 15 and 16. Land rolling Soil 2d rate

---

Cast on a random line between Sec's. 10 and 15
Va. 13° 00' E.

33.50 a Drain Course S. E Soon S.W.

40.00 Set post for temporary 1/4 sec. cor.

80.80 Intersected N and S line 30 chs S. of the cor. to Sec's. 10. 11. 14 and 15 from which corner I run S 89° 47' W on a true line between Sec's. 10 and 15.
Va. 13° 00' E.

40.40 Set post deposited Charred Stake raised Mound of earth with pits as per instructions for 1/4 Sec cor.

80.80 The Cor. to Sec's. 9. 10. 15 and 16.

Township 25 N. Range 6 W. 6th P.M.

Land rolling Soil 2d rate

North between Sec's. 9 and 10
Va 13.00' E.

40.00 Set post deposited Charred Stake raised Mound of earth with pits as per instructions for 1/4 Sec. cor.

63.00 a Drain Course S. E.

80.00 Set post deposited Charred Stake raised Mound of earth with pits as per instructions for Cor. to Sec's. 3. 4. 9 and 10 Land rolling Soil 2d rate

---

Cast on a random line between Sec's. 3 and 10.
Va 13.00' E.

15.10 a Ravine bears S.W.

40.00 Set post for temporary 1/4 Sec. cor.

80.86 Intersected N and S line at the Corner to Sec's. 2. 3. 10 and 11.

Township 25 N. Range 6 W. of 6th P.M.

From which Corner. I run
West on a true line between
Sec. 3 and 10
Va, 13.00' E

40,43 Set post deposited Charred Stake
raised mound of earth with pits
as per instruction for. 1/4 Sec. Cor,
80,86 The Corner to Sec. 3. 4. 9 and 10.
Land rolling Soil 2nd rate

North on a random line between
Sec. 3 and 4.
Va, 13°00' E.

40,00 Set post for temporary 1/4 Sec. Cor,
79,88 Intersected North Boundary of
Township 18 Rs East of the
Corner. to Sec. 3 and 4
from which Corner. I run
S 0.08' E. on a true line between
Sec. 3 and 4,
Va, 13.00' E.

39,88 Set post deposited Charred

Township 25 N. Range 6 W. of 6th P.M.

Stake raised mound of earth
with pits as per instructions
for 1/4 Sec. Cor,
79,88 The Cor. to Sec. 3. 4. 9 and 10,
Land rolling Soil 2 rate
July 20th 1865

North between Sec. 32 and 33
Va 12.50' East

40,00 Set post deposited Charred Stake
raised mound of earth with
pits as per instructions for
1/4 Sec. Cor,
70,00 Leave upland and enter bottom
bears N.W. and S.E.
80,00 Set post deposited Charred
Stake raised mound of earth
with pits as per instructions
for Cor. to Sec. 28. 29. 32 and 33,
Land rolling Soil 2nd rate

East on a random line between

Town Ship 25 N. Range 6 W. of 6th P.M.

Secs. 28 and 33.

Va 12°50' East

19.00 To Elk horn River 200 lks wide (by measurement) runs S.E., West bank high. East bank low enter timber on East side of River bears N.W. & S.E.

3000 To Elk Horn River 110 lks wide runs North. West bank low, and marshy East bank light cane timber on west side of of River bears North and S.W.

38.00 Leave prairie and enter timber bears N 80° W and S.E.,

40.00 Set temporary 1/4 Sec cor,

41 60 To Elk horn River 110 lks wide runs South banks high and sandy water clear.

5000 Leave timber and enter prairie bears N.W. and S.E.

80.30 Intersected N and S line 11 lks N. of the cor to Secs. 27.28.33 & 34 from which cor. I run,

Town Ship 25 N. Range 6 W. of 6th P.M.

N. 89° 55' W on a true line between Secs. 28 and 33

Va. 12.50' E.

40.15 Set post deposited charred stake for 1/4 Sec cor, from which Burouk 12 in. dia. bears N 70 3/4 W. 117 lks dist.

Burouk 7 in dia bears S 33° 25' E, 91 lks dist.

80.30 The cor to Secs. 28. 29. 32 and 33. Land level bottom Soil 1st rate Timber. Cottonwood. Burouk Ash and Willow. Undergrowth same plum and vine

---

North between Secs. 28 and 29

Va. 12° 30' E.

39.85 As the point for 1/4 Sec. cor. will come on the bank of Elk horn River. where the same can not be permanently established. I therefore at this point 15 lks South of the true point for 1/4

Township 25 N. Range 6 W. of 6th P.M.

Sec. cor. Set post deposited charred stake raised mound of earth with pits as per instructions for Witness Corner.

40,00 The point for 1/4 Sec cor on bank of Elk horn River.

40,20 To waters edge of River runs N.E.

42.35 Across River runs N.E.
Enter timber on North side of Elk-horn, bears N.E. and S.W.

60,00 To bend of Elk horn River Comes from North and runs S 80° W.

64,00 Across bend Comes from N.W. and runs South

74,25 To Elk horn River 115 lks wide runs West water clear bottom Sandy.

80,00 Set post for Cor to Secs. 20.21.28 and 29 from which. A Cottonwood 16 in dia bears S 59 1/4 E. 69 lks dist. An Ash 4 in dia bears S 25° W 47 lks dist. Willow 7 in dia bears

Township 25 N. Range 6 W. of 6th P.M.

N. 81 3/4 W. 81 lks dist. Willow 5 in dia bears N 52° E. 184 lks dist. Land level bottom Soil 1st rate Timber Cottonwood Bur oak Willow and Ash. Undergrowth Same plum and vines

---

East on a random line between Secs. 21 and 28.

Va 12°50' E.

8,00 To Elk-horn River 200 lks wide runs S.W. leave timber on West bank of River bears N.W and S.E.

40,00 Set post for temporary 1/4 Sec. cor.

71.30 Wagon Road bears N.W. and S.E.

80,30 Intersected N and S line 41 lks N. of the Cor. to Secs. 21.22.27 and 28, from which Cor. I run.
N 89° 42' W. on a true line between Secs 21 and 28

Va, 12°50' E.

40.15 Set post deposited charred stake

raised mound of earth with pits
as per instructions for ¼ Sec cor.
80.30 Lk cor. to Secs. 20. 21. 28 and 29.
Land level & Soil 1st rate
Timber cottonwood Ash and Willow
Underbrush Same plum & Vines

North between Secs. 20 and 21
Va. 12.30 E.
33.90 To Elk Horn River 225 lks wide
(by Measurement) runs S.E. water
Clear. bottom Sandy. Bare timber
on South bank of River. bears
N.W and S.E.
10.00 Set post deposited Charred Stake
raised Mound of earth with pits
as per instructions for ¼ Sec cor.
113.10 Road bears E and W.
80.00 Set post deposited Charred Stake
raised Mound of earth with pits
as per instructions for ¼ Sec cor.
to Secs. 16. 17. 20 and 21

Land level bottom Soil 1st rate
Timber Cottonwood Ash and Willow
Underbrush Same and Plum.

East on a random line between
Secs. 16 and 21.
Va. 12.30 E.
4.52 Leave bottom and enter upland
bears N and S.
10.00 Set post for temporary ¼ Sec cor.
80.22 Intersected N and S line 11 lks N.
of the cor. to Secs. 15. 16. 21 and 22.
from which cor. I run
N. 89.54 W. on a true line between
Secs. 16 and 21.
Va. 12.30 E.
10.11 Set post deposited Charred Stake
raised Mound of earth with
pits - as per instructions for ¼ Sec. cor.
81.22 Lk Cor. to Secs. 15. 16. 16. 17. 20 and 21
Land broken Soil 2nd rate

Township 25 N. Range 6 W. of 6th P.M.

North between Secs. 16 and 17
Va. 12° 30' E.

1.00 Lease bottom bears N.W and S.E.
40.00 Set post deposited Charred stake raised Mound of earth with pits. as per instructions for ¼ Sec. cor.
80.00 Set post deposited Charred ~~Stake~~ stake raised Mound of earth with pits as per instructions for Cor to Secs. 8. 9. 16 and 17.
Land rolling Soil good 2nd rate

Cast on a random line between
Secs. 9 and 16
Va 13° 10' E.

40.00 Set post for temporary ¼ Sec cor.
79.96 Intersected N and S line 39 lks W. of the Cor. to Secs. 9. 10. 15 and 16. from which cor. I run
N. 89° 45' W on a true line between
Secs. 9 and 16.
Va 13° 10' E.

Township 25 N. Range 6 W. of 6 P.M.

39.98 Set post deposited Charred stake raised Mound of earth with pits as per instructions for ¼ Sec cor.
79.96 The Cor. to Secs. 8. 9. 16. and 17.
Land rolling Soil good 2nd rate

North between Secs. 8 and 9.
Va. 13° 10' E

40.00 Set post deposited Charred stake raised Mound of earth with pits as per instructions for ¼ Sec cor.
80.00 Set post deposited Charred stake raised Mound of earth with pits as per instructions for Cor. to Secs. 4. 5. 8 and 9.
Land gently rolling Soil good 2 rate

Cast on a random line between
Secs. 4 and 9.
Va 13° 10' E.

40.00 Set post for temporary ¼ Sec cor.
79.62 Intersected N and S line 13 lks W.

Township 25 N. Range 6 W. of 6th P.M.

of the cor. to Secs. 3. 4. 9 and 10.
from which cor. I run.
N. 89° 34' W on a true line between
Secs. 4 and 9.
Va. 13° 10' E.

39.81 Set post - deposited Charred Stake
raised mound of earth with pits
as per instructions for 1/4 Sec cor.
79.62 The Cor. to Secs. 4. 5. 8 and 9.
Land gently rolling Soil good 2nd rate.

North on a random line between
Secs. 4 and 3.
Va. 13° 10' E.

40.00 Set post - for temporary 1/4 Sec cor.
79.20 Intersected N. Boundary of Township
48 Lks East of the Cor. to Secs. 4 & 5
from which Corner. I run,
S. 0° 21' E on a true line between
Secs. 4 and 5.
Va 13° 10' E.

39.20 Set post deposited Charred Stake

Township 25 N. Range 6 W of 6th P.M.

raised mound of earth with pits
as per instructions for 1/4 Sec cor,
79.20 The cor. to Secs. 4. 5. 8 and 9.
Land rolling Soil 2nd rate,
July 21st 1865

North between Secs. 31 and 32
Va. 13° 00' E.

40.00 Set post deposited Charred Stake
raised mound of earth with pits
as per instruction for 1/4 Sec. cor.
80.00 Set post deposited Charred Stake
raised mound of earth with pits
as per instruction for Cor to Secs.
29. 30. 31 and 32.
Land broken and Sandy Soil 3rd rate

East on a random line between
Secs. 29 and 32
Va. 13° 00' E.

40.00 Set post for temporary 1/4 Sec cor.
71.00 Enter bottom N.W. and S.E.,

Township 25 N. Range 6 W. of 6th P. M.

79.72 Intersected N and S line at the cor. to Sec's. 28. 29. 32 and 33.
From which cor. I run
West on a true line between Sec's. 29 and 32.
Va 13° 00' E.

39.86 Set post - deposited Charred Stake raised mound of earth with pits as per instructions for ¼ Sec cor.

79.72 The Cor. to Sec's. 29. 30. 31 and 32.
Land broken and Sand Soil 3rd rate

West on a random line between
Sec's 30 and 31.
Va. 13° 00' E.

40.00 Set post for temporary ¼ Sec cor.

81.60 Intersected West Boundary of the Township 10 lks South of the Cor. to Sec's. 30 and 31. from which Cor. Iron S 89° 30' E on a true line between Sec's. 30 and 31.
Va 13° 00' E.

Township 25 N. Range 6 W of 6th P. M.

41.60 Set post deposited Charred Stake raised Mound of earth with pits as per. instructions for ¼ Sec cor.

81.60 The Corner. to Sec's. 29. 30. 31 and 32.
Land. Surface broken Soil 3rd rate

North between Sec's. 29 and 30
Va 13° 00' E.

40.00 Set post deposited Charred Stake raised mound of earth with pits as per instructions for ¼ Sec cor.

79.25 Leave upland and enter bottom bears N. W and S. E.

80.00 Set post deposited Charred Stake raised Mound of earth with pits as per instructions for cor. to Sec's. 19. 20. 29 and 30.
Land broken and Sandy 3rd rate

East on a random line between
Sec's 20 & 29
Va 13° 00' E.

Township 25 N. Range 6 West 6 P.M.

40.00	Set post for temporary 1/4 Sec cor.
66.50	Enter timber bears N.W and S.E.
79.50	Intersected N and S line 8 lks N. of the cor. to Secs. 20. 21. 28 & 29 from which Cor. I run N. 89° 57' W on a true line between Secs. 20 and 29
	Va. 13° 00' E.
39.75	Set post deposited charred stake raised mound of earth with pits as per instructions for 1/4 Sec cor.
79.50	The cor. to Secs. 19. 20 29 and 30 Land level Soil 1st rate. Timber Cottonwood ash Elm and Willow Undergrowth Same plum and vines
	West on a random line between Secs. 19 and 30
	Va 13° 00' E.
2.00	Leave bottom and enter upland.

Township 25 N. Range 6 W. 6 P.M.

	bears S.E and N.W.
40.00	Set post for temporary 1/4 Sec cor.
81.70	Intersected West Boundary of Township 20 lks South of the cor. to Secs. 19 and 30. from which Cor. I run. S 89° 51' E on a true line between Secs. 19 and 30
	Va 13° 00' E.
41.70	Set post deposited charred stake raised mound of earth with pits as per instructions for 1/4 Sec Cor.
81.70	The cor to Secs. 19. 20. 29 and 30 Land broken and Sundy 3rd rate
	North between Secs. 19 and 20
	Va. 13° 00' E.
18.00	Enter scattering timber bears E & W.
22.75	Elk horn River 140 lks wide runs E.
38.70	Elk horn River. 270 lks wide (by measurement) runs S.S.W.

Township 25 N. Range 6 W. of 6 P.M.

the point for 1/4 Sec cor. being in the River and cannot be established I therefore at a point 168 lks N. of true point. Set post for Witness Corner from which ash 10 in dia bears N 50° W 28 lks dist. an Elm 12 in dia bears N 42° E 42 lks dist

60.75 Elkhorn River 175 lks wide runs N.E. soon turns S.
South side of River leave timber bears N E and S.W.

80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to Secs. 17.18.19 and 20.
Land level Soil 1st rate
Timber. Cottonwood Elm ash and Willow. Undergrowth same plum and grapevines

---

East on a random line between

Township 25 N. Range 6 W. 6th P.M.

Secs. 17 and 20
Va. 13°00' E.

30.15 Road bears W.N.W. and E.S.E.

40.00 Set post for temporary 1/4 Sec cor.

79.60 Intersected N and S line 21 lks N. of the Cor. to Secs. 16.17.20 and 21 from which Cor. I run N 89°51 W on a true line between Secs. 17 and 20
Va. 13°00' E.

39.80 Set post deposited charred stake raised mound of earth with pits as per instructions for 1/4 Sec cor.

79.60 The cor. to Secs. 17.18.19 and 20.
Land level Soil 1st rate

West on a random line between Secs. 18 and 19.
Va. 13°00' E.

5.60 Elkhorn River 150 lks wide runs S. soon W.
Enter timber on West side of River

Township 25 N. Range 6 W. of 6th P.M.

	bears N and S.
24.50	Same River 200 lks wide runs N.
40.00	Set post for temporary 1/4 Sec cor.
42.25	Same River 150 lks wide runs South. West side of river bare timber bears N and S.
70.00	A Slough 325 lks wide bears N & S. West side of Slough enter timber bears N and S.
81.68	Intersected West Boundary of the Township 10 lks S. of the cor to Secs. 18 and 19. from which cor. I run S 89° 56' E. on a true line between Secs 18 and 19. Va 13.00 E.
41.68	Set post for 1/4 Sec cor. from which. a Cottonwood 36 in dia bears S 51° E. 44 lks dist. Cottonwood 24 in dia bears N 32½ W. 154 lks dist.
81.68	The cor. to Secs. 17. 18. 19 and 20. Land level Soil 1st rate

Township 25. Range 6 W. of 6 P.M.

	Timber Cottonwood Elm ash and Willow. Undergrowth Same Plum and Grape vine. July 22nd 1865
	North between Secs 17 and 18. Va. 13.00 E.
34.00	A branch 15 lks wide runs W. Soon South. S cattering timber on banks
40.00	Set post for 1/4 Sec cor. from which Ash 10 in dia bears N 40° W 183 lks dist; Ash 8 in dia bears S 84° E. dist 60 links
41.80	Same branch 15 lks wide runs S.E. Scattering timber on banks after crossing Creek bare bottom bears N.W and S.E.
44.60	Wagon Road bears N.W. and S.E.
56.00	Same branch 10 lks wide runs S W Scattering brush and timber on banks
65.50	Same branch 8 lks wide runs S E Scattering timber and brush on banks
70.80	Same branch 10 lks wide runs S.W.

Township 25 N. Range 6 W. 6th P.M.

80.00	Setting timber and brush on banks Set post deposited Chained stake raised mound of earth with pits as per instructions for Cor to Secs. 7. 8. 17. and 18. Land. South ½ level Soil 1st rate North ½ rolling Soil 2nd rate Timber Cottonwood Elm ash and Willow. Undergrowth Same & vines
	East on a random line between Secs. 8 and 17. Va. 13° 00' E.
1.80	Brook 3 lks wide runs S.
40.00	Set post for temporary ¼ Sec cor.
79.96	Intersected N and S. line 17 lks N. of the Cor to Secs. 8. 9. 16. and 17 from which cor. I run N. 89° 33 W on a true line between Secs. 8 and 17. Va. 13° 00' E.
39.98	Set post deposited chained stake

Township 25 N. Range 6 W. of 6 P.M.

	raised mound of earth with pits as per instructions for ¼ Sec. cor.
79.96	The Cor to Secs. 7. 8. 17. and 18. Land rolling Soil 2nd rate
	West on a random line between Secs. 7 and 18. Va 13° 00' E.
33.00	Leave upland and enter Bottom bears N 60° W and S 60° E.
4.00	Set post for temporary ¼ Sec cor.
66.00	Wagon Road bears N 70° W and S 70° E.
81.94	Intersected W. Boundary of the Township 86 lks North of the Cor to Secs 7 and 18. from which cor. I run N 89° 23' E on a true line between Secs. 7 and 18. Va 13° 00' E.
41.94	Set post deposited chained stake raised mound of earth with pits as per instructions for ¼ Sec cor.

Township 25 N. Range 6 W. of 6 P.M.

81.94 The cor. to Secs. 7.8.17 and 18.
Land. upland rolling Sil 2d rate
bottom land Sil 1st rate

North between Secs. 7 and 8
Va. 13°.10' East

11.50 a Ravine bears E. general course S.E.
40.00 Set post deposited charred stake
raised mound of earth with pits
as per instructions for 1/4 Sec cor.
61.00 a Ravine bears S.E.
80.00 Set post deposited charred stake
raised mound of earth with
pits as per instructions for
Cor. to Secs. 5.6.7 and 8.
Land S. 1/2 broken N. 1/2 rolling
Sil 2d rate

East on a random line between
Secs. 5 and 8
Va 13°.00' E.

23.50 Ravine bears S.E.

Township 25 N. Range 6 West 6 P.M.

40.00 Set post for temporary 1/4 Sec cor.
45.70 Ravine bears S.E.
56.00 a Brook 3 lks wide runs S.
79.94 Intersected N. & S. line 20 lks S. of
the cor. to Secs. 4.5.8 and 9.
from which corner I run
S 89° 57' W on true line between
Secs. 5 and 8.
Va. 13°00' E.
89.97 Set post deposited charred stake
raised mound of earth with pits
as per instructions for 1/4 Sec. cor.
99.94 The Cor. to Secs. 5.6.7 and 8.
Land rolling Sil 2d rate

West on a random line between
Secs. 6 and 7.
Va. 13°00' E.

28.00 a Ravine bears S.E.
40.00 Set post for temporary 1/4 Sec cor.
60.00 Leave upland and enter bottom
bears N.W and S

Township 25 N. Range 6 W. of 6th P.M.

81.18 Intersected W. Boundary of Township 81 lks N. of the Cor. to Secs. 6 & 7 from which Cor. I run N 89° 25' East on a true between Secs. 6 and 7.

Va. 13° 00' E.

41.18 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ Sec cor.

81.18 The Cor. to Secs. 5, 6, 7 and 8.

Land East 68 Chains broken 2 rest balance level Soil 1st rate

North on a random line between Secs. 5 and 6.

Va. 13° 10' E.

40.00 Set post for temporary ¼ Sec. cor.

79.18 Intersected N. Boundary of the Township 10 lks East of the Cor. to Secs. 5 and 6 from which Cor. I run S 0° 04' E. on a true line between Sections 5 and 6.

Township 25 N. Range 6 W 6th P.M.

Va. 13° 10' E.

39.18 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ Sec cor.

79.18 The Cor. to Secs. 5, 6, 7 and 8.

Land rolling Soil good 2d rate

July 24th 1865

General Description

The Land in this Township is of a very good quality and well adapted to cultivation, There is a fair proportion of good bottom land, on both sides of Elkhorn River which runs from West to South East through the Township. The River is about 130 lks wide and has Sandy bed and banks, the water is about 2 feet deep and very clear The uplands are rolling and of good 2d rate quality

Timber, Chiefly Cottonwood, ash, Elm oak and Willow.

No stone in the Township

54

55

List of Names

A list of the names of the individuals employed to assist in running, measuring, or marking the lines and corners described in the foregoing field notes of Township 25 North of the base line of Range No. 6 West of the 6th Principal Meridian, showing the respective capacities in which they acted.

Merit Howard, Chainman.
Charles Stark, Chainman.
James H Holderby, Axeman.
Robert Rabe, Flagman.

Contract No. 313

Field Notes
Of the subdivisional lines of Township No. 26 North. Range No 6, West of the 6th Principal Meridian in the Territory of Nebraska, as surveyed by Robert Armstrong Deputy Surveyor, under contract No 313, bearing date of May 12th 1865, wherein Hackbusch and Armstrong are joint contractors

Survey commenced Sept. 15th 1865
Survey completed Sept. 21st 1865

Names of Assistants

Merit Howard	Chainman
Charles Stark	Chainman
James H. Holderby	Axeman
Robert Rabe	Flagman.

Township 26 Range 6 W 6 P. M.

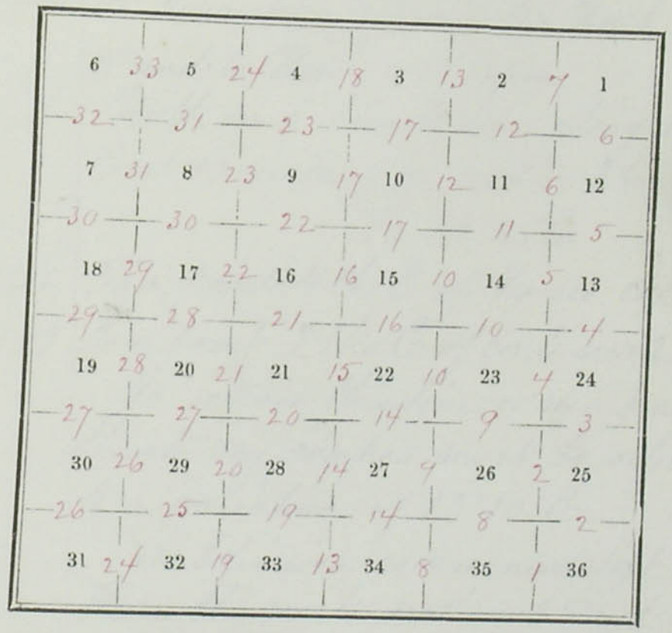

S 58 60

Township 26 N. Range 6 West of 6th Prin. Mer.

To determine the proper adjustment of my compass for subdividing this Township I commence at the corner to Townships 25 and 26 North, Ranges 5 and 6 West, and run
North on a blank line along the East Boundary of section 36
Va 13°05' E

40.06 To a point 4 lks E of 1/4 sec. cor.
80.09 To a point 7 lks E of cor. to secs 25 and 36

To retrace this line, or run parallel thereto my compas must be adjusted to a variation of 13°10' E.

Subdivision commenced Sept. 15th 1865
From the cor. to sections 35 and 36 on the South Boundary of the Township I run
North between secs. 35 and 36
Va. 13°08' E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

Township 26 N. R. 6 W. of 6th Prin. Mer

80.00	Set post deposited charred stake and raised mound of earth, with pits as per instructions for cor to secs 25, 26, 35 and 36 Land rolling, soil 2nd rate.
	East on a random line between secs 25 and 36 Va. 13°08' E.
40.00	Set post for temporary 1/4 sec. cor.
79.86	Intersected East Boundary of Township 14 lks South of cor to secs 25 and 36 from which cor. I run S. 89°54' W. on a true line between secs 25 and 36 Va. 13°08' E.
39.93	Set post deposited charred stake and raised mound of earth, with pits as per instructions for 1/4 sec. cor.
79.86	The cor. to secs. 25, 26, 35 and 36 Land rolling soil 2nd rate
	North between secs 25 and 26 Va. 13°08' E.

Township 26 N. R. 6 W. of 6th Prin Mer.

40.00	Set post deposited charred stake and raised mound of earth, with pits as per instructions for 1/4 sec. cor.
80.00	Set post deposited charred stake and raised mound of earth, with pits as per instructions for cor. to secs. 23, 24, 25 and 26 Land rolling, soil 2nd rate.
	East on a random line between secs. 24 and 25 Va 13°14' E.
40.00	Set post for temporary 1/4 sec. cor.
79.76	Intersected East Boundary of Township 8 lks. North of cor. to secs 24 and 25 from which cor I run N. 89°57' W on a true line between secs 24 and 25 Va 13°14' E.
39.88	Set post deposited charred stake and raised mound of earth, with pits as per instructions for 1/4 sec. cor.
79.76	The cor to secs. 23, 24, 25 and 26 Land rolling, soil 2nd rate.

Township 26 N. R. 6 W. of 6th Prin. Mer.

North between secs. 23 and 24
Va 13° 08' E.

40.00 Set post, deposited charred stake and raised mound of earth, with pits as per instructions for 1/4 sec. cor.

80.00 Set post, deposited charred stake and raised mound of earth, with pits as per instructions for cor. to secs 13. 14. 23 and 24
Land rolling, soil 2nd rate

East on a random line between secs 13 and 24
Va. 13° 14' E.

40.00 Set post for temporary 1/4 sec. cor.

79.78 Intersected East Boundary of Township 30 lks. North of cor. to secs 13 and 24 from which cor. Bears N. 89° 47' W. on a true line between secs. 13 and 24.
Va 13° 14' E.

39.89 Set post, deposited charred stake and raised mound of earth, with pits as per instructions for 1/4 sec. cor.

Township 26 N. R. 6 W. of 6th Prin. Mer.

79.78 The cor. to secs 13. 14. 23 and 24
Land rolling, soil 2nd rate

North between secs 13 and 14
Va 13° 08' E.

40.00 Set post deposited charred stake and raised mound of earth, with pits as per instructions for 1/4 sec. cor.

80.00 Set post deposited charred stake and raised mound of earth, with pits as per instructions for cor. to secs. 11. 12. 13 and 14.
Land rolling, soil 2nd rate.

East on a random line between secs. 12 and 13
Va. 13° 14' E.

40.00 Set post for temporary 1/4 sec. cor.

79.84 Intersected East Boundary of Township 46 lks. North of cor. to secs 12 and 13 from which cor. Bears N. 89° 40' West on a true line between secs. 12 and 13.
Va. 13° 14' E.

Township 26 N. R. 6 W. of 6th Prin. Mer.

39.92	Set post, deposited charred stake and raised mound of earth, with pits as per instructions for ¼ sec. cor.
79.84	The cor. to secs. 11, 12, 13 and 14, Land rolling, soil 2nd rate.

North between secs. 11 and 12
Va. 13° 08' E.

40.00	Set post, deposited charred stake and raised mound of earth, with pits, as per instructions for ¼ sec. cor.
80.00	Set post, deposited charred stake and raised mound of earth, with pits as per instructions for cor. to secs. 1, 2, 11 and 12, Land rolling, soil 2nd rate.

East on a random line between secs 1 and 12
Va. 13° 14' E.

40.00	Set post for temporary ¼ sec. cor.
79.88	Intersected East boundary of Township 62 lks North of cor to secs 1 and 12 from which cor. I run

Township 26 N. R. 6 W. of 6th Prin. Mer.

N. 89° 33' West on a true line between secs. 1 and 12
Va. 13° 14' E.

39.94	Set post deposited charred stake and raised mound of earth, with pits as per instructions for ¼ sec. cor.
79.88	The cor. to secs 1, 2, 11 and 12, Land rolling, soil 2nd rate.

North on a Random line between secs. 1 and 2
Va. 13° 08' E.

40.00	Set post for temporary ¼ sec. cor.
79.40	Intersected North Boundary of Township 18 lks west of cor to secs. 1 and 2 from which cor. I run.

S. 0° 08' W. on a true line between secs 1 and 2
Va. 13° 08' E.

39.40	Set post, deposited charred stake and raised mound of earth with pits as per instructions for ¼ sec. cor.
79.40	The cor. to secs. 1, 2, 11 and 12, Land rolling, soil 2nd rate Sept. 15th 1865

8/68

Township 26 N. R. 6. W. of 6th Prin. Mer

North between secs. 34 and 35
Va. 13° 08' E.

40.00 Set post, deposited charred stake and raised ½ of earth mound with pits as per instructions for ¼ sec. cor.

80.00 Set post, deposited charred stake and raised ½ of earth mound with pits as per instructions for cor. to secs 26 27, 34 and 35

Land rolling, soil 2nd rate.

East on a random line between secs 26 and 35
Va 13° 14' E.

40.00 Set post for temporary ¼ sec. cor.

80.24 Intersected N. and S. line 12 lks South of cor. to secs. 25. 26. 35 and 36. from which cor. B run
S. 89° 55' W. on a true line between secs. 26 and 35,
Va. 13° 14' E.

40.12 Set post, deposited charred stake and raised ½ of earth mound with pits as per instruction for ¼ sec. cor.

80.24 The cor. to secs. 26. 27. 34 and 35

Land rolling. soil 2nd rate.

9/69

Township 26. N. R. 6 W. of 6th Prin Mer

North between secs. 26 and 27
Va. 13° 08' E.

40.00 Set post deposited charred stake and raised ½ of earth mound with pits as per instructions for ¼ sec. cor.

80.00 Set post, deposited charred stake and raised ½ of earth mound with pits as per instructions for cor. to secs. 22. 23. 26 & 27

Land rolling, soil 3rd rate.

East on a random line between secs. 23 and 26
Va 13° 14' E.

40.00 Set post for temporary ¼ sec. cor.

80.28 Intersected N. and S. line 14 lks South of cor to secs 23. 24. 25 and 26. from which cor. B run.
S. 89° 54' W. on a true line between secs. 23 and 26,
Va. 13° 14' E.

40.14 Set post, deposited charred stake and raised ½ of earth mound with pits as per instructions for. ¼ sec. cor.

80.28 The cor. to secs. 22. 23. 26 and 27.

Land rolling, soil 3rd rate.

Township 26 N. R. 6 W. of 6th Prin. Mer.

North between secs. 22 and 23
Va. 13° 08' E.

40.00 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

80.00 Set post, deposited charred stake and raised mound of earth with pits as per instructions for corner to secs. 14, 15, 22 and 23.

Land rolling, soil 3rd rate.

East on a random line between secs 14 and 23
Va. 13° 14' E.

40.00 Set post for temporary 1/4 sec. cor.

80.40 Intersected N. and S. line at cor. to secs 13, 14, 23 and 24, from which cor I run West on a true line between secs. 14 and 23
Va 13° 14' E.

40.20 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

80.40 The cor. to secs 14, 15, 22 and 23.

Land rolling, soil 3rd rate.

North between secs. 14 and 15

Township 26 N. R. 6 W. of 6th Prin. Mer.

Va. 13° 08' E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs 10, 11, 14 and 15

Land rolling, soil 3rd rate.

East on a random line between secs. 11 and 14
Va 13° 14' E.

40.00 Set post for temporary 1/4 sec. cor.

80.78 Intersected N and S. line 28 lks North of cor to secs. 11, 12, 13 and 14 from which cor. I run N. 89° 48' W on a true line between secs. 11 and 14.
Va 13° 14' E.

40.39 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

80.78 The cor. to secs. 10, 11, 14 and 15.

Land rolling, soil 3rd rate.

Township 26 N. R. 6 West of 6th Prin. Mer.

North between secs. 10 and 11
Va 13° 08' E.

40.00 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

80.00 Set post, deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 2, 3, 10 and 11.

Land rolling, soil 2nd rate.

East on a random line between secs 2 and 11
Va 13° 14' E.

40.00 Set post for temporary 1/4 sec. cor.

80.28 Intersected N. and S. line 8 lks W of cor to secs 1, 2, 11 and 12 from which cor I run

N. 89° 57' W on a true line between secs. 2 and 11.

Va 13° 14' E

40.14 Set post, deposited charred stake, and raised mound of earth with pits as per instructions for 1/4 sec. cor.

80.28 The cor. to secs 2, 3, 10 and 11.

Land rolling, soil 2nd rate.

Township 26 N. R. 6 W. of 6th Prin. Mer.

North on a random line between secs 2 and 3
Va 13° 08' E.

40.00 Set post for temporary 1/4 sec. cor.

79.50 Intersected N. Boundary of Township 28 lks West of cor. to secs 2 and 3 from which cor. I run

S. 0° 12' West on a true line between secs 2 and 3

Va. 13° 08' E.

39.50 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

79.50 The cor. to secs. 2, 3, 10 and 11

Land rolling, soil 2nd rate.

Sept. 16th 1865

North between secs 33 and 34
Va. 13° 08' E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 27, 28, 33 and 34,

Land rolling, soil 2nd rate.

Township 26 N. R. 6 W. of 6th Prin. Mer.

East on a random line between secs. 27 and 34
Va. 13° 14' E.

40.00 Set post for temporary 1/4 sec. cor.
79.84 Intersected N and S. line 10 lks. North of cor to secs 26. 27, 34 and 35 from which cor. I run N. 89° 56' W. on a true line between secs 27 and 34. Va 13° 14' E.
39.92 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.84 The cor. to secs. 27, 28. 33 and 34
Land rolling, soil 2nd rate.

North between secs. 27 and 28
Va. 13° 08' E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor,
80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 21. 22. 27 and 28.
Land rolling, soil 2nd rate.

East on a random line between secs. 22 and 27

Township 26 N. R. 6 West of 6th Prin. Mer.

Va. 13° 14' E.

40.00 Set post for temporary 1/4 sec. cor.
79.50 Intersected N and S. line 18 lks. South of cor. to secs. 22, 23. 26 and 27 from which cor. I run S. 89° 52' W. on a true line between secs. 22 and 27
Va. 13° 14' E.
39.75 Set post. deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.50 The cor. to secs. 21. 22. 27 and 28.
Land rolling, soil 2nd rate.

North between secs 21 and 22
Va. 13° 08' E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor,
80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 15. 16. 21 and 22.
Land rolling, soil 2nd rate

16/76

Township 26 N. R. 6 W. of 6th Prin. Mer.

East on a random line between secs. 15 and 22
Va. 13° 14' E.

40.00 Set post for temporary 1/4 sec. cor.
79.16 Intersected N. and S. line 4 lks. North of cor to secs. 14, 15, 22 and 23 from which cor. B run
N. 89° 58' W. on a true line between secs 15 and 22. Va. 13° 14' E.
39.58 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.16 The cor. to secs. 15, 16, 21 and 22.
Land rolling, soil 2nd rate.

North between secs. 15 and 16
Va 13° 08' E.

40.00 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.00 Set post, deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 9, 10, 15 and 16.
Land rolling, soil 2nd rate

17/77

Township 26 N. R. 6 W. of 6th Prin. Mer.

East on a random line between secs. 10 and 15
Va 13° 14' E.

40.00 Set post for temporary 1/4 sec. cor.
79.18 Intersected N. and S. line at cor. to secs 10, 11, 14 and 15 from which cor. B run
West on a true line between secs 10 and 15
Va 13° 14' E.
39.59 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.18 The cor. to secs. 9, 10, 15 and 16.
Land rolling, soil 2nd rate.

North between secs. 9 and 10
Va 13° 08' E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 3, 4, 9 and 10.
Land rolling, soil 2nd rate

East on a random line between secs. 3 and 10

Township 26 N. R. 6 W. of 6th Prin. Mer.

Va 13°14' E.

40.00 Set post for temporary 1/4 sec. cor.

79.60 Intersected N. and S. line 20 lks. South of cor to secs 2. 3. 10 and 11 from which cor. B run.
S. 89°51' W. on a true line between secs 3 and 10. Va. 13°14' E.

39.80 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

79.60 The cor. to secs. 3, 4, 9 and 10,
Land rolling. soil 2nd rate.

North on a random line between secs 3 and 4
Va 13°08' E.

40.00 Set post for temporary 1/4 sec. cor.

79.90 Intersected North Boundary of Township 32 lks. West of cor to secs. 3 and 4, from which cor. B run
S. 0°14' West on a true line between secs 3 and 4
Va 13°08' E.

39.90 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

79.90 The cor. to secs. 3. 4. 9 and 10.

Township 26 N. R. 6 W. of 6th Prin. Mer.

Land rolling soil 2nd rate
Sept. 17th 1865

North between secs 32 and 33
Va 13°08' E.

1.70 Ravine bears S. 20° W.

22.75 Ravine bears S. E.

40.00 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

80.00 Set post, deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 28. 29. 32 and 33
Land rolling, soil 2nd rate

East on a random line between secs 28 and 33
Va. 13°14' E.

40.00 Set post for temporary 1/4 sec. cor.

80.04 Intersected N. and S. line 8 lks. North of cor to secs. 27, 28. 33 and 34 from which cor. B run
N. 89°57' W. on a true line between secs 28 and 33. Va. 13°14' E.

40.02 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

Township 26 N. R. 6 W. of 6th Prin. Mer.

80.04	The cor. to secs 28. 29. 32 and 33 Land rolling, soil 2nd rate.
	North between secs. 28 and 29 Va 13° 08' E.
40.00	Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.00	Set post, deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 20. 21. 28 and 29. Land rolling, soil 2nd rate.
	East on a random line between secs. 21 and 28 Va. 13° 14' E.
40.00	Set post for temporary 1/4 sec. cor.
80.10	Intersected N. and S. line 53 lks. South of cor. to secs. 21. 22. 27 and 28, from which cor. B run S. 89° 37' W. on a true line between secs 21 and 28 Va 13° 14' E.
40.05	Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

Township 26 N. R. 6 W. of 6th Prin. Mer.

80.10	The cor. to secs. 20. 21. 28 and 29 Land rolling, soil 2nd rate.
	North between secs. 20 and 21 Va. 13° 08' E.
40.00	Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.00	Set post, deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs 16. 17. 20 and 21. Land rolling, soil 2nd rate.
	East on a random line between secs. 16 and 21 Va. 13° 14' E.
40.00	Set post for temporary 1/4 sec. cor.
80.00	Intersected N. and S. line 50 lks. South of cor. to secs. 15. 16. 21 and 22 from which cor. B run. S. 89° 39' W. on a true line between secs 16 and 21. Va 13° 14' E.
40.00	Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

Township 26 N. R. 6 W. of 6th Prin. Mer.

80,00 The cor. to secs. 16. 17. 20 and 21.
Land rolling, soil 2nd rate.

North between secs. 16 and 17
Va 13° 08' E.

49,00 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

80,00 Set post deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 8. 9. 16 and 17.
Land rolling, soil 2nd rate.

East on a random line between secs 9 and 16
Va. 13° 14' E.

40,00 Set post for temporary 1/4 sec. cor.

79.88 Intersected N. and S. line 27 lks. South of cor. to secs. 9. 10. 15 and 16 from which cor. Bears,
S. 89° 48' W. on a true line between sections 9 and 16. Va. 13° 14' E.

39.94 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

Township 26 N. R. 6. W. of 6th Prin. Mer.

79,88 The cor. to secs. 8. 9. 16 and 17
Land rolling, soil 2nd rate.

North between secs. 8 and 9
Va, 13° 08' E.

40,00 Set post, deposited charred stake and raised mound of earth with pits, as per instructions for 1/4 sec. cor.

80,00 Set post deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs 4. 5. 8 and 9.
Land rolling, soil 2nd rate.

East on a random line between secs. 4 and 9
Va 13° 14' E.

40,00 Set post for temporary 1/4 sec. cor.

79.90 Intersected N. and S. line. 9 lks North of cor. to secs. 3. 4. 9 and 10. from which cor. Bears
N. 89° 56' W. on a true line between secs. 4 and 9.
Va. 13° 14' E.

39,95 Set post, deposited charred stake and raised

Township 26 N. R. 6 W. of 6th Prin. Mer.

79.90	Mound of earth with pits as per instructions for 1/4 sec cor.
	The cor to secs 4, 5, 8 and 9. Land rolling, soil 2nd rate.
	North on a random line between secs. 4 and 5 Va. 13°08' E.
40.00	Set post for temporary 1/4 sec. cor.
80.18	Intersected North Boundary of Township 20 lks. East of cor. to secs. 4 and 5 from which cor I run. S. 0°09' E. on a true line between secs 4 and 5 Va. 13°08' E.
40.18	Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.18	The cor. to secs. 4. 5. 8 and 9. Land rolling, soil 2nd rate Sept. 18th. 1865.
	North between secs 31 and 32 Va. 13°08' E.
40.00	Set post deposited charred stake and raised

Township 26 N. R. 6 W. of 6th Prin. Mer.

	mound with pits as per instructions for 1/4 sec. cor.
80.00	Set post deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 29. 30. 31 and 32. Land rolling. soil 2nd rate
	East on a random line between secs 29 and 32 Va. 13°14' E.
11.25	Head of brushy ravine bears S.
40.00	Set post for temporary 1/4 sec. cor.
80.06	Intersected N. and S. line 18 lks. North of cor to secs. 28. 29. 32 and 33 from which cor. I run N. 89°52' W. on a true line between secs 29 and 32 Va. 13°14' E.
40.03	Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.06	The cor. to secs. 29. 30. 31 and 32 Land rolling. soil 2nd rate

Township 26 N. R. 6 W. of 6th Prin. Mer.

West on a random line between secs 30 and 31
Va. 13° 14' E.

40,00 Set post for temporary 1/4 sec. cor.
79.52 Intersected West Boundary of Township 15 lks south of cor. to secs. 30 and 31 from which cor. I run
S. 89° 54' E. on a true line between secs 30 and 31
Va. 13° 14' E.
39,52 Set post, deposited charred stake and raised mound of earth, with pits as per instructions for 1/4 sec. cor.
79.52 The cor. to secs 29. 30. 31 and 32
Land rolling, soil 2nd rate

North between secs. 29 and 30
Va. 13° 08' E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80,00 Set post, deposited charred stake and raised mound of earth with pits, as per instructions for cor to secs 19. 20. 29 & 30
Land rolling, soil 2nd rate.

Township 26 N. R. 6 W. of 6th Prin. Mer.

East on a random line between secs 20 and 29
Va. 13° 14' E.

40,00 Set post for temporary 1/4 sec. cor.
80,10 Intersected N. and S. line 20 lks North of cor. to secs. 20. 21. 28 and 29 from which cor. I run
N. 89° 51' W. on a true line between sections 20 and 29
Va. 13° 14' E.
40,05 Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80,10 The cor. to secs. 19, 20, 29 and 30
Land rolling, soil 2nd rate.

West on a random line between secs, 19 and 30
Va. 13° 14' E.

40,00 Set post for temporary 1/4 sec. Cor.
79.36 Intersected West Boundary of Township 10 lks. South of cor. to secs. 19 and 30 from which cor. I run S. 89° 56 E. on a true line between secs. 19 and 30 Va. 13° 14' E.
39.36 Set post Deposited charred stake and raised mound of earth

Township 26 N. R. 6 W. of 6th Prin. Mer.

	with pits as per instructions for 1/4 sec. cor.
78.36	The cor. to secs. 19. 20. 29 and 30
	Land rolling. soil 2nd rate.

North between secs 19 and 20
Va. 13° 08' E.

40.00	Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.00	Set post deposited charred stake and raised mound of earth with pits as per instructions for cor to secs 17. 18. 19. and 20
	Land rolling. soil 2nd rate
	Sept. 20th 1865

East on a random line between secs 17 and 20
Va. 13° 14' E.

40.00	Set post for temporary 1/4 sec. cor.
80.00	Intersected N. and S. line 18 lks North of cor. to secs 16. 17. 20 and 21. from which cor. Prum
	N. 89° 52' W. on a true line between secs 17 and 20. Va 13° 14' E.

Township 26 N. R. 6 W. of 6th Prin. Mer.

40.00	Set post, deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.00	The cor. to secs. 17. 18. 19 and 20.
	Land rolling. soil 2nd rate.

West on a random line between secs 18 and 19
Va. 13° 14' E.

40.00	Set post for temporary 1/4 sec. cor.
79.28	Intersected West Boundary of Township 6 lks. North of cor to secs 18 and 19 from which cor. Prum. N. 89° 57' E. on a true line between secs 18 and 19. Va 13° 14' E.
39.28	Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.28	The cor to sects 17. 18. 19 and 20
	Land rolling. soil 2nd rate.

North between secs 17 and 18
Va 13° 08' E.

40.00	Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

Township 26 N. R. 6 W. of 6th Prin. Mer.

80,00 Set post deposited charred stake and raised mound of earth with pits as per instructions for cor to secs 7. 8. 17 and 18.
Land rolling. soil 2nd rate.

East on a random line between secs 8 and 17
Va 13° 14' E.

40,00 Set post for temporary 1/4 sec cor
80,02 Intersected N. and S. line 10 lks. South of cor. to secs. 8. 9. 16 and 17 from which cor Brun
S. 89° 56' W. on a true line between secs. 8 and 17
Va. 13° 14' E.
40,01 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80,02 The cor to secs. 7. 8. 17 and 18.
Land gently rolling. soil 2nd rate

West on a random line between secs 7 and 18
Va. 13° 14' E.
40,00 Set post for temporary 1/4 sec. cor.

Township 26 N. R. 6 W. of 6th Prin. Mer.

79,04 Intersected West Boundary of Township 11 lks. South of cor to secs 7 and 18 from which cor. Brun
S. 89° 55' E on a true line between secs. 7 and 18 Va. 13° 14' E.
39,04 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
79,04 The cor. to secs. 7. 8. 17 and 18
Land rolling soil 3rd rate

North between secs 7 and 8
Va 13° 08' E.
40,00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80,00 Set post deposited charred stake and raised mound of earth with pits as per instructions for cor. to secs. 5. 6. 7 and 8
Land rolling. soil 2nd rate.

East on a random line between secs 5 and 8
Va. 13° 14' E.
40,00 Set post for temporary 1/4 sec. cor.

Township 26 N. R. 6 W. of 6th Prin. Mer.

80.00	Intersected North and South line at cor to secs. 4. 5. 8 and 9 from which cor Prun West on a true line between secs 5 and 8 Va. 13° 14' E.
40.00	Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.00	The cor. to secs. 5. 6. 7 and 8 Land rolling. soil 2nd rate

West on a random line between secs. 6 and 7
Va. 13° 14' E.

40.00	Set post for temporary 1/4 sec. cor.
78.92	Intersected West Boundary of Township 13 Rks. S of cor to secs 6 and 7 from which cor Prun S. 89° 54' E on a true line between secs 6 and 7 Va. 13° 14' E.
38.92	Set post. deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
78.92	The cor. to secs 5. 6. 7 and 8 Land rolling. soil 2nd rate.

Township 26 N. R. 6 W. of 6th Prin. Mer.

North on a random line between secs. 5 and 6
Va. 13° 08' E.

40.00	Set post for temporary 1/4 sec. cor.
80.04	Intersected North Boundary of Township 5 Rks. West of the cor to secs 5 and 6 from which cor. Prun S. 0° 02' W. on a true line between secs 5 and 6 Va 13° 08' E.
40.04	Set post. deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.04	The cor. to secs. 5. 6. 7 and 8 Land rolling. soil 2nd rate Sept 21st 1865

Township 26 N. R. 6 W of 6th Prin. Mer.

General Description

The land in this Township is rolling; mostly 2nd rate quality. There is some 3rd rate land which is not very well adapted to farming. The surface is rolling and apt to wash when cultivated. We found no water within the Township. There is a scarcity of Timber. We only found scattering Elm and Oak trees along the banks of a ravine bearing S.E through Sec. 32. No stone in the Township.

List of Names

A list of the names of the individuals employed to assist in running, measuring, or marking the lines and corners described in the foregoing Field Notes of Township No 26 North of the Base Line, of Range No 6 West of the 6th Prin. Mer., showing the respective capacities in which they acted

Merit Howard	Chainman
Charles Stark	Chainman
James H. Holderby	Axeman
Robert Rabe	Flagman.

We hereby certify that we assisted Robert Armstrong, Deputy Surveyor, in Subdividing Townships number twenty-five, twenty-six, twenty-seven, twenty eight, twenty nine, and thirty North of the base line of Range number Six West of the Sixth principal Meridian, and Townships number twenty nine, and thirty North of the base line of Range number Seven and eight West of the of the Sixth Principal Meridian, and that said Townships have been in all respects, to the best of our Knowledge and belief, well and faithfully Surveyed, and the boundary Monuments planted according to the instructions furnished by the Surveyor General; and that all the corners are not constructed of less size and demension, then prescribed in the Printed Manual of Surveying instructions, dated Febuary 22nd 1855. and the printed instructions

marked and conditioned in every respect as therein required, —

Merit Howard, Chainman.
Charles Stark, Chainman,
J H Holderly, Axeman,
Robert Rabe, Flagman,

Subscribed and Sworn to by the above named persons, before me, a Justice of the Peace for the County of Cuming in the Territory of Nebraska, this the 25th day of September, 1865.

Josiah McKinahan

Justice of the Peace,

I, Robert Armstrong, Deputy Surveyor do solemnly swear that in pursuance of a joint contract wherein H. C. F. Hackbusch and Robert Armstrong are joint contractors with H. S. Sleeper, United States Surveyor General for Kansas and Nebraska, bearing date the 12th day of May 1865, I have well, faithfully, and truly, in my own proper person, and in strict conformity with the instructions furnished by the Surveyor General, the Surveying Manual, and the laws of the United States, surveyed all those parts or portions of Townships number twenty-five, twenty-six - twenty-seven twenty-eight twenty-nine and thirty North of the base line of Range number Six West of the 6th Principal Meridian and Township number twenty-nine and thirty North of the base line of Range number seven and eight West of the

38
98

6th Principal Meridian. in the Territory of Nebraska, as are represented in the foregoing field notes as having been surveyed under my directions: And I do further solemnly swear that all the corners of said surveys have been established and perpetuated in strict accordance with the Surveying Manual and printed instructions. and that the foregoing are the true and original field notes of such survey.

Robt Armstrong
Deputy Surveyor

Sworn to and subscribed before me this 18th day of October AD 1865

S. B. Williams,
Justice of the Peace
of Leavenworth County
Kansas

39
99

Surveyor Gen'l's Office
Leavenworth, Kansas, November 10, 1865

The foregoing field notes of the survey of the subdivisional lines of Townships number twenty-five, twenty six-twenty-seven, twenty-eight-, twenty-nine and thirty North, of Range Six West and Townships number twenty nine and thirty North of the base line of Ranges seven and eight West of the Sixth Principal Meridian in the Territory of Nebraska executed by Robert Armstrong under joint contract of H. C. F. Hackbusch and Robert Armstrong of the 12th day of May 1865, in the months of July August & September 1865, having been critically examined the necessary corrections and explanations made the said field notes and the surveys they describe are hereby approved

K. L. Sleeper
Surveyor General

~~Surveyor Generals Office~~

~~Leavenworth Kansas~~ 1865

~~I certify that the foregoing transcript of the field notes of the survey of the subdivisional lines of Township number twenty six North of the base line of Range number six West of the sixth principal meridian in the Territory of Nebraska has been correctly copied from the original~~

D L Mad
27 - 6 Armstrong

Contract No. 313.

Field Notes
of the
Subdivision lines in Township 27
N. R. 6 West of the 6th Principal
Meridian surveyed by Robert Armstrong,
deputy surveyor, under joint Contract
No 313, dated May 12th 1865 wherein
H. C. F. Hackbusch and Robert Armstrong
are joint Contractors

Survey
Commenced Sept. 9th 1865
Completed Sept. 14th 1865

Examined No 13 &
Plotted No 13 &
Copied [illegible]
Compl [illegible]

Names and duties of assistants

Merritt Howard	Chainman
Charles Stark	Chainman
James H. Holdenby	Axeman
Robt Kabe	Flagman

Township 27 S. Range 6 W. 6 P. M.

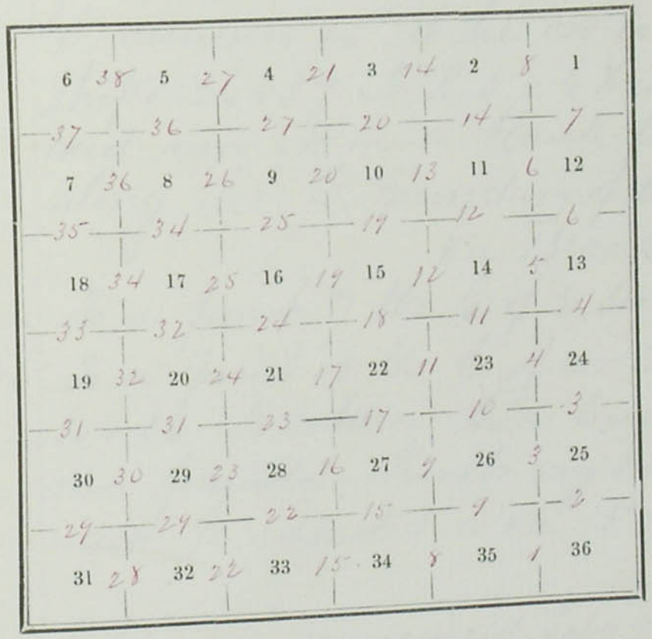

for 1/4 Sec Cor.

10 102 104

105

T 27 N. R. 6 W.

To determine the proper adjustment of my compass for subdividing this Township I commence at the cor to Townships 26 & 27 N. R. 5 & 6 West and run N. on a blank line along the E Boundary of sec 36.

Va 13° 00 E.

40.08 To a point 7 lks E of ¼ sec cor.

80.15 To a point 12 lks E of cor to secs 25 & 36. To retrace this line or run parallel thereto my compass must be adjusted a va 13° 05' E.

Subdivision commenced Sept 9th 1865 From the corner to secs 1, 2, 35 & 36 on the South Boundary of the Township I run North between secs 35 & 36.

Va 13° 05' E.

40.00 Set post deposited charred stake mixed with earth mounded with pits as per instructions for ¼ sec cor.

T 27 N. R. 6 W.

80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to secs. 25. 26. 35. 36.
Land rolling soil sandy 3° rate.

East on a random line between secs. 25 & 36.
Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
80.22 Intersected East Boundary 30 lks South of cor to secs. 25 & 36. from which cor I run.
S 89° 47' W. on a true line between secs. 25 and 36.
Va 13° 05' E.

40.11 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.
80.22 The cor to secs. 25. 26. 35. 36.
Land rolling soil sandy 3° rate.

T. 27 N. R. 6 W.

North between secs. 25 and 26.
Va 13° 05' E.

40.00 Set post deposited charred stick raised mound of earth with pits as per instructions for ¼ sec cor.
80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to secs. 23. 24. 25 and 26.
Land rolling soil sandy. 3rd rate.

East on a random line between secs. 24 and 25.
Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
80.18 Intersected East Boundary. 32 lks S of cor to secs. 24 and 25. from which cor I run.
S 89° 46' W. on a true line between secs. 24 and 25.
Va 13° 05' E.

2/10 4/108

T 27 N. R. 6 W.

40.09	Set post deposited chared stake raised mound south with pits as per instructions for 1/4 sec cor.
80.18	The cor to sec's 23. 24. 25. 26. Land rolling soil sandy 3rd rate.

North between sec's 23 and 24
Va 13° 05' E.

40.00	Set post deposited chared stake raised mound south with pits as per instructions for 1/4 sec cor.
80.00	Set post deposited chared stake raised mound south with pits as per instructions for cor to sec's 13. 14. 23 and 24. Land rolling soil sandy 3° rate.

East on random line between sec's 13 and 24
Va 13° 05' E.

40.00	Set post for temporary 1/4 sec cor.

5/109

T 27 N. R. 6 W.

79.96	Intersected East Boundary 16 lks S of cor to sec's 13 and 24. from which cor. I ran. S 89° 55' W. on a true line between sec's 13 and 24. Va 13° 05' E.
39.98	Set post deposited chared stake raised mound south with pits as per instructions for 1/4 sec cor.
79.96	The cor to sec's 13. 14. 23. 24. Land ~~ing~~ rolling soil 2d rate.

North between sec 13 and 14.
Va 13° 05' E.

40.00	Set post. deposited chared Stake raised mound south with pits as per instructions for 1/4 sec cor.
80.00	Set post deposited chared stake raised mound south with pits as per instructions for cor to sec's 11. 12 13. 14. Land gently rolling soil sandy 3rd rate.

2/10 6/110

T 27 N. R. 6 W.

East on a random line
between Sec.s 12 and 13.
Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
79.84 Intersected E Boundary 10 lks S.
of cor to sec.s 12 and 13. from
which cor. I run
S 89° 56' W. on a true line between
sec.s 12 and 13
Va 13° 05' E.

39.92 Set post deposited chared stake
raised mound, with pits as per
instructions for ¼ sec cor.
79.84 The cor to Sec.s 11, 12, 13, 14.
Land gently rolling soil 2.d rate

North between sec.s 11 and 12.
Va 13° 05' E.

40.00 Set post deposited chared stake
raised mound, with pits as per
instructions for ¼ sec cor.

7/111

T 27 N. R. 6 W.

80.00 Set post deposited chared stake
raised mound, with pits as per
instructions for cor to sec.s 1, 2
11 and 12.
Land rolling soil 2.d rate

East on random line between
sec.s 1 and 12.
Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
79.70 Intersected East Boundary. 20 lks
S of cor to sec.s 1 and 12. from
which cor. I run.
S 89° 51' W. on a true line between
sec.s 1 and 12.
Va 13° 05' E.

39.85 Set post deposited chared stake
raised mound, with pits as per
instructions for ¼ sec cor.
79.70 The cor to sec.s 1, 2, 11, 12.
Land rolling sandy soil 3.rd rate.

2/106 8/112

T 27 N. R. 6 W.

North on a random line between
secs 1 and 2.

Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
80.32 Intersected North Boundary of Town-
ship 42 lks E. of cor to secs 1 and 2.
from which cor I run.
S 0° 18' E. on a true line between
secs 1 and 2.

Va 13° 05' E.

40.32 Set post deposited chared stake
raised mound south with pits as per
instructions for ¼ sec cor.
80.32 The cor to secs 1, 2, 11, 12.
Land rolling soil 3rd rate Sept 9th 1865

North between secs 34 and 35.

Va 13° 05' E.

40.00 Set post deposited chared stake
raised mound south with pits as per
instructions for ¼ sec cor.
80.00 Set post deposited chared stake
raised mound south with pits as per
instructions for cor to secs 26. 27. 34. 35.

9/113

T. 27 N. R. 6 W.

Land rolling soil 3rd rate.

East on a random line between
secs 26 and 35.

Va 13° 05' E

40.00 Set post for temporary ¼ sec cor.
80.10 Intersected North and South line
18 lks N. of cor to secs 25. 26 35 36 from
which cor I run
N 89° 52' W. on a true line between secs
26 and 35.

Va 13° 05' E.

40 05 Set post deposited chared stake
raised mound south with pits as per
instructions for ¼ sec cor.
80.10 The cor to secs 26. 27. 34. 35
Land rolling soil 3rd rate

North between secs 26 and 27.

Va 13° 05' E.

40.00 Set post deposited chared stake raised
mound south with pits as per instructions
for ¼ sec cor.

T 27 N. R. 6 W.

80.00 Set post deposited chared stake raised mound of earth with pits as per instructions for cor to secs. 22. 23 26. 27.
Land rolling soil 3rd rate.

East on a random line between secs. 23 and 26.
Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
79.98 Intersected North and South line 40 lks N. of cor to secs. 23. 24. 25. 26 from which cor. I run
N 89° 43' W on a true line between secs. 23 and 26.
Va 13° 05' E.

39.99 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec cor.
79.98 The cor to secs. 22. 23 26. 27.
Land rolling sandy 3rd rate.

T. 27 N. R. 6 W.

North between Secs. 22 and 23.
Va 13° 05' E.

40.00 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec cor.
80.00 Set post deposited chared stake raised mound of earth with pits as per instructions for cor to secs. 14. 15. 22. 23.
Land rolling sandy 3rd rate.

East on a random line between secs. 14 and 23.
Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
79.88 Intersected North and South line 30 lks North of cor to secs. 13. 14. 23. 24 from which cor. I run
N 89° 39' W. on a true line between secs 14 and 23.
Va 13° 05' E.

T 27 N. R. 6 W.

39.94 Set post deposited chared stake raised mound of earth with pits as per instructions for 1/4 sec cor.

79.88 The cor to secs. 14. 15. 22. 23.
Land rolling Sandy soil 3rd rate.

North between secs. 14 and 15.
Va 13° 05' E

40.00 Set post deposited chared stake raised mound of earth with pits as per instructions for 1/4 sec cor.

80.00 Set post deposited chared stake raised mound of earth with pits as per instructions for cor to secs. 10. 11. 14. 15.
Land rolling soil sandy 3rd rate

East on random line between secs. 11 and 14.
Va 13° 05' E.

40.00 Set post for temporary 1/4 sec cor.

T 27 N. R. 6 W.

79.86 Intersected North and South line 32 lks N. of cor. to secs. 11. 12. 13. 14. from which cor. I run
N 89° 46' W. on a true line between secs. 11 and 14.
Va 13° 05' E.

39.93 Set post deposited chared stake raised mound of earth with pits as per instructions for 1/4 sec cor.

79.86 The cor to secs. 10. 11. 14. 15.
Land rolling soil sandy 3rd rate.

North between secs. 10 and 11
Va 13° 05' E.

40.00 Set post deposited chared stake raised mound of earth with pits as per instructions for 1/4 sec cor.

80.00 Set post deposited chared stake raised mound of earth with pits as per instructions for cor to secs. 2. 3. 10. 11.
Land nearly level soil Sandy 3rd rate.

T 27 N. R. 6 W.

East on random line between sec^s. 2 and 11

Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.

79.72 Intersected North and South line 20 lks North of cor to sec^s. 1, 2, 11, 12. from which cor. I run

N 89° 51' W. on a true line between sec^s. 2 and 11

Va 13° 05' E.

39.86 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec cor.

79.72 The cor to sec^s. 2, 3, 10, 11.

Land gently rolling soil sandy 3rd rate.

North on a random line between sec^s. 2 and 3.

Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.

80.26 Intersected N Boundary 46 lks E of cor to sec^s 2 and 3. from which cor. I run

T 27 N. R. 6 W.

S 0° 20' E. on a true line between sec^s 2 and 3.

Va 13° 05' E.

40.26 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.26 The cor to sec^s 2, 3, 10, 11

Land gently rolling soil sandy 3 rate.

Sept 11' 1865.

North between sec^s 33 and 34.

Va 13° 05' E.

40.00 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.00 Set post deposited chared stake raised mound of earth with pits as per instructions for cor to sec^s 27, 28 33 and 34.

Land rolling soil 3° rate

East on a random line between sec^s 27 and 34

Va 13° 05' E.

T 27 N. R. 6 W.

40.00 Set post for temporary ¼ sec cor.
80.12 Intersected North and South line at cor. of sec.s 26. 27. 34. 35. from which cor. I run W
West on a true line between sec.s 27 and 34.
Va 13°05' E.
40.06 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec cor.
80.12 The cor to sec.s 27. 28 33. 34
Land rolling soil 3rd rate

North between sec.s 27 and 28
Va 13°05' E.
40.00 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec cor.
80.00 Set post deposited chared stake raised mound of earth with pits as per instructions for cor to sec.s 21. 22 27. 28.

T. 27 N. R. 6 W.

Land rolling soil 3rd rate.

East on a random line between sec.s 22 and 27.
Va 13°05' E
40.00 Set post for temporary ¼ sec cor.
80.18 Intersected North and South line 20 lks North of cor to sec.s 22. 23. 26. 27. from which cor. I run
N 89°51' W. on a true line between sec.s 22 and 27.
Va 13°05' E.
40.09 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec cor.
80.18 The cor to sec.s 21. 22. 27. 28.
Land rolling soil 3rd rate.

North between sec.s 21 and 22.
Va 13°05' E
40.00 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec cor.

2/106 18—/122

T. 27 N. R. 6 W.

80.00 Set post deposited chared stake raised Mound ~~south~~ with pits as per instructions for cor to sec. 15. 16. 21. 22.
Land rolling soil sandy 3rd rate.

East on a random line between sec. 15 and 22
Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
80.10 Intersected North & South line 10 lks North of cor to sec. 14. 15. 22. 23. from which cor. I run
N 89° 56' W. on a true line between sec. 15 and 22.
Va 13° 05' E.
40.05 Set post deposited chared stake raised mound ~~south~~ with pits as per instructions for ¼ sec cor.
80.10 The cor to sec. 15; 16. 21, 22.
Land rolling soil sandy 3rd rate.

19/123

T. 27 N. R. 6 W.

North between sec. 15 and 16
Va 13° 05' E.

40.00 Set post deposited chared stake raised Mound ~~south~~ with pits as per instructions for ¼ sec cor.
80.00 Set post deposited chared stake raised mound ~~south~~ with pits as per instructions for cor to sec. 9, 10 15. 16.
Land rolling soil sandy 3rd rate.

East on a random line between sec. 10 and 15
Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
80.00 Intersected North & South line 12 lks N of cor to sec. 10. 11. 14. 15. from which cor. I run
N 89° 55' W. on a true line between sec. 10 and 15.
Va 13° 05' E.
40.00 Set post deposited chared stake raised mound ~~south~~ with pits as per instructions for ¼ sec cor.

T 27 N. R. 6 W.

80.00 The cor to sec[s] 9. 10. 15. 16.
Land rolling soil sandy 3rd rate.

North between sec[s] 9 and 10.
Va 13° 05' E.

40.00 Set post deposited chared stake
raised mound south with pits as per
instructions for 1/4 sec cor.

80.00 Set post. deposited chard stake
raised mound south with pits as per
instructions for cor to sec[s] 3. 4. 9. 10.
Land rolling soil sandy 3rd rate.

East on a random line between
sec. 3 and 10
Va 13° 05' E.

40.00 Set post for temporary 1/4 sec cor.
79.92 Intersected North & South line
10 lks North of cor to sec[s] 2. 3. 10. 11.
from which cor I run
N. 89° 56' W. on a true line between
sec 3 and 10
Va 13° 05' E.

T 27 N. R. 6 W.

39.96 Set post deposited chared stake
raised mound south with pits as per
instructions for 1/4 sec cor.
79.92 The cor to secs 3. 4. 9. 10
Land gently rolling soil sandy 3 rate.

North on a random line between
sec[s] 3 and 4
Va 13° 05' E.

40.00 Set post for temporary 1/4 sec cor.
80.20 Intersected North Boundary 62 lks.
E. of cor to sec[s] 3 and 4 from which
cor. I run
S 0° 27' E. on a true line between
Secs 3 and 4
Va 13° 05' E.

40.20 Set post deposited chared stake
raised mound east with pits as per
instructions for 1/4 sec cor.
80.20 The cor to sec[s] 3. 4. 9. 10.
Land gently rolling soil sandy 3 rate.
Sept 12th 1865.

North between Sec.s 32 and 33
Va 13° 05' E.

40.00 Set post deposited chared stake raised Mound of earth with pits as per instructions for ¼ sec cor.

80.00 Set post deposited chared stake raised mound of earth with pits as per instruction for cor. to sec.s 28.29.32.33 Land rolling and sandy 3rd rate.

East on a random line between sec.s 28. and 33.

Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.

80.04 Intersected North & South line 10 lks S of cor to sec.s 27. 28. 33. 34. from which cor. I run S 89° 56' W. on a true line between sec.s 28 and 33.

Va 13° 05' E.

40.02 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec.s cor.

80.04 The cor to sec.s 28. 29. 32. 33 Land rolling. Sandy 3° rate.

North between sec.s 28 and 29.
Va 13° 05' E.

40.00 Set post deposited charred stake raised mound of earth with pits as per instruction for ¼ sec cor.

80.00 Set post deposited chared stake raised mound of earth with pits as per instructions for cor to sec.s 20. 21. 28. 29 Land rolling Sandy 3° rate.

East on random line between sec.s 21 and 28.

Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.

79.85 Intersected North & South line at cor. to sec.s 21, 22. 27. 28. from which cor. I run West on a true line between sec.s 21 and 28.

Va 13° 05' E.

T 27 N. R. 6 W.

39.92½ Set post deposited chained stake raised mound with earth with pits as per instructions for ¼ sec cor.
79.85 The cor to secs 20. 21. 28. 29.
Land rolling sandy 3° rate.

North between secs 20. 21.
Va 13° 05' E.
40.00 Set post deposited chained stake. raised mound with earth with pits as per instructions for ¼ sec cor.
80.00 Set post deposited chained stake. raised mound with earth with pits as per instructions for cor to secs 16. 17. 20. 21.
Land rolling soil sandy 3° rate.

East on random line between secs 16 and 21,
Va 13° 05' E.
40.00 Set post for temporary ¼ sec. cor.
79.92 Intersected. North and South line 8 lks North of cor to secs 15. 16 21. 22.

T 27 N. R. 6 W.

From which cor. I run
N. 89° 55' W. on a true line
between secs 16 and 21.
Va 13° 05' E.
39.96 Set post deposited chained stake raised mound with earth with pits as per instructions for ¼ sec cor.
79.92 The cor to secs 16. 17. 20 21.
Land rolling. Land 3° rate.

North between secs 16 and 17.
Va 13° 05' E.
40.00 Set post deposited chained stake raised mound with earth with pits as per instructions for ¼ sec cor.
80.00 Set post deposited chained stake raised Mound with earth with pits as per instructions for cor to secs 8. 9. 16. 17.
Land rolling soil Sandy 3° rate.

East on random line between

T 27 N. R. 6 W.

sec.s 9 and 16.

Va 13°05' E.

40.00 Set post for temporary ¼ sec cor.
79.98 Intersected North and South line
22 lks N of cor to sec.s 9.10.15.16.
from which cor. I run
N 89°51' W. on a true line between
sec.s 9 and 16.

Va 13°05' E.

39.99 Set post deposited charred stake
raised mound of earth with pits as per
instructions for ¼ sec cor.
79.98 The cor to sec.s 8.9.16.17
Land gently rolling soil 2.° rate.

North between sec.s 8. and 9.

Va 13°05' E.

40.00 Set post deposited charred stake
raised mound of earth with pits as per
instructions for ¼ sec cor.
80.00 Set post deposited charred stake
raised mound of earth with pits as per.

T. 27 N. R. 6 W.

instructions for cor to sec.s 4.5
8.9.
Land gently rolling soil 3.° rate.

East on random line between
sec.s 4 and 9.

Va 13°05' E.

40.00 Set post for temporary ¼ sec cor
79.90 Intersected North and South line
34 lks North of cor to sec.s 3.4.9.10
from which cor. I run
N 89°45' W. on a true line between
sec.s 4 and 9.

Va 13°05' E.

39.95 Set post deposited charred stake
raised mound of earth with pits as per.
instructions for ¼ sec cor.
79.90 The cor to sec.s 4.5.8.9.
Land rolling gently. soil 3.rd rate.

North on a random line between
sec.s 4 and 5.

Va 13°05' E.

T 27. N. R. 6 W.

40.00 Set post for temporary ¼ sec cor.
80.22 Intersected North Boundary 40 lks E. of cor to secs 4 and 5. from which cor. I run
S 0°17' E on a true line between secs 4 and 5.
Va 13°05' E.
40.22 Set post deposited charred stake raised mound ~~south~~ with pits as per instructions for ¼ sec cor.
80.22 The cor to secs 4. 5. 9. 8.
Sand gently rolling soil 3rd rate.
Sept 13th

North between secs 31 and 32
Va 13°05' E.
40.00 Set post deposited charred stake raised mound ~~south~~ with pits as per instructions for ¼ sec cor.
80.00 Set post deposited charred stake raised mound ~~south~~ with pits as per instructions for cor to secs. 29. 30. 31. 32.

T 27 N. R. 6 W.

Land rolling sandy 3rd rate.

East on a random line between Secs. 29 and 32.
Va 13°05' E.
40.00 Set post for temporary ¼ sec cor.
80.08 Intersected north and south line 32 lks south of cor for secs 28. 29. 32. 33. from which cors. I run
S 89°46' W on a true line between secs 29. and 32.
Va 13°05' E.
40.04 Set post deposited charred stake raised mound ~~south~~ with pits as per instructions for ¼ sec cor.
80.08 The cor to secs 29. 30. 31. 32.
Sand rolling sandy 3rd rate.

West on a random line between Secs 30 and 31.
Va 13°05' E.
40.00 Set post for temporary ¼ sec cor.

18/122 — 30/134

T 27 N. R. 6 W.

79.10 Intersected West Boundary 38 lks
N of cor to sec. 30 and 31. from
which cor. I run
N 89°44' E. on a true line between
sec. 30 and 31.
Va 13°05' E.

39.10 Set post deposited chained stake
raised mound of earth with pits as per
instructions for 1/4 sec cor.

79.10 The cor to sec. 29. 30. 31. 32.
Land broken and sandy 3rd rate.

North between sec. 29 and 30
Va 13°05' E.

40.00 Set post deposited chained stake
raised mound of earth with pits as per
instructions for 1/4 sec cor.

80.00 Set post deposited chained stake
raised mound of earth with pits as per
instructions for cor to sec. 19.
20. 29. 30.
Land broken & sandy 3rd rate.

31/135

T 27 N. R. 6 W.

East on a random line between
sec. 20 and 29
Va 13°05' E.

40.00 Set post for temporary 1/4 sec cor.

79.96 Intersected North and South line
at cor to sec. 20. 21. 28. 29. from
which cor. I run
West on a true line between
sec. 20 and 29
Va 13°05' E.

39.98 Set post deposited chained stake
raised mound of earth with pits as per
instructions for 1/4 sec cor.

79.96 The cor to sec. 19. 20. 29. 30.
Land rolling soil sandy 3rd rate.

West on a random line be-
tween sec. 19 and 30
Va 13°05' E.

40.00 Set post for temporary 1/4 sec cor.

79.55 Intersected West Boundary 22 lks
North of cor to sec. 19 and 30

N 27 N. R. 6 W.

From which cor. I run
N 89° 51' E on a true line between
sec.s 19 and 30
Va 13° 05' E.

39.58 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

79.58 The cor to sec.s 19. 20. 29. 30
Land gently rolling soil sandy 3° rate.

North between sec.s 19 and 20
Va 13° 05' E

40.00 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to sec.s 17. 18. 19. 20.
Land nearly level soil sandy 3° rate

East on a random line between

N 27 N. R. 6 W.

sec.s 17 and 20.
Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
80.10 Intersected North and South line 10 lks E of cor to sec.s 16. 17. 20. 21
from which cor. I run
N 89° 56' W on a true line between sec.s 17 and 20.
Va 13° 05' E.

40.05 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.10 The cor to sec.s 17. 18. 19. 20.
Land gently rolling soil sandy 3° rate.

West on a random line between
sec.s 18 and 19
Va 13° 05' E

40.00 Set post ~~for tem~~porary ¼ sec cor.
79.52 Intersected West Boundary 10 lks S of cor to sec.s 18 and 19 from which cor. I run

S 89°56' E. on a true line between sec.s 18 and 19.

Va 13°05' E.

39.52 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

79.52 The cor to sec 17. 18. 19. 20

Land gently rolling soil sandy 3rd rate

North between sec.s 17 and 18

Va 13°05' E

40.00 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to sec.s 7. 8. 17. 18

Land nearly level soil sandy 3rd rate

East on a random line between sec.s 8 and 17

Va 13°05' E.

40.00 Set post for temporary ¼ sec cor.

80.20 Intersected North and South line 14 lks North of cor to sec.s 8. 9. 16. 17. from which cor. I run

N 89°54' W on a true line between sec.s 8 and 17.

Va 13°05' E.

40.10 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.20 The corner to secs. 7. 8. 17. and 18

Land gently rolling soil sandy 3rd rate.

West on a random line between sec.s 7 and 18.

Va 13°05' E.

40.00 Set post for temporary ¼ sec cor.

79.36 Intersected West Boundary 24 lks S. of cor to sec.s 7 and 18. from which cor. I run

36
140

T. 27 N. R. 6 W.

S 89° 58' East on a true line between
sec.s 7 and 18.

Va 13° 05' E.

39.36 Set post deposited charred stake
raised mound of earth with pits as per
instructions for ¼ sec cor.

79.36 The cor to sec.s 7. 8. 17. 18
Land nearly level soil sandy 3rd rate.

North between sec.s 7 and 8

Va 13° 05' E.

40.00 Set post deposited charred stake
raised mound of earth with pits as per
instructions for ¼ sec cor.

80.00 Set post deposited charred stake
raised mound of earth with pits as per
instructions for cor to sec.s 5. 6. 7. 8.
Land gently rolling soil sandy 3rd rate.

East on a random line between
sec.s 5 and 8

Va 13° 05' E.

37
141

T. 27 N. R. 6 W.

40.00 Set post for temporary ¼ sec cor.
80.15 Intersected North and South line
30 lks S of cor to sec.s 4. 5. 8. 9
from which cor. I run
N. 89° 47' W. on a true line between
sec.s 5 and 8

Va 13° 05' E.

40.07½ Set post deposited charred stake
raised mound of earth with pits as per
instructions for ¼ sec cor.

80.15 The cor to sec.s 5. 6. 7. 8.
Land gently rolling soil sandy 3rd rate.

West on a random line between
sec.s 6 and 7.

Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor.
79.20 Intersected West Boundary 16 lks S.
of cor to sec.s 6 and 7. from which
cor. I run
S 89° 53' E. on a true line between
sec.s 6 and 7.

Va 13° 05' E

T 27 N. R. 6 W.

39.20 Set post deposited charred stakes raised mound South with pits as per instructions for ¼ sec cor
79.20 The cor to sec. 5. 6. 7. 8.
Land gently rolling soil sandy 3rd rate.

North on a random line between sec. 5 and 6

Va 13° 05' E.

40.00 Set post for temporary ¼ sec cor
80.98 Intersected North Boundary 10 lks E. of cor to sec. 5 and 6. from which cor. I run
S 0° 04' E. on true line between sec. 5 and 6.

Va 13° 05' E.

40.98 Set post deposited charred stakes raised mound South with pits as per instructions for ¼ sec cor
80.98 The cor to sec. 5. 6. 7. 8
Land gently rolling soil sandy 3rd rate

Sept 14th 1865.

General Description

The quality of this land in this Township is below the common average. The land is mostly rolling sandy soil of 2d and 3d rate quality and not well adapted to cultivation. There is no Timber. Water or Stone. with-in the Township

List of Names

A list of the names of the individuals employed to assist in running, measuring, or marking the lines and corners, described in the foregoing field notes of Township No 27 North of Range No 6 West of the 6th Principal Meridian, showing the respective capacities in which they acted

Merritt Howard, Chainman
Charles Stark, Chainman
James H. Holderby, Axman
Robert Rabe, Flagman

D L Made

Township No 28 North Range No 6 West of 6th P. M.

Contract No. 313

Field Notes
of the
Subdivision lines in Township 28 N. R 6 West of the 6th Principal Meridian surveyed by Robert Armstrong, deputy Surveyor, under joint Contract No 313, dated May 12th 1865 wherein H. C. F. Hackbusch and R. Armstrong are joint Contractors

Survey
Commenced September 2d 1865
Completed September 8th 1865

Ex'd N. & B. C.
Plotted Nov 3 B. C.
Copied J P S
Compd S. & B.

Names and duties of Assistants:

Merrit Howard, Chainman.
Charles Stark, Chainman.
James H. Holderby, Axman.
Robert Robe, Flagman.

Township 28 N. Range 6 W. 6 P. M.

6	37	5	28	4	21	3	15	2	8	1
36		35		27		20		14		7
7	35	8	27	9	20	10	13	11	7	12
34		34		26		19		13		6
18	33	17	26	16	19	15	12	14	5	13
33		32		25		18		12		5
19	32	20	24	21	18	22	11	23	4	24
31		30		24		17		10		4
30	30	29	23	28	16	27	10	26	3	25
30		29		22		16		9		2
31	29	32	22	33	15	34	8	35	1	36

T 28 N. R. 6 W.

To determine the proper adjustment of my compass for subdividing this Township. I commence at the corner to Townships 27 and 28 N. R. 5. and 6 W. and run North on a blank line along the East Boundary of Sec 36.

Va 13° 00' E.

40.03 To a point 22 lks East of ¼ Sec Cor. to Secs. 25 & 36

80.05 To a point 47 lks East of ~~Sec~~ Cor. 1

To retrace this line or run parallel thereto. my compass must be adjusted to a Va of 13° 20' E.

Subdivision commenced
Sept 2nd 1865.

From the cor to Sect. 1, 2, 35 & 36. on the South Boundary of the Township. I run.

North between Sect 35 and 36
Va 13° 20' E.

T. 28 N. R. 6 W.

40.00 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

73.00 Leave upland and enter bottom bears South W and South East.

80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to sec's 25. 26 35. 36.

Land nearly level soil 2nd rate.

East on a random line between sec's 25 and 36.

Va 13° 15' E.

4.15 A Slough 60 lks wide bears N W. com S W.

8.00 Leave bottom bears N W and S E.

40.00 Set post for temporary ¼ sec cor.

80.28 Intersected East Boundary 5 lks S. of cor to sec's 25 and 36. from which cor. I run

S 89° 58' W on a true line between

T 28 N. R. 6 W.

Sec's 25 and 36.

Va 13° 15' E.

40.14 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.28 The cor to Sec's 25. 26. 35. 36.

Land mostly rolling soil 2nd rate.

North between Sec's 25 and 26.

Va 13° 20' E.

6.50 A Slough 60 lks wide bears S W.

26.00 A slough 360 lks wide bears E N E and W S W.

40.00 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

46.50 Leave bottom land bears E and W.

80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to sec's 23. 24 25. 26.

Land. South 46½ Chains level bottom soil 1 rate. balance rolling 2nd rate.

East on a random line between
sec.s 24 and 25
Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor.
80.68 Intersected East Boundary of Lts
S. of cor to sec.s 24 and 25 from which
cor. I run
S 89° 58' W on a true line between
sec.s 24 and 25.
Va 13° 15' E.

40.34 Set post deposited charred stake
raised mound of earth with pits as per
instructions for ¼ sec cor.
80.68 The cor to sec.s 23. 24. 25. 26.
Land gently rolling soil 2° rate.

North between Sec.s 23 and 24
Va 13° 20' E.

40.00 Set post deposited charred stake
raised mound of earth with pits as per
instructions for ¼ sec cor.
80.00 Set post deposited charred stake

raised mound of earth with pits as
per instructions for cor to sec.s
13. 14. 23. 24
Land gently rolling sandy 3rd rate.

East on a random line between
sec.s 13 and 24
Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor.
80.54 Intersected East Boundary 14 Lks
North of cor to sec.s 13 and 24
from which cor. I run
N. 89° 54' W on a true line be-
tween sec.s 13 and 24
Va 13° 15' E.

40.25 Set post deposited charred stake
raised mound of earth with pits as per
instructions for ¼ sec cor.
80.50 The cor to sec.s 13. 14. 23. 24
Land gently rolling sandy soil 3 rate

North between sec.s 13 and 14.
Va 13° 24' E.

T 28 N. R. 6 W.

40.00	Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor
80.00	Set post deposited charred stake raised mound of earth with pits as per instructions for cor to sec's 11.12.13.14
	Land gently rolling sandy soil 3rd rate.

East on a random line between sec's 12 and 13.

Va 13° 15' E.

40.00	Set post for temporary ¼ sec cor.
80.82	Intersected East Boundary 20 lks N of cor to sec's 12 and 13 from which cor. I run
	N 89° 51' W on a true line between sec's 12 and 13.
	Va 13° 15' E
40.41	Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.
80.82	The cor to sec's 11. 12. 13. 14.

T 28 N. R. 6 W.

Land rolling sandy soil 3rd rate

North between sec's 11 and 12

Va 13° 30' E.

40.00	Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.
80.00	Set post deposited charred stake raised mound of earth with pits as per instructions for cor to sec's 1. 2. 11. 12.
	Land gently rolling soil sandy 3rd rate.

East on a random line between sec's 1 and 12.

Va 13° 15' E

40.00	Set post for temporary ¼ sec cor.
80.22	Intersected East Boundary 10 lks N of cor to sec's 1 and 12. from which cor. I run
	N 89° 56' W. on a true line between sec's 1 and 12.
	Va 13° 15' E.

8/157

T 28 N. R. 6 W.

40.11 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.22 The cor to sec^s 1. 2. 11. 12.
Land gently rolling Soil sandy 3rd rate

North on a true line between sec^s 1 and 2.

Va 13° 20' E.

40.00 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

X 82.70 Intersected 7th Standard Parallel North (East of the 17.18 chs.) Standard cor to sec^s 35 and 36.
There is a Sandstone 16 x 10 x 6. for close cor to sec^s 1 and 2.
Land gently rolling sandy 3rd rate.
Sept 2^d 1865.

North between sec^s 34 and 35

Va 13° 20' E.

40.00 Set post deposited charred stake raised mound of earth with pits as per.

9/158

T. 28. N. R. 6 W.

instructions for ¼ sec cor.

80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to sec^s 26. 27. 34 & 35.
Land nearly level Soil 2° rate

East on a random line between sec^s 26 and 35.

Va 13° 15' E.

23.00 Enter bottom bears N E & S W.

40.00 Set post for temporary ¼ sec cor.

68.00 To a Slough. 3 ½ lks wide contains very little water bears N N E & S S W.

72.50 A Slough 60 lks wide bears S W.

79.78 Intersected North and South line 15 lks S. of cor to sec^s 25. 26. 35. 36. from which cor. I run S 89° 54' W. on a true line between sec^s 26 and 35.

Va 13° 15' E.

39.89 Set post deposited charred stake

T 28 N. R. 6 W.

raised mound south with pits as per instructions for ¼ sec cor

79.78 The cor to Secs 26. 27. 34. 35

Land upland of soil 2° rate bottom land good rich soil 1 rate.

North between Secs 26 and 27.

Va 13° 20' E

40.00 Set post deposited charred stake raised mound south with pits as per instruction for ¼ sec cor.

80.00 Set post deposited charred stake raised mound with pits as per instructions for cor to Secs 22. 23 26. 27.

Land nearly level. Sandy 3 rate

East on a random line between Secs 23 and 26

Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor.

79.76 Inter sected North and South Line

T 28 N. R. 6 W.

10 lks S. of cor to Secs 23. 24. 25. 26. from which cor. I run S 89° 56' W. on a true line between Secs 23 and 26

Va 13° 15' E

39.88 Set post deposited charred stake raised mound south with pits as per instructions for ¼ sec cor.

79.76 The cor to Secs 22. 23 26. 27.

Land gently rolling soil sandy 2 rate.

North between Secs 22 and 23.

Va 13° 20' E.

40.00 Set post deposited charred stake raised mound south with pits as per instructions for ¼ sec cor.

80.00 Set post deposited charred stake raised mound with pits as per instructions for cor to Secs 14. 15 22. 23.

Land nearly level. Soil Sandy 3rd rate

T 28 N. R. 6 W.

East on random line between sec^s 14 and 23.

Va 13° 15' E

40.00 Set post for temporary ¼ sec cor.

79.80 Intersected North & South line at cor of sec^s of ~~sec^s~~ 13.14.23.24 from which cor. I run

West on a true line between sec^s 14 and 23.

Va 13° 15' E

39.90 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

79.80 The cor to sec^s 14.15.22.23.

Land gently rolling sandy 2° rate

North between sec^s 14 and 15

Va 13° 20' E

40.00 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.00 Set post deposited charred stake

T 28 N. R. 6 W.

raised mound of earth with pits as per instructions for cor to sec^s 11.11 14 and 15.

Land gently rolling soil sandy 2° rate

East on a random line between sec^s 11 and 14.

Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor.

79.46 Intersected North and south line 11 lks N of cor to sec^s 11.12.13.14 from which cor. I run

N 89° 55' W. on a true line between sec^s 11 and 14

Va 13° 15' E.

39.73 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor

79.46 The cor to sec^s 10.11.14.15

Land gently rolling soil sandy 3° rate

North between sec^s 10 and 11

Va 13° 20' E.

14/163

T 28 N. R. 6 W.

40.00	Set post deposited charred stake raised mound 7 each with pits as per instructions for ¼ sec cor.
80.00	Set post deposited charred stake raised mound 7 each with pits as per instructions for cor to sec 2.3. 10.11. Land rolling sandy 3rd rate.

East on random line between sec 2 and 11.

Va 13° 15' E.

40.00	Set post for temporary ¼ sec cor.
79.90	Intersected North and south line 31 lks E of cor to sec 1. 2. 11. 12. from which cor. I run N 89.4 ½ W. on a true line between secs 2 and 11

Va 13° 15' E.

39.95	Set post deposited charred stake raised mound 7 each with pits as per instructions for ¼ sec cor.

15/164

T 28 N. R. 6 W.

79.90	The cor to sec 1. 2. 11. 12. Land gently rolling soil 2nd rate

North on a true line between sec 1. 2 and 3.

Va 13° 20' E.

40.00	Set post deposited charred stake raised mound 7 each with pits as per instruction for ¼ sec cor.
82.66	Intersected 7th Standard Parallel North 16.70 chs East of Standared cor. to sec 34 and 35. There Set Sandstone 4 x 12 x 6. for closing cor to sec 2 and 3. Land rolling soil 2nd rate Sept 4th 1865

North between sec 33 and 34.

Va 13° 20' E.

40.00	Set post deposited charred stake raised mound 7 each with pits as per instructions for ¼ sec cor
80.00	Set post deposited charred stake raised mound 7 each with pits as per.

instructions for cor to secs. 27. 28
33. 34.
Land nearly level sandy 2d rate

East on a random line between
secs. 27 and 34
Va 13°15' E.

40.00 Set post for temporary 1/4 sec cor
79.92 Intersected North and South line
at cor. to secs. 26. 27. 34. 35 from
which cor I run.
West on a true line between
secs. 27. and 34
Va 13°15' E.

39.96 Set post deposited charred stake
raised mound with pits as per
instructions for 1/4 sec cor.
79.92 The cor to secs. 27. 28. 33. 34.
Land nearly level 2nd rate

North between secs 27 and 28.
Va 13°20' E.

40.00 Set post deposited charred stake
raised mound of earth with pits as per
instructions for 1/4 sec cor.
80.00 Set post deposited charred stake
raised mound of earth with pits as per
instructions for cor to secs. 21. 22
27. 28.
Land gently rolling soil 2nd rate.

East on a random line between
secs. 22 and 27.
Va 13°15' E.

40.00 Set post for temporary 1/4 sec cor.
79.72 Intersected North and South line
20 lks N of cor to secs. 22. 23. 26. 27
from which cor. I run
N 89°51' W. on a true line between
secs. 22 and 27.
Va 13°15' E.

39.86 Set post deposited charred stake
raised mound of earth with pits as per
instructions for 1/4 sec. cor.

T 28 S. R. 6 W.

79.72 The cor. to sec.s 21. 22. 27 28.
Land rolling gently sil sandy 3rd rate.

North between sec.s 21 and 22.
Va 13° 20' E.

40.00 Set post deposited chared stake raised mound of earth with pits as per instructions for ¼ sec cor.
80.00 Set post deposited charred stake raised mound with pits as per instructions for cor to sec.s 15. 16 21. 22.
Land gently rolling sandy 3rd rate

East on a random line between sec.s 15. and 22.
Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor.
79.38 Intersected north and south line on the S. of cor to sec.s 14. 15 22 23.
From which cor. I run
S 89° 56' W. on a true line between

T 28 S. R. 6 W.

sec.s 15 and 22.
Va 13° 15' E.

39.69 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.
79.38 The cor to sec.s 15. 16. 21. 22
Land nearly level sandy 3rd rate

North between sec.s 15 and 16
Va 13° 30' E.

40.00 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.
80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to sec.s 9. 10 15. 16.
Land nearly level sandy soil 2d. rate.

East on a random line between sec.s 10 and 15.
Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor.

T 28 N. R. 6 W.

79.78 Intersected North and South line 11 lks N of cor to secs 10. 11. 14. 15. from which cor. I run N 89° 56' W. on a true line between secs 10 and 15

Va 13° 15' E.

39.89 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

79.78 The cor to secs 9. 10 15. 16.
Land rolling: Soil 2° rate

North between secs 9 and 10.

Va 13° 30' E.

40.00 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to secs 3. 4. 9. 10.
Land rolling soil 2° rate.

East on a random line between

T 28 N. R. 6 W.

secs 3 and 10

Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor.

79.82 Intersected North and South line 12 lks N. of cor to secs 2. 3. 10. 11 from which cor. I run N 89° 55' W. on a true line between secs 3 and 10.

Va 13° 15' E.

39.91 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

79.82 The cor to secs 3. 4. 9. 10.
Land rolling Sandy 3rd rate.

North on a true line between secs 3 and 4.

Va 13° 30' E

28.70 Drain containing pools of water bearing N. W.

40.00 Set post deposited charred stake raised mound of earth with pits as per

T 28 N. R. 6 W.

instructions for ¼ sec cor.

+ 82.76 Intersected 7th Standard Parallel North 17.10 chs East of Standard cor. to secs 33 and 34. Set post and deposited charred stake raised mound of earth with pits as per instructions for closing cor to secs 3 and 4

Land rolling soil 2c. rate.

Sept 6th 1865.

North between secs 32 and 33

Va 13°25' E.

40.00 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.00 Set post deposited charred stake raised mound with pits as per instructions for cor to secs 28. 29. 32. 33.

Land level soil 2c. rate.

East on a random line between secs 28 and 33.

Va 13°15' E.

T 28 N. R. 6 W.

40.00 Set post for temporary ¼ sec cor.

79.86 Intersected North and South line 26 lks N. of cor to sec 27 28. 33. 34. from which cor. I run N 89°49' W. on a true line between secs 28 and 33.

Va 13°15' E.

39.93 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

79.86 The cor to secs 28. 29. 32. 33.

Land nearly level soil 2c. rate

North between secs 28 and 29.

Va 13°30' E.

40.00 Set post deposited charred stake raised mound of earth with pits as per instructions for ¼ sec cor.

80.00 Set post deposited charred stake raised mound of earth with pits as per instructions for cor to sec 20. 21 28. 29.

T 28 N. R. 6 W.

Land level Sandy 3rd rate.

East on a random line between
sec.s 21. and 28

Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor.
80.16 Intersected North and South line
30 lks N of cor to secs 21. 22. 27. 28.
from which cor. I run
N 89° 47' W. on a true line between
sec.s 21 and 28.

Va 13° 15' E

40.08 Set post deposited chained stake
raised mound with pits as per
instructions for ¼ sec cor.
80.16 The cor to secs. 20. 21. 28. 29.
Land nearly level Soil 2nd rate.

North between sec.s 20. and 21

Va 13° 30' E

40.00 Set post deposited chained stake
raised mound with pits as per
instructions for ¼ sec cor
80.00 Set post deposited chained stake
raised mound with pits as per
instructions for cor to sec.s 16. 17
21. 21.
Land nearly level ~~Land~~ 3rd rate.

East on a random line between
sec.s 16 and 21.

Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor.
80.22 Intersected North and South line
28 lks N of cor to secs 15. 16. 21. 22
from which cor. I run
N 89° 48' W. on a true line between
secs. 16 and 21.

Va 13° 15' E.

40.11 Set post deposited chained stake
raised mound with pits as per
instructions for ¼ sec cor.
80.22 The cor to secs. 16. 17. 20. 21.
Land surface broken sandy 3rd rate.

T 28 N. R. 6 W.

T 28 S. R. 6 W.

North between sec.s 16 and 17.
Va 13° 30' E.

40.00 Set post deposited chained stake raised mound south with pits as per instructions for ¼ sec cor.

80.00 Set post deposited chained stake raised mound south with pits as per instructions for cor to sec.s 8. 9. 16. 17.
Land nearly level soil 2nd rate

East on a random line between sec.s 9 and 16
Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor.

79.90 Intersected North and South line 22 lks S of cor to sec.s 9. 10. 15. 16 from which cor. I run S. 89° 51' W. on a true line between sec.s 9 and 16
Va 13° 15' E.

39.95 Set post deposited chained stake

T 28 S. R. 6 W.

raised mound south with pits as per instructions for ¼ sec cor.

79.90 The cor to sec.s 8. 9. 16. 17.
Land gently rolling soil gravelly 3rd rate.

North between sec.s 8 and 9.
Va 13° 30' E.

40.00 Set post deposited chained stake raised mound south with pits as per instructions for ¼ sec cor.

80.00 Set post deposited chained stake raised mound with pits as per instructions for cor to sec.s 4. 5. 8. 9
Land rolling soil 2nd rate

East on a random line between sec.s 4 and 9
Va 13° 15' E.

40.00 Set Limestone Stone for temporary ¼ sec cor

79.84 Intersected North and South line 20 lks S of cor to sec.s 3. 4. 9. 10

From which cor. I run
N 89°51' W. on a true line between
secs. 4 and 9.
Va 13°15' E.

39.92 Set Limestone 16 x 8 x 5 for quarter
section corner

79.84 The cor to secs. 4. 5. 8. 9.
Land rolling soil sandy 3rd rate

North on a true line between
secs 4 and 5.
Va 13°30' E.

40.00 Set post deposited charred stake
raised mound of earth with pits a per
instructions for ¼ sec cor.

78.05 Branch 5 lks wide runs W. N W.

X 83.53 Intersected 7th Standard Parallel North 17.36 chs East of
Standard cor to sec 32 and 33.
Set post deposited charred stake
raised mound with pits as per.
for closing cor to secs. 4 and 5.

Land rolling soil 2nd rate

North between secs 31 and 32
Va 13°30' E.

40.00 Set Limestone 14 x 9 x 7 for ¼ sec cor
80.00 Set Lime stone 20 x 8 x 7 for cor to secs
29. 30. 31. 32.
Land level and sandy 2d rate

East on a random line between
secs 29 and 32.
Va 13°15' E.

40.00 Set post for temporary ¼ sec cor.
80.68 Intersected North and South line
24 lks N of cor to secs. 28. 29. 32. 33
from which cor. I run
N 89°50' W on a true line between
secs. 29 and 32
Va 13°15' E.

40.34 Set Limestone 15 x 8 x 6 for ¼ sec cor.
80.68 The cor to sec 29. 30. 31. 32
Land surface broken sandy 3rd rate.

West on a random line between
Sec.s 30 and 31.
Va 13° 15' E

40.00 Set post for temporary ¼ sec cor.
78.30 Intersected West Boundary 20 lks S.
of cor to Sec.s 30 and 31. from which
cor. I run
S 89° 30' E. on a true line between
Sec.s 30 and 31.
Va 13° 15' E

38.30 Set Limestone 17 x 8 x 5 for ¼ sec cor.
78.30 The cor to Sec.s 29. 30. 31. 32.
Land level soil 2° rate

North between Sec.s 29 and 30.
Va 13° 30' E

40.00 Set Limestone 17 x 9 x 5 for ¼ sec cor.
80.00 Set Limestone 18 x 10 x 3 for cor to Sec.s
19. 20. 29. 30.
Land nearly level soil 2° rate

East on a random line between

Sec.s 20 and 29
Va 13° 15' E

40.00 Set post for temporary ¼ sec cor.
80.64 Intersected North and South line
20 lks N of cor to Sec.s 20. 21. 28. 29
from which cor. I run
N 89° 51' W on a true line between
Sec.s 20 and 29.
Va 13° 15' E.

40.32 Set Limestone 12 x 11 x 8 for ¼ sec cor.
80.64 The cor to Sec 19. 20. 29 30
Land nearly level soil 2° rate

West on a random line between
Sec.s 19 and 30.
Va 13° 15' E

40.00 Set post for temporary ¼ sec cor.
78.80 Intersected West Boundary 16 lks
S of cor to Sec.s 19 and 30 from
which cor. I run
S 89° 57' E on a true line between
Sec.s 19 and 30
Va 13° 15' E.

T 28 N. R. 6 W.

38.10	Set Limestone 14 x 9 x 7 for ¼ sec cor.
78.10	The cor to sec^{s} 19. 20. 29. 30.
	Land gently rolling soil 2^{d} rate

North between Sec^{s} 19 and 20.
Va 13° 30' E.

40.00	Set Limestone 17 x 9 x 8 for ¼ sec cor.
80.00	Set Limestone 16 x 9 x 7 for cor to sec^{s} 17. 18. 19. 20
	Land nearly level soil 2^{d} rate

East on a random line between Sec^{s} 17 and 20
Va 13° 15' E

40.00	Set post for temporary ¼ sec cor.
80.70	Intersected North and South line 38 lks S of cor to sec^{s} 16, 17. 20. 21 from which cor. I run S 89° 44' W on a true line between sec^{s} 17 and 20
	Va 13° 15' E
40.35	Set Limestone 12 x 12 x 5 for ¼ sec cor.

T 28 N. R. 6 W.

80.70	The cor to sec^{s} 17. 18. 19. 20.
	Land gently rolling soil 2^{d} rate

West on a random line between sec^{s} 18 and 19.
Va 13° 15' E

40.00	Set post for temporary ¼ sec cor
76.86	Intersected West Boundary 42 lks S of cor to sec^{s} 18 and 19. from which cor I run S 89° 42' E on a true line between sec^{s} 18 and 19
	Va 13° 15' E
36.86	Set Limestone 14 x 10 x 5 for ¼ sec cor
76.86	The cor to sec^{s} 17. 18. 19. 20.
	Land gently rolling soil 2^{d} rate

North between Sec^{s} 17 and 18.
Va 13° 30' E

40.00	Set Limestone 14 x 9 x 7 for ¼ sec cor
80.00	Set Limestone 18 x 12 x 6 for cor to sec^{s} 7. 8. 17. 18.

Land level soil 2° rate

East on a random line between sec^s 8. 17.

Va 13° 15' E.

40.00 Set post for temporary ¼ sec cor
80.66 Intersected North and South line 36 lks N of cor to sec^s 8. 9. 16. 17 from which cor I run
N 89° 45' W on a true line between sec^s 8 and 17

Va 13° 15' E

40.33 Set Limestone 15 x 10 x 7 for ¼ sec cor.
80.66 The cor to sec^s 7. 8. 17. 18.
Land rolling 2° rate

West on a random line between sec^s 7 and 18

Va 13° 15' E

40.00 Set post for temporary ¼ sec cor.
76.18 Intersected W. Boundary 24 lks S of cor to sec^s 7 and 18 from which

cor. I run
S 89° 50' E on a true line between sec 7 and 18

Va 13° 15' E

36.18 Set Limestone 16 x 8 x 6 for ¼ sec cor.
76.18 The cor to sec^s 7. 8. 17. 18
Land gently rolling soil 2° rate

North between sec^s 7 and 8

Va 13° 30' E

40.00 Set Limestone 14 x 8 x 7 for ¼ sec cor
80.00 Set Limestone 14 x 8 x 6 for cor to sec^s 5. 6. 7. 8
Land gently rolling soil 2° rate

East on a random line between sec^s 5 and 8

Va 13° 15' E

40.00 Set post for temporary ¼ sec cor.
80.46 Intersected North and South line 12 lks N of cor to sec^s 4. 5. 8. 9 from which cor. I run

T 28 N. R. 6 W

N 89° 55' W on a true line between
sec° 5 and 8
Va 13° 15' E
40.23 Set Limestone 16 x 8 x 5 for ¼ sec cor
80.46 The cor to sec° 5. 6. 7. 8
Land gently rolling soil 2° rate

West on a run down line between
sec! 6 and 7
Va 13° 15' E
40.00 Set post for temporary ¼ sec cor
75.61 Intersected West Boundary 12 lks
S of cor to sec 6 and 7 from
which cor. I run
S 89° 55' E on a true line between
sec° 6 and 7
Va 13° 15' E
35.61 Set Limestone 17 x 12 x 5 for ¼ sec cor.
75.61 The cor to sec! 5. 6. 7 8
Land nearly level sandy 2° rate

T 28 N. R. 6 W.

on a true line
North between sec! 5 and 6
Va 13° 30' E
40.00 Set Limestone 12 x 10 x 8 for ¼ sec cor
84.00 Intersected 7th Standard Parallel 17.42 chains
E of Standard Corner to secs. 31 & 32
at which point I set a Limestone
14 x 10 x 4½ inches for C. C. to
secs. 5 and 6
Land rolling soil 3d rate
Sept. 8th 1865

General Description
This Township contains a large
amount of good 2nd rate land
there is some 3rd & 2 rate land which
is not very well adapted to farm-
ming
We found no water in the
Township except on the line
between sec! 3 and 4 and between
4 and 5 where a branch 5 lks
wide. Which contains good clear
water. runs N. W. into Township

29. N. I found a very good quality of Limestone in Sec 4.

List of Names.

A list of the names of the individuals employed to assist in running, measuring or marking the lines and corners described in the foregoing field notes of Township No. 28 North of the Base Line of Range No. 6 West of the 6th P. M., showing the respective capacities in which they acted:

Merit Howard,	Chainman
Charles Stark,	Chainman
James H. Holderby,	Axman
Robert Rabel,	Flagman.

General Land Office • Original Field Notes

Book Number

327

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.
