General Land Office • Original Field Notes

Book Number

361

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.

Index Diagram

Town 25 N. R. 10 W

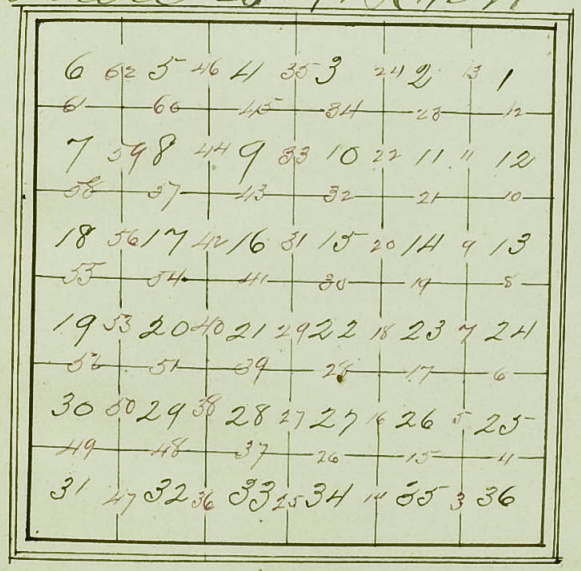

(a.)

T 25-28 N
R 10 W

Field Notes

of the Subdivisional lines of Township No 25 N. Range 10 West of the 6th Principal Meridian in the State of Nebraska, Surveyed by James N. Paul Deputy Surveyor under joint Contract No 32 bearing date the 4th day of August AD 1870, wherein Nicholas J. Paul and James N. Paul are joint Contractors with Robert R Livingston United States Surveyor General for the District of Iowa and Nebraska.

Survey Begun, Sept 20th 1870

Survey finished, Sept 24th 1870

Names and duties of Assistants

Robert Harvey,	Chainman
Lot C. Griffith,	Chainman
Bevington H. Savage,	Cornerman
Daniel Livingston,	Cornerman
Walter Lawrence,	Flagman

(B.)

To determine the proper adjustment of my Compass for subdividing this Township I begin at the corner to Townships 25 North Ranges 9 and 10 W. and run North on a blank line along the East Boundary of sec. 36 Va 13° 12' E.

39.98 To a point 7 lks west of the 1/4 sec. cor

79.99 To a point 14 lks west of the corner to secs 25 and 36.

To retrace this line or run parallel thereto, my Compass must be adjusted to a Variation of 13° 06' E

Subdivision Commenced September 20th 1870

T. 25 N. R. 10 W. 6th P. M.

From the Standard corner to secs. 35 and 36 on the South Boundary I run North between Secs. 35 and 36 Va. 13° 06' E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

76.00 Leave level plain and enter Sandhills bearing NW & SE.

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to secs. 25, 26, 35 & 36

Land level firstrate, except last 4 chains which is Sandy 3d rate

T 25 N. R. 10 W 6th P M

East on random line between
Secs 25 and 36
Va. 13°06' E

4000 Set temporary M Sec. Cor.

7996 Intersected East Boundary 5 lks North of the corner to secs 25 and 36 from which corner I run

N 89°58' West on true line between secs 25 and 36
Va. 13°06' E

3998 Set post deposited chamd stake and raised mound of earth with pits as per instructions for 1/4 sec cor

7996 The corner to secs 25, 26, 35 and 36
Rolling Sand hills
Soil Thirdrate

T 25 N. R. 10 W 6th P M

North between secs 25 and 26
Va. 13°06' E

4000 Set post deposited chamd stake and raised mound of earth with pits as per instructions for 1/4 Sec cor.

8000 Set post deposited chamd stake and raised mound of earth with pits as per instructions for corner to sections 23, 24, 25 and 26
Land rolling Sandy
Soil Thirdrate

T 25 N R 10 W 6th P M

East on random line
between secs 24 and 25
va, 13°06'E.

35.00 Leave Sand hills and enter level plain bears NW and SE

40.00 Set temporary 1/4 sec cor

66.50 Drain course SE.

79.98 Intersected East Boundary 8 lks South of the corner to secs 24 and 25 from which corner I run

S89°57' West on true line
between secs 24 & 25
va. 13°06'E

39.99 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec cor

79.98 The corner to sections 23, 24, 25 and 26 ~~1/4~~ 35 chains Sandy Thirdrate —
Balance firstrate

T 25 N R 10 W 6th P M

North between Secs 23 & 24
va, 13°06'E

9.00 Leave Sand hills and enter level plain bears E & W

32.00 Drain course East

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec cor

57.00 Leave plain and enter Sand hills bearing E & SW

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 13, 14, 23 and 24
Plain level firstrate
Balance Sandy
Soil Third rate

T. 25 N. R. 10 W 6th P.M.

East on random line
between Secs 13 & 24
Va. 13°06' E

40.00 Set temporary 1/4 Sec. cor.
80.04 Intersected East Boundary
10 lks South of the corner
to sections 13 and 24 from
which corner I run
S 89°56' West on true line
between Secs 13 & 24
Va. 13° 06' E

40.02 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. Cor.
80.04 The corner to sections
13, 14, 23 and 24
Rolling Sandhills
Soil Thirdrate

T. 25 N. R. 10 W 6th P.M.

North between Secs. 13 and 14
Va. 13°06' E

40.00 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for 1/4 sec cor.
80.00 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for corner
to secs 11, 12, 13 and 14
Rolling Sandhills
Soil Thirdrate

T. 25 N. R. 10 W 6th PM

East on random line
between secs. 12 & 13
Va, 13°06'E

4000 Set post ~~deposited chaned~~
~~stake and raised mound~~
~~of earth with pits as~~
~~per instructions for~~
temporary 1/4 sec cor, ~~temporary~~

79.98 Intersected East Boundary
4 lks South of the corner to
secs 12 and 13 from which
Corner I run
S 89°58' West on true line
between secs 12 & 13
Va, 13°06'E

39.99 Set post deposited chaned
stake and raised mound
of earth with pits as
per instructions for
1/4 sec cor,

79.98 The corner to sections
11, 12, 13 and 14
Rolling Sandhills
Soil Thurdrate

T. 25 N. R. 10 W 6th PM

North between secs 11 & 12
Va, 13°06'E

4000 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec Cor,

8000 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for corner
to sections 1, 2, 11 and 12
Land rolling sandhills
Soil. Thurdrate

T. 25 N R 10 W 6th P.M.

East on random line
between Secs 1 and 12
Va, 13° 06' E.

4000 Set temporary 1/4 sec cor.

80.06 Intersected East Boundary
5 lks North of the corner
to secs. 1 and 12 from which
corner I run
N 89° 58' West on true line
between secs. 1 & 12
Va, 13° 06' E.

40.03 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.

80.06 The corner to sections
1. 2. 11 and 12
Rolling Sand hills
Soil Thirdrate

T. 25 N R 10 W 6th P.M.

North on random line
between secs 1 and 2
Va, 13° 06' E

4000 Set temporary 1/4 sec cor.

7000 Leave sand hills and enter Bottom NE & SW.

79.96 Intersected North Boundary
8 lks West of the corner to
secs 1 and 2 from which
corner I run
S 3' W on true line
between secs 1 and 2
Va, 13° 06' E

39.96 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.

79.96 The corner to secs
1. 2. 11 and 12
Rolling Sand hills, 10 chs. of good, bottom except
Soil Thirdrate

September 25th 1870

T 25 N R 10 W 6th P M

North between Secs 34 & 35
Va, 13°06' E

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec cor,

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 26, 27, 34 and 35
Land level
Soil firstrate

T 25 N R 10 W. 6th P M

East on random line between Secs 26 and 35'
Va, 13°06' E

4000 Set temporary 1/4 sec cor

7700 Leave Plain and enter Sand hills bearing NW & SE,

8014 Intersected N & S. line 20 lks North of the corner to secs 25, 26, 35 & 36 from which corner I run
N 89°51' West on true line between secs 26 & 35
Va, 13°06' E

4007 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec cor,

8014 The corner to secs. 26, 27, 34 and 35
Land level
Soil firstrate

T. 25 N. R. 10 W. 6th P.M.

North between Secs. 26 & 27
Va. 13°06'E

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

60.00 Leave Plain and enter Sand hills bearing NW & SE.

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 22, 23, 26 & 27
Plain first rate
Balance third rate

T. 25 N R 10 W 6th P.M.

East on a random line between secs 23 and 26
Va. 13°06'E

4000 Set temporary 1/4 sec cor

8006 Intersected N & S line 32 lks North of the corner to secs 23, 24, 25 and 26 from which Corner Drum
N 89°46' West on true line between secs 23 and 26
Va. 13°06'E

4003 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

8006 The corner to sections 22, 23, 26 and 27
Gently Rolling
Soil Second rate

T. 26 N. R. 10 W. 6th P.M.

North between secs. 22 & 23
Va. 13°06' E

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 14, 15, 22 & 23
Land gently rolling
Soil Second rate

T. 25 N. R. 10 W. 6th P.M.

East on random line between secs 14 and 23
Va. 13°06' E

4000 Set temporary 1/4 sec. cor

8006 Intersected N. & S. line 8 chs North of the corner to secs 13, 14, 23 & 24 from which corner Iron
N 89°57' West on true line between secs. 14 & 23
Va. 13°06' E.

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

8006 The corner to secs 14 15, 22 and 23
Rolling Sandhills
Soil Third rate

T. 25 N., R 10 W 6th PM

North between secs 14 & 15
Va, 13°06' E

4000 Set post deposited chard stake and raised mound of earth with pits as per instructions for 1/4 sec cor,

8000 Set post deposited chard stake and raised mound of earth with pits as per instructions for corner to secs 10, 11, 14 and 15
Rolling Sandhills
Soil Thirdrate

T. 25 N., R 10 W 6th PM

East random line
between secs. 11 & 14
Va, 13°06' E

4000 Set temporary 1/4 sec. cor.

8000 Intersected N & S line 10 lks North of the corner to secs 11, 12, 13 and 14 from which
Corner Drum
N 89°56' West on true line
between secs. 11 and 14
Va 13°06' E

4000 Set post deposited chard stake and raised mound of earth with pits as per instructions for 1/4 sec cor

8000 The corner to secs, 10, 11, 14 & 15
Rolling Sandhills
Soil Thirdrate

T. 25 N. R 10 W. 6th PM

North between Secs 10 & 11
Va. 13° 06' E
4000 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.
8000 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for corner
to sections 2, 3, 10 & 11
Land Rolling
Soil Sandy Third rate

T. 25 N R 10 W 6th PM

East on random line
between Secs 2 & 11
Va. 13° 06' E
4000 Set temporary 1/4 sec. cor
8006 Intersected N & S line
12 lks North of the corner to
Secs 1, 2, 11 and 12 from
which corner a true
N 89° 55' West on true line
between Secs 2 & 11
Va 13° 06' E
4003 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.
8006 The corner to secs. 2, 3
10 and 11
Rolling Sandhills
Soil Third rate

T. 25 N. R. 10 W. 6th P.M.

North on random line between secs 2 & 3
Va 13°06' E

4000 Set temporary 1/4 sec cor,
80.00 Intersected North boundary 4 lks East of the corner to secs 2 and 3 from which corner I run S. 2' East on true line between secs 2 & 3
Va 13°06' E,

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec cor

8000 The corner to secs 2, 3, 10 and 11

Rolling Sandhills
Soil Third rate
September 21st 1870

T. 25 N. R. 10 W. 6th P.M.

North between secs 33 & 34
Va. 12°54' E

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor.

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to secs. 27, 28, 33 & 34
Land level.
Soil rich black loam
firstrate producing
heavy grass

T. 25 N. R 10 W 6th PM

East between Secs 27 & 34
Va. 12° 57' E

40.00 Set temporary 1/4 sec. cor.
79.94 Intersected N & S line 30th
South of the corner to secs
26, 27, 34 and 35 from
which corner I run
S 89° 47' West on the line
between secs. 27 & 34
Va. 12° 57' E

39.97 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. Cor.
79.94 The corner to sections
27, 28, 33 and 34
Land level
Soil Rich firstrate

T 25 N R 10 W 6th PM

North between secs 27 & 28
Va. 12° 57' E

40.00 Set post deposited charred
stake and raised mound of
earth with pits as per
instructions for 1/4 sec. Cor.
80.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for corner
to secs. 21, 22, 27 and 28
Land level
Soil Rich firstrate

T. 25 N. R 10 W 6th PM

East on random line
between secs 22 & 27
Va 13° 06' E

4000 Set temporary 1/4 sec. cor.
4600 Leave level Plain and
enter sandhills bear NW & SE
8008 Intersected N & S line 16 chs
North of the corner to secs
22, 23, 26 and 27 from
which corner Drum
N. 89° 53' West on true line
between secs. 22 & 27
Va. 13° 06' E
4004 Set post deposited chamd
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.
8008 The corner to secs 21
22, 27 and 28
Sand hills Thirdrate
Plain level first rate

T. 25 N. R 10 W 6th PM

North between secs. 21 and 22
Va. 13° 06' E
4000 Set post deposited chamd
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.
4200 Leave Plain and enter Sand
hills bearing NW and SE
8000 Set post deposited chamd
stake and raised mound
of earth with pits as per
instructions for corner
to secs 15, 16, 21 and 22
Plain level rich first rate
Balance sandy Thirdrate

T. 25 N. R 10 W 6th PM

East random line
between secs 15 & 22
Va, 13° 06' E

4000 Set temporary 1/4 sec cor,
80,04 Intersected N & S line 15 lks
North of the corner to secs
14, 15, 22 & 23 from
which corner I run
N 89° 54' West on true line
between secs. 15 & 22
Va. 13° 6 ~~45~~' E

4,002 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
sec. Cor.

80,04 The corner to secs
15-16, 21 and 22
Rolling Sandhills
Soil Thirdrate

T 25 N. R 10 W 6th PM

North between secs 15 & 16
Va, 13° 06' E

4000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec
cor

8000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for corner
to sections 9, 10, 15 & 16
Rolling Sandhills
Soil Thirdrate

T. 25 N. R. 10 W. 6th P.M.

East on random line
between secs 10 & 15
Va. 13° 09' E

40.00 Set temporary 1/4 Sec cor
80.10 Intersected N. & S. line 30
lks North of the corner to
secs 10, 11, 14 and 15 from
which corner Town
N 89° 24' W Weston true line
between secs 10 & 15
Va 13° 09' E

40.05 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec cor.

80.10 The corners to secs
9, 10, 15 & 16
Rolling Sandhills
Soil Thirdrate

T. 25 N. R. 10 W. 6th P.M.

North between Secs. 9 & 10
Va 13° 09' E

40.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec
cor

80.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for corner
to sections 3, 4, 9 & 10
Rolling Sandhills
Soil Thirdrate

T. 25 N R 10 W 6th PM

East on random line
between Secs. 3 & 10
va. 13° 09' E
4000 Set temporary 1/4 sec cor.
79.98 Intersected N & S line 14
lks North of the corner to
secs. 2, 3, 10 & 11 from which
corner S run
N 89° 54' West on true line
between secs 3 & 10
va 13° 09' E
39.99 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec cor.
79.98 The corner to sections
3. 4. 9 and 10
Rolling Sandhills
Soil. Thirdrate

T 25 N R 10 W 6th PM

North on random line between
Sections 3 and 4
va. 13° 09' E.
4000 Set temporary 1/4 sec cor.
60.00 Leave Sandhills and enter Cache Cr.
Bottom bears NE and SW
80.02 Intersected North Boundary
6 lks West of the corner to
secs. 3 and 4 from which
corner S run
South 3' W. on true line
between secs 3 & 4
va. 13° 09' E
40.02 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 sec cor
80.02 The corner to secs
3, 4, 9 and 10
Sandhills Thirdrate
Balance firstrate

September 22nd 1870

T. 25 N. R. 10 W 6th P M

North between Secs 32 & 33
Va. 12° 54' E

40.00 Set post deposited chand stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor.

80.00 Set post deposited chand stake and raised mound of earth with pits as per instructions for corner to sections 28, 29, 32 and 33

Land level.
Soil first rate black loam
very heavy thick grass

T. 25 N. R 10 W 6th P M

East on random line
between secs 28 & 33
Va 12° 57' E

40.00 Set temporary 1/4 sec cor

80.10 Intersected N & S line 2 links South of the corner to secs 27, 28, 33 and 34 from which corner I run S 89° 50' West true line between Secs 28 & 33
Va. 12° 57' E

40.05 Set post deposited chand stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

80.10 The corner to secs 28, 29, 32 and 33
Land level
Soil first rate

T. 25 N. R. 10 W. 6th P.M.

North between Secs 28 & 29
Va. 13° 57' E

4000 Set post deposited chand stake and raised mound of earth with pits as per instructions for 1/4 Sec cor.

8000 Set post deposited chand stake and raised mound of earth with pits as per instructions for corner to sections 20, 21, 28, 29
Land level
Soil firstrate

T. 25 N. R. 10 W. 6th P.M.

East on random line
between Secs 21 and 28
Va. 13° 06' E

4000 Set temporary 1/4 Sec cor.

8.06 Intersected N & S line 12 chs North of the corner to secs 21, 22, 27 and 28 from which corner I run N 89° 55' West on true line between Secs 21 & 28
Va. 13° 06' E

4.00 Set post deposited chand stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

8.06 The corner to secs 20, 21, 28 & 29
Land level
Soil rich firstrate

T. 25 N. R 10 W. 6th PM.

North between Secs 20 & 21
Va. 13° 06' E

31.00 Leave level Plain and enter sand hills bearing E & W.

40.00 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

80.00 Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to sections 16. 17. 20 & 21
Plain level, first rate
Balance Rolling Sandy third rate

T. 25 N. R 10 W 6th PM

East on random line between Secs. 16 and 21
Va. 13° 06' E

40.00 Set temporary 1/4 sec. cor.

80.00 Intersected N & S line at the corner to secs 15. 16 21 and 22 from which corner I run
West on true line between Secs 16 & 21
Va. 13° 06' E

40.00 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

80.00 The corner to sections 16. 17. 20 and 21
Low Sandhills
Soil third rate

T. 25 N. R 10 W 6th P.M.

North between Secs 16 and 17
Va 13°06' E

4000 Set post deposited chamd stake and raised mound of earth with pits as per instructions for 1/4 Sec cor.

8000 Set post deposited chamd stake and raised mound of earth with pits as per instructions for corner to secs. 8, 9, 16 and 17
Rolling Sand hills
Soil Thirdrate

T 25 N. R. 10 W 6th PM

East on random line
between secs 9 and 16
Va. 13° 06' E

4000 Set temporary 1/4 sec cor

8014 Intersected W'rly line 10 lks South of the corner to secs 9, 10, 15 and 16 from which corner I view
S 89° 56' West on true line
between secs 9 and 16
Va. 13° 06' E

14007 Set post deposited chamd stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

8014 The corner to secs 8, 9, 16 and 17
Land Sand hills
Soil Thirdrate

T. 25 N. R. 10 W 6th P.M.

North between Secs 8 and 9
Va. 13° 06' E

4000 Set post deposited chamd stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

8000 Set post deposited chamd stake and raised mound of earth with pits as per instructions for corner to sections 4, 5, 8 and 9
Rolling Sand hills
Soil Third rate

T. 25 N. R. 10 W 6th P.M.

East on random line between Secs 4 & 9
Va. 13° 09' E

4000 Set temporary 1/4 Sec cor.

79.94 Intersected N. & S. line 80 lks North of the corner to secs 3, 4, 9 and 10 from which corner I run
N 89° 57' West on true line between secs 4 and 9
Va. 13° 09' E

39.97 Set post deposited chamd stake and raised mound of earth with pits as per instructions for 1/4 sec. Cor.

79.94 The corner to secs. 4 5, 8 and 9
Rolling Sand hills
Soil Third rate

T. 25 N. R. 10 W 6th PM

North on random line
between secs 4 & 5
Va. 13° 09' E.

38.00 Leave Sand hills and enter Cedar
Cr. Bottom bears E and W.

40.00 Set temporary 1/4 sec. Cor

80.14 Intersected North Boundary
4 chs East of the corner
to secs 4 and 5 from
which corner I run
South 2' E on true line
between secs 4 and 5
Va. 13° 09' E

40.14 Set post deposited chamd
stake and raised mound
of earth with pits as
per instructions for
1/4 sec cor

80.14 The corner to secs
4, 5, 8 and 9
Sandhills Third rate
Bottom level firstrate
Sept. 23d 1870

T. 25 N. R. 10 W 6th PM

North between Secs 31 and 32
Va. 12° 45' E

40.00 Set post deposited chamd
stake and raised mound of
earth with pits as per
instructions for 1/4
Sec. Cor.

80.00 Set post deposited chamd
stake and raised mound
of earth with pits as per
instructions for corner
to secs 29, 30, 31 and 32
Land level
Soil firstrate

T. 25 N. R. 10 W. 6th P.M.

East on random line
between Secs 29 & 32
Va. 12° 54' E

4000 Set temporary 114 Sec cor.
80.20 Intersected N & S line 20 lks
South of the corner to secs
28, 29, 32 and 33 from
which corner I run
S 89° 51' West on true line
between secs 29 & 32
Va. 12° 54' E

40.10 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 114 sec cor.
80.20 The corner to sections
29, 30, 31 and 32
Land level
Soil Rich firstrate

T. 25 N. R. 10 W. 6th P.M.

West on a random line
between Secs. 30 and 31
Va. 12° 54' E

4000 Set temporary 114 Sec. cor.
79.80 Intersected West Boundary
20 lks South of the corner
to secs 30 and 31 from
which corner I run
S 89° 51' East on true line
between Secs 30 and 31
Va. 12° 54' E

39.80 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 114
Sec. cor.
79.80 The corner to secs
29, 30, 31 and 32
Land level
Soil firstrate

T. 25 N. R. 10 W 6th PM

North between Secs 29 & 30
Va. 12° 54' E

40.00 Set post deposited chaned stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

76.00 Leave level plain and enter sand hills bear NE & SW.

80.00 Set post deposited chaned stake and raised mound of earth with pits as per instructions for corner to sections 19, 20, 29 & 30

Plain level first rate
4 chs. of Sand hills third rate

T. 25 N. R 10 W 6th PM

East on random line between Secs 20 & 29
Va. 13° 06' E

3.00 Leave sand hills and enter level plain bears NE & SW

40.00 Set temporary 1/4 sec cor

79.90 Intersected N & S line 6 chs North of the corner to secs 20, 21, 28 and 29 from which corner I run
N 89° 57' West on true line between secs 20 & 29
Va. 13° 06' E

39.95 Set post deposited chaned stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

79.90 The corner to secs. 19, 20, 29 and 30

Plain rich first rate
3 chs. of Sand hills third rate

T. 25 N. R 10 W 6th PM

West on random line
between Secs. 19 & 30
Va. 13° 06' E

4000 Set temporary 1/4 Sec cor,
79.98 Intersected West Boundary
16 lks South of the corner
to secs 19 and 30 from
which corner I run
S 89° 53' East on true line
between secs 19 & 30
Va. 13° 06' E
39.98 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for 1/4 sec cor,
79.98 The corner to secs. 19, 20
29 and 30
Surface gently rolling
Soil Sandy Thirdrate

T. 25 N. R. 10 W 6th PM

North between secs. 19 & 20
Va. 13° 06' E
4000 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor
8000 Set post deposited chaned
stake and raised mound
of earth with pits as
per instructions for
Corner to secs 17, 18
19 and 20
Land low Sand hills
Soil Thirdrate

T. 25 N. R. 10 W. 6th P.M.

East on random line
between Secs 17 & 20
Va 13°06' E

40.00 Set temporary 1/4 Sec cor
79.76 Intersected N & S line 18 lks
North of the to secs 16. 17
20 & 21 from which
corner S. run
N 89°52' West on true line
between Secs 17 & 20
Va. 13°06' E

39.88 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for 1/4 sec cor.
79.76 The corner to secs
17, 18, 19 and 20
Rolling Sandhills
Soil Third rate

T. 25 N. R. 10 W. 6th P.M.

West on random line
between Secs 18 & 19
Va. 13°06' E

40.00 Set temporary 1/4 Sec cor.
80.16 Intersected West Boundary
40 lks South of the corner
to secs. 18 and 19 from
which corner S run
S 89°42' East on true line
between secs 18 & 19
Va. 13°06' E

40.16 Set post deposited chained
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec Cor
80.16 The corner to secs
17, 18, 19 and 20
Rolling Sandhills
Soil Third rate

T. 25 N R 10 W 6th PM

North between Secs 17 & 18
Va. 13°06' E

4000 Set post deposited chand stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

8000 Set post deposited chand stake and raised mound of earth with pits as per instructions for corner to sections 7, 8, 17, & 18
Rolling Sand hills
Soil Thirdrate

T. 25 N R 10 W 6th PM

East on random line
between secs 8 & 17
Va. 13°06' E

4000 Set temporary 1/4 sec cor.

7964 Intersected N&S line 35 lks. North of the corner to secs 8, 9, 16 and 17 from which corner I run
N 89°45' West on true line
between secs 8 & 17
Va. 13°06' E

3982 Set post deposited chand stake and raised mound of earth with pits as per instructions for 1/4 sec cor

7964 the corner to sections 7, 8, 17 and 18
Rolling Sand hills
Soil Third rate

T. 25 N. R. 10 W. 6th P.M.

West on random line
between secs 7 & 18
va. 13°06'E

4000 Set temporary 1/4 sec cor.

80.28 Intersected West Boundary
12 lks South of the corner
to secs 7 and 18 from
which corner I run
S 89°55' East on true line
between Secs 7 & 18
va. 13°06'E

40.28 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for ~~corner~~
~~to secs~~ 1/4 sec cor

80.28 The corner to secs.
7, 8, 17 & 18
Rolling Sandhills
Soil. Thirdrate

T. 25 N. R. 10 W. 6th P.M.

North between Secs 7 & 8
va 13°06'E

4000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.

8000 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
corner to sections 5,
6, 7 and 8
Rolling Sandhills
Soil Thirdrate

T. 25 N. R. 10 W 6th P.M.

East on random line
between secs 5 & 8
Va. 13°06' E

40.00 Set temporary 1/4 sec. cor.
80.10 Intersected N & S line 20
lks North of the corner to secs
4, 5, 8 and 9 from which
corner I run
S 89°51' West on true line
between Secs 5 and 8
Va. 13°06' E

40.05 Set post deposited chared
stake and raised mound
of earth with pits as per
instructions for 1/4
sec cor

80.10 The corner to secs
5, 6, 7 and 8
Rolling Sand hills
Soil, Nitrate

T. 25 N. R. 10 W. 6th P.M.

West on random line
between secs 6 and 7
Va. 13°06' E.

5.00 Leave Sandhills and enter
Bottom bears N E & S W.
26.28 Cache cnk dry on line
course N E.
40.00 Set temporary 1/4 sec cor.
41.38 Cache cnk 20 lks wide
course S E.
55.80 Same cnk dry on line
course N E.
80.38 Intersected West Boundary 6th
South of the corner to secs 6 &
7 from which corner I run
S 89°57' East on true line
between secs 6 and 7
Va. 13°06' E

40.38 Set post deposited chared stake
and raised mound of earth
with pits as per instructions
for 1/4 sec cor
80.38 The cor. to secs. 5, 6, 7 & 8
Bottom good rich
Nitrate soil

T. 25 N. R. 10 W 6th PM

North on random line
between secs 5 and 6
Va. 13°06' E

8.00 Leave Sand hills and enter
Bottom bears N E & S W.

40.00 Set temporary 1/4 Sec cor.

47.40 Cache creek dry on line
course N E

79.90 Intersected North boundary 8 lks
West of the corner to secs
5 and 6 from which corner
I run
South 3' W. on true line
between secs 5 & 6
Va. 13°06' E

39.90 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 sec cor.

79.90 The corner to secs 5. 6,
7 and 8
Bottom level first rate
86 lks. of Sandhills third rate
September 24th 1870

T. 25 N. R. 10 W 6th PM

General Description

The Central portion of this Township is ~~is~~ dry and Sandy Surface rolling and hilly - Soil third rate The South, S E. and N W parts are good rich first rate low lands well adapted to farming or grazing. The Soil is a deep rich black loam producing very thick heavy grass. Water may be obtained at any place on this level plain by digging from 4 to 8 feet.

The Township is destitute of timber

T. 25 N R 10 W 6th PM

List of Names

A list of the names of the individuals employed to assist in running measuring or marking the lines and corners described in the foregoing field Notes of Township No. 25 N, Range No. 10 West of the 6th Principal Meridian in the State of Nebraska, showing the respective capacities in which they acted:

Robert Harvey Chainman
Sot C. Griffith Chainman
Berington A. Savage Cornerman
Daniel Livingston Cornerman
Walter Lawrence Flagman

We hereby certify that we assisted James H. Paul deputy surveyor in surveying the subdivisional lines of Township No. 25 North of the Base line of Range No. 10 West of the 6th Principal Meridian in the State of Nebraska and that said surveys have been in all respects to the best of our knowledge and belief, well and faithfully surveyed, and the Boundary Monuments planted according to the instructions furnished by the Surveyor General

Robert Harvey Chainman
Sot. C. Griffith Chainman
Berington A. Savage Cornerman
Daniel Livingston Cornerman
Walter Lawrence Flagman

Subscribed and sworn to by the above named persons before me, a Notary Public for Douglas County in the State of Nebraska this 21st day of October 1870.

Lewis S. Reed
Notary Public

I, James N. Paul, deputy Surveyor, do solemnly swear that in pursuance of a joint Contract with Nicholas J. Paul and James N. Paul United States Surveyor General for the District of Iowa and Nebraska bearing date the 4th day of August A.D. 1870, I have well faithfully and truly, in my own proper person and in strict conformity with the instructions furnished by the Surveyor General, the Surveying Manual and the Laws of the United States, surveyed the Subdivisional lines of Townships No. 25 N. of the Base line of Range No. 10 West of the 6th Principal Meridian in the State of Nebraska, as represented in the foregoing field Notes as having been done under my directions; and I do further solemnly swear that all the corners of said said Surveys have been established and perpetuated in strict accordance with the Surveying Manual, and United Instructions and that the foregoing are the true and Original field Notes of such Survey.

James N. Paul

Deputy Surveyor

Subscribed and sworn to by said James N. Paul Deputy Surveyor before me a Notary Public for Douglas County in the State of Nebraska this 27th day of October A.D. 1870.

Lewis S. Reed
Notary Public

Surveyor Generals Office

Plattsmouth Neb. Jany. 21. 1871

The foregoing field notes of the survey of the subdivision Lines of Township No 25 North of the Base Line of Range No 10 West of the Sixth Principal Meridian in the state of Nebraska executed by James N. Paul under joint Contract No 32 of the 4th day of August 1870 wherein Nicholas J. and James N. Paul are joint contractors in the month of September 1870 having been critically examined the necessary corrections and explanations made the said field notes and the surveys they describe are hereby approved

Robt. R. Livingston

Surveyor General

Index Diagram

Town 26 N. R 10 W

6	62	5	46	4	35	3	24	2	13	1	
61		60		45		34		23		12	
7	59	8	44	9	33	10	22	11	11	12	
58		57		43		32		21		10	
18	56	17	42	16	31	15	20	14	9	13	
55		54		41		30		19		8	
19	53	20	40	21	29	22	18	23	7	24	
52		51		39		28		17		6	
30	50	29	38	28	27	27	16	26	5	25	
49		48		37		26		15		4	
31	47	32	36	33	25	34	14	35	3	36	

(A.)

Field Notes

of the Subdivisional lines of Township 26 North of the Base line Range No. 10 W of the 6th Principal Meridian in the State of Nebraska; Surveyed by James H. Paul, deputy Surveyor, under joint Contract No. 32 bearing date the 4th day of August 1870 wherein Nicholas Paul and James H. Paul are joint Contractors with Robert R. Livingston United States Surveyor General for the District of Iowa and Nebraska.

Survey Begun Sept. 26th 1870
Survey Completed Sept. 30th 1870

Names and duties of Assistants

Robert Harvey Chainman
Lot C. Griffith Chainman
Bevington H. Savage Cornerman
Daniel Livingston Cornerman
Walter Lawrence Flagman

(B.)

To determine the proper adjustment of my Compass for subdividing this Township I begin at the corner to Townships 25 & 26 N. Ranges 9 and 10 W and run North on a blank line along the East Boundary of section 36

Va 13° 12' E

40.02 To a point 3 lks East of the 1/4 sec cor

80.05 To a point 7 lks East of the corner to sections 25 and 36

To retrace this line or run parallel thereto my Compass must be adjusted to a Variation of 13° 15' East

Subdivision Commenced September 26th 1870

T. 26 N. R 10 W 6th P.M.

From the corner to sections 1, 2, 35 and 36 on the South Boundary I run North between Secs 35 and 36

Va. 13° 15' E

32.65 Cache creek 8 lks wide runs East

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor

65.00 Leave Bottom and enter Upland bears East and West

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to secs 25, 26, 35 & 36

Bottom Rich firstrate

Upland secondrate

T. 26 N. R. 10 W. 6th P.M.

East on random line
between Secs 25 and 36
Va. 13° 06' E

40.00	Set temporary 1/4 Sec. cor.
80.04	Intersected East Boundary 5 lks South of the corner to sections 25 & 36 from which corner I run S 89° 58' West on true line between Secs 25 & 36 Va. 13° 06' E
40.02	Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.
80.04	The corner to secs. 25, 26, 35 and 36 Rolling Sandy Soil Third rate

Rich bottoms 10 chs. S of line

T. 26 N. R. 10 W. 6th P.M.

North between Secs 25 and 26
Va. 13° 06' E

40.00	Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec cor
80.00	Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to secs 2, 23, 24 25 and 26

Land, Rolling Sandy Soil Third rate.

T. 26 N. R 10 W 6th PM

East on random line
between Secs 24 and 25
Va. 13°06' E

40.00 Set temporary 1/4 Sec. Cor.

80.16 Intersected East Boundary
14 lks South of the corner
to secs 24 and 25 from
which corner I run
S 87°34' West on true line
between Secs 24 & 25
Va. 13°06' E

40.08 Set post deposited chamd
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.

80.16 The corner to secs
23. 24. 25 and 26
Rolling Sandy
Soil Third rate

T. 26 N. R 10 W 6th P. M.

North between Secs 23 & 24
Va. 13°06' E

40.00 Set post deposited chamd
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.

80.00 Set post deposited chamd
stake and raised mound
of earth with pits as per
instructions for corner
to secs. 13, 14, 23 & 24
Land Sandy rolling
Soil Third rate

T. 26 N. R 10 W 6th P M

East on random line
between Secs. 13 and 24
Va. 13° 06' E

40.00 Set temporary 114 Sec Cor.

80.48 Intersected East Boundary
6 lks South of the corner
to secs 13 and 24 from
which corner I run
S 89° 57' West on true line
between Secs 13 & 24
Va. 13° 06' E

40.24 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 114 sec. Cor.

80.48 The corner to secs.
13, 14, 23 and 24
Rolling Sandy
Soil, Thirdrate

T. 26 N. R 10 W 6th P M

North between Secs, 13 and 14
Va. 13° 06' E

40.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 114 Sec

73.00 ~~Leave~~ Sand hills & enter Bottom bears E & W.

80.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for corner
to secs. 11, 12, 13 & 14
Rolling Sandy
Soil Thirdrate
except 7 Chs. of 1st rate bottom

T. 26 N. R. 10 W 6th P.M.

East on random line
between secs. 12 & 13
va. 13° 06' E

40.00 Set temporary 1/4 Sec cor.

80.10 Intersected East boundary
10 lks North of the corner
to secs 12 & 13 from which
Corner ~~T~~ run
N 89° 56' West on true line
between Secs 12 & 13
va. 13° 06' E

40.05 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor

80.00 The corner to secs.
11, 12, 13 and 14
~~Sandy Rolling~~
~~Soil Thirdrate~~
Land level Bottom
Soil firstrate

T. 26 N. R. 10 W 6th P.M.

North between Secs. 11 & 12
va. 13° 06' E

30.56 South Branch of Elkhorn river
29 lks wide runs N E

40.00 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for 1/4 Sec. cor.

42.00 Marshy Slough 2 chains
wide bears Mounds E

80.00 Set post deposited chaned
stake and raised mound
of earth with pits as
per instructions for
corner to secs 1, 2, 11 & 12
Land gently Rolling bottoms
Soil Secondrate

T. 26 N. R 10 W 6th P.M.

East on random line
between Secs 1 and 12
Va. 13° 06' E

4000 Set temporary 1/4 Sec. cor.

79.92 Intersected East Boundary
40 lks North of the corner
to secs 1 and 12 from
which corner I run
N. 89° 43' West on true line
between secs 1 & 12
Va. 13° 06' E

39.96 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec cor

79.92 The corner to sections
1, 2, 11 and 12
Gently Rolling Bottoms
Soil Second rate

T. 26 N. R 10 W. 6th P.M.

North on random line
between Secs 1 and 2
Va. 13° 06' E

20.00 Leave Bottom and enter Sand hills bns NE & SW

40.00 Set temporary 1/4 Sec Cor

80.18 Intersected North Boundary
10 lks West of the corner to secs
1 and 2 from which corner
I run
South 4' W. on true line
between Secs 1 and 2
Va. 13° 06' E

40.18 Set post deposited charred stake
and raised mound of earth
with pits as per instructions
for 1/4 sec cor

80.18 The corner to secs. 1, 2
11 and 12
Land Rolling
Soil Sandy Third rate
Except S. 20 lks. which is 2nd rate bottom land
September 26th 1870

T. 26 N. R 10 W 6th P.M.

North between Secs 34 & 35
Va. 13° 12' E

28.00 Leave Upland and enter Bottom
bears E and W

40.00 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.

47.85 Cache crik dry on line
course East

75.00 Leave Bottom and enter Upland
bears E and W.

80.00 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for corner
to sections 26, 27, 34 & 35
Bottom First rate
Upland Thirdrate

T. 26 N. R. 10 W. 6th P.M.

East on random line
between Secs 26 and 35
Va. 13° 06' E

40.00 Set temporary 1/4 sec. cor.

80.00 Intersected N & S line 14 lks
South of the corner to secs
25, 26, 35 and 36 from
which corner I run
S 89° 54' West on true line
between Secs 26 & 35
Va. 13° 06' E.

40.00 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.

80.00 The corner to sections
26, 27, 34 and 35
Land Rolling
Soil Sandy Thirdrate
First rate bottom land 10 chs S. of line

T. 26 N. R 10 W 6th PM

North between Secs 26 & 27
Va, 13°06' E

4000 Set post deposited chamd stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

8000 Set post deposited chamd stake and raised mound of earth with pits as per instructions for corner to secs 22, 23, 26 & 27
Rolling Sandy Soil, Hardrate

T. 26 N. R 10 W 6th PM

East on random line between secs 23 & 26
Va, 13°06' E

4000 Set post ~~deposited chamd stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.~~ for temporary 1/4 Sec cor

80.06 Intersected N&S line 4 chs North of the corner to secs 23, 24, 25 and 26 from which corner I run
N 89° 58' West on true line between secs 23 & 26
Va, 13°06' E

40.03 Set post deposited chamd stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

80.06 The Corner to sections 22, 23, 26 and 27
Rolling Sandhills Soil & Hardrate

T. 26 N. R 10 W 6th PM

North between Secs 22 & 23
Va, 13° 06' E

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to secs. 14, 15, 22 & 23
Rolling Sand hills
Soil Thirdrate

T. 26 N. R 10 W 6th PM

East on random line
between Secs 14 & 23
Va, 13° 06' E

4000 Set temporary 1/4 Sec Cor

79.78 Intersected N & S line 18 lks South of the corner to secs. 13, 14, 23 and 24 from which corner I run S 89° 52' West on true line
between secs 14 & 23
Va, 13° 06' E

39.89 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

79.78 The corner to secs. 14, 15, 22 & 23
Rolling Sand hills
Soil Thirdrate

T. 26 N. R. 10 W. 6th P.M.

North between secs 14 & 15
Va. 13°06' E

4000 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

8000 Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to secs 10 & 11 14 & 15

Rolling Sandhills
Soil Thirdrate

T. 26 N. R. 10 W. 6th P.M.

East on random line between Secs. 11 & 14
Va. 13°06' E

4000 Set temporary 1/4 Sec. Cor.

52.00 Leave upland and enter Bottom bears N.W. and S.E.

79.96 Intersected N & S line 8 lks South of the corner to secs. 11, 12, 13 & 14 from which corner I run S 89°57' West on line line between secs 11 & 14
Va. 13°06' E

39.98 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 sec. Cor.

79.96 The corner to secs. 10, 11 14 and 15

Sandhills Thirdrate
Bottom firstrate

T. 26 N. R. 10 W. 6th PM

North between Secs 10 & 11
Va. 13° 06' E.

1300 Leave upland and enter Bottom bearing E and W

4000 Set post deposited chand stake and raised mound mound of earth with pits as per instructions for 1/4 Sec cor

56.20 North Branch of Elkhorn River ~~Creek~~ Creek 18 lks wide runs N.E.

57.60 Same Creek 10 lks wide runs N.W.

61.40 Same Creek 16 lks wide runs East

8000 Set post deposited chand stake and raised mound of earth with pits as per instructions for corner to secs 2, 3, 10 and 11

Upland Thirdrate
Bottom First rate

T. 26 N R 10 W 6th PM

East on random line between secs 2 & 11
Va 13° 06' E.

3000 Leave Bottom and enter Upland bears N.W. and S.E.

4000 Set temporary 1/4 sec cor

5000 Leave Sand hills and enter Bottom bears N.E. & S.W.

8004 Intersected N. & S. line 20 lks North of the corner to secs. 1, 2, 11 and 12 from which corner I run N 89° 51' Western line between secs 2 & 11
Va 13° 06' E

4002 Set post deposited chand stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

8004 The corner to sections 2, 3, 10 and 11

Bottom First rate
Upland Thirdrate

T. 26 N. R. 10 W. 6th P.M.

North on random line
between secs 2 and 3
Va 13° 06' E

10.00 Leave Bottom and enter
Sandhills bears E & W

22.00 Leave Sand ridge and enter
rich level plain bears N E & W.

4.00 Set temporary 1/4 sec cor.

79.66 Intersected North Boundary
6 lks west of the corner to
secs. 2 and 3 from which
Corner I runs
South 3' W. on the line
between secs 2 & 3
Va 18° 06.

39.66 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.

79.66 The corner to secs 2, 3
10 and 11
Sand ridge Thirdrate
Balance, good, Firstrate
September 24th 1870

T. 26 N. R. 10 W. 6th P.M.

North between Secs. 33 & 34
Va 13° 09' E

27.75 Cache creek 5 lks wide
runs East

4.00 Set post deposited charred
stake and raised
mound of earth with
pits as per instructions
for 1/4 sec cor.

43.00 Leave Bottom and enter
Sand hills bearing E & W.

80.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
corner to secs 27, 28
33 and 34
Bottom Firstrate
Balance Thirdrate

T. 26 N R 10 W 6th PM

East on random line
between secs 27 & 34
Va 13° 09' E.

40.00 Set temporary 1/4 sec. cor.

80.06 Intersected N & S line 18 lks
North of the corner to
secs. 26, 27, 34 and 35
from which corner
I run
N 89°52' West on true line
between secs. 27 & 34
Va 13° 09' E

40.03 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec cor

80.06 The corner to secs
27, 28, 33 and 34.
Land rolling Sandy
Soil Thirdrate

T. 26 N R 10 W 6th PM

North between Secs 27 & 28
Va 13° 09' E.

40.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec. cor.

80.00 Set post deposited,
charred stake and raised
mound of earth with pits
as per instructions for
Corner to secs 21, 22
27 and 28
Rolling Sandy
Soil Thirdrate

T. 26 N R 10 W 6th PM

East on random line
between secs 22 & 27
Va 13° 09' E

40.00 Set temporary 1/4 sec cor,
80.48 Intersected N & S line
at the corner to secs. 22
23, 26 & 27 from
which corner I run
West on true line
between secs 22 & 27
Va 13° 09' E

4.24 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec cor

80.48 The corner to secs,
21, 22, 27 & 28
Rolling Sandy
Soil Thirdrate

T. 26 N R 10 W 6th PM

North between secs 21 & 22
Va 13° 09' E

40.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec cor

80.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
Corner to secs 15
16, 21 and 22
Rolling Sandhills
Soil Thirdrate

T. 26 N R 10 W 6th PM

East on random line
between secs. 15 & 22
Va 13° 09' E

40.00 Set temporary 1/4 sec cor.
80.12 Intersected N & S line
1 lks South of the corner
to secs. 14, 15, 22 & 23
from which corner
I run
S 89° 58' West on true line
between secs 15 & 22
Va 13° 09' E.

40.06 Set post deposited chained
stake and raised
mound of earth with
pits as per instructions
for 1/4 sec cor

80.12 The corner to sections
15, 16, 21 and 22
Rolling Sandhills
Soil Third rate

T. 26 N R 10 W 6th PM

North between secs 15 & 16
Va 13° 09' E

40.00 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec cor

80.00 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for corner
to sections 9, 10, 15 & 16
Rolling Sandhills
Soil Third rate

T. 26 N. R. 10 W. 6th P.M.

East on random line
between secs. 10 & 15
Va 13° 09' E.

40.00 Set temporary 1/4 sec. cor.

79.96 Intersected N. & S. line 10 lks
North of the corner to
secs. 10, 11, 14 & 15 from
which I run
N 89° 56' West on true
line between secs. 10 & 15
Va 13° 09' E

39.98 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor

79.96 The corner to secs
9, 10, 15 and 16 —
Rolling Sandhills
Soil Thirdrate

Good bottoms 10 to 15 chs. N.

T. 26 N. R. 10 W. 6th P.M.

North between Secs 9 and 10
Va 13° 09' E

2.00 Leave Upland and enter
Bottom bears E & W

33.00 Slough 50 lks wide bears NE & SW

40.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 Sec. Cor.

46.50 South Branch of Elkhorn river
30 lks wide runs N.E.

70.00 Leave Bottom and enter Sand
ridge bears E and W

80.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for corner
to secs. 3, 4, 9 and 10
Bottom level first rate
Balance thirdrate.

T. 26 N. R 10 W 6th PM

East on random line
between secs 3 & 10
Va 13° 09

40.00 Set temporary 1/4 sec cor
45.00 Leave Sand ridge and enter
Valley bears N E & S W.
80.06 Intersected N & S line 14
lks South of the corner to secs.
2, 3, 10 & 11 from which
corner I run
S 89° 54' West on true
line between secs 3 & 10
Va 13° 09' E
40.03 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec. cor.
80.06 The corners to sections
3, 4, 9 and 10
Sand Ridge Third rate
Bottom first rate

T. 26 N R 10 W 6th PM

North on random line
between secs 3 & 4
Va 13° 09' E
25.00 Leave Sand ridge and enter rich
level plain bears N W & S E.
40.00 Set temporary 1/4 sec cor.
79.75 Intersected North Boundary
10 lks west of the corner to
sections 3 and 4 from
which corner I run
South 4' West on true line
between secs 3 & 4
Va 13° 09' E
39.75 Set post deposited charred stake
and raised mound of earth
with pits as per instructions
for 1/4 sec. cor.
79.75 The corners to secs. 3, 4,
9 and 10
25 lks of Sand hills Third rate
Balance level first rate
September 28th 1870

T. 26 N R 10 W 6th PM

North between secs 32 & 33
Va 13° 09' E

33.85 Coche creek dry on line course E.
37.00 Leave Bottom and enter Sandy Upland bears E and W.
40.00 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 sec cor.
80.00 Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to sections 28, 29, 32 and 33
Bottom first rate
Balance third rate

T. 26 N R 10 W 6th PM

East on random line
between Secs 28 & 33
Va 13° 09' E

40.00 Set temporary 1/4 Sec. cor.
80.04 Intersected N. & S. line 14 lks North of the corner to secs 27, 28, 33 and 34 from which corner S. run N 89° 54' West on true line
between secs. 28 & 33
Va 13° 09' E.
40.02 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec cor.
80.04 The corner to sections 28, 29, 32 and 33
Rolling Sandhills
Soil third rate

T 26 N R 10 W 6th PM

North between Secs 28 & 29
Va 13° 09' E

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 20, 21, 28 and 29
Rolling Sandhills
Soil Thirdrate

T 26 N R 10 W 6th PM

East on random line
between Secs 21 & 28
Va 13° 09' E

40.00 Set temporary 1/4 Sec cor

80.10 Intersected N & S line 14 lks North of the corner to secs 21, 22, 27 & 28 from which corner I run N 89° 54' West on true line between secs. 21 & 28
Va 13° 09' E

40.05 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

80.10 Fin corner to sections 20, 21, 28 and 29
Rolling Sandhills
Soil Thirdrate

T. 26 N R 10 W 6th PM

North between secs 20 & 21
Va 13° 09' E.

40.00 Set post deposited chaned stake and raised mound of earth with pits as per instructions for 1/4 Sec cor

80.00 Set post deposited chaned stake and raised mound of earth with pits as per instructions for corner to secs 16, 17, 20 and 21
Rolling Sand hills
Soil Thirdrate

T. 26 N R 10 W 6th PM

East on random line between Secs 16 & 21
Va 13° 09' E

40.00 Set temporary 1/4 Sec. cor.

80.10 Intersected N & S line 5 lks South of the corner to secs 15, 16, 21 and 22 from which corner I run S 89° 58' West on true line between secs 16 & 21
Va 13° 09' E.

40.05 Set post deposited chaned stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor.

80.10 The corner to sections 16, 17, 20 and 21
Rolling Sand hills
Soil Thirdrate

T. 26 N R 10 W 6th PM

North between Secs 16 & 17
Va 13° 09' E.

18.00 Leave Upland and enter Bottom
bears N E and S W.

40.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec. cor.

70.50 South Branch of Elkhorn
river 40 lks wide runs N E.

77.00 Same Stream 30 lks wide
runs N W

78.40 Same Stream 25 lks wide
runs N. E.

80.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
corner to secs 8. 9. 16 & 17
Upland Sandy Thirdrate
Bottom level Firstrate
Scattering trees Ash
Elm and Cottonwood
but none near enough for bearings to Sec. Cor.

T. 26 N R 10 W 6th PM

East on random line
between Secs. 9 & 16
Va 13° 09' E

13.00 South fork of Elkhorn river
runs N E. 30 lks wide

40.00 Set temporary 1/4 Sec. cor.

68.00 Leave Bottom and enter Upland
bears N E and S W.

80.04 Intersected N & S line 10 lks
North of the corner to secs
8, 9, 10, 15 & 16 from which
corner I run
N 89° 56' West on true line
between secs 9 & 16
Va 13° 09' E

40.02 Set post deposited
charred stake and raised
mound of earth with
pits as per instructions
for 1/4 Sec. cor

80.04 The corner to secs.
8, 9, 16 and 17
Bottom Firstrate
Upland Thirdrate
Good wood on SW4 sec. 9

T. 26 N R 10 W 6th PM

North between secs 8 and 9
Va 13° 09' E

2.00 Leave ~~Upland~~ Bottom and
Enter Upland bears NE & N.

40.00 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor.

80.00 Set post deposited chained
stake and raised mound
of earth with pits as
per instructions for
Corner to sections
4, 5, 8 and 9
Land Rolling
Soil Sandy Thirdrate

T. 26 N R 10 W 6th PM

Easton random line
Between Secs 4 and 9
Va 13° 09' E

40.00 Set temporary 1/4 Sec cor

80.00 Intersected No Line 20
lks South of the corner to secs
3, 4, 9 and 10 from which
corner I run
S 89° 51' West on true
line between secs 4 & 9
Va 13° 09' E.

40.00 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for 1/4 Sec
Corner

80.00 The corner to sections
4, 3, 8 and 9.
Rolling Sandhills
Soil Thirdrate

T. 26 N. R 10 W 6th PM

North on a random line between secs 4 & 5
Va 13° 09' E

40.00 Set temporary 1/4 Sec cor,
79.80 Intersected North Boundary 10 lks West of the corner to secs. 4 and 5 from which corner I run South 4' West on true line between secs 4 & 5
Va 13° 09' E

39.80 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor,
79.80 The corner to secs 4, 5, 8 and 9
Rolling & Sandy Soil Third rate

September 29th 1870

T 26 N R 10 W 6th PM

North between secs 31 & 32
Va 13° 09' E,

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor,
64.00 Leave Bottom and enter Sand Hills bears East and West
80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 29, 30, 31 and 32
Bottom first rate
Hills Third rate

T. 26 N R 10 W 6th PM

East on random line
between Secs 29 & 32
Va 13° 09' E

4000 Set temporary 1/4 sec cor
79.92 Intersected N & S line
20 lks South of the corner
to sections 28, 29, 32 &
33 from which corner I run
S 89° 51' West on true line
between Secs 29 & 32
Va 13° 09' E,

39.96 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 sec. cor

79.92 The corners to secs.
29, 30, 31 and 32
Rolling Sandy
Soil Hardwood

T. 26 N R 10 W 6th PM

West on random line
between Secs 30 & 31
Va 13° 09' E

4000 Set temporary 1/4 sec cor
80.40 Intersected West Boundary
30 lks South of the corner
to secs 30 & 31 from
which corner I run
S 89° 47' East on true line
between Secs. 30 and 31
Va 13° 09' E,

40.40 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
sec cor.

80.40 The corner to secs
29, 30, 31 and 32
Rolling and Sandy
Soil Hardwood

T. 26 N R 10 W 6th PM

North between Secs 29 & 30
Va 13° 09' E.

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 114 Sec. Cor.

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for Corner to sections 19, 20, 29 and 30
Land, rolling Sandy
Soil Thirdrate

T. 26 N R 10 W 6th PM

East on random line
between secs 20 & 29
Va 13° 09' E.

4000 Set temporary 114 Sec Cor.

79.86 Intersected N & S line 56 lks North of the corner to sections 20, 21, 28 and 29 from which corner S run
N 89° 36' West on true line
between secs 20 & 29
Va 13° 09' E

39.93 Set post deposited charred stake and raised mound of earth with pits as per instructions for 114 Sec. Cor.

79.86 The corner to secs. 19, 20, 29 & 30
Rolling Sandhills
Soil Thirdrate

T. 26 N R 10 W 6th PM

West on random line
between Secs 19 & 30
Va 13° 09' E

40.00 Set temporary 1/4 sec cor,
80.08 Intersected West Boundary
20 lks South of the corner
to sections 19 & 30 from
which corner Bears
S. 89° 51' East on true
line between secs
19 and 30
Va 13° 09' E,
40.08 Set post deposited charred
stake and raised
mound of earth
with pits as per
instructions for 1/4
Sec cor
80.08 The corner to secs.
19, 20, 29 & 30.
Rolling Sandhills
Soil Thurdate

T. 26 N R 10 W 6th PM

North between Secs 19 & 20
Va 13° 09' E
40.00 Set post deposited
charred stake and
raised mound of
earth with pits as
per instructions
for 1/4 Sec. Cor,
80.00 Set post deposited
charred stake and
raised mound of earth
with pits as per
instructions for corner
to secs., 17, 18, 19 & 20
Rolling Sandhills
Soil Thurdate

T. 26 N. R. 10 W 6th PM

East on random line
between Secs 17 & 20
Va 13° 09' E.

5.00 Leave Upland and enter Bottom
bears NW and SE.

40.00 Set temporary 1/4 sec cor.

50.00 Leave Bottom and enter
Upland bears N E & S W

80.04 Intersected N & S line 35 lks
North of the corner to secs. 16,
17, 20 & 21 from which
corner I run
N 89° 45' West on true line
between secs 17 & 20
Va 13° 09' E

40.02 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec cor.

80.04 The corner to secs
17, 18, 19 and 20 —
Upland Thirdrate
Bottom firstrate
Limestone quarry in SW4
of section 17 —

T. 26 N R 10 W 6th PM

West on random line
between secs. 18 & 19
Va 13° 09' E.

40.00 Set temporary 1/4 sec. cor.

49.80 Intersected West Boundary
24 lks South of the corner
to secs 18 and 19 from
which corner I run
S 89° 50' East on true line
between secs 18 & 19
Va 13° 09' E.

39.80 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
sec cor.

79.80 The corner to secs
17, 18, 19 and 20.
Rolling Sand hills

Sol Thurdrall

T. 26 N R 10 W, 6th PM

North between Secs. 17 & 18
Va 13° 09' E.

4,00 Leave Upland and enter Bottom bears NW and SE.

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor.

64,35 South Branch of Elkhorn 15 lks wide runs East,

70,00 Leave Bottom and enter Sand hills bears E & W

80,00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to secs. 7, 8, 17 & 18
Upland Thirdrate
Bottom firstrate

T 26 N R 10 W 6th PM

East on random line between Secs. 8 & 17
Va 13° 09' E.

40,00 Set temporary 1/4 Sec cor.

50,00 Leave Upland and enter Bottom bears NE & SW

79,96 Intersected N and S line 30 lks North of the corner to secs 8, 9, 16 & 17
from which corner I run between secs. 8 & 17
S 89° 47' West on true Va line 13° 09' E.

39,98 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor.

79,96 The corner to secs 7, 8, 17 and 18
Bottom firstrate
Upland Thirdrate
There is a large Beaver Pond in the NE 4 of sec 17
Scattering timber on creek. Ash & Cottonwood

T. 26 N R 10 W 6th PM

West on random line
between secs 7 & 18
Va 13° 09' E.

40.00 Set temporary 1/4 Sec. Cor.

79.42 Intersected West Boundary
12 chs South of the corner
to secs 7 & 18 from which
corner B. ~~[illegible]~~
S. 89° 55' East on true line
between secs 7 & 18
Va 13° 09' E

39.42 Set post deposited chained
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec. Cor.

79.42 The corner to secs.
7, 8, 17 and 18
Rolling hillside
Soil Secondrate

Bottom land 10 chs. S of line

T. 26 N R 10 W 6th PM

North between Secs. 7 & 8
Va 13° 09' E.

40.00 Set post deposited
chained stake and
raised mound of earth
with pits as per
instructions for
1/4 Sec. Cor.

80.00 Set post deposited
chained stake and
raised mound of
earth with pits as
per instructions
for corner to secs
5, 6, 7 and 8
Rolling Sandhills
Soil Thirdrate

T. 26 N. R 10 W 6th P.M.

East on random line between Secs 5 & 8
Va 13° 09' E.

4000 Set temporary 1/4 sec cor
7988 Intersected N & S line 14 lks North of the corner to sections 4, 5, 8 and 9 from which corner I run
N. 89° 54' West on true line between Secs 5 & 8
Va 13° 09' E

39.94 Set post deposited charred stake and raised mound of earth with pits as per instruction for 1/4 Sec. cor.
79.88 The corner to secs. 5, 6, 7 and 8
Rolling Sandhills
Soil Thirdrate

T. 26 N R 10 W 6th P.M.

West on random line between Secs 6 & 7
Va 13° 09' E

40.00 Set temporary 1/4 Sec cor.
79.13 Intersected West Boundary 14 lks North of the corner to sections 6 and 7 from which corner I run
N 89° 54' East on true line between secs 6 & 7
Va 13° 09' E

39.13 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor
79.13 The corner to secs. 5, 6 and 7 & 8
Rolling Sandhills
Soil Thirdrate

T. 26 N. R. 10 W 6th P.M.

North on random line
between secs 5 & 6
Va 13° 09' E

1,000 Set temporary 1/4 sec cor
79.90 Intersected North boundary
22 lks East of the
corner to sections
5 and 6 from which
corner I run
South 9' E, on true
line between secs
5 and 6
Va 13° 09'

39.90 Set post deposited
charred stake and
raised mound of
earth with pits as
per instructions for 1/4 sec cor,
79.90 The corner to secs
5, 6, 7 and 8
Land Rolling
Soil Thirdrate
September 30th 1870

T. 26 N R 10 W 6th P.M.

General Description

There is some first rate
rich bottom land in this
Township along Eagle
Creek and the South
Branch of Elkhorn
good black sand
loam. Generally
the Upland is sandy
dry and thirdrate
There is but little
timber in the Township
and that is immediately
along the Banks
of the Streams

T. 26 N. R 10 W 6th PM

A List of Names

A list of the names of the individuals employed to assist in running measuring or marking the lines and corners as described in the foregoing field Notes of Township No 26 North of the Base Line of Range No 10 West of the 6th Principal Meridian in the State of Nebraska showing the respective capacities in which they acted;

Robert Harvey, Chainman
Lot C. Griffith, Chainman
Bennington H. Savage, Cornerman
Daniel Livingston Cornerman
Walter Lawrence, Flagman

T. 26 N. R. 10 W 6th PM

We, hereby certify that we assisted James H. Paul, Deputy Surveyor, in surveying the Subdivisional lines of Township No 26 North of the Base line of Range No 10 West of the 6th Principal Meridian in the State of Nebraska, and that said Surveys have been in all respects to the best of our knowledge and belief well and faithfully surveyed and the Boundary Monuments planted according to the instructions furnished by the Surveyor General

Robert Harvey, Chainman
Lot C. Griffith, Chainman
Bennington H. Savage, Cornerman
Daniel Livingston, Cornerman
Walter Lawrence, Flagman

Subscribed and sworn to by the above named persons before me a Notary Public for Douglas County in the State of Nebraska this 21st day of October AD 1870.

Lewis S. Reed
Notary Public

T. 26 N R 10 W 6th P M

I, James N. Paul, deputy surveyor do solemnly swear that in pursuance of a joint Contract wherein Nicholas J Paul and Robert R. Livingston United States Surveyor General for the District of Iowa and Nebraska, bearing date the 14th day of August 1870, I have over faithfully and truly in my own proper person and in strict conformity with the instructions furnished by the Surveyor General the Surveying Manual and the Laws of the United States, surveyed the Subdivisional lines of Township No. 26 North of the Base line of Range No. 10 West of the 6th Principal in the State of Nebraska as are represented in the foregoing field Notes as having been done under my directions; and I do further solemnly swear that the Corners of said surveys have been established and perpetuated in strict accordance with the Surveying Manual and printed Instructions and that the foregoing are the true and original field Notes of such Survey —

James N. Paul
Deputy Surveyor

Subscribed by said James N. Paul, deputy Surveyor and sworn to before me a Notary Public for Douglas County in the State of Nebraska this 22nd day of October 1870 —

Lewis S. Reed
Notary Public

Surveyor General's Office
Plattsmouth Neb Jany 21. 1871

The foregoing field notes of the survey of the Subdivision lines of Township 26 North of the Base Line of Range 10 West of the 6th Principal Meridian in the State of Nebraska executed by James H. Paul under joint contract No 32 of the 4th day of August 1870 wherein Nicholas J. & James H. Paul are joint contractors in the month of September 1870 having been critically examined the necessary corrections and explanations made the said field note and the surveys they describe are hereby approved

Robt. R. Livingston,
Surveyor General

Index Diagram
Town 27 N. R 10 W.

6	62 5	46	4	35 3	24	2	13	1	
61	60	45	34	23	12				
7	59 8	44	9	33 10	22	11	11	12	
58	57	48	32	21	10				
18	56 17	42	16	31 15	20	14	9	13	
55	54	41	30	19	8				
19	53 20	40	31	29 22	18	23	7	24	
52	51	39	28	17	6				
30	50 29	38	28	27 27	16	26	5	25	
49	48	37	26	15	4				
31	47 32	36	33	25 34	14	35	3	36	

The foregoing
division lin
Line of Ra
Meridian in
James H. C
4th day of
H. Paul ar
September
the necessary
the said fe
are hereby

(a.)

Field Notes
of the
Subdivisional lines of Township No 27 North of the Base line of Range No 10 West of the Sixth Principal Meridian in the State of Nebraska Surveyed by James H. Paul, deputy Surveyor, under joint Contract No 32 bearing date the 4th day of August 1870 - wherein Nicholas J. Paul and James H. Paul are joint Contractors with Robert A. Livingston, U. S. Surveyor General for the District of Iowa and Nebraska.

Survey Commenced - Oct. 3d 1870

Survey Completed - Oct. 17th 1870

(B)

Names and duties of assistants

Robert Harvey	Chainman
Lot C. Griffith	Chainman
Daniel Livingston	Cornerman
Bevington H. Savage	Cornerman
Walter Lawrence	Flagman

To determine the proper adjustment of my Compass for Subdividing this Township I commence at the corner to Township 26 and 27 N. Ranges ~~8 and~~ 9 & 10 West of mer North on a blank line along the East boundary of sec 36

Var. 13° 09' E

39.96 To a point 3 lks West of the 1/4 sec cor

79.93 To a point 6 lks West of the corner to secs 25 and 36

To retrace this line or run parallel thereto my Compass must be adjusted to a Variation of 13° 06' East

Subdivision Commenced Oct. 3d 1870

T 27 N. R 10 W 6th P M

From the corner to sections 1, 2, 35 and 36 on the South Boundary I run North between Secs 35 and 36

Var. 13° 06' E

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to Secs. 25, 26, 35, 36

Land rolling Sand hills

Soil Thirdrate

T 27 N. R. 10 W 6th P.M.

East on a random line
between Secs 25 & 36
Va 13° 6' E

4000 Set temporary 1/4 Sec cor
80.24 Intersected East boundary
18 chs North of the corner
to secs 25 & 36 from which
Corner I run
N 89° 52' West on true
line between Secs 25 & 36
Va 13° 6' E

40.12 Set post deposited chained
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec cor.

80.24 The corner to sections 25
26, 35 & 36
Land Rolling Sandhills
soil Thirdrate

T 27 N. R. 10 W 6th P.M.

North between Secs 25 & 26
Va 13° 6' E.

4000 Set post deposited chained
stake and raised mound
of earth with pits as
per instructions for 1/4
Sec cor

8000 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for corner
to sections 23, 24
25 and 26.
Land rolling Sandhills
Soil Thirdrate

T. 27 N R 10 W 6th PM

East on random line between Secs 24 & 25
Va 13° 06' E

4000 Set temporary 1/4 Sec cor

80.40 Intersected Eastboundary 30 lks North of the corner to secs 24 & 25 from which corner I run N 89° 47' West on true line between secs 24 & 25
Va 13° 06' E

40.20 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor

80.40 The corner to secs 23, 24, 25 & 26
80.40 Land rolling Sandhills
Soil Thirdrate

T. 27 N R 10 W 6th PM

North between Secs 23 & 24
Va 13° 06' E.

12.00 Leave Sand hills and enter high bottom bears E & NW

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor.

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to secs. 13, 14, 23 and 24

Up-Land. Sandhills, Thirdrate
Bottom Firstrate

T. 27 N R 10 W 6th PM

East on random line
between Secs. 13 & 24
Va 13° 06' E.

40.00 Set temporary 1/4 Sec Cor
80.50 Intersected East boundary
30 lks North of the corner
to secs 13 & 24 from
which corner I run
N. 89° 47' West on true
line between Secs. 13 & 24
Va 13° 06' E.

110.25 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec Cor.

80.50 The corner to secs. 13
14, 23 & 24
Land high Bottom
Soil Firstrate

T. 27 N R 10 W 6th PM

North between Secs. 13 & 14
Va 13° 06' E

40.00 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions

80.00 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for corner
to sections 11, 12, 13 & 14
Land high, level Bottom
Soil Firstrate

T. 27 N. R 10 W 6th PM

East on random line
between Secs 12 & 13
Va 13° 06' E

4000 Set temporary 1/4 Sec cor.

8000 Intersected East boundary
30 lks north of the corner to
Secs. 12 & 13 from which
corner I run
N 89° 47' West on true line
between Secs 12 & 13
Va 13° 06' E

4000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec cor

8000 The corner to Sections
11, 12, 13 & 14
Land high Bottom
Soil Firstrate

T. 27 N. R 10 W 6th PM

North between Secs 11 & 12
Va 13° 06' E

4000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. cor.

8000 Set post deposited
charred stake and raised
mound of earth with pits
as per instructions for
corner to sections
1, 2, 11 and 12
Land firstrate Bottom
Soil & Sandy loam
producing heavy grass.

T 27 N. R 10 W 6th PM

East on random line
between Secs. 1 & 12
Va 13° 09' E.

29.15 Elkhorn River 60 lks wide
runs S E.

1.00 Set temporary 1/4 Sec. cor.

80.32 Intersected East boundary 15 lks
north of the corner to secs.
1 and 12 from which
corner I run
N 89° 54' West on true
line between Secs 1 & 12
Va 13° 09' E

40.16 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 Sec. cor.

80.32 The corner to secs. 1, 2
11 and 12
Land rich Bottom
Soil first rate

T 27 N R 10 W 6th PM

North on random line
between Secs. 1 & 2
Va 13° 09' E

19.25 Elkhorn River 50 lks wide
runs N E.

1.00 Set temporary 1/4 Sec. Cor.

80.05 Intersected North boundary
15 lks West of the corner
to secs 1 and 2 from which
corner I run
South, 6' West on true line
between Secs. 1 and 2
Va 13° 09' E.

40.05 Set post deposited charred
stake and raised
mound of earth with pits
as per instructions for
1/4 Sec. Cor.

80.05 The corner to secs.
1, 2, 11 and 12
Land rich level Bottom
Soil first rate

October 3d 1870

T. 27 N R. 10 W 5th PM

North between Secs. 34 & 35
Va 13° 09' E.

10.00 Leave level plain and enter Sand Ridge bearing N W & E.

40.00 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 sec cor.

80.00 Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to secs 26, 27, 34 & 35
Sand hills Thirdrate
Balance level firstrate

T. 27 N R 10 W 6th PM

Eastow random line
between Secs. 26 & 35
Va 13° 12' E

40.00 Set temporary 1/4 sec. cor.

79.92 Intersected N. & S. line 14 lks North of the corner to secs 25, 26, 35 and 36 from which corner I run W 89° 57' West on the line between Secs 26 & 35
Va 13° 12' E.

39.96 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

79.92 The corner to sections 26, 27, 34 and 35
Rolling Sand hills
Soil Thirdrate

T. 27 N R 10 W 6th PM

North between Secs. 26 & 27
Va 13° 12' E

4000 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor.

8000 Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to sections 22, 23, 26 and 27
Rolling Sandhills
Soil Thirdrate

T. 27 N R 10 W 6th PM

East on random line
between Secs 23 & 26
Va 13° 12' E.

4000 Set temporary 1/4 Sec. cor.

79.88 Intersected N & S line 18 lks. North of the corner to secs. 23, 24, 25 & 26 from which corner I run N 89° 52' West on true line between Secs 23 & 26
Va 13° 12' E.

39.94 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

79.88 The corner to Secs. 22, 23, 26 and 27
Rolling Sandhills
Soil Thirdrate

T 27 N R 10 W 6th Pm

North between Secs. 22 & 23
Va 13° 12' E.

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

75.00 Leave Sandhills and enter Level Bottom bears NW and SE

8000 Set S.E. post deposited charred stake and raised mound of earth with pits as per instructions for Corner to Secs 14. 15. 22 & 23

Up-Land: Sandhills Thirdrate
Bottom level firstrate

T 27 N R 10 W 6th Pm

East on random line between Secs. 14 & 23
Va 13° 12' E.

4000 Set temporary 1/4 sec. cor.

79.90 Intersected N & S. line 8 lks South of the corner to Secs 13, 14, 23 & 24 from which corner I run S 89° 57' West on true line between Secs 14 & 23
Va 13° 12' E.

39.95 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

79.90 The Corner to secs 14, 15, 22 and 23
High level Bottom
Soil firstrate

T 27 N R 10 W 6th Pm

North between Secs. 14 & 15
Va 13° 12' E.

4000 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor.

8000 Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to Sections 10, 11, 14 & 15
Land level Bottom Soil fine timber

T 27 N R 10 W 6th Pm

East on random line between Secs. 11 & 14
Va 13° 12' E

4000 Set temporary 1/4 Sec cor

8006 Intersected N & S line 5 lks North of the corner to secs. 11, 12, 13 & 14 from which corner I run
N 89° 58' West on true line between Secs. 11 & 14
Va 13° 12' E

4003 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor.

8006 The corner to secs. 10, 11, 14 and 15
Land level Bottom Soil rich timber

T 27 N. R 10 W 6th PM

North between Secs 10 & 11
Va 13° 12' E

4000 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor.

8000 Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to sections 2, 3, 10 & 11
Rich level Bottom Soil fine silt

T 27 N R 10 W 6th PM

East on random line between Secs 2 & 11
Va 13° 12' E

4000 Set temporary 1/4 Sec. cor.

8002 Intersected N & S line 12 lks North of the corner to secs. 1, 2, 11 and 12 from which corner I run
N 89° 55' West on true line between Secs. 2 & 11
Va 13° 12' E

10.01 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor

8002 The corner to secs. 2 3, 10 & 11
Land rich level Bottom Soil fine silt

T. 27 N R 10 W 6th PM

North on random line
between Secs 2 & 3
Va 13° 12' E

4000 Set temporary 1/4 Sec. cor.
41.40 Elkhorn river 70 lks and
runs S E

79.90 Intersected North boundary
10 lks East of the corner
to secs. 2 & 3 from which
corner I run
South 4' E. on true line
between Secs 2 & 3
Va 13° 12' E

39.90 Set post deposited chained
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec cor

79.90 The corner to sections
2, 3, 10 & 11
Land level Bottom
Soil firstrate
Scattering timber
on River. Cottonwood
and Willow. Oct. 4th 1870.

T. 27 N R 10 W 6th PM

North between Secs. 33. 34
Va 13° 12' E

4000 Set post deposited chained
stake and raised mound
of earth with pits as
per instructions for 1/4
Sec. cor.

80.00 Set post deposited chained
stake and raised mound
of earth with pits as per
instructions for Corner
to sections 27, 28, 33 and
34
Land level
Soil firstrate

T. 27 N R 10 W 6th P.M.

East on random line
between Secs. 27 & 34
Va 13° 12' E

4000 Set temporary 1/4 sec. cor.

58.00 Leave level plain and enter
Sandhills bearing N W & S E

80.26 Intersected N & S line 12 lks
North of the corner to secs
26. 27. 34 and 35 from
which corner I run
N 89° 55' West on true line
between Secs 27 & 34
Va 13° 12' E.

40.13 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
sec. cor.

80.26 The corner to sections
27. 28. 33 and 34
Sandhills Thirdrate
Balance rich firstrate

T. 27 N R 10 W 6th P.M.

North between Secs. 27 & 28
Va 13° 12' E.

4000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. cor.

78.00 Leave rich level plain
and enter Sandhills
bearing East and West.

8000 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
Corner to sections 21
22. 27 and 28
1st 78 chs. rich level
firstrate
Balance Thirdrate

T 27 N R 10 W 6th PM

East on random line
between Secs 22 & 27
Va 13° 12' E.

40.00 Set temporary 1/4 Sec. cor.

80.36 Intersected N & S line
10 lks North of the corner
to sections 22, 23, 26
and 27 from which
Corner S run
N 89° 56' West on true line
between Secs. 22 & 27
Va 13° 12' E.

40.18 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. cor.

80.36 The corner to sections
21, 22, 27 and 28
Rolling Sandhills
Soil Thirdrate

T 27 N R 10 W 6th PM

North between Secs. 21 & 22
Va 13° 12' E.

4000 Set post deposited
charred stake and raised
mound of earth with pits
as per instructions for
1/4 Sec. Cor.

8000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for corner
to secs 15, 16, 21 and 22
Rolling Sandhills
Soil Thirdrate

T 27 N R 10 W 6th PM

East on random line
between Secs. 15 & 22
Va 13° 12' E

40.00 Set temporary 1/4 Sec. Cor.
46.00 Leave Sandhills and enter
Elkhorn Valley bears N W & E
80.14 Intersected N & S line 10 lks
North of the corner to
sections 14, 15, 22 & 23 from
which corner I run
N 89° 56' West on true line
between Secs 15 & 22
Va 13° 12' E
40.07 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for 1/4 sec Cor.
80.14 The corner to Sections
15, 16, 21 and 22
Sandhills thirdmile
Valley rich level firstmile

T 27 N R 10 W 6th PM

North between Secs. 15 & 16
Va 13° 12' E.

32.00 Leave Sandhills and enter
Valley bears N W and S E
40.00 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor.
76.00 Leave Valley and enter
Sandhills bearing N E & S W
80.00 Set post deposited chaned
stake and raised mound
of earth with pits as per
instructions for corner
to sections 9, 10, 15
and 16
Sandhills thirdmile
Valley level firstmile

T 27 N R 10 W 6th PM

East on random line
between Secs. 10 & 15
Va 13° 12' E

12.00 Leave Sandhills and enter
Valley, bears NE & SW

40.00 Set temporary 1/4 Sec. Cor.

79.92 Intersected Pr. of line
8 lks North of the corner
to Secs 10, 11, 14 and 15 from
which corner I run
N 89° 57' West on true line
between Secs. 10 & 15
Va 13° 12' E,

39.96 Set post deposited charred
stake and raised mound
of earth, with pits as per
instructions for 1/4 Sec.
Cor.

174.92 The corner to sections
9, 10, 15 & 16.
Sandhills Thirdrate
Valley level firstrate

T 27 N R 10 W 6th PM

North between Secs. 9 & 10
Va 13° 12' E

26.00 Leave Sandhills and enter
Valley, bears NW & SE,

40.00 Set post deposited
charred stake and
raised mound of earth
with pits as per
instructions for 1/4
Sec. Cor.

80.00 Set post deposited
charred stake and raised
mound of earth with pits
as per instructions
for corner to sections
3, 4, 9 and 10.
Sandhills thirdrate
Valley firstrate

T 27 N R 10 W 6th PM

East on random line
between Secs. 3 & 10
Va 13° 12' E.

40.00 Set temporary 1/4 Sec. Cor.
80.10 Intersected N. & S. line
4 lks South of the corner
to secs. 2, 3, 10 & 11 from
which corner I run
S 89° 58' West on true line
between Secs 3 & 10
Va 13° 12' E

40.05 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for ~~corner to secs~~ 1/4 Sec Cor.

80.10 The corner to Sections
3, 4, 9 & 10
Laid level Bottom
Soil first rate.

T. 27 N R 10 W 6th PM

North on random line
between secs. 3 & 4
Va 13° 12' E

40.00 Set temporary 1/4 Sec. Cor.
75.28 Elkhorn River 76 lks wide
runs East.
80.04 Intersected Northboundary
10 lks West of the corner to
secs 3 & 4, from which
corner I run
S 4' West on true line
between Secs 3 & 4
Va 13° 12' E

40.04 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 Sec
Corner

80.04 80.04 The corner to Sections
3, 4, 9 and 10
Rich level Bottom
Soil first rate
Scattering Cottonwood &
Willow on Rivers
October 5th 1870

T 27 N R 10 W 6th PM

North between Secs 32 & 33
Va 13° 12' E.

5.00 Leave Clayey Knoll and enter Valley bears NW and SE

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for Corner to sections 28, 29, 32 and 33
Rich level plain
Soil firstrate

T 26 N R 10 W 6th PM

East on random line between Secs. 28 & 33
Va 13° 12' E

40.00 Set temporary 1/4 Sec. Cor.

79.94 Intersected N & S line 10 lks North of the corner to secs 27, 28, 33 and 34 from which corner I run N 89° 56' West on true line between Secs 28 & 33
Va 13° 12' E.

39.97 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

79.94 The Corner to Secs. 28, 29, 32 & 33
Land, Sand & Clay loam mixed firstrate
good heavy grass—

T. 27 N R 10 W 6th PM

North between Secs. 28 & 29
Va 13° 12' E

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to Sections 20, 21, 28 & 29
Rich level plain
Soil first rate

T 27 N R 10 W 6th PM

East on random line between Secs. 21 & 28
Va 13° 12' E

~~4000~~
6.00 Leave plain and enter Sandhills bears Nevand SE

4000 Set temporary 1/4 sec cor.

79.86 Intersected N & S line 5 lks South of the corner to secs 21, 22, 27 & 28 from which corner I run S 89° 58' West on true line between secs 21 & 28
Va 13° 12' E.

39.93 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec cor

79.86 The corner to secs 20, 21, 28 & 29,
Sandhills thirdrate
Balance first rate

T 27 N R 10 W 6th PM

North between Secs. 20 & 21
Va 13° 12' E.

14.00 Leave level plain and enter Sand hills bears NW and SE.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 114 Sec cor

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 16. 17. 20 & 21
Plain level first rate
Hills rolling third rate

T 27 N R 10 W 6th PM

East on random line between Secs. 16 & 21
Va 13° 12' E

40.00 Set temporary 114 Sec. Cor

80.12 Intersected R & S line 8 lks South of the corner to sections 15. 16. 21 and 22 from which corner I run S 89° 57' West on true line between Secs 16 & 21
Va 13° 12' E

40.06 Set post deposited charred stake and raised mound of earth with pits as per instructions for 114 Sec. Cor

80.12 The corner to secs 16. 17. 20 and 21
Rolling Sandhills
Soil Third rate

T 27 N R 10 W 6th PM

North between Secs. 16 & 17
Va 13° 12' E

4000 Set post deposited chained stake and raised mound of earth with pits as per instructions for ~~corner to sections~~ 1/4 Sec. Cor.

8000 Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to sections 8, 9, 16, & 17
Rolling Sandhills
Soil Thirdrate

T 27 N R 10 W 6th PM

East on random line between secs 9 & 16
Va 13° 12' E

4000 Set temporary 1/4 Sec. Cor

8004 Intersected T N S line 10 lks North of the corner to sections 9, 10, 15 & 16 from which corner I run
N 89° 56' West on true line between Secs 9 & 16
Va 13° 12' E

4002 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

8004 The corner to sections 8, 9, 16 and 17
Rolling Sandhills
Soil Thirdrate

T 27 N R 10 W 6th PM

North between secs. 8 & 9
Va 13° 12' E

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for ~~corner~~ 1/4 sec cor.

49.00 ~~49.00~~ Leave Sandhills and Enter Valley bears SE and SW

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to secs. 4, 5, 8 and 9
Sandhills Thirdrate
Valley Firstrate

T 27 N R 10 W 6th PM

East on random line between secs. 4 & 9
Va 13° 12' E

4000 Set temporary 1/4 sec Cor

79.96 Intersected N & S line 12 lks South of the corner to secs 3, 4, 9 & 10 from which corner I run S 89° 55' West on true line between secs 4 & 9
Va 13° 12' E

39.98 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

79.96 The corner to sections 4, 5, 8 and 9
Rich level Valley
Soil Firstrate

T 27 N R 10 W, 6th P.M.

North on random line
between Secs 4 & 5
Va 13° 12' E

4000 Set temporary 1/4 Sec Cor

79.90 Intersected North boundary
at the corner to secs 4 &
5 from which corner True
South on a true line between Secs 4 & 5
Va 13° 12' E

39.90 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for 1/4
Sec cor.

79.90 The corner to Secs 4, 5
8 and 9
Land level Bottom
Soil Firstrate

October 6th 1870

T 27 N R 10 W 6th P.M.

North between Secs 31 & 32
Va 13° 12' E.

4000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec cor

8000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for corner
to sections 29, 30, 31 & 32
Rolling Sandhills
Soil Thirdrate

T 27 N R 10 W 6th PM

East on random line
between Secs 29 & 32
Va 13° 12' E

40.00 Set temporary 1/4 Sec Cor.

42.00 Leave Sandhills and enter level plain bears NW & SE

80.00 Intersected N & S line 20 lks North of the corner to Secs 28, 29, 32 & 33 from which corner I run N 89° 51' West on true line between Secs 29 & 32
Va 13° 12' E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor.

80.00 The corner to Sections 29, 30, 31 and 32
Sandhills Thirdrate
Balance first rate

T 27 N R 10 W 6th PM

West on random line
between Secs 30 & 31
Va 13° 12' E.

40.00 Set temporary 1/4 Sec Cor.

78.57 Intersected West boundary 43 lks South of the corner to secs. 30 & 31 from which corner I run
S 89° 42' East on true line between Secs. 30 & 31
Va 13° 12' E

38.57 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor

78.57 The corner to Sections 29, 30, 31 and 32
Rolling Sandhills
Soil Thirdrate

T 27 N R 10 W 6th PM

North between Secs. 29 & 30
Va 13° 12' E

24.00 Leave Sandhills and enter level plain bears NW & SE

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 19, 20, 29 & 30
Sandhills Thirdrate
Balance firstrate

T 27 N R 10 W 6th PM

East on random line between Secs. 20 & 29
Va 13° 12' E

40.00 Set temporary 1/4 Sec. Cor.

80.10 Intersected N & S line 30 Ks North of the corner to secs. 20, 21, 28 & 29 from which corner I run
N 89° 47' West on true line between Secs 20 & 29
Va 13° 12' E

40.05 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor

80.10 The corner to Sections 19, 20, 29 and 30
Rich level plain
Soil firstrate —

T. 27 N R 10 W 6th PM

West on random line
between Secs. 19 & 30
Va 13° 12' E

4000 Set temporary 1/4 Sec. Cor.

78.17 Intersected West boundary
25 lks South of the corner
to secs. 19 & 30 from
which corner I run
S 89° 49' East on true line
between Secs. 19 & 30
Va 13° 12' E

38.17 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for 1/4
Sec. Cor

78.17 The corner to secs.
19, 20, 29 & 30
Rich level plain
Soil fine loam

T. 27 N R 10 W 6th PM

North between Secs. 19 & 20
Va 13° 12' E

4000 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec. Cor.

8000 Set post deposited
Charred stake and raised
Mound of earth with
pits as per instructions
for corner to sections
17, 18, 19 and 20
Rich level plain
Soil fine loam

T 27 N R 10 W 6th PM

East on random line
between Secs. 17 & 20
Va 13° 12' E.

40.00 Set temporary 1/4 Sec cor
41.00 Leave level plain and
Enter Sandhills bearing N&S.
80.04 Intersected N & S line 15 lks
North of the corner to secs
16, 17, 20 & 21 from
which corner I run
N 89° 54' West on true line
between Secs. 17 & 20
Va 13° 12' E
40.02 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec cor
80.04 The corner to secs.
17, 18, 19 & 20
Sandhills Thirdrate
balance firstrate

T 27 N R 10 W 6th PM

West on random line
between Secs. 18 and 19
Va 13° 12' E.

40.00 Set temporary 1/4 Sec. Cor.
78.06 Intersected West boundary
10 lks South of the corner
to secs 18 & 19 from which
corner I run
S 89° 56' East on true line
between Secs. 18 & 19
Va 13° 12' E.
38.06 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 Sec. Cor.
78.06 The corner to secs.
17, 18, 19 and 20
Rich level plain
Soil firstrate

T 27 N R 10 W 6th PM

North between Secs. 17 & 18
Va 13° 12' E.

4.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

8.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 7, 8, 17 and 18

Rich level plain
Soil fine sand

T 27 N R 10 W 6th PM

East on random line
between Secs 8 & 17
Va 13° 12' E.

2.00 Leave plain and enter Sandhills bearing NE & S.

4.00 Set temporary 1/4 Sec. Cor.

8.14 Intersected W & S line 20 lks North of the corner to Secs 8, 9, 16 and 17 from which corner I run N 89° 51' West on true line between Secs 8 & 17
Va 13° 12' E.

4.00 7 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

8.14 The corner to Secs 7, 8 17 and 18

Sandhills Thickets
Balance fine sand

T. 27 N R 10 W 6th PM

West on random line
between Secs 7 & 18
Va 13° 12' E
4000 Set temporary 114 sec cor,
77.94 Intersected West boundary
5 lks South of the corner
to secs. 7 & 18 from which
corner I run
S 89° 58' East on true
line between secs 7 & 18
Va 13° 12' E
37.94 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 114 sec cor,
77.94 The corner to sections
7, 8, 17 and 18
Rich level plain
Soil first rate

T 27 N. R 10 W 6th PM

North between Secs 7 & 8
Va 13° 12' E.
4000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 114
sec cor,
8000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for ~~corner~~
to sections 5, 6, 7 & 8
Rich level plain
Soil first rate

T 27 N R 10 W 6th PM

East on random line
between secs 5 & 8
Va 13° 12' E.

4000 Set temporary 1/4 sec cor

80.20 Intersected N & S. line
20 lks North of the corner
to secs. 4, 5, 8 & 9 from
which corner I run
N 89° 51' West on true line
between secs 5 & 8
Va 13° 12' E.

40.10 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 sec. cor.

80.20 The corner to secs
5, 6, 7 and 8
Rich level plain
Soil firstrate

T 27 N R 10 W 6th PM

West on random line
between secs. 6 & 7
Va 13° 12' E

4000 Set post for temporary
1/4 sec cor.

77.82 Intersected West boundary
15 lks North of the corner
to secs. 6 & 7 from which
corner I run
N 89° 54' East on true line
between secs 6 & 7
Va 13° 12' E.

37.82 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
sec cor

77.82 The corner to sections
5, 6, 7 and 8
Rich level plain
Soil firstrate

T. 27 N R 10 W 6th Pm

North between Secs. 5 & 6
Va 13° 12' E.

4000 Set temporary 1/4 Sec. cor.

79.70 Intersected North
Boundary 30 lks West
of the corner to secs 5 & 6
from which corner
I run S
South 13' W. on true line
between Secs. 5 & 6
Va 13° 12' E

39.70 Set post deposited charred
Stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor.

79.70 The corner to Secs.
5. 6. 7 and 8
Rich level plain
Soil Firstrate

October 7th 1870.

T 27 N R 10 W 6th Pm

General Description:-

Generally this is a firstrate
Township being rich
friable alluvial,
sandy loam producing
very heavy grass
Except the portion
represented as sand
hills. There is no
distinct line of
demarcation between
the Rich level plain
and the Elkhorn
valley or bottom all being the
same kind of land.
There is some wood
scattered along the
Elkhorn River
principally Ash
Cottonwood & Elm
The Elkhorn is a
beautiful Stream of

T. 27 N. R 10 W 6th P.M.

Soft, pure, clear Spring Water, abounding in fish. The Township will sustain a large settlement.
The portion represented as Sandhills produces good grazing

T 27 N R 10 W 6th P.M.

List of Names—

A list of the names of the individuals employed to assist in running measuring or marking the lines and corners described in the foregoing field Notes of Township 27 North of the base line of Range No. 10 West of the 6th Principal Meridian, in the State of Nebraska showing the respective capacities in which they acted:

Robert Harvey, Chainman
Sol. C. Griffith—, Chainman
Bevington H Savage, Cornerman
Daniel Livingston, Cornerman
Walter Lawrence, Flagman

Surveyor Generals Office.
Plattsmouth Neb ~~Feb~~ Mch. 1. 1871.

The foregoing field notes of the survey of the subdivision lines of Township No. 27 North of the Base Line, of Range No. 10 West of the 6th Principal Meridian in the State of Nebraska, executed by James N. Paul under Joint Contract No. 32 dated August 4th. 1870. wherein Nicholas J and James N. Paul are Joint Contractors, in the month of October 1870. having been critically examined, the necessary corrections and explanations made the said field notes and the surveys they describe are hereby approved.

Robt. R. Livingston
Surveyor General.

We hereby certify that we assisted James N. Paul deputy Surveyor in Surveying the Subdivisional lines of Township 27 North of the Base line of Range No 10 West of the 6th Principal Meridian in the State of Nebraska, and that said Surveys have been, in all respects, to the best of our knowledge and belief, well and faithfully done and the Boundary Monuments planted according to the instructions furnished by the Surveyor General:—

Robert Harvey, Chainman.
Sent. C. Griffith, Chainman.
Henry [illegible] Savage, Cornerman.
Daniel Livingston, Cornerman.
Walter Lawrence Flagman.

Subscribed and sworn to by the above named persons before me a Notary Public for Douglas County in the State of Nebraska this 21st day of October A.D. 1870

Lewis S. Reed
Notary Public

I, James N. Paul, deputy Surveyor do solemnly
Contract wherein Nicholas J.
with Robert R. Livingston, United States
Iowa and Nebraska bearing date
have well faithfully and truly in my
Conformity with the instructions furnished
Manual and the Laws of the United
of Township No. 27 North of Range
in the State of Nebraska as are
Notes as having been done under
solemnly swear that all the corners
and perpetuated in strict
Manual and printed instructions
and original field Notes of such

Subscribed by said James N. Paul
me a Notary Public for
Nebraska this 22nd day of

Surveyor Generals
Approval see pg 68

swear that in pursuance of a joint
Paul and James N. Paul are joint Contractors
Surveyor General for the district of
the 4th day of August 1870 - I
own proper person and in strict
by the Surveyor General the Surveying
States surveyed the Subdivisional lines
No. 10 West of the 6th Principal Meridian in
represented in the foregoing field
my direction, and I do further
of said Surveys have been established
accordance with the Surveying
and that the foregoing are the true
Survey -

James N. Paul
Deputy Surveyor

deputy Surveyor and sworn to before
Douglas County in the State of
October 1870 -

Lewis S. Reed
Notary Public

Surveyor Generals Approval
see pg 68

Index Diagram
Town 28 N. R 10 W

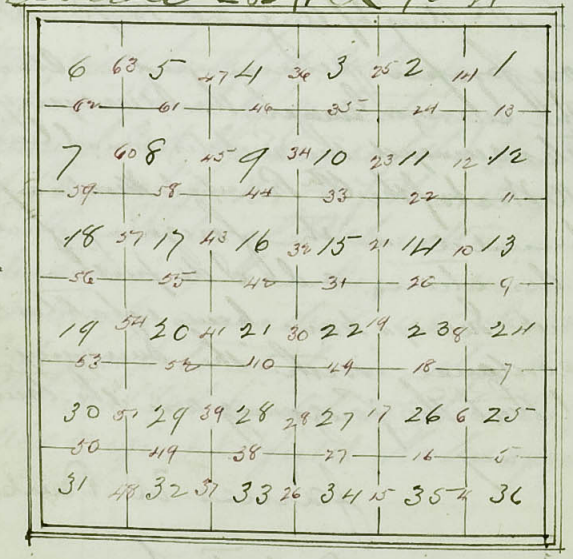

(a)

Field Notes

of the Subdivisional lines of Township No 28 North of the Base line. Range No 10 West of the 6th Principal Meridian in the State of Nebraska. Surveyed by James N. Paul deputy Surveyor. under joint Contract No 32 bearing date the 4th day of August 1870 wherein Nicholas J. Paul and James N. Paul are joint Contractors with Robert R. Livingston United States Surveyor General for the District of Iowa and Nebraska.

Survey Commenced Oct. 9th 1870

Survey Completed Oct. 13th 1870

(B.)

Names and duties of assistants

Robert Harvey } Chainmen
Lot C. Griffith }
Daniel Livingston } Cornermen
B. H. Savage }
Walter Lawrence, Flagman

T 28 N R 10 W 6th P M

To determine the proper adjustment of my Compass for subdividing this Township I begin at the corner to Townships 27 & 28 N, Ranges 9 and 10 West and run North on a blank line along East Boundary of sec. 36 va 13° 06' E

39.95 To the 1/4 Sec. Cor.
79.91 To the corner to secs 25 and 36 -

Therefore, my Compass is in proper adjustment for subdividing this Township.

Subdivision Commenced October 9th 1870 -

T 28 N R 10 W 6th P. M.

From the corner to sections 1, 2, 35 & 36 on the South boundary of the Township I run North between secs 35 & 36 Va 13° 06' E

18.00 Leave Bottom and enter Upland bears N 10° E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

81.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for Corner to sections 25, 26, 35 & 36

Bottom Jinstrate
Upland rolling
Soil Secondrate

T 28 N. R 10 W 6th P. M.

East on random line between secs. 25 & 36 Va 13° 06' E.

40.00 Set temporary 1/4 Sec. Cor

79.70 Intersected East boundary 35 lks North of the corner to secs. 25 & 36 from which corner I run N 89° 45' West on true line between secs 25 & 36 Va 13° 06' E

39.85 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

79.70 The corner to secs. 25, 26, 35 & 36

Rolling surface
Soil Sandy 2nd rate

T 28 N. R 10 W 6th P. M.

North between Secs 25 & 26
Va 13° 06' E

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor.

8000 Set post deposited charred stake and raised mound of Earth with pits as per instructions for Corner to sections 23, 24, 25 & 26
Surface rolling
Soil Sandy Second rate

T 28 N. R 10 W 6th P M

East on random line
between Secs. 24 & 25
Va 13° 06' E

4000 Set temporary 1/4 Sec cor.

79.70 Intersected East boundary 21 lks North of the corner to secs. 24 & 25 from which corner a bear. N 89° 51' West on true line between Secs 24 & 25
Va 13° 06' E

3985 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor.

79.70 The corner to sections 23, 24, 25 & 26
Land rolling
Soil Sandy 2nd rate

T. 28 N. R. 10 W. 6th P.M.

North between Secs 23 & 24
Va 13° 06' E.

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for Corner to Sections 13, 14, 23 & 24
Rolling Surface
Soil Sandy Secondary

T. 28 N. R. 10 W. 6th P.M.

East on random line
between Secs. 13 & 24
Va 13° 06' E

40.00 Set temporary 1/4 Sec. Cor.

79.84 Intersected East boundary 21 lks North of the corner to sections 13 & 24 from which corner I run N 89° 51' West on true line between Secs 13 & 24
Va 13° 06' E.

39.92 Set post deposited, charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

79.84 The corner to secs. 13, 14, 23 & 24.
Surface rolling
Soil Secondary

T 28 N R 10 W 6th P M

North between Secs 13 & 14
Va 13° 06' E

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor.

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to secs. 11, 12, 13 & 14

Land rolling
Soil Sandy 2nd rate

T 28 N R 10 W 6th P M

East on random line between Secs. 12 & 13
Va 13° 09' E

40.00 Set temporary 1/4 Sec Cor.

79.34 Intersected Eastboundary 20 lks North of the corner to secs. 12 & 13 from which corner I run N 89° 51' West on true line between Secs 12 & 13
Va 13° 09' E.

39.67 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor

79.34 The corner to secs. 11, 12, 13 and 14

Land Rolling
Soil Second rate

T. 28 N. R. 10 W. 6th P.M.

North between Secs 11 & 12
Va 13° 09' E.

40.00 Set post deposited
charred stake and
raised mound of earth
with pits as per
instructions for 1/4
Sec. cor.

80.00 Set post deposited
charred stake and
raised mound of
Earth with pits as
per instructions for
corner to sections
1, 2, 11 and 12,
Land rolling
Soil Secondrate

T. 28 N. R. 10 W. 6th P.M.

East on random line
between Secs. 1 & 12
Va 13° 09' E.

40.00 Set temporary 1/4 Sec Cor.

79.34 Intersected East boundary
35 lks North of the
corner to secs. 1 & 12
from which corner
I run N
N 89° 45' West on true
line between Secs. 1 & 12
Va 13° 09' E.

39.67 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 Sec
Corner

79.34 The corner to sections
1, 2, 11 and 12
Land rolling
Soil Secondrate

T 28 N. R 10 W 6th PM

North between Secs. 1 and 2
Va 13° 09' E.

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

77.75 Intersected 7th Standard Parallel N. 16.85 chs. West of the 1/4 Sec cor on the South boundary of sec 36 - T 29 N R 10 W and Set post deposited charred stake and raised mound of earth with pits as per instructions for Closing Corner to Sections 1 and 2
Land rolling
Soil Secondrate
October 9th 1870

T 28 N R 10 W 6th PM

North between Secs. 34 & 35
Va 13° 15' E.

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for Corner to Sections 26, 27, 34 & 35
Rich level Bottom
Soil firstrate

T. 28 N. R 10 W 6th RM

East on random line
between Secs 26 & 35
Va 13° 15' E

40.00 Set temporary 114 sec. cor

52.00 Leave Bottom and enter
Upland bears N & S E

80.22 Intersected N & S line
4 3 lks North of the corner
to secs. 25, 26, 35 & 36
from which corner
I run
N 89° 42' West on true line
between Secs. 26 & 35
Va 13° 15' E

40.11 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
114 Sec. Cor.

80.22 The corner to sections
26, 27, 34 & 35
Bottom firstrate
Upland Secondrate

T 28 N R. 10 W 6th RM

North between Secs. 26 & 27
Va 13° 15' E

17.00 Leave lower Bottom and
enter high plateau bears
E and W

40.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
114 Sec cor

80.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
Corner to Sections
22, 23, 26 & 27
Land rich valley
Soil firstrate

T. 28 N. R. 10 W 6th PM

East on random line
between Secs 23 & 26
Va 13° 15' E

40.00 Set temporary 1/4 Sec Cor.

46.00 Leave High Bottom and
enter rolling hills bearing
North and South

79.86 Intersected N & S line
20 lks North of the corner
to sections 23, 24, 25 & 26
from which corner I run
N 89° 57' West on true line
between Secs 23 & 26
Va 13° 15' E.

59.93 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 Sec
Corner

79.86 The corner to sections
22. 23. 26 and 27
Valley Firstrate
Upland or Secondrate

T. 28 N. R. 10 W 6th PM

North between Secs. 22 & 23
Va 13° 15' E.

40.00 Set post deposited,
charred stake and raised
mound of earth with pits
as per instructions
for 1/4 Sec cor.

80.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
corner to sections 14
15. 22 and 23
Rich level plateau
Soil Firstrate

T. 28 N R 10 W 6th PM

East on random line
between Secs 14 & 23
Va 13° 15' E.

40.00 Set temporary 1/4 Sec Cor.

44.00 Leave Valley and enter
rolling Upland bears S & W.

79.96 Intersected N & S line 3 chs
North of the corner to secs
13, 14, 23 & 24 from
which corner I run
N 89° 59' West on true line
between Secs 14 & 23
Va 13° 15' E.

34.98 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor.

79.96 The corner to sections
14, 15, 22 and 23
Valley rich Firstrate.
Upland rolling
Soil Secondrate

T. 28 N R 10 W 6th PM

North between Secs 14 & 15
Va 13° 15' E.

40.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec. cor.

42.00 Leave Valley and enter
Rolling Upland bears
N and S E

80.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
Corner to Sections
10, 11, 14 and 15
Valley level Firstrate
Upland rolling Clayey
Soil Secondrate

T 28 N R 10 W 6th PM

East on random line
between Secs 11 & 14
Va 13° 15' E

40.00 Set temporary 1/4 Sec. Cor.
80.10 Intersected N & S line
15 lks North of the corner
to secs 11, 12, 13 & 14 from
which corner I run
N 89° 34' West on true line
between Secs 11 & 14
Va 13° 15' E

40.05 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for 1/4
Sec. Cor.
80.10 The corner to sections
10, 11, 14 and 15
Rolling & hilly
Soil Secondrate

T 28 N R 10 W 6th PM

North between Secs. 10 & 11
Va 13° 15' E.

40.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor.
80.00 Set post deposited
charred stake and raised
mound of earth with pits
as per instructions for
corner to sections
2, 3, 10 & 11
Land rolling
Soil Clayey Secondrate

T 28 N R 10 W 6th PM

East on random line
between Secs 2 & 11
Va 13° 15' E.

4000 Set temporary 1/4 sec. cor.
8000 Intersected N & S line 12 chs
North of the corner to
Secs. 1, 2, 11 and 12, from
which corner I run
N 89° 55' West on the
line between Secs 2 & 11
Va 13° 15' E.

4000 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec. Cor.

8000 The corner to secs
2, 3, 10 and 11
Land rolling
Soil good Secondrate

T 28 N R 10 W 6th PM

North between Secs 2 & 3
Va 13° 15' E

4000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 Sec. Cor.

7685 Intersected the 17th Standard
Parallel N. 16.70 chs. West of
the 1/4 Sec cor on the
South boundary of sec 35
T 29 N R 10 West
Set post deposited
charred stake and raised
mound of earth with pits
as per instructions for
Closing Corner to secs
2 and 3
Land rolling
Soil Secondrate

October 10th 1870

T 28 N R 10 W 6th PM

North between Secs 33 & 34
Va 13° 15' E.

21.90 Elkhorn river 80 lks wide runs SW. Enter woods on Right Bank

34.60 Elkhorn River 75 lks wide runs SE Leave wood on Right bank

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 114 sec cor.

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to secs 27, 28, 33 & 34
Rich level Bottom
Soil Firstrate
Timber Cottonwood Ash and Elm

T 28 N R 10 W 6th PM

East on random line between Secs 27 & 34
Va 13° 15' E.

4000 Set temporary 114 Sec. cor.

79.90 Intersected N & S. line 6 lks South of the corner to secs 26, 27, 34 and 35 from which corner I run S 89° 57' West on true line between Secs. 27 & 34
Va 13° 15' E.

39.95 Set post deposited charred stake and raised mound of earth with pits as per instructions for 114 Sec. cor.

79.90 The corner to sections 27, 28, 33 and 34
Rich level Bottom
Soil Firstrate

T 28 N R 10 W 6th PM

North between Secs 27 & 28
Va 13° 15' E,

3700 Leave lower and enter high Bottom or plateau bears N W & S E,

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 114 Sec cor,

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 21, 22, 27 and 28
Land level
Soil Firstrate

T 28 N R 10 W 6th PM

East on random line between Secs 22 & 27
Va 13° 15' E

4000 Set temporary 114 Sec cor,

8006 Intersected N & S line 15 lks South of the corner to secs. 22, 23, 26 and 27 from which corner I run S 89° 54' West on true line between secs 22 & 27
Va 13° 15' E,

4003 Set post deposited charred stake and raised mound of earth with pits as per instructions for 114 Sec cor

8006 The corner to sections 21, 22, 27 and 28
Rich level plateau
Soil Firstrate

T 28 N R 10 W 6th PM

North between Secs 21 & 22
Va 13°15' E

40.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor

80.00 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 15, 16, 21 and 22
Rich level plateau
Soil fine sand

T 28 N R 10 W 6th PM

East on random line between Secs 15 & 22
Va 13°15' E

40.00 Set temporary 1/4 Sec Cor

80.10 Intersected W & S line 5 lks South of the corner to secs 14, 15, 22 and 23 from which corner S 89°58' West on true line between Secs 15 & 22
Va 13°15' E

40.05 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor

80.10 The corner to sections 15, 16, 21 and 22
Rich level plateau
Soil fine sand

T 28 N. R 10 W 6th PM

North between Secs 15 & 16
Va 13° 15' E

40,00 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec Corner

48,00 Leave plateau and enter high rolling Clayey hills bearing NW and SE.

80,00 Set post deposited charred stake and raised mound of earth with pits as per instructions for Corner to sections 9, 10 15 & 16

Plateau level Jurstrate
Balance rolling Secondrate

T. 28 N R 10 W 6th PM

East on random line between Secs 10 & 15
Va 13° 15' E.

40,00 Set temporary 1/4 Sec cor.

80,04 Intersected N & S line at the corner to secs 10, 11, 14 and 15 from which corner I run

West on true line between Secs. 10 & 15
Va 13° 15' E.

40,02 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor.

80,04 The corner to sections 9, 10, 15 & 16

Rolling Clayey hills
Soil Secondrate

T 28 N R 10 W 6th PM

North between secs. 9 & 10
Va 13° 15' E

4000 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

8000 Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to sections 3, 4, 9 and 10
Rolling Clayey hills
Soil Secondrate

T 28 N R 10 W 6th PM

East on random line
between secs 3 & 10
Va 13° 15' E.

4000 Set temporary 1/4 Sec. Cor.

79.96 Intersected West line 10 chs North of the corner to secs 2, 3, 10 and 11 from which corner I send
N 89° 56' West on true line
between secs 3 & 10
Va 13° 15' E.

39.98 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 sec. cor.

79.96 The corner to sections 3, 4, 9 and 10
Land rolling Clayey hills - Soil Secondrate

T 28 N R 10 W 6th PM

North between Secs 3 & 4
Va 13° 15' E,

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 sec cor,

76.05 Intersected 7th Standard Parallel S. 16.60 chs West of the 1/4 sec cor on the South boundary of sec 34 T 29 R 10 W
Set post deposited charred stake and raised mound of earth with pits as per instructions for closing Corner to sections 3 & 4
Rolling Clay hills
Soil Secondrate

October 11th 1870

T. 28 N R 10 W 6th PM

North between Secs 32 & 33
Va 13° 15' E

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor

65.00 Leave High & Enter lower Bottom bearing NW and SE,

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 28, 29, 32 and 33
Land level Bottom
Soil firstrate
lower Bottom produces heavy grass,

T. 28 N. R. 10 W. 6th P.M.

	East on random line between Secs 28 & 33 Va 13° 15' E
40.80	Set temporary 1/4 Sec Cor.
42.30	Elkhorn River 80 lks wide runs S.E. - Scattering timber on banks
80.08	Intersected N & S line 5 lks South of the corner to sections 27, 28, 33 and 34 from which corner S. run S 89°58' West on true line between Secs 28 & 33. Va 13° 15' E
40.04	Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor
80.08	The corner to sections 28, 29, 32 and 33 Rich level Bottom Soil choice first rate

T. 28 N. R. 10 W. 6th P.M.

	North between Secs 28 and 29 Va 13° 15' E.
18.00	Elkhorn River 80 lks wide runs S.E. Timber on left Bank
28.50	Same River 70 lks wide runs S.W. Leave grove at left Bank
41.00	Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.
53.75	Same River 90 lks wide runs S.E. Scattering trees on banks
80.00	Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 20, 21, 28 and 29 Rich level Bottom Soil first rate Timber, cottonwood and Willow with Undergrowth of same, and Plum and Vines

T 28 N R 10 W 6th PM

East on random line between Secs 21 and 28
Va 13° 15' E

1800 Leave lower Bottom and enter plateau bears NW and SE

4000 Set temporary 1/4 Sec cor.

80.22 Intersected N & S line 8 lks North of the corner to secs 21, 22, 27 and 28 from which corner I run N 89° 57' West on true line between Secs. 21 & 28
Va 13° 15' E

40.11 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

8022 The corner to sections 20, 21, 28 and 29
Choice rich level
Soil Firstrate

T. 28 N R 10 W 6th PM

North between Secs 20 & 21
Va 13° 15' E.

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec cor

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to Sections 16, 17, 20 and 21
Choice rich level Bottom
Soil Firstrate

T 28 N R 10 W 6th PM

East on random line
between Secs 16 & 21
Va 13° 15' E.

600 Leave lower Bottom and enter
Plateau bears NW and SE

4000 Set temporary 1/4 Sec cor.

8010 Intersected N & S line
10 lks North of the corner
to secs 15, 16, 21 and 22
from which corner I run
N 89° 56' West on true line
between Secs 16 & 21
Va 13° 15' E.

4005 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec. cor.

8010 The corner to sections
16, 17 20 and 21
Land rich level
soil Firstrate

T 28 N R 10 W 6th PM

North between Secs. 16 and 17
Va 13° 15' E.

4000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec cor.

4500 Leave Valley and enter
high dry Upland bears E & NW.

8000 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions. for
corner to sections
8, 9, 16 and 17
Valley firstrate
Upland rolling 2nd rate

T. 28 N R 10 W 6th PM

East on random line
between Secs 9 and 16
Va 13° 15' E.

4000 Set temporary 1/4 Sec. cor.

79.94 Intersected N. & S. line
10 lks North of the corner
to secs. 9.10.15 and 16 from
which corner I run
N 89° 56 West on true line
between Secs 9 & 16
Va 13° 15' E

3997 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec cor.

79.94 The corner to sections
8.9.16 and 17
Rolling Clayey hills
Soil Secondrate

T 28 N R 10 W 6th PM

North between Secs 8 & 9
Va 13° 15' E.

4000 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec. cor.

8000 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for corner
to sections 4.5.8 and 9
Rolling Clayey hills
Soil Secondrate

T 28 N R 10 W 6th P M

East on random line
between Secs 4 & 9
Va 13° 15' E.

40.00 Set temporary 1/4 Sec. cor.
80.04 Intersected N & S line
18 lks North of the corner
to sections 3, 4, 9 and 10
from which corner I run
N 89° 52' West on true line
between Secs 4 & 9
Va 13° 15' E

40.02 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 sec cor
80.04 The corner to secs. 4
5, 8 and 9
Rolling Clayey hills
Soil Secondrate

T 28 N R 10 W 6th P M

North between Secs. 4 & 5
Va 13° 15' E

40.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4 Sec. Cor.
75.20 Intersected 7th Standard
Parallel N. 16.40 chs West of
the 1/4 Sec. cor. on the South
boundary of Sec 33 T. 29
R 10 W. where I
Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for Closing
Corner to sections 4
and 5
Rolling Clayey hills
Soil Secondrate

October 19th 1870

T 28 N R 10 W 6th PM

North between secs 31 & 32
Va 13° 15' E.

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor.

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for corner to sections 29, 30, 31 and 32
Rich level plateau
Soil Firstrate

T 28 N R 10 W 6th PM

East on random line between secs. 29 & 32
Va 13° 15' E.

4000 Set temporary 1/4 Sec. cor.

7200 Leave plateau and enter lower Bottom bears NW & SE.

7994 Intersected N & S line 16 lks North of the corner to sections 28, 29, 32 and 33 from which corner I run N 89° 53' West on true line between Secs 29 & 32
Va 13° 15' E.

3997 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. cor.

7994 The corner to sections 29, 30, 31 and 32
Rich level land
Soil Firstrate

T. 28 N R 10 W 6th PM

West on random line
between Secs 30 & 31
Va 13° 15' E.

4000 Set temporary 1/4 sec cor.

77.30 Intersected West boundary
12 lks South of the corner
to secs. 30 & 31 from
which corner I run
S 89° 55' East on true line
between Secs 30 & 31
Va 13° 15' E

37.30 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec. cor

77.30 The corner to secs.
29. 30. 31 and 32
Rich level plateau
Soil Firstrate

T. 28 N R 10 W 6th PM

North between Secs. 29 & 30
Va 13° 15' E.

4000 Set post deposited
charred stake and raised
mound of earth with pits
as per instructions for
1/4 Sec cor.

8000. Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for Corner
to sections 19. 20. 29 & 30
Rich level plateau
Soil Firstrate

T 28 N R 10 W 6th PM

East on random line
between Secs 20 & 29
Va 13° 15' E.

32.00 Leave plateau and enter
lower Bottom bears NW & SE

4000 Set temporary 1/4 sec cor,

50.20 Elkhorn River 60 lks wider
runs SE.

79.88 Intersected N & S line 12 lks
North of the corner to secs
20, 21, 28 & 29 from which
corner I run
N 89° 55' West on true line
between Secs 20 & 29
Va 13° 15' E

39.94 Set post deposited charred stake
and raised mound of earth
with pits as per instructions
for 1/4 Sec cor,

79.88 The corner to sections
19, 20, 29 and 30
Land level and rich
Soil Firstrate

T 28 N R 10 W 6th PM

West on random line
between Secs 19 & 30
Va 13° 15' E

4000 Set temporary 1/4 Sec cor,

77.44 Intersected West boundary
8 lks South of the corner
to sections 19 & 30 from
which corner I run
S 89° 57' East on true line
between Secs 19 & 30
Va 13° 15' E.

37.44 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor,

77.44 The corner to Sections
19, 20, 29 and 30
Rich level plateau
Soil Firstrate

T. 28 N. R. 10 W. 6th P.M.

North between Secs. 19 & 20
Va 13° 15' E.

4000 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

4000 Leave Plateau and enter lower bottom bearing N. and S.E.

8000 Set post deposited charred stake and raised mound of earth with pits as per instructions for Corner to secs. 17, 18, 19 and 20
Soil rich level first rate

T. 28 N. R. 10 W. 6th P.M.

East on random line between Secs. 17 and 20
Va 13° 15' E.

31,00 Enter woods bearing N.W. & S.E.

31,50 Elkhorn River 100 lks wide runs S.E. Leave woods on Right Bank

40,00 Set temporary 1/4 Sec. Cor.

79,82 Intersected Wand's line 23 lks North of the corner to sections 16, 17, 20 and 21 from which corner I run
N. 89° 50' West on true line between Secs. 17 & 20
Va 13° 15' E.

39,91 Set post deposited charred stake and raised mound of earth with pits as per instructions for 1/4 Sec. Cor.

79,82 The corner to sections 17, 18, 19 and 20
Rich level bottom
Soil first rate. rather low for agriculture

T 28 N R 10 W 6th PM

West on random line
between Secs 18 & 19
Va 13° 15' E,

39.00 Leave lower Bottom and
enter Plateau bears NW & SE

40.00 Set temporary 1/4 Sec. Cor,

77.58 Intersected West boundary
20 lks South of the corner to
sections 18 and 19 from which
corner I run
S 89° 51' East on true line
between Secs 18 & 19
Va 13° 15' E,

37.58 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor

17.58 The corner to sections
17, 18, 19 and 20
Goodrich land
Soil Firstrate
Lower Bottom is a
little wet,

T 28 N R 10 W 6th PM

North between Secs 17 & 18
Va 13° 15' E,

15.50 Elkhorn River 50 lks wide
runs S.E. Banks lined
with timber

40.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for 1/4
Sec. Cor.

48.00 Enter high Bottom bears NW & East

80.00 Set post deposited charred
stake and raised mound
of earth with pits as per
instructions for corner
to secs 7, 8, 17 & 18
Rich level Bottom
Soil firstrate
producing heavy grass
but a little too low
for Agriculture

T 28 N R 10 W 6th PM

East on random line
between Secs 8 and 17
Va 13° 15' E.

4000 Set temporary 1/4 Sec. Cor.

6400 Leave Valley and enter Upland
bears NW and SE

79.80 Intersected W. S line 5 chs
North of the corner to Secs
8, 9, 16 and 17 from which
Corner S 9 runs
N 89° 58' West on true line
between Secs 8 & 17,
Va 13° 15'

3990 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec. Cor

79.80 The corner to secs
7, 8, 17 and 18
Valley Firstrate
Upland rolling
Secondrate

T. 28 N R 10 W 6th PM

West on random line
between Secs 7 & 18
Va 13° 15' E.

3800 Leave plateau and enter lower
Bottom bears NW and SE.

4000 Set temporary 1/4 Sec. Cor.

6600 Elkhorn river 75 lks wide
runs SE. banks lined with trees

+17.77 Intersected West boundary
20 chs South of the corner to
Sections 7 and 18 from
which corner S 9 runs
S 89° 51' East on true line
between Secs 7 & 18
Va 13° 15' E

37.77 Set post deposited charred stake
and raised mound of earth
with pits as per instructions
for 1/4 Sec. Cor

+17.77 The corner to secs. 7, 8, 17
and 18
Level rich bottom
Soil Firstrate
Timber Cottonwood and
Willow

T. 28 N R. 10 W 6th PM

North between Secs 7 & 8
Va 13° 15' E.

3400 leave plain and enter rolling Clayey hills bearing NW and SE

4000 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec cor.

8000 Set post deposited chained stake and raised mound of earth with pits as per instructions for corner to sections 5, 6, 7 and 8

Plateau Primary
Balance rolling
Secondary

T 28 N R 10 W 6th PM

East on random line
between Secs 5 & 8
Va 13° 15' E.

4000 Set temporary 1/4 Sec. cor.

79.92 Intersected Mrs. line 1/4 chs, South of the corner to Secs 4, 5, 8 and 9 from which corner I run S 89° 54' West on true line between Secs 5 & 8
Va 13° 15' E.

39.96 Set post deposited chained stake and raised mound of earth with pits as per instructions for 1/4 Sec Cor.

79.92 The corner to Sections 5, 6, 7 and 8
Rolling Clay hills
Soil Secondary

T. 28 N R 10 W 6th PM

West on random line
between Secs 6 & 7
Va 13° 15' E

40.00 Set temporary 1/4 Sec cor

77.70 Intersected West boundary
42 lks South of the corner
to Secs 6 and 7 from
which Corner I run
S 89° 42' East on true line
between Secs 6 & 7
Va 13° 15' E

37.70 Set post deposited charred
stake and raised mound of
earth with pits as per
instructions for 1/4
Sec Cor

77.70 The corner to sections
5, 6 7 and 8
Land rolling clay hills
Soil Secondrate

T 28 N R 10 W 6th PM

North between Secs 5 & 6
Va 13° 15' E

40.00 Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
1/4 Sec cor

75.33 Intersected 7th Standard
Parallel N. 16.27 chs West
of the 1/4 sec cor, on the
South boundary of sec 3 ~~4~~ 2
T 29 N, R 10 W, and
Set post deposited charred
stake and raised mound
of earth with pits as
per instructions for
Closing Corner to secs.
5 & 6
Land rolling clay hills
Soil Secondrate

October 13th 1870

T. 28 N R 10 W 6th P.M.

General Description

There is a large amount of good land in this Township represented as lower Bottom and high Bottom or plateau. The soil is a fine state loam with sand and clay mixed — There is a belt of timber mostly Cottonwood along the river which is a beautiful stream of water. The upland in the township is fine state for grazing —

T. 28 N R 10 W 6th P.M.

A List of Names

A list of the names of the individuals employed to assist in running, measuring or marking the lines & corners described in the foregoing field notes of Township No. 28 North of the base line of Range No. 10 West of the 6th Principal Meridian in the State of Nebraska showing the respective capacities in which they acted =

Robert Harvey, Chainman
Sol. C. Griffith, Chainman
Berington H. Savage, Cornerman
Daniel Livingston, Cornerman
Walter Lawrence, Flagman

T. 28. N. R. 10 W 6th P M

We hereby certify that we assisted James H. Paul deputy Surveyor, in Surveying the Subdivisional lines of Township No. 28 North of the Base line of Range No. 10 West of the 6th Principal Meridian in the State of Nebraska, and that said Surveys have been in all respects, to the best of our knowledge and belief well and faithfully Surveyed and the Boundary Monuments planted according to the instructions furnished by the Surveyor General

Robert Harvey Chainman
Sgt. C. Griffith Chainman
Benjamin H. Savage Cornerman
Daniel Livingston Cornerman
Walter Lawrence Flagman

Subscribed and sworn to by the above named persons, before me a Notary Public for Douglas County in the State of Nebraska this 21st day of October A D 1870

Lewis S. Reed
Notary Public

I, James N. Paul, Deputy Surveyor, do solemnly
Contract, wherein Nicholas J. Paul and
with Robert R. Livingston, United States
Iowa and Nebraska, bearing date the 14th
well faithfully and truly in my
conformity with the instructions furnished
Surveying Manual and the Laws of
Subdivisional lines of Township
No. 10 West of the 6th Principal Meridian
represented in the foregoing field Notes
directions; and I do further solemnly
Surveys have been established
accordance with the Surveying
and that the foregoing are the
of such Survey.

Subscribed and sworn to by
before me a Notary Public
State of Nebraska this 22nd

Swear that in pursuance of a joint
James N. Paul are joint Contractors
Surveyor General for the District of
day of August A.D. 1870. I have
own proper person and in strict
by the Surveyor General, the
the United States, Surveyed the
No. 28 North of the Base line of Range
in the State of Nebraska, as are
as having been done under my
swear that all the corners of said
and perpetuated in strict
Manual and printed instructions.
true and original field Notes

James N. Paul
Deputy Surveyor

Said James N. Paul, deputy Surveyor,
for Douglas County in the
day of October 1870

Lewis S. Reed
Notary Public

Surveyor General's Office
Plattsmouth Neb. March 1. 1871

The foregoing field notes of the survey of the subdivision lines of Township No. 20 North of the Base Line, of Range No. 10 West of the 6th Principal Meridian, in the State of Nebraska, executed by James A. Paul under joint Contract No. 32 dated August 4th. 1870. wherein Nicholas J. and James A. Paul are joint Contractors, in the month of October 1870. having been critically examined, the necessary corrections and explanations made, the said field notes and the surveys they describe are hereby approved.

Robt R. Livingston
Surveyor General

General Land Office • Original Field Notes

Book Number

361

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.
