General Land Office • Original Field Notes

Book Number

631

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.

Index Diagram

Town 9 N. Range 41 W

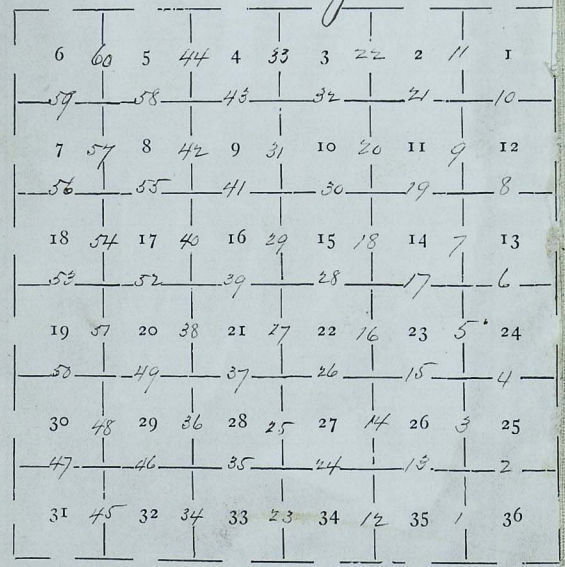

Field Notes

of

The survey and Subdivision of Township No. 9 N. R. 41 W. 6th P.M.

in the

State of Nebraska

Executed

By John R. Patrick Deputy Surveyor under joint Contract No. 62 dated June 29th 1872

Survey

Commenced Aug. 3rd 1872

Completed August 9th " 1872

List of names

of persons employed to assist in surveying this Township showing the respective Capacities in which they acted

H. H. Williams	Chainman
T. Daily	Chainman
C. Reobrig	Flagman
T. M. Robinson	Moundman

Township 9. N.R. 41 W. 6th P.M.

Chains	To determine the proper adjustment of my compass for the Subdivision of this Township I commence at the corner to Townships 9. N.R. 40 W. and ~~Township 9 N.R.~~ 41 W. and run North on a blank line along the east boundary of sec. 36 Va. 13°.55' E.
39.60	to a point 41 links E. of ¼ cor
79.82	to a point 81 links East of the Cor. to Sec. 25 and 36.
	To retrace this line or run parallel thereto my compass must be adjusted to a Variation 14°.30' E.

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 35 & 36 Va. 14° 30' E.
40	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	Set Post deposit charred stake raised mound of earth with pits as per intructions for Cor. to sec. 25. 26. 35 and 36
	Land rolling
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 25 and 36 Va. 14° 30' E.
40	Set Post for temporary 1/4 sec. cor
80	intersected 5th Guide Mer. W. East boundary of Township 10 N.R. of Cor to sec 25 & 36 from which Tran
N 89° 56'	West on a true line between sec. 25 and 36 Va. 14° 30' E
40	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	The cor. to sec. 25. 26. 35. 36
	Land rolling
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 25 and 26 Va. 14° 30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor. to sec. 23. 24. 25 and 26
	Land rolling
	Soil 2° rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 24 and 25 Va. 14° 30' E
40	set Post for temporary 1/4 sec. cor.
79.90	intersected 5th Guide Mer. W. East boundary of Township 14 N. of cor. to sec. 24. 25 from which Gran N 89° 54'
	West on a true line between sec. 24 and 25 Va. 14° 30' E
39.95	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.90	The cor. to sec. 23. 24. 25 & 26
	Land rolling prairie
	Soil 2° rate

Township 9. N.R. 41 W. 6th P.M.

Chains	
	North between sec. 23 and 24
	Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor to sec. 13. 14. 23 and 24
	Land rolling
	Soil 2° rate

Township 9. N.R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 13 and 24
	Va. 14° 30' E
40	set Post for temporary 1/4 sec. cor
79.86	intersected 5th Guide Mer W. East Boundary of Township 17 Lns N of cor to sec. 13 & 24 from which Gran N 89° 33'
	West on a true line between sec. 13 and 24
	Va. 14° 30' E
39.93	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.86	The cor. to sec. 13. 14. 23 and 24
	Land rolling
	Soil 2° rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	North between sec. 13 and 14
	Va. 14°30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor to sec. 11. 12. 13 and 14
	Land rolling
	Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 12 and 13
	Va. 14°30' E
40	set Post for temporary 1/4 sec. cor
79.68	intersected 5th Guide Mer W. East boundary of Township 14 N of Cor. to sec. 12 & 13 from which Grun N 89° 54'
	West on true line between sec. 12 and 13
	Va 14°30' E.
39.89	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.68	The cor. to sec. 11. 12. 13 & 14
	Land level prairie
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains.	North between sec. 11 and 12 Va. 14° 30' E
40	set Post deposit charred stake raise a mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raise a mound of earth with pits as per instructions for Cor to sec. 1. 2. 11 & 12

Land level prairie
Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	East on a random line between sec. 1 and 12 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor.
79.70	intersected 5th guide meri. W. East boundary of Township 14 links South of the cor. to sec. 1 and 12 from which Gran S. 89. 54 W. on a true line between sec. 1 and 12 Va. 14° 30' E
39.85	set Post deposit charred stake raise mound of earth with pits as per instructions for 1/4 sec. cor
79.70	The cor. to sec. 1. 2. 11 and 12

Land rolling prairie
Soil 2d rate

Aug 3rd 1872

Township 9 N. R. 41 W. 6th P.M.

Chains	
	North on a random line between sec. 1 and 2 Va. 14° 30' E
45	set Post for temporary 1/4 sec. cor
68.50	crossed a draw or drain with gravel bottom bears E. N. W.
80.55	intersected North boundary of Township 23 limits last of Cor. to sec. 1 and 2. from which Gran S. 10' E. on a true line between sec. 1 and 2 Va. 14° 30' E.
40.55	set Post - deposit charred stake raised mound of earth with pits as per instruction for 1/4 sec. cor.
80.55	The. Cor to sec. 1, 2, 11 & 12
	Land rolling Soil 2d rate on S. and sandy on the N. end of line

Township 9 N. R. 41 W. 6th P.M.

Chains	
	North between sec. 34 and 35 Va. 14° 30' E.
40	set Post - deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post - deposit charred stake raised mound of earth with pits as per ~~contract~~ instructions for Cor. to sec. 26, 27, 34, 35
	Land rolling prairie Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	East on a random line between Sec. 26 and 35 — Va. 14° 30' E
40	set Post for temporary 1/4 Sec. Cor
80	intersection N D S line 1.5 lks N of Cor to Sec. 25, 26, 35 and 36 from which Brass N 89° 54' West on a true line between Sec. 26 and 35 — Va. 14° 30' E.
40	set Post - deposit - Charred stake raised mound of earth with pits as per instructions for 1/4 Sec. Cor.
80	The Cor to Sec 26, 27, 34 & 35

Land level prairie
Soil 2d Rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North between Sec. 26 & 27 Va. 14° 30' E.
40	set Post deposit - charred stake raised mound of earth with pits as per instructions for 1/4 Sec. Cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to Sec. 22, 23, 26 and 27

Land rolling
Soil 2d Rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 23 and 26
	Va. 14°30' East
40	set Post for temporary 1/4 sec. cor
80.12	intersected N. and S. line 21 lks N of Post Cor to sec. 23, 24, 25 & 26 from which Iran N 89°51'
	West on true line between sec. 23, 26.
	Va. 14°30' E.
40.06	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.12	The cor to sec. 22, 23, 26 & 27
	Land rolling prairie
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 22 and 23
	Va. 14°30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor,
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor to sec. 14, 15, 22 & 23
	Land rolling
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

chains	
	East on a random line between Sec. 14 and 23 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
80.22	intersected North and South line 17 links N. of cor to sec. 13, 14, 23 and 24 from which Gran N. 89 53 W. on a true line between Sec. 14 and 23 Va. 14° 30' E.
40 11	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.22	The cor to Sec. 14, 15, 22, 23

Land rolling prairie
Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North between Sec. 14 and 15 Va 14° 30' E.
40	set Post deposit charred stake ~~80~~ raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor to Sec. 10, 11, 14 & 15

Land level prairie
Soil 2d rate

Township 9 north R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 11 and 14 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor.
80.38	intersected N. & S. line 9 links N. of cor. to sec. 11, 12, 13, 14. from which I ran S. 89.56 W. on a true line between sec. 11 and 14 Va. 14° 30' E.
40.19	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.38	The cor. to sec. 10, 11, 14 & 15

Land level on line
Soil 2d rate

Aug. 1st 1872

Township 9 N. R. 41 W. 6th P.M.

Chains	
	North between sec. 10 & 11 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
	~~Land gently rolling prairie Soil 2d rate~~
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to sec. 2, 3, 10 & 11

Land gently rolling prairie
Soil 2d rate

Aug 5th 1872

Township 9 N. R. 41 W. 6th P.M.

Chains	
	East on a random line between Sec. 2 and 11 Va. 14° 30' E.
40	set Post for temporary 1/4 Sec. cor
80.29	intersected N. and S. line 16 links W. of cor to Sec. 1.2.11.12 from which I run W. 89.53 W. on a true line between Sec. 2 and 11 Va. 14° 30' E.
40.14½	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 Sec. cor.
80.29	The cor. to Sec. 2.3.10 & 11
	Land gently rolling prairie Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	North on a random line between Sec. 2 & 3. Va. 14° 30' E
40	set Post for temporary 1/4 Sec. cor
70.40	Crossed draw or drain with gravel bottom bears E & W.
79.92	intersected North boundary of Township 9 links West of the cor. to Sec. 2 and 3 from which I run S. 3' W. on true line between Sec. 2 and 3 Va. 14° 30' E.
39.92	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 Sec. cor.
79.92	The cor. to Sec. 2.3.10 and 11
	Land rolling Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 33 and 34 Va. 14° 30' E.
40	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	Set Post deposit charred stake raised mound of earth with pits as per instruction for cor to sec. 27, 28, 33, and 34
	Land level on line Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 27 and 34 Va. 14. 30
40	Set Post for temporary 1/4 sec. cor
80	intersected N. & S. line 26 Lks N of cor. to sec. 26, 27, 34 and 35 from which I run N 89° 49' West on a true line between sec. 27 and 34 Va. 14° 30' E.
40	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80	The cor to sec. 27, 28, 33 & 34
	Land level prairie on line but rolling to the northward Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	North between sec. 27 & 28 Va. 14°30' E
40	Set Post deposit charred stake raised mound of earth with pits as per instruction for 1/4 sec. cor.
80	Set Post deposit charred stake raised mound of earth with pits as per instructions for cor to sec. 21, 22, 27 & 28
	Land rolling
	Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 22 and 27 Va 14°30' E.
40	Set Post for temporary 1/4 sec. cor
80.02	intersected N & S. line 15 links N. of the Post cor. to sec. 22, 23, 26, and 27 from which Gran N 89.54 W. on a true line between sec. 22, and 27. Va 14°30' E.
4001	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.02	The cor. to sec. 21, 22, 27, 28
	Land rolling
	Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	North between sec. 21 and 22 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor to sec. 15.16.21 and 22
	Land rolling soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	East on a ~~transition~~ line between sec. 15 and 22 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
80.14	in the sector N & S. line 8 links N. of the cor to sec. 14, 15, 22 & 23 from which I ran W. 89° 57' W. on a true line between sec. 15 and 22 Va. 14° 30' E.
40.07	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.14	The cor. to sec. 15.16.21 & 22
	Land gently rolling prairie soil 2d rate

Township 9 N.R 41 W 6th P.M.

Chains	North between sec. 15 & 16 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor. to sec. 9, 10, 15 and 16

Land gently rolling
Soil 2d rate

Township 9 N.R 41 W. 6th P.M.

Chains	East on a random line between sec. 10 and 15 — Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
79.84	intersected N. & S. line 9 links S. of the cor. to sec. 10, 11, 14 & 15 from which I ran S 89. 56 W. on a true line between sec. 10 and 15 Va. 14° 30' E.
39.92	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.84	The cor. to sec. 9, 10, 15 and 16

Land rolling
Soil 2d rate

Aug 6th 1872

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 9 and 10
	Va. 14° 30' E.
40	Set Post deposit charred stake
	raised mound of earth
	with pits as per instructions
	for 1/4 Sec. Cor.
80	Set Post deposit charred
	stake raised mound of
	earth with pits as per
	instructions for Cor. to Sec.
	3, 4, 9 and 10
	Land level
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	E on a random line
	between sec. 3 and 10
	Va. 14° 30' E.
40	Set Post for temporary 1/4 sec. cor
80.18	intersected N. and S. line 8
	links S. of the cor to sec. 2, 3, 10
	and 11, from which I run
	S. 89. 57 W. on a true line
	between sec. 3 and 10
	Va. 14° 30' E.
400.9	Set Post deposit charred stake
	raised mound of earth
	with pits as per instructions
	for 1/4 Sec. Cor.
80.18	The cor. to sec. 3, 4, 9 and 10
	Land rolling gently
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North on a random line between sec. 3 and 4 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
72.60	crossed drain or draw with gravel bottom bears E and W.
80.42	intersected North boundary of Township 16 Lks W of Cor to sec 3 and 4 from which I ran South 7 W on a true line between sec. 3 and 4 Va. 14° 30' E.
40.42	set Post-deposit-charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.42	The cor. to sec. 3.4. 9 and 10

Land gently rolling
Soil sand at the north end of line
2° rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 32 and 33. Va. 14° 30' E.
40	set Post-deposit-charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post-deposit-charred stake raised mound of earth with pits as per instructions for cor. to sec. 28. 29. 32. 33.

Land gently rolling
Soil 2° rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	East on a random line between Sec. 28 and 33. Va 14° 30' E.
40	Set Post for temporary 1/4 Sec. Cor
80	intersected N. & S. line 11 lks N of Post-Cor to Sec. 27. 28. 33. 34 from which Bran N 89° 45' West on a true line between Sec. 28 and 33 Va. 14. 30
40	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	The cor. to. sec. 28. 29. 32. 33.
	Land rolling Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	North between Sec. 28 and 29 Va. 14° 30' E
40	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	Set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to Sec. 20. 21. 28. and 29
	Land rolling Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 21 and 28 Va. 14° 30' E.
40	Set Post for temporary 1/4 sec. cor.
80.04	intersected N & S line 14 links N of Post cor. to sec. 21, 22, 27 and 28, from which I ran
N 89° 54'	West on a true line between sec. 21 and 28 Va. 14° 30' E.
40.02	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80.04	Cor. to sec. 20, 21, 28 and 29
	Land level prairie soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	North between sec. 20 and 21 Va. 14° 30' E.
40	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	Set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to sec. 16, 17, 20 and 21
	Land gently rolling prairie Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	East on a random line between Sec. 16 and 21 Va. 14°30' E
40	set Post for temporary ¼ Sec. Cor
80.12	Intersected North and South line 5 links S. of the cor to Sec. 15, 16, 21 and 22 from which I ran S. 89°58' W. on a true line between Sec. 16 and 21 Va. 14°30' E.
40.06	set Post deposit charred stake raised mound of earth with pits as per instructions for ¼ Sec. Cor.
80.12	The cor to Sec. 16, 17, 20 & 21

Land level

Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

Chains	
	North between Sec. 16 & 17 Va. 14°30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for ¼ Sec. Cor.
80	set Post deposit charred stake raised mound of earth with pits as per instruction for cor to Sec. 8, 9, 16 & 17

Land gently rolling

Soil 2d rate

Aug. 7th 1872

Township 9 N. R. 41 W. 6th P.M.

chains	
	East - on a random line between sec. 9 and 16 Va. 14° 30' E
40	set Post for temporary 1/4 sec. cor.
79.94	intersected N. & S. line 8 links S. of the cor. to sec. 9. 10. 15 & 16 from which I ran S 89° 57' W. on a true line between sec. 9 and 16 Va. 14° 30' E
39.97	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.94	The cor. to sec. 8. 9. 16 and 17

Land level prairie. - so level that I could plainly see the mound on the N & S. line

Soil 2° rate

Township 9 N R 41 W. 6th P.M.

chain	
	North between sec. 8 and 9 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to sec. 4. 5. 8 and 9

Land rolling

Soil 2 rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 4 and 9 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor.
79.90	intersected N. and S. line 13. links S. of the Post-cor to sec. 3. 4. 9 and 10 from which I ran S. 89.54 W. on a true line between sec. 4 and 9 Va. 14° 30' E.
39.95	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.90	The cor. to sec. 4. 5. 8 and 9

Land rolling
Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North on a random line between sec. 4 & 5 Va. 14.30
40	set Post for temporary 1/4 sec. cor
74	crossed draw or drain with gravel bottom bears E. & W.
80.36	intersected North Township line 27 links East of the cor to sec. 4 and 5 from which I ran S. 12' E. on a true line between sec. 4 and 5 Va. 14° 30' E.
~~40.36~~	
40.36	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.36	The cor to sec. 4. 5. 8 and 9

Land rolling prairie
Soil 2d rate

Township 9. N.R. 41 W. 6th P.M.

Chains	
	North between sec. 31 and 32 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to Sec. 29. 30. 31 and 32
	Land. rolling
	Soil 2d rate

Township 9. N.R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 29 and 32 Va. 14° 30' E
40	set Post for temporary 1/4 sec. cor
80.03	intersected N. and S. line 13.6 1/2 N of cor. to sec. 28. 29. 32 and 33 from which I ran N 89° 55'
	West on a true line between sec. 29 and 32 Va. 14° 30' E.
40.01 1/2	set Post deposit charred stake raised mound of earth with pits as per instruction for 1/4 sec. cor.
80.03	The cor. to sec. 29. 30. 31 and 32
	Land. rolling
	Soil 2d rate

Township 9. N.R. 41 W. 6th P.M.

chains	
	West between sec. 30 and 31 on a random line
	Va. 14°30' E.
40	set Post for temporary 1/4 sec. cor.
79.95	intersected West boundary of Township 16 lks N of cor to sec. 30 and 31. from which I ran
N 89°53'	East on a ~~random~~ true line between sec. 30 and 31
	Va. 14°30' E.
39.95	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.95	The cor. to sec. 29. 30. 31. and 32
	Land rolling
	Soil 2d rate

Township 9. N.R. 41 W. 6th P.M.

chains	
	North between sec. 29 and 30
	Va. 14°30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor. to sec. 19. 20. 29 and 30
	Land rolling
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	East on a random line between sec. 20 and 29 Va. 14°30' E.
40	set Post for temporary ¼ sec. cor
80.07	intersected N. & S. line 3 links S. of Post cor. to sec. 20.21.28.29 from which Gran S. 89.59 W. on a true line between sec. 20 and 29 Va. 14°30' E.
40.03½	set Post deposit charred stake raised mound of earth with pits as per instructions for ¼ sec. cor.
80.07	The cor to sec. 19.20.29.30

Land rolling
Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	West on a random line between sec. 19 and 30 Va. 14°30' E.
40	set Post for temporary ¼ sec. cor
79.90	intersected West boundary of Township 5 links N. of the cor to sec. 19 & 30 from which Gran N. 89.58 E on a true line between sec. 19 and 30 Va. 14°30' E.
39.90	set Post deposit charred stake raised mound of earth with pits as per instructions for ¼ sec. cor
79.90	The cor. to sec. 19.20.29 & 30

Land rolling prairie
Soil 2d rate

Aug 5th 1872

Township 9 N. R. 41 W. 6th P.M.

chains	
	North between sec. 19 and 20 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor. to sec. 17, 18, 19 & 20.
	Land level prairie soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

chains	
	East on a random line between sec. 17, and 20 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
80.12	intersected N. and S. line 5 links S. of the cor. to sec. 16, 17, 20 & 21 from which I ran S 89° 58' W. on a true line between sec. 17 and 20 Va. 14° 30' E
40.06	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.12	The cor. to sec. 17, 18, 19 and 20
	Land gently rolling prairie soil 3d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	West on a random line between Sec. 18 and 19 Va. 14°30' E
40	set Post for temporary 1/4 sec. cor
79.84	intersected West boundary of Township 12 N.R. N of cor to sec 18 and 19 from which Gran
N 89°55'	East on a true line between Sec. 18 and 19 Va. 14°30' E
39.84	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
79.84	The cor. to Sec. 17, 18, 19 & 20
	Land level prairie Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North between Sec. 17 and 18 Va. 14°30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor. to Sec. 7, 8, 17 and 18
	Land gently rolling Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

chains	
	East on a random line between sec. 8 and 17 Va. 14°30' E
40	set Post for temporary 1/4 sec. cor
80	intersected N. & S. line 6 links North of the Post cor to sec. 8.9 16. and 17 from which Gran W. 89.57 W. on a true line between sec. 8 & 17 Va. 14°30' E.
40	set Post deposit charred stake raised mound of earth with fits as per instructions for 1/4 sec. cor.
80	The cor. to sec. 7.8.17 and 18
	Land rolling
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

chains	
	West on a random line between sec. 7 and 18 Va. 14°30' E.
40	set Post for temporary 1/4 sec. cor
79.68	intersected West boundary of Township 10 links S. of cor to sec. 7 and 18 from which Gran S 89.56 E. on a true line between sec. 7 and 18 Va. 14°30' E
39.68	set Post deposit charred stake raised mound of earth with fits as per instructions for 1/4 sec. cor.
79.68	Cor. to sec. 7.8.17 and 18
	Land rolling
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 7 and 8 Va. 14° 30' E
40	set Post-deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post-deposit charred stake raised mound of earth with pits as per instructions for cor. to sec. 5.6. 7 and 8.
	Land rolling
	Soil 2d rate

Township 9 N.R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 5 and 8 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor.
80.02	intersected N. & S. line 15 South of cor. to sec. 4.5. 8 and 9 from which I ran S. 89° 54' W. on a true line between sec. 5 and 8 Va. 14° 30' E.
40.01	set Post ~~deposit~~ charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.02	Cor. to sec. 5.6. 7 and 8
	Land level on line. The cor. on N. & S. line in plain sight
	Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

chains	
	West on a random line between Sec. 6 and 7 Va. 14° 30' E.
40	Set Post for temporary 1/4 sec. cor.
79.23	intersected West boundary of Township 34 links N. of the cor. to sec. 6 and 7 from which I run N. 89 45' E. on a true line between sec. 6 and 7 Va. 14° 30' E.
39.23	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.23	The cor. to sec. 5. 6. 7 and 8

Land rolling
Soil 2d rate

Township 9 N. R. 41 W. 6th P.M.

chains	
	North on a random line between sec. 5 and 6 Va. 14° 30' E.
40	Set Post for temporary 1/4 sec. cor.
79.50	Crossed draw or drain with gravel bottom bears E & W.
80.59	intersected North boundary of Township 27 links W. of cor. to sec. 5 and 6. from which I run S. 12' W. on a true line between sec. 5 and 6 Va. 14° 30' E.
40.59	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.59	The cor. to sec. 5. 6. 7 and 8

Land somewhat broken
Soil 2d rate

Aug 9th 1872

General Description

This Township is all gently rolling prairie except at the North side where it is a little broken and sandy The soil is very light having but a thin layer. undu-neath coarse gravel. - only fit for light grazing

2d Rate.

A. List
of the names of the individuals
who assisted in running-
measureing and marking
the subdivision lines and
Corners of Township No 9
North Range 41 West of
the 6th Principal Meridian

H. H. Williams	Chainman
Thomas Daily	Chainman
Charles Rochrig	Flagman
J. M. Robinson	Moundman

We hereby certify that we assisted John. R. Patrick deputy Surveyor in subdividing Township 9 North Range 41 West of the 6th Principal Meridian and that said Township has been in all respects, to the best of our Knowledge and belief well and faithfully surveyed and the boundary monuments planted according to the instructions of the Surveyor General

Harry Williams Chainman
[illegible] Chainman
Chas Roehrig Flagman
J. W. M. Robinson Mounaman

Subscribed and sworn to by the above named persons before me a Notary Public in and for the County of Lancaster in the state of Nebraska. this 29th. day of Nov 1872

Thos H. Hyde
Notary Public

I John R. Patrick do solemnly swear that in pursuance of a joint contract No 62 wherein John R. Patrick and H. B. Stout are joint contractors with E. E. Cunningham United States Surveyor General for the district of Nebraska and Iowa bearing date the 29th day of June A.D. 1872

I have well faithfully and truely in my own proper person and in strict conformity with the instructions of the Surveyor General the Surveying manual and the Laws of the United States Surveyed all those parts or portions of the Township No 9 North of the Base line of Range 41 West of the 6th Principal Meridian in the State of Nebraska, as are represented in the foregoing Field Notes as having been surveyed under my direction, and I do further solemnly swear that all the corners of said surveys have been established and perpetuated in strict accordance with the

Surveying manual and Printed instructions and that the forgoing are the true and original Field Notes of said Survey

Jno R Patrick

Deputy Surveyor

Subscribed by the said John R Patrick Deputy surveyor and sworn to before me a Notary Public within and for the County of Lancaster in the State of Nebraska this 29th day of November A.D. 1872

Thos. H. Hyde
Notary Public

Surveyor General's Office
Plattsmouth Jany 6th 1873

The forgoing Field Notes of the Survey and Subdivision of Township No 9 North of the Base Line. of Range No 41 West of the 6th Principal Meridian in the State of Nebraska. Executed by Jno. R. Patrick Deputy Surveyor under joint Contract No 62 Dated June 29th 1872. Wherein John R Patrick and H. B. Stout are joint Contractors, in the Month of August 1872, having been Critically Examined the necessary corrections and Explanations made, the said Field Notes and Surveys they describe are hereby approved

E. E. Cunningham
Surveyor General

Index Diagram of Town 10 N. Range 41 W.

6	60	5	44	4	33	3	22	2	11	1
59		58		43		32		21		10
7	57	8	42	9	31	10	20	11	9	12
56		55		41		30		19		8
18	54	17	40	16	29	15	18	14	7	13
53		52		39		28		17		6
19	51	20	38	21	27	22	16	23	5	24
50		49		37		26		15		4
30	48	29	36	28	25	27	14	26	3	25
47		46		35		24		13		2
31	45	32	34	33	23	34	12	35	1	36

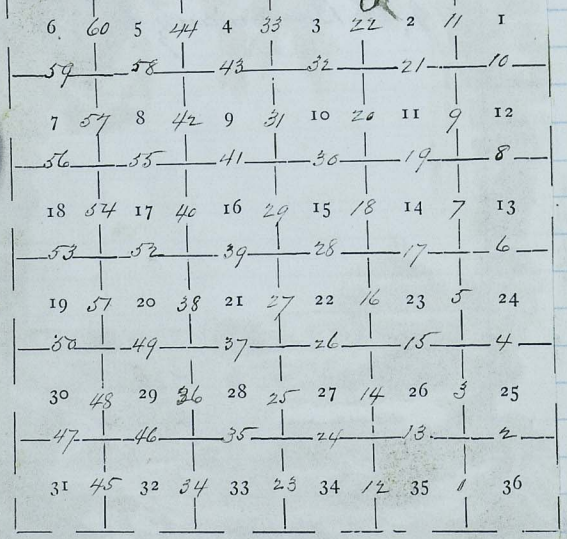

Field Notes of

The Survey and Subdivision of Town-Ship No. 10. N. R. 41 W. 6th P. M. in the State of Nebraska

Executed By John R. Patrick Dep^y Surveyor under joint contract No. 62 dated June 29th 1872

Survey commenced July 27th 1872
Completed Aug 1 2nd 1872

List of names of persons employed to assist in surveying this Township showing the respective capacities in which they acted

Harry H. Williams	Chainman
Thomas Daly	Chainman
Charles Roehrig	Flagman
John M. Robinson	Moundman

Township 10. N. R. 41 W. 6th P. M.

Chains	
	To determine the proper adjust-ment of my Compass for the Subdivision of this Township I commenced at the corner to Townships 10 N. R. 40 and T. 10 N R. 41 W. and run on 5th Guide mer. W North on a blank line along the East-Boundary of Sec. 36 Variation 13°.56' E.
40	To a point 42 lks E of the ¼ sec. cor
80	To a point 93 links East of the Cor. to Sec. 25 and 36.
	To retrace this line or run parallel thereto my compass must be adjusted to a Variation of 14°30' East

Township 10 N. R. 41 W. 6th P.M.

chains	
	From the Cor. to Sec. 35 and 36 on the South boundary of the Township I run North between Sec. 35 and 36
	Variation 14°.30' E
40	set Post deposit Charred Stake raised mound of earth with pits as per instructions for 1/4 Sec. Cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to Sec. 25. 26. 35 and 36
	Land level Prairie Soil
	Sandy with gravel 2d rate

Township 10 N. R. 41 W. 6th P.M.

chains	
	East on a Random line between Sec. 25 and 36
	Variation 14°.30' E.
40	set Post for temporary 1/4 Sec. Cor
80	intersected East boundary of Township 5 chs N. of Cor. to Sec. 25 & 36
	from which Cor I ran
N. 89°.58'	West on true line between Sec. 25 & 36
	Variations 14°.30' E.
40	set Post deposit Charred stake raised mound of earth with pits as per instructions for 1/4 Sec. Cor.
80	The Cor. to Sec. 25. 26. 35 and 36
	land level 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	North between sec. 25 and 26 Va. 14°30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 Sec. Cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor to Sec. 23. 24. 25 and 26
	Land level soil 2d rate

Township 10. N. R. 41 W. 6th P. M.

Chains	East on a random line between sec. 24 and 25 Va. 14.30 E.
40	set Post for temporary 1/4 sec. cor.
80.09	Intersected East boundary of Township 7 Chs W. of Post Cor. to Sec. 24 and 25 from which Tran
N89°57'	West on true line between Sec. 24 and 25 Va. 14°30' E.
40.04 1/2	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 Sec. Cor.
80.09	The cor. to sec. 23. 24. 25 and 26
	Land level soil 2d rate

Township 10. N. R. 41 W. 6th P. M

chains	
	North between Sec. 23 and 24 Va. 14°30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instruction for cor to sec. 13. 14. 23 and 24
	Land. level soil 2d rate

Township 10. N. R. 41 W. 6th P. M

chains	
	East on a random line between sec. 13 and 24 Va. 14°30' E.
40	set Post for temporary 1/4 sec. cor
80	Intersected East boundary of Township 14 lks N of Post cor. to sec. 13 and 24 From which Cor. I ran
N. 89°54'	West on a true line between sec. 13 & 24 Va. 14.30
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	The cor to sec. 13. 14. 23 & 24
	Land Rolling soil 2d rate

Township 10 N. R. 41 W. 6th P. M

chains	North between Sec. 13 and 14 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for ¼ Sec. Cor.
80	set Post deposit charred stake raised mound of earth with pits as per. instructions for cor to sec. 11, 12, 13 and 14
	Land Rolling soil 2d rate

Township 10 N. R. 41 W. 6th P. M

chains	East on a random line between Sec. 12 & 13, Va. 14° 30' E
40	set Post for temporary ¼ sec. cor
80	intersected East boundary of Township at Post cor. to Sec. 12 and 13. from which I run West on true line between Sec. 12 and 13 Va. 14° 30' E
40	set Post deposit charred stake raised mound of earth with pits as per instruction for ¼ sec. cor.
80	The cor to sec. 11, 12, 13, and 14
	Land Rolling soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 11 and 12
	Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80	set Post deposit charred stake raised mound of earth with pits as per instruction for Cor to sec. 1, 2, 11 and 12
	Land gently rolling
	Soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	
	East between sec. 1 & 12
	on a Random line
	Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
80.60	intersected east boundary of Township 20 links North of cor to sec. 1 and 12
	From which I run ~~west~~
	north 89.51 west on true line
	between sec. 1 and 12
	Va. 14° 30' E.
40.30	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80.60	The Cor to sec. 1, 2, 11 and 12
	Land Rolling soil 2d rate

Township 10 N. R. 41 W. 6th P. M.

Chains	
	North on a random line between Sec. 1 and 2 Va. 14° 30' E
40	set Post for temporary 1/4 sec. cor.
79.40	intersected North boundary of Township 55 links East of Cor. to Sec. 1 and 2 from which I run South 24' East on true line between Sec. 1 and 2 Va. 14° 30' E
39.40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.40	The cor to sec. 1, 2, 11 and 12
	Land gently rolling prairie soil 2d rate

Township 10 N. R. 41 W. 6th P. M.

Chains	
	North between Sec. 34 and 35 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to Sec. 26, 27, 34 and 35
	Land level soil 2d rate

July 29th 1872

Township 10 N. R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 26 & 35 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
80.04	intersected N. & S line 11 links South of cor. to sec. 25.26.35.36 from which I run South 89.55 West on true line between sec. 26 and ~~35~~ 35 Va. 14° 30' E
40.02	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.04	The cor to sec. 26.27.34 & 35
	Land level. soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	
	North between sec. 26 and 27 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to sec. 22, 23, 26. and 27
	Land gently rolling prairie soil 2d rate

Township 10 N.R. 41 W., 6th P.M.

Chains	
	East on a random line between sec. 23 and 26 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
80	intersected M. & S. line 18 lks. N. of Cor to sec. 23. 24. 25 and 26 from which I run N 89° 30' West on a true line between sec. 23 and 26 Va. 14° 30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor,
80	The cor to sec. 22. 23. 26 & 27
	Land Rolling soil 2d rate

Township 10 N.R. 41 W., 6th P.M.

Chains	
	North between sec. 22 and 23 Va. 14° 30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to sec. 14. 15. 22 and 23
	Land Rolling soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

chains	
	E. on a random line between sec. 14 and 23 Va. 14°30' E
40	set Post for temporary 1/4 sec. cor
80.07	intersected N & S. line ~~at~~ 6 lks N. of Post Cor. to sec. 13. 14. 23 and 24 From which cor I run
N. 89°57'	West on true line between sec. 14 and 23
40.03½	Va 14°30' E
40.03½	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.07	The cor. to sec. 14. 15. 22. & 23

Land gently Rolling
Soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

chains	
	North between sec. 14 and 15 Va. 14°30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor to sec. 10. 11. 14 and 15

Land rolling prairie
Soil 2d rate

Township 10 N. R. 41 W 6th PM

Chains	
	East on a random line between sec. 11 and 14 Va. 14° 30' E
40	set Post for temporary 1/4 sec. Cor
79.80	intersected N & S. line 25 links South of Post-Cor to sec. 11, 12, 13 and 14 from which I ran South 89.49 West on true line between sec. 11 & 14 Va. 14° 30' E
39.90	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. Cor.
79.80	The Cor. to sec. 10, 11, 14 & 15
	Land rolling Soil 2d rate

Township 10 N. R. 41 W. 6th PM

Chains	
	North between sec. 10 and 11 Va. 14° 30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. Cor
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to sec. 2, 3, 10, and 11
	Land rolling Soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	East on a random line between Sec. 2 and 11 Va. 14.30 E
40	set Post for temporary 1/4 sec. cor
80.15	intersected N. & S. line 14 links South of the Post Cor to Sec. 1. 2. 11 and 12 from which I run South 89.54 West on a true line between Sec. 2 and 11 Va. 14°30' E
40.07½	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.15	The cor. to Sec. 2. 3. 10 and 11

Land rolling prairie soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	North on a random line between Sec. 2 and 3 Va. 14°30' E
40	set Post for temporary 1/4 sec. cor
80	intersected North boundary of Township 10 links West of Cor. to Sec. 2 and 3 from which I run South 4' West on true line between Sec. 2 and 3 Va. 14°30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80	The cor. to Sec. 2. 3. 10 and 11

Land rolling soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	
	North between Sec. 33 and 34
	Va. 14°30' E
40	Set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 Sec. Cor
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to Sec. 27. 28. 33 and 34
	Land gently rolling prairie soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	
	East on a random line between Sec. 27 and 34
	Va. 14°30' E.
40	set Post for temporary 1/4 Sec. Cor.
79.30	intersected N. & S. line 22 links South of the Post Cor. to Sec. 26. 27. 34 and 35 from which Gem South 89.57 West on true line between Sec. 27 & 34
	Va. 14°30' E
39.65	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 Sec. Cor.
79.30	The cor. to Sec. 27. 28. 33 & 34
	Land gently rolling soil 2d rate

July 30th 1872

Township 10 N. R. 41 W. 6th P. M

chains	North between sec. 27 and 28 Va. 14° 30' E
40	set Post deposit Charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit Charred stake raised mound of earth with pits as per instructions for Cor. to sec. 21. 22. 27 and 28
	Land gently rolling Soil 2d rate

Township 10 N. R. 41 W. 6th P. M

chains	East on a random line between sec. 22 and 27 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor.
80.10	intersected N. & S line 12 links South of the Post Cor to sec 22. 23. 26 & 27 from which I run South 89. 55 West on a true line between sec. 22 and 27 Va. 14° 30' E
40.05	set Post deposit Charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80.10	The Cor to sec. 21. 22. 27 & 28 L
	Land rolling Soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	
	North between Sec. 21 and 22 Va. 14°30' E
40	set Post deposit Charred Stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit Charred Stake raised mound of earth with pits as per instructions for Cor. to Sec. 15. 16. 21 and 22
	Land rolling soil 2d rate

Township 10. N. R. 41 W. 6th P.M.

Chains	
	East on a random line between Sec. 15 and 22. Va. 14°30' E
40	set Post for temporary 1/4 sec. cor.
79.78	intersected N. & S. line 15 links South of the Post cor. to Sec. 14. 15. 22 and 23 from which Gran
	South 89°54' West on true line between Sec. 15 and 22 Va. 14°30' E.
39.89	set Post deposit Charred Stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.78	The cor. to Sec. 15. 16. 21 & 22
	Land gently rolling prairie soil 2d rate

Township 10 N.R. 41 West 6th P.M.

Chains	
	North between sec. 15 and 16
	Va. 14°30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. Cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to sec. 9. 10. 15 and 16
	Land rolling soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 10 and 15
	Va. 14°30' E.
40	set Post for temporary 1/4 sec. cor
80.02	intersected N & S. line 13 lks S of Cor to sec. 10. 11. 14 & 15 from which Green
389°55'	West on true line between sec. 10 and 15
	Va 14°30' E
40.01	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. Cor.
80.02	The corner to Secs. 9. 10. 15 & 16.
	Land rolling prairie soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	
	North between sec. 9 and 10 Va. 14°30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to sec. 3. 4. 9 and 10
	Land rolling soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	
	E. on a random line between sec. 3 and 10 Va. 14°30' E.
40	set Post for temporary 1/4 sec. cor.
79.81	intersected N. & S. line 9 links South of the cor. to sec. 2. 3. 10 and 11. from which True South 89°52' West on true line between sec. 3 and 10 Va. 14°30' E.
39.90½	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
79.81	The cor. to. sec. 3. 4. 9 and 10
	Land rolling prairie soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

chains	
	North on a random line between sec. 3 and 4 Va. 14° 30' E
40	set Post for temporary 1/4 sec. cor
80.27	intersected North boundary of Township 31 links East of Cor. to sec. 3 and 4 from which I run S. 13' East on a true line between sec. 3 and 4 Va 14° 30' E.
40.27	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.27	The cor. to sec. 3.4.9 & 10
	Land rolling prairie soil 3d rate

Township 10 N. R. 41 W. 6th P.M.

chains	
	North between sec. 32 + 33 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor. to sec. 28. 29. 32 and 33
	Land rolling soil 3d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	E. on a random line between sec. 28 & 33 Va. 14°30'
40	set Post for temporary 1/4 sec. cor
80	intersected N. & S. line 9 links North of the cor to sec. 27, 28 33 and 34 from which Gram N. 89.56' West on true line between sec. 28 and 33 Va. 14°30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80	The cor. to sec. 28, 29, 32, 33

Land rolling gently
soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	North between sec. 28 & 29 Va. 14°30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor. to sec. 20, 21, 28 and 29

Land rolling soil 2d rate

July 31st 1872

Township 10 N.R. 41 W. 6th P.M.

chains	East between sec. 21 and 28 on a random line Va. 14° 30' E
40	set Post for temporary 1/4 sec. cor
80.13	intersected N. & S. line 14 links North of the cor to sec. 21, 22, 27 and 28. from which I saw N. 89.54 W. on true line between sec. 21 and 28 Va. 14° 30' E
40.06 1/2	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.13	The cor to sec. 20, 21, 28 & 29

Land rolling prairie
Soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

chains	North between sec. 20 and 21 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raise mound of earth with pits as per instructions for cor. to sec. 16, 17, 20 and 21

Land rolling soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 16 and 21 Va. 14°30' E.
40	Set Post for temporary 1/4 sec. cor.
80.09	intersected N. & S. line of lists North of the Post cor. to sec 15.16.21 & 22 from which Gran N. 89.56 W. on a true line between sec. 16 and 21 Va. 14°30' E
40.04½	Set Post deposit Charred Stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.09	The cor to sec. 16.17.20 and 21
	Land rolling soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	
	North betw sec. 16 and 17 Va. 14°30' E.
40	Set Post deposit Charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	Set Post deposit Charred stake raised mound of earth with pits as per instructions for cor to sec. 8.9.16 and 17.
	Land rolling prairie soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	
	East on a random line between sec. 9 and 16 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
80.35	intersected N. & S. line 2 7/links North of the cor. to sec. 9. 10. 15 and 16 from which I ran N. 89. 48 W. on a true line between sec. 9 and 16 Va. 14° 30' E
40 17 1/2	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80.35	The cor to sec. 8. 9. 16 and 17
	Land rolling soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 8 and 9 Va. 14° 30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor to sec. 4. 5. 8 and 9
	Land gently rolling prairie soil 2d rate

Township 10 N.R. 41 West 6th P.M.

Chains	
	East ~~on~~ a random line between Sec. 4 and 9 Va. 14°30' E
40	set Post for temporary 1/4 sec. cor.
80.20	intersected N & S. line 19 links N. of the cor to sec. 3. 4. 9 and 10. from which I ran N 89.52 W. on a true line between Sec. 4 and 9 Va. 14°30' E
40.20	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.20	The cor to Sec. 4. 5. 8 and 9
	Land level prairie soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 4 and 5 on a random line Va. 14°30' E
40	set Post for temporary 1/4 sec. cor.
79.65	intersected North boundary of Township 21 links West of cor. to sec. 4 and 5 from which I ran S. 9' W. on a true line between sec. 4 and 5 Va. 14°30' E
39.65	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
79.65	The cor to sec. 4. 5. 8 and 9
	Land Rolling soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	
	North between sec. 31 and 32
	Va. 14° 30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to sec. 29. 30. 31 and 32
	Land rolling prairie
	soil 2d rate

Township 10 N. R. 41 W. 6th P.M.

Chains	
	East on a random line
	between sec. 29 and 32
	Va. 14° 30' E
40	set Post for temporary 1/4 sec. cor
79.82	intersect N. & S. line 5 links N.
	of the cor. to sec. 28. 29. 32 & 33 from
	which I run
	N 89. 58 W. on a true line
	between sec. 29 and 32
	Va. 14° 30' E.
39.91	set Post deposit charred stake raised
	mound of earth with Pits as
	per instructions for 1/4 sec. cor
79.82	The cor. to sec. 29. 30. 31 and 32
	Land level on line rolling
	to the N & S. soil 2d rate

Township 10 N.R. 41 W 6th P.M.

Chains	
	West on a random line between sec. 30 and 31 Va. 14°30' E.
40	set Post for temporary 1/4 sec. cor
78.29	intersected West boundary of Township 19 links South of Cor to sec. 30 and 31 From which I run S. 89.52 E. on a true line between sec. 30 and 31 Va 14°30' E.
38.29	set Post deposit charred stake raised mound of earth with pits as per instructions for N. 1/4
78.29	The cor. to sec. 29. 30. 31. and 33.
	Land rolling soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 29 and 30 Va. 14°30' E
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor to sec. 19. 20. 29 and 30
	Land rolling prairie soil 2d rate
	Aug 1st 1872

Township 10 N.R. 41 W. 6th P.M.

Chains	East on a random line between sec. 20 and 29 Va. 14° 30' E
40	set Post for temporary 1/4 sec. cor
80.03	intersected N. & S. line 2.8 lks N. of cor. to sec. 20. 21. 28 and 29 from which I ran N 89° 48' West on true line between sec. 20 and 29 Va. 14° 30' E
40.01½	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.03	The cor. to sec. 19. 20. 29. 30
	Land level. Soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	West on a random line between sec. 19. and 30 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
78.41	intersected West boundary of Township 9 links S. of cor to sec. 19 and 30 from which I ran S. 89. 56 E. on a true line between sec. 19 and 30 Va. 14° 30' E.
38.41	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
78.41	The cor to. sec 19. 20. 29 and 30
	Land level Soil 2d rate

Township 10 N. R. 41 W. 6th P. M.

Chains	
	North between sec. 19 & 20 Va. 14° 30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. Cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for cor. to sec. 17, 18, 19 and 20
	Land, Rolling prairie Soil 2d rate

Township 10 N. R. 41 W. 6th P. M.

Chains	
	East on a random line between sec. 17 and 20 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
80.34	intersected N. & S. line 17 links N. of cor to sec. 16, 17, 20 & 21 from which I run N. 89. 53 W. on a true line between sec. 17 & 20 Va. 14° 30' E
40.17	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.34	The cor. to sec. 17, 18, 19, 20
	Land level prairie Soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	
	West on a random line between sec. 18 & 19 Va. 14°30' E.
40	set Post for temporary ¼ sec. cor
78.44	intersected West boundary of Township 7 links South of the cor. to sec. 18 & 19 from which I run S. 89.57 E. on a true line between sec. 18 & 19 Va. 14°30' E.
38.44	set Post deposit charred stake raised mound of earth with pits as per instructions for ¼ sec. cor.
78.44	The cor. to sec. 17, 18, 19, 20.
	Land level prairie Soil 2d rate

Township 10 N.R. 41 W. 6th P.M.

Chains	
	North between sec. 17 and 18 Va. 14°30' E.
40	set Post deposit charred stake raised mound of earth with pits as per instructions for ¼ sec. cor.
80	set Post deposit charred stake raised mound of earth with pits as per instructions for Cor. to sec. 7, 8, 17 and 18
	Land Rolling prairie Soil 2d rate

chains	
	East on a random line between sec. 8 & 17 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
80.55	intersected N. & S. line 29 links N. of the cor. to sec. 8. 9. 16 and 17 from which I ran North 89° 48' West on true line between sec. 8 and 17 Va. 14° 30' E.
40.27 1/2	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
80.55	The cor. to sec. 7. 8. 17. & 18.
	Land rolling soil Grade

chains	
	West on a random line between sec. 7 and 18 Va. 14° 30' E.
40	set Post for temporary 1/4 sec. cor
78.83	intersected West boundary of Township 10 Links South of cor. to sec. 7 and 18 from which I ran S. 89.56 E. on a true line between sec. 7 and 18 Va. 14° 30' E.
38.83	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
78.83	The cor. to sec. 7. 8. 17 and 18
	Land rolling soil 2d Grade

Township 10. N.R. 41 W. 6th Prin.

North between sec. 7 and 8
Va. 14° 30′ E.
40 set Post deposit charred stake
raised mound of earth with
pits as per instructions for
1/4 sec. cor.
80. set Post deposit charred stake
raised mound of earth with
pits as per instructions for
cor. to sec. 5. 6. 7 and 8

Land level Prairie
Soil 2nd rate

Township 10 N.R. 41 W. 6th P.M.

East on a Random line
between sec. 5 and 8
Va. 14° 30′ E.
40 set Post for temporary 1/4 sec. cor
80.42 intersected N. and S. line 15 links
N. of the cor to sec. 4. 5. 8 D. 9
from which I run
N. 89. 54 W. on a true line
between sec. 5 and 8
Va. 14° 30′ E.
40.21 set Post deposit charred stake
raised mound of earth with
pits as per instructions for
1/4 sec. cor.
80.42 The cor to sec. 5. 6. 7. and 8

Land rolling prairie
Soil 2nd rate

Township 10 N.R. 41 W. 6th P.M.

chains	West on a random line between sec. 6 & 7 Va. 14° 30' E.
40	Set Post for temporary 1/4 sec. cor
78.94	intersected West boundary of Township 19 links South of cor. to sec. 6 & 7 from which I ran South 89.52. E. on a true line between sec. 6 and 7 Va. 14° 30' E.
38.94	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. cor.
78.94	The cor. to Sec 5. 6. 7 and 8
	Land rolling Soil mixed with lime 2d rate

Township 10 N.R. 41 W. 6th P.M.

chains	North on a random line between sec. 5 and 6. Va. 14° 30' E.
40	Set Post for temporary 1/4 sec. cor
78.70	intersected North Boundary of Township 30 links West of the cor. to sec. 5 and 6 from which I ran South 13' West on a true line between sec. 5 and 6 Va. 14° 30' E.
38.70	set Post deposit charred stake raised mound of earth with pits as per instructions for 1/4 sec. Cor
78.70	~~intersected~~ The cor. to sec. 5. 6. 7. & 8
	Land rolling Soil 2d rate
	Aug 2d. 1872

General Discription

This whole of this Township is gently rolling prairie, and covered with a good growth of short grass - the soil is on the average good but the turf is thin being not more than 5 inches thick with a coarse gravel underneath. - In the N. W. cor. of the Township the soil seems to be mixed with small particles of lime. — This Township I do not think is fit for anything but grazing on account of the thinness of the soil. —

Surveyor General's Office
Plattsmouth Jany 6th 1873

The fregoing field Notes of the Survey and subdivision of Township 10 North of the base line of Range No 41 West of the 6th Principal Meridian in Nebraska, executed by John R. Patrick Deputy Surveyor under joint contract No 62, dated June 29th 1872, wherein John R. Patrick and H. B. Stout are joint contractors in the months of July and August AD 1872, having been critically examined the necessary corrections and explanations made, the said field Notes and the Survey they describe are hereby approved

E. E. Cunningham
Surveyor General

A List
of the names of the individuals who assisted in running, measuring and marking the subdivision lines and corners of Township No. 10 North Range 41 West of the 6th Principal Meridian

Harry H. Williams	chainman
Thomas Daily	chainman
Charles Roehrig	Flagman
John M. Robinson	moundman
	Compassman

We hereby certify that we assisted John R. Patrick Deputy Surveyor in subdividing Township No. 10. North Range 41 west of the 6th Principal Meridian and that said Township has been in all respects to the best of our Knowledge and belief well and faithfully surveyed and the boundary monuments planted according to the instructions of the Surveyor General

Harry Williams chainman
[illegible] Gaily chainman
Jno M Robinson. moundan
Charlie Roehrig Flagman

Subscribed and sworn to by the above named persons before me a Notary Public in and for the county of Lancaster in the state of Nebraska this 29th day of Nov 1872

[illegible]
Notary Public.

J. John R. Patrick do solemnly swear that in pursuance of a joint Contract No. 62 wherein John R. Patrick H. B. Stout are joint contractors with E. E. Cunningham United States Surveyor General for the district of Nebraska and Iowa bearing date the 29th day of June A.D. 1872

I ~~will~~ have well faithfully and truly in my own proper person and in strict conformity with the Instructions of the Surveyor General the Surveying manual and the Laws of the United States surveyed all those parts or portions of the Township No 10 North of the Base line of Range 41 west of the 6th Principal Meridian in the state of Nebraska, as are represented in the foregoing Field notes as having been surveyed under my direction and I do further solemnly swear that all the corners of said surveys have been established and perpetuated in strick accordance

with the Surveying Manual and Printed Instructions and that the foregoing are the true and original Field Notes of such Survey

Jno R Patnode

Deputy Surveyor

Subscribed by the said John R Patnode Deputy Surveyor and sworn to before me a Notary Public within and for the County of Lancaster in the state of Nebraska, this 29 day of November A.D. 187

W. H. Hyde
Notary Public

Surveyor Generals Approval see page 63

T 11 N., R 41 West

6	60	5	44	4	33	3	22	2	11	1
59		58		43		32		21		10
7	57	8	42	9	31	10	20	11	9	12
62		55		41		30		19		8
18	54	17	40	16	29	15	18	14	7	13
53		52		39		28		17		6
19	51	20	38	21	27	22	16	23	5	24
50		49		37		26		15		4
30	48	29	36	28	25	27	14	26	3	25
47		46		35		24		13		2
31	45	32	34	33	23	34	12	35	1	36

Subdivision of Township
No 11 North of Range
No 41 West of the
6th Meridian
State of Nebraska

Commenced October 2nd 1871

Finished October 6th 1871

By William E. Daugherty
Deputy Surveyor

Township No 11 North

Names of assistants

Henry Heidel
Frank M. Daugherty } Chainmen

Henry Lear
Oscar P. Milton } Flagmen

Spoundmen

Range No 41 West 6th Meridian

To determine the course of the East boundary of the Township I commence at the corner of Townships 10 and 11 North Ranges 40 and 41 West and run thence North on a blank line along the East boundary of Section 36

Variation 13° 50' East

40.05 To a point 4 links East of quarter section corner

80.08 To corner of sections 25 & 36

My compass is therefore in proper adjustment

Subdivisions Commenced October 2nd 1871

From the corner of sections 1 2 35 and 36

~~I run (North)~~

Township No. 11 North

I run

North between Sections
35 & 36
Variation 13°50

40.00 Set chased post in mound of Earth with pits as per instructions for 1/4 Section corner

80.00 Set chased post in mound of Earth with pits as per instructions for corner to Sections
25 26 35 and 36
Land rolling
Soil 2 Rate

Range No 41 West 6th Meridian

East on a random line between Sections 25 & 36
Variation 13°50' East

40.00 Set post for temporary 1/4 sec corner

80.16 Intersect East boundary of Township 7 links North of corner to sections 25 and 36 from which corner I run N 89°57' W on a true line between Sections 25 and 36
Variation 13°50' East

40.08 Set chased post in mound of Earth with pits as per instructions for 1/4 Section corner

80.16 The corner of Sections
25 26 35 and 36
Land rolling
Soil 2 Rate

Township No 11 North

North between Sections
25 & 26
Variation 13° 45' East

40.00 Set chain post in mound of Earth
with pits as per instructions
for 1/4 Section corner

80.00 Set chain post in mound of
Earth with pits as per
instructions for corner to
Sections 23 24 25 and 26
Land rolling
Soil 2d Rate

Range No 41 East 6th Meridian

East on a random line
between Sections 24 & 25
Variation 13° 45' East

40.00 Set post for temporary 1/4 cor
79.92 Intersect East boundary of Township
21 links South of corner to sections
24 and 25 from which corner bears
S 89° 51' W on a true line between
Sections 24 and 25
Variation 13° 45' East

39.96 Set chain post in mound of Earth
with pits as per instructions
for 1/4 Section corner

79.92 The corner of Sections
23 24 25 and 26
Land rolling
Soil 2d Rate

Township No 11 North

North between Sections
23 & 24
Variation 13° 50' East

40,00 Set chain post in mound of Earth
with pits as per instructions
for 1/4 Section corner

80,00 Set chain post in mound of Earth
with pits as per instructions
for corner to sections
13 14 23 and 24
Land rolling
Soil 2nd Rate

Range No 41 West 6th Meridian

East on a random line between
Sections 13 & 24
Variation 13° 50' East

40,00 Set post for temporary 1/4 sec corner

80,24 Intersect ~~North and South line~~ East & West Boundary of 32
links North of corner to sections 13
and 24 from which corner I saw
N 89° 46' W on a true line between
Sections 13 and 24
Variation 13° 50' East

40,12 Set chain post in mound of Earth
with pits as per instructions
for 1/4 Section corner

80,24 The corner of sections
13 14 23 and 24
Land rolling
Soil 2nd Rate

Township No 11 North

North between Sections
13 & 14
Variation 13° 40' East

40.00 Set chain post in mound of Earth with pits as per instructions for 1/4 Section corner

80.00 Set chain post in mound of Earth with pits as per instructions for corner to sections 11, 12, 13 and 14

Land rolling
Soil 2nd Rate

Range No 41 West 6th Meridian

East on a random line between Sections 12 & 13
Variation 13° 40' East

40.00 Set post ~~post~~ for temporary 1/4 corner

83.14 Intersect North and South line 10 links North of corner to sections 12 and 13 from which corner I saw N 89° 56' W on a true line between Sections 12 and 13
Variation 13° 40' East

40.17 Set chain post in mound of Earth with pits as per instructions for 1/4 Section corner

80.14 The corner of sections 11, 12, 13 and 14

Land rolling
Soil 2nd Rate

Township No 11 North

North between Sections
11 & 12
Variation 13°50' East
40.00 Set chaned post in mound of Earth
with pits as per instructions for
1/4 Section corner
80.00 Set chaned post in mound of
Earth with pits as per instructions
for corner to sections
1, 2, 11 and 12
Land nothing
Surl 2nd Rate

Range No 41 West 6th Meridian

East on a random line between
Sections 1 & 12
Variation 13°30' East
40.00 Set post for temporary 1/4 sec corner ~~in mound of Earth with~~
79.84 ~~Intersect~~ East boundary of Township
18 links South of corner to sections
1 and 12 from which corner I am
S 89°52' W on a true line between
Sections 1 and 12
Variation 13°30' East
39.92 Set chaned post in mound of
Earth with pits as per
instructions for 1/4 sec corner
79.84 The corner of sections
1, 2, 11 and 12
Land nothing
Surl 2nd Rate

Township No 11 North

North on a random line
between Sections 1 & 2
Variation 13° 40' East

40.00 Set post for temporary 1/4 sec corn
80.39 Intersect North boundary of Township
16 links East of corner to sections
1 and 2 from which corn I am
S 7' E on a true line between
Sections 1 and 2
Variation 13° 40' East
40.39 Set chaned post in mound of Earth
with pits as per instructions
for 1/4 section corner
80.39 The corner of sections
1 2 11 and 12
Land rolling
Soil 2nd Rate

October 2nd 1871

Range No 41 East 6th Meridian

North between Sections
34 & 35
Variation 13° 50' East
40.00 Set chaned post in mound of Earth
with pits as per instructions
for 1/4 Section corner
80.00 Set chaned post in mound of
Earth with pits as per
instructions for corner to
Sections 26 27 34 and 35
Land rolling
Soil 2nd Rate

Township No 11 North

East on a random line between Sections 26 & 35

Variation 13° 50' East

4000 Set post for Temporary 1/4 sec corner

79.92 Intersect North and South line 20 links south of corner to sections 25 26 35 and 36 from which corner I now S 89° 51' W on a true line between sections 26 and 35

Variation 13° 50' East

39.96 Set chased post in mound of Earth with pits as per instructions for 1/4 section corner

79.92 The corner of sections 26 27 34 and 35

Land rolling

Soil 2 Rate

Range No 41 West 6th Meridian

North between Sections 26 & 27

Variation 13° 55' East

4000 Set chased post in mound of Earth with pits as per instructions for 1/4 section corner

8000 Set chased post in mound with pits as per instructions for corner to sections 22 23 26 and 27

Land rolling

Soil 2 Rate

Township No 11 North

East on a random line between
Sections 23 & 26
Variation 14° East

40.00 Set post for temporary 1/4 sec corner
79.86 Intersect North and South line 33 links
North of corner to sections 23
24 25 and 26 from which
corner I run N 89°46' W on a true
line between sections 23 and 24
Variation 14° East
39.93 Set chained post in mound of
Earth with pits as per
instructions for 1/4 Section corner
79.86 The corner of sections
22 23 26 and 27
Land rolling
Soil 2nd Rate

Range No. 41 West 6th Meridian

North between Sections
22 & 23
Variation 14° East

40.00 Set chained post in mound of Earth
with pits as per instructions for
1/4 Section corner
80.00 Set chained post in mound of
Earth with pits as per
instructions for corner
to sections
14 15 22 and 23
Level rolling
Soil 2nd Rate

Township No. 11 North

East on a random line between Sections 14 & 23

Variation 14° East

40.00 40.00 Set ~~chard post~~ post for Cor 1/4 sec cor

79.[illegible] 80.24 Intersect North and South line 34 links North of corner to sections 13 14 23 and 24 from which corner I now N 89° 45' W on a true line between Sections 14 and 23

Variation 14° East

39.[illegible] 40.12 Set chared post in mound of Earth with pits as per instructions for 1/4 Section corner

79.[illegible] 80.24 The corner of sections 14 15 22 and 23

Land rolling

Soil 2nd Rate

Range No 41 West 6th Meridian

North between Sections 14 & 15

Variation 13° 50' East

40.00 Set chared post in mound of Earth with pits as per instructions for 1/4 sec corner

80.00 Set chared post in mound of Earth with pits as per instructions for corner to Sections 10 11 14 and 15

Land rolling

Soil 2nd Rate

Township No 11 North

East on a random line between Sections 11 & 14
Variation 13°45' East

4000 Set post for temporary 1/4 sec cor
8000 Intersect North and South line 15 links South of corner to sections 11 12 13 & 14 from which corner I run S 89°54' W on a true line between sections 11 and 14
Variation 13°45' East

4000 Set chased post in mound of Earth with pits as per instructions for 1/4 section corner

8000 ~~Set chased post in mound of~~ The corner of sections 10 11 14 and 15
Land rolling
Soil 2nd Rate

Range No. 41 West 6th Meridian

North between Sections 10 & 11
Variation 14° East

4000 Set chased post in mound of Earth with pits as per instructions for 1/4 section corner

8000 Set chased post in mound of Earth with pits as per instructions for corner to sections 2 3 10 and 11
Land rolling
Soil 2nd Rate

Township No. 11 North

East on a random line
between Sections 2 & 11
Variation 14° East

40.00 Set ~~a~~ post for temporary 1/4 sec cor
79.8 80.14 Intersect North and South line 25 lks
North of corner to sections 1 2 11
and 12 from which corner I run
N 89° 49' W on a true line between
sections 2 and 11
Variation 14° East
39.9 40.07 Set chained post in mound of
Earth with pits as per
instructions for 1/4 sec corner
79.8 80.14 The corner of sections
2 3 10 and 11
Land rolling
Soil 2nd Rate

Range No 41 West 6th Meridian

North on a random line between
Sections 2 & 3
Variation 14° East
40.00 Set post for temporary 1/4 sec corner
80.67 Intersect North boundary of Town
ship 10 links west of corner to
sections 2 and 3 from which corner
I run S 4' W on a true line
between sections 2 and 3
Variation 14° East
40.67 Set chained post in mound
of Earth with pits as per
instructions for 1/4 sec corner
80.67 The corner of sections
2 3 10 and 11
Land rolling
Soil 2nd Rate

Township No 11 North

North between Sections
33 & 34
Variation 13° 50' East

40.00 Set chaud post in mound of Earth with pits as per instructions for 1/4 Section corner

80.00 Set chaud post in mound of Earth with pits as per instructions for corner to sections
27 28 33 and 34
Land rolling
Soil 2d Rate

Range No 41 West 6th Meridian

East on a random line between Sections 27 & 34
Variation 13° 50' East

40.00 Set post for temporary 1/4 sec corner

80.40 Intersect North and South line 16 links South of corner to sections 26 27 34 and 35 from which corner I run S 89° 53' W on a true line between sections 27 & 34
Variation 13° 50' East

40.20 Set chaud post in mound of Earth with pits as per instructions for 1/4 sec corner

80.40 The corner of sections
27 28 33 & 34
Land rolling
Soil 2d Rate

October 3rd 1871

Township No 11 North

North between Sections
27 & 28
Variation 13° 30' East

40.00 Set chain post in mound of Earth with Pits as per instructions for 1/4 Section corner

80.00 Set chain post in mound of Earth with Pits as per instructions for corner to sections 21 22 27 and 28

Send rolling
Sol 2d Rate

Range No 41 East 6th Meridian

East on a random line between Sections 22 & 27
Variation 13° 55' East

40.00 Set temporary 1/4 section corner

80.18 Intersect North and south line 33 links North of corner to sections 22 23 26 and 27 from which corner I run N 89° 46' W on a true line between sections 22 & 27
Variation 13° 55' East

40.00 Set chain post in mound of Earth with Pits as per instructions for 1/4 sec corner

80.18 The corner of sections 21 22 27 and 28

Send rolling
Sol 2d Rate

Township No 11 North

North between Sections
21 & 22
Variation 13° 45' East

40.00 Set chained post in mound of Earth with pits as per instructions for 1/4 Section corner

80.00 Set chained post in mound of Earth with pits as per instructions for corner to sections 15 16 21 and 22
Land rolling
Soil 2nd Rate

Range No 41 West 6th Meridian

East on a random line between Sections 15 & 22
Variation 13° 40' East

40.00 Set post for temporary 1/4 sec corner

80.04 Intersected North and South line 15 links South of corner to sections 14 15 22 and 23 from which corner I run S 89° 56' W on a true line between sections 15 and 22
Variation 13° 40' East

40.00 Set chained post in mound of Earth with pits as per instructions for 1/4 Section corner

80.04 The corner of sections 15 16 21 and 22
Land rolling
Soil 2nd Rate

Township No 11 North

North between Sections
15 & 16
Variation 13° 30' East

4000 Set chained post in mound of Earth
with pits as per instructions for
1/4 Section corner

8000 Set chained post in mound of Earth
with pits as per
instructions for corner to sections
9, 10, 15 and 16
Level rolling
Soil 2nd Rate

Range No 41 East 6th Meridian

East on a random line between
Sections 10 & 15
Variation 13° 45' East

4000 Set post for temporary 1/4 sec cor
80.16 Intersected North and South line 7 links
South of corner to sections 10 11 14
15 from which corner I saw
S 89° 57' W on a true line between
Sections 10 and 15
Variation 13° 45' East

4008 Set chained post in mound of
Earth with pits as per instructions
for 1/4 Section corner

8016 The corner of sections
9 10 15 and 16
Level rolling
Soil 2nd Rate

Township No 10 North

North between Sections
9 & 10
Variation 13° 50' East

4.00 Set chased post in mound of Earth with pits as per instructions for 1/4 Section corner

8.00 Set chased post in mound of Earth with pits as per instructions for corner to sections
3 4 9 and 10
Lowed rolling
Soil 2nd Rate

Range No 41 West 6th Meridian

East on a random line between Sections 3 & 10
Variation 13° 50' East

4.00 Set ~~chased post in mound of Earth with pits as per instructions for 1/4 Section corner~~ post for temporary 1/4 sec corner

80.28 Intersect ~~North boundary of Township~~ North and South line 18 links ~~east~~ North of corner to sections 2 3 10 and 11 from which corner I run N 89° 52' W on a true line between sections 3 and 10
Variation 13° 50' East

40.14 Set chased post in mound of Earth with pits as per instructions for 1/4 Section corner

80.28 The corner of sections
3 4 9 and 10
Lowed rolling
Soil 2nd Rate

Township No 10 North

North on a random line between
Sections 3 & 4
Variation 13° 40' East
4 40.00 Set post for temporary 1/4 sec cor
80.85 Intersect North boundary of Township
12 links East of corner to sections
80 3 and 34 from which corner I run
S 5' E on a true line between
Sections 3 and 34
Variation 13° 40' East
40.85 Set chained post in mound of Earth
with pits as per instructions for
1/4 Section corner
80.85 The corner of sections
3, 4, 9 and 10
Land rolling
Soil 2nd Rate

Range No 41 West 6th Meridian

North between Sections
32 & 33
Variation 13° 30' East
40.00 Set chained post in mound of Earth
with pits as per instructions for
1/4 Section corner
80.00 Set chained post in mound of Earth
with pits as per instructions
for corner to sections
28 29 32 and 33
Land rolling
Soil 2nd Rate

Township No 11 North

East on a random line between Sections 28 & 33

Variation 13°50' East

4000 Set post for temporary 1/4 sec cor

7980 Intersect North and South line 26 links North of corner to sections 27 28 33 and 34 from which corner I now N 89°49' W on a true line between Sections 28 and 33

Variation 13°50' East

3990 ~~Intersect~~ Set chared post in mound of Earth with pits as per instructions for 1/4 Section corner

7980 The corner of sections 28 29 32 and 33

Land rolling

Soil 2 Rate

Range No 41 West 6th Meridian

North between Sections 28 & 29

Variation 14° East

4000 Set chared post in mound of Earth with pits as per instructions for 1/4 Section corner

8000 Set chared post in mound of Earth with pits as per instructions for corner to sections 20 21 28 and 29

Land rolling

Soil 2 Rate

Township No 11 North

East on a random line between Sections 21 & 28

Variation 13° 30' East

40.00 Set post for temporary 1/4 sec corner

79.96 Intersect North and South line 38 links South of corner to sections 21 22 27 and 28 from which corner I run S 89° ~~43'~~ 43' W on a true line between Sections 21 and 28

Variation 13° 30' East

39.98 Set chared post in mound of Earth with pits as per instructions for 1/4 Section corner

79.96 The corner of sections 20 21 28 and 29

Land rolling

Soil 2d Rate

October 4th 1871

Range No. 41 West 6th Meridian

North between Sections 20 & 21

Variation 14° East

40.00 Set chared post in mound of Earth with pits as per instructions for 1/4 Section corner

80.00 Set chared post in mound of Earth with pits as per instructions for corner to sections 16 17 20 and 21

Land rolling

Soil 2d Rate

Township No 11 North

East on a random line between
Sections 16 & 21
Variation 13° 30' East

40.00 Set post for temporary 1/4 sec corner
80.10 Intersect North and South line 32 links
North of corner to sections 15 16 21
and 22 from which corner a mound
N 89° 46' W on a true line between
Sections 16 and 21
Variation 13° 30' East

40.03 Set chained post in mound of Earth
with pits as per instructions
for 1/4 Section corner
80.10 The corner of sections
16 17 20 and 21
Land rolling
Soil 2nd Rate

Range No. 41 West 6th Meridian

North between Sections
16 & 17
Variation 13° 30' East

40.00 Set chained post in mound of Earth
with pits as per instructions for
1/4 Section corner
80.00 Set chained post in mound of
Earth with pits as per
instructions for corner to sections
8 9 16 and 17
Land rolling
Soil 2nd Rate

Township No 11 North

East on a random line between
Sections 9 & 16
Variation 13°40' East
40.00 Set post for temporary 1/4 sec corner
80.22 Intersect North and South line at ~~cor~~
post corner to Sections 9 10 15 & 16
~~post~~ corner which corner I run West on a
true line between sections 9 and 16
Variation 13°40' East
40.11 Set chained post in mound of Earth
with pits as per instructions
for 1/4 Section corner
80.22 The corner of sections
8 9 16 and 17
Land rolling
Soil 2nd Rate

Range No. 41 West 6th Meridian

North between Sections
8 & 9
Variation 13°40' East
40.00 Set chained post in mound of Earth
with pits as per instructions for
1/4 Section corner
80.00 Set chained post in mound of Earth
with pits as per instructions
for corner to sections
4 5 8 and 9
Land rolling
Soil 2nd Rate

Township No 11 North

East on a Random line between Sections 4 & 9

Variation 13°40' East

40.00 Set post for temporary 1/4 sec corner

80.08 Intersect North and South line ~~between~~ 15 links South of corner to sections 3 4 9 and 10 from which corner I now S 89° 54' W on a true line between sections 4 and 9

Variation 13°40' East

40.04 Set chained post in mound of Earth with pits as per instructions for 1/4 Section corner

80.08 The corner of sections 4 3 8 and 9.

Land rolling

Soil 2nd Rate

Range No. 41 West 6th Meridian

North on a random line between Sections 4 & 5

Variation 13°40' E

40.00 Set post for temporary 1/4 sec corner

80.14 Intersect North boundary of Township 19 links East of corner to sections 4 and 5 from which corner I now S 8' E on a true line between sections 4 and 5

Variation 13°40' East

40.14 Set chained post in mound of Earth with pits as per instructions for 1/4 Section corner

80.14 The corner of sections 4 3 5 8 and 9

Land rolling

Soil 2nd Rate

Township No 11 North

North between Sections
31 & 32
Variation 13°50' East

40.00 Set chained post in mound of Earth with pits as per instructions for 1/4 Section corner

80.00 Set chained post in mound of Earth with pits as per instructions for corner to sections 29 30 31 and 32
Land rolling
Soil 2nd Rate

Range No 41 West 6th Meridian

East on a Random line between Sections 29 & 32
Variation 13°50' East

40.00 Set post for temporary 1/4 sec corner ~~Chained post in mound of Earth with pits as per instructions for 1/4 section~~ corner

80.12 Intersect North and south line 60 links North of corner to sections 28 29 32 and 33 from which corner I run N 89°34' W in a true line between sections 29 and 32
Variation 13°50' East

40.06 Set chained post in mound of Earth with pits as per instructions for ~~for corner to~~ 1/4 sec corner

80.12 The corner of sections 29 30 31 and 32
Land rolling
Soil 2nd Rate

Township No. 11 North

West on a ~~random~~ True line between Sections 30 & 31
Variation 13° 50' East

4000 Set chased post in mound of Earth with pits as per instructions for 1/4 Section corner

8191 Intersect State line between Colorado and Nebraska 3,76 Chains North of 61st mile post and Set chased post in mound of Earth with pits as per instructions for corner to Sections 30 and 31
Land gently rolling
Soil 2nd Rate

Range No. 41 West 6th Meridian

North between Sections 29 & 30
Variation 13° 50' East

4000 Set chased post in mound of Earth with pits as per instructions for 1/4 section corner

8000 Set chased post in mound of Earth with pits as per instructions for corner to sections 19 20 29 and 30
Land rolling
Soil 2nd Rate

Township No 11 North

East on a random line between
Sections 20 & 29
Variation 13°45' East

40.00 Set post for temporary 1/4 sec corner
80.30 Intersect North and South line 23
links South of corner to sections 20
21 28 and 29 from which corner I run
S 89° 57' W on a true line between
Sections 20 and 29
Variation 13°45' East

40.15 Set chained post in mound of Earth
with pits as per instructions
for 1/4 Section corner
80.30 The corner of sections
19 20 29 and 30
Sand rolling
Set 2" Stake -

October 5th 1871

Range No 41 West 6th Meridian

West on a ~~random~~ true line between
Sections 19 & 30
Variation 13°58' East

40.00 Set ~~Section~~ chained post in mound
of Earth with pits as per
instructions for 1/4 Section corner
80.82 Intersect State line 4.02 chains
North of 62nd mile post and
set chained post in mound of
Earth as per instructions
for corner to sections 19 and 30
Sand rolling
Set 2" Stake

Township No 11 North

North between Sections
19 & 20
Variation 13° 40' East

40 4000 Set chained post in mound of Earth
with pits as per instructions
for 1/4 Section corner

81 8000 Set chained post in mound of Earth
with pits as per instructions
for corner to sections
17 18 19 and 20
Land rolling
Soil 2nd Rate

Range No 41 West 6th Meridian

East on a random line between
Sections 17 & 20
Variation 13° 50' East

4000 Set post for temporary 1/4 Sec corner

80.14 Intersected North and South line 17
miles South of post corner to sections
16 17 20 and 21 from which
course I run S 89° 53' W on a true
line between sections 17 and 20
Variation 13° 50' East

40.07 Set chained post in mound of
Earth with pits as per
instructions for 1/4 section corner

80.14 The corner of sections
17 18 19 and 20
Land rolling
Soil 2nd Rate

Township No 11 North

West on a ~~random~~ true line between
Sections 18 & 19
Variation 13° 50' East

40.00 Set chard post in mound of Earth
with pits as per instructions for
81 1/4 Section corner
80.24 Intersect State line 4.09 Chains
South of 63rd Mile post and set
chard post in mound of Earth
with pits as per instructions
for corner to sections 18 and 19
Land rolling
Soil 2nd Rate

Range No 41 West 6th Meridian

North between Sections
17 & 18
Variation 13° 50' East

40.00 Set chard post in mound of
Earth with pits as per instruc
tions for 1/4 Section corner
80.00 Set chard post in mound of
Earth with pits as per
instructions for corner to sections
7 8 17 and 18
Land rolling
Soil 2nd Rate

Township No. 11 North

East on a random line between Sections 8 & 17

Variation 13° 35' East

40.00 Set post for temporary 1/4 sec corner

80.10 Intersect North and South line 30 links North of corner to sections 8 9 16 and 17 from which corner I run N 89° 47' W on a true line between Sections 8 and 17

Variation 13° 55' East

40.05 Set chained post in mound of Earth with pits as per instructions for 1/4 Section corner

80.10 The corner of sections 7 8 17 and 18

Land rolling

Soil 2nd Rate

Range No 41 West 6th Meridian

West on a ~~random~~ true line between Sections 7 & 18

Variation 13° 50' East

40.00 Set chained post mound of Earth with pits as per instructions for 1/4 Section corner

79.48 Intersect State line 3.87 chains North of the 64th Mile post and set chained post in mound of Earth with pits as per instructions for 1/4 ~~Section corner~~ to sections 7 and 18

Land rolling

Soil 2nd Rate

Township No 11 North

North between Sections
7 & 8
Variation 13° 45' East

40. 4000 Set chained post in mound of Earth with pits as per instructions for 1/4 Section corner

81. 8000 Set chained post in mound of Earth with pits as per instructions for corner to sections 5 6 7 and 8
Land rolling
Soil 2nd Rate

Range No 41 West 6th Meridian

East on a random line between Sections 5 & 8
Variation 13° 40' East

40.00 Set post for temporary 1/4 sec corner

79.90 Intersect North and South line 28 links North of corner to sections 4 5 8 and 9 from which corner I find N 89° 48' W on a true line between Sections 5 and 8
Variation 13° 40' East

39.95 Set chained post in mound of Earth with pits as per instructions for 1/4 Section corner

79.90 The corner of sections 5 6 7 and 8
Land rolling
Soil 2nd Rate

Township No 11 North

West on a ~~random~~ true line between Sections 6 & 7

Variation 13° 50' East

4 4000 Set chared post in mound of Earth with pits as per instructions for 1/4 Section corner

81 78.56 Intersect State line 3.85 Chains North of 65th Mile post and set chared post in mound of Earth with pits as per instructions for corner to sections 6 and 7

Land gently rolling

Soil 2d Rate

Range No 41 West 6th Meridian

North on a random line between Sections 5 & 6

Variation 13° 35' East

4000 Set post for temporary 1/4 sec corner

81.10 Intersect North boundary of Township 6 links west of corner of sections 5 and 6 from which corner I run S 3' W on a true line between sections 5 and 6

Variation 13° 35' East

41.10 Set chared post in mound of Earth with pits as per instructions for 1/4 sec corner

81.10 The corner of sections 5 6 7 and 8

Land rolling

Soil 2d Rate

October 6th 1871

47 59

4 40

8 78

Township No 11 North

General Description

This Township is a rolling Prairie being high and dry no water within its limits Soil is 2nd Rate of good quality

Range No 41 West 6th Meridian

List of Names

A list of names of the individuals employed to assist in running, measuring & marking the lines & corners described in the foregoing field notes of Township No 11 north of the base line of Range No. 41 west of the 6th principal Meridian showing the respective capacities in which they acted.

Henry Heisel } Chainmen
Frank M. Daugherty }
Henry Sears } Mound men and Axmen
Oscar P. Melton }

We hereby certify that we assisted William E. Daugherty Deputy Surveyor in surveying & subdividing Township No 11 North of base line of Range No. 41 west of 6th principal Meridian, & that said Township has been in all respects to the best of our knowledge & belief well & faithfully surveyed & the boundary monuments planted according to the instructions furnished by the Surveyor General.

Henry Heisel L Chainmen
Frank M Daugherty

59

40

Township No 11 North

Henry Lear } Mound men
Oscar P. Milton

Subscribed and sworn to before me at my office in the city of Plattsmouth State of Nebraska this 20 day of Oct 1871

A S Child
Probate Judge

I William E. Daugherty Deputy Surveyor do solemnly swear that in pursuance of a joint contract wherein William E. Daugherty & Martin B. Cutler are joint contractors with E. E. Cunningham United States Surveyor General for the State of Nebraska bearing date the 25th day of May 1871, I have well faithfully & truly in my own proper person & in strict conformity to the instructions furnished by the Surveyor General the Surveying Manual & the laws of the United States Surveyed Township No 11 north of base line of Range No 41 west 6th principal Meridian as represented in the foregoing field notes as having

Range No 41 West 6th Meridian

been surveyed under my direction; & I do further solemnly swear that all the corners of said survey have been established & perpetuated in strict accordance with the Surveying Manual & printed instructions & that the foregoing are the true & original field notes of such survey.

William E Daugherty
Deputy Surveyor

Subscribed and sworn to before me at my office in the city of Plattsmouth State of Nebraska this 20 day of Oct 1871

A S Child
Probate Judge

Township No 11 North

Surveyor General's Office
Plattsmouth, Nov 26th 1871.

The foregoing field notes of the Survey and Sub-Divisions of Township No 11 North of the Base Line of Range No 41. West of the 6th P.M. in the State of Nebraska, executed by Wm. E. Daugherty Deputy Surveyor under joint contract No 44. wherein Wm. E. Daugherty & Martin B Cutler are joint Contractors - bearing date May 26th 1871. in the month of September 1871. having been critically examined, the necessary corrections and explanations made the said field notes and the Survey they describe are hereby approved

E. E. Cunningham
Surveyor General

Range No 41 West 6th Meridian

I hereby certify that the foregoing transcript of the field notes of the Survey and Subdivisions of Township No 11 North of the Base Line of Range No 41. West of the 6th Principal Meridian in the State of Nebraska has been correctly copied from the original notes on file in this office

Surveyor General

Field notes of the Survey of the

Sub-divisions of Township 12 North of Range 47 West of the 6th Principal Meridian in the State of Nebraska by William Hardin deputy Surveyor under his contract No 40 dated the sixth day of August 1870

Sub-division commenced Sept 23 1870
Sub-division Completed Sept 28th

T12 S R 41 W of 6th P.M.

A List of the names of assistants and their several duties

John Glenn Chainman
Charles Hardin Chainman

Fred Meihe Mound builder
J. J. Leger Mound builder

T12 N R 41 W of 6th P.M.

To ascertain the proper adjustment of my compass for sub-dividing this township I commence at the corner to Townships 11 and 12 N. Ranges 40 and 41 W and run North on a blank line along the east bound-ary of Section 36, & on the 5th Guide Mer. W.

Chs	
	Va 13° 30' East
40.00	To point 75 lks East of the 1/4 sec Cor
80.07	To a point 153 lks East of the corner to Sections 25 and 36

To retrace this line or run a parallel thereto my compass must be adjusted to a variation of 14° 36' E *

Subdivision commenced Sept 23d 1870

* The bearing of this line by my Burts improved Solar Compass is N 11° W

T12 N R 41 W of 6th P.M.

Chains	
	From the corner to sections 1, 2, 35 and 36 on the south boundary of the township I run North between sections 35 and 36
	Va 14°36'E
40.00	Set a post deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for corner to sections 25, 26, 35 and 36
	Land Surface gently rolling
	Soil 2d rate

T12 N of R 41 W of 6th P.M.

Chs	
	East on a random line between sections 25 and 36
	Va 14°36'E
40.00	Set a post for temporary 1/4 Sec cor
80.13	Intersected the east boundary of the township or 5th Guide Mer W. 28 lks north of the corner to sections 25 and 36. from which corner I run N 89°48' W on a true line between sections 25 and 36
	Va 14°36'E
40.06½	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.13	The corner to sections 25, 26, 35 and 36
	North between Sections 25 and 26
	Va 14°36'E
40.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for corner to sections 23, 24 25 and 26.
	Land gently rolling
	Soil 2d rate

T12N R41W of 6th P.M.

Chs	
	East on a random line between sections 24 and 25 Va 14°36'E
4.00	Set a post ~~for temporary~~ 1/4 Sec cor
79.74	Intersected the east boundary of the township, or 5th Guide Mer W. 12 chs north of the corner to sections 24 and 25 from which corner I run N89°55'W on a true line between sections 24 and 25 Va 14°36'E
39.87	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
79.74	The corner to sections 23, 24, 25 and 26 Land gently rolling Soil 2d rate

T12N R41W of 5th P.M.

Chs	
	North between sections 23 and 24 Va 14°36'E
40.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec - cor
51.00	Circular dry lake or basin
53.50	Lean dry lake, bears S.E. & S.W.
80.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for corner to sections 13, 14, 23 and 24 Land rolling Soil 2d rate

T12 N. R 41 W of 6th P.M.

Chs	East on a random line between sections 13 and 24 Va 14° 36' E
4.00	Set a post for temporary 1/4 Sec. Cor.
79.31	Intersected the east boundary of the township or 5th Guide Mer. W 12 chs North of the corner to sections 13 and 24 from which corner I run N 89° 55' W. on a true line between sections 13 and 24 Va 14° 36' E
39.65½	Set a post deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
79.31	The corner to sections 13, 14 23 and 24

Land Surface gently rolling
Soil 2d rate

T12 N R 41 W of 6th P.M.

Chs	North between sections 13 and 14 Va 14° 45' E
29.00	Ravine running W of S
40.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec. Cor
80.00	Set a post deposited a charred stake and raised a mound of earth with pits as per instructions for corner to sections 11, 12, 13 and 14

Land Surface somewhat broken
Soil 2d rate

T12N R41W of 6th P.M

Chs	
	East on a random line between sections 12 and 13
	Va 14°45'E
1,00	Ravine runs E of North
6 00	Touch a northern bend of same ravine descends SW from S.E ~~Nest~~
21,90	Ravine running N.W.
4000	Set a post for temporary 1/4 Sec-cor-
80,02	Intersected the East boundary of the township or 5th Guide Mer W. 27 lks north of the corner to sections 12 and 13 from which corner I run
	N89°48' W on a true line between sections 12 and 13
	Va 14°45'E
4001	Set a post deposited a charred Stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80,02	The corner to sections 11,12 13 and 14
	Land somewhat broken
	Soil poor 2d rate

T12N R41W of 6th P.M

Chs	
	North between sections 11 and 12
	Va 14°40'E
7.50	Ravine running ~~N~~ W of N
15.50	Enter same ravine running N
21 90	Leave ravine bearing N.W.
4000	Set a post deposited a charred Stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
8000	Set a post deposited a charred Stake and raised a mound of earth with pits as per instructions for corner to sections 1,2,11 and 12
	Land rolling
	Soil 2d rate

T 12 N R 41 W of 6th P M

Chs.	East on a random line between Sections 1 and 12 Va 14° 40' E
29.50	Ravine running North
40.00	Set a post for temporary 1/4 Sec cor
80.30	Intersected the East boundary of the township or 5th Guide Mer. W. 93 lks South of the corner to sections 1 and 12 from which corner I run S 89° 20' W on a true line between sections 1 and 12 Va 14° 48' E
40.15	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.30	The corner to sections 1, 2, 11 and 12 Land surface broken Soil poor 2d rate

T 12 N R 41 W of 6th P M

Chs	North on true line between sections 1 and 2 Va 14° 35' E
40.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
83.06	Intersected the 3d Standard parallel 11.50 chs East of the corner to Tp 13 N Ranges 40 and 41 W. on 5th Guide Mer. W. Where I set a post deposited a marked stone and raised a mound of earth with pits as per instructions for closing corner to sections 1 and 2 Land surface rolling Soil poor 2d rate Sept 23d 1870

T12N R41W of 6th P.M.

Chs	
	North between sections 34 and 35
	S Va 14°36'E
40.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 26 27 34 and 35
	Land level soil 2d rate

East on a random line between sections 26 & 35
Va 14°36'E

40.00	Set a post for temporary 1/4 Sec cor
80.03	Intersection on N and S line 15 lks north of the corner to sections 25, 26, 35, 36 from which corner I run N 89°52' W on a true line between sections 26 and 35 va 14°36'E
400½	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
8003	The corner to sections 26, 27, 34, 35
	Land level soil 2d rate

T12N R41W of 6th P.M.

Chs	
	North between Sections 26 and 27
	Va 14°36'E
20.00	Head of a ravine runs W of N
40.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.00	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 22 23 26 and 27
	Land Smooth level
	Soil 2d rate

T12N R41W of 6th P.M.

Chs	
	East on a random line between sections 23 and 26 Va 14°36'
7.90	Ravine running W of N
79.83	Intersected the N and S line 23 lks North of the corner to sections 23, 24 25 and 26 from which corner I run
	N89°50'W. on a true line between sections 23 and 26 Va 14°36'E
39.91½	Set a post-deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec-cor-
79.83	The corner to sections 22, 23 26 and 27
	Land Rolling
	Soil 2d rate

T12N R41W of 6th P.M.

Chs	
	North between sections 22 and 23 Va 14°40'E
19.50	Ravine runs N W
40.00	Set a post-deposited a marked stone raised a mound of earth with pits as per instructions for 1/4 Sec cor
56.56	Ravine running N W
80.00	Set a post-deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 14 15 22 and 23
	Land broken gravelly points
	Soil 3d rate

T 12 N. R 41 W. of 6th P.M.

Chs	East on a random line between sections 14 and 23 Va 14°40'E
24,40	Ravine running N.W.
40,00	Set a post for temporary 1/4 Sec-cor-
80,31	Intersected the N and S line 56 lks north of the corner to sections 13 14 23 and 24 from which corner I run N 59°36' W on a true line between sections 14 and 23 Va 14°40'E
40 15½	Set a post- deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80,31	The corner to sections 14 15 22 and 23

Land rolling
Soil 3d rate

T 12 N R 41 W of 6th P.M.

Chs	North between sections 14 and 15 Va 14°36'E
31,90	Ravine running W of N
40,00	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor-
56,00	Ravine running N.W.
80,00	Set a post- deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 10 11, 14 and 15

Land Surface broken
Soil gravelly 3d rate

T12 N of R 41 W of 6th P.M.

Chs	East on a random line between sections 11 and 14 Va 14° 36' E.
20.40	Ravine running North
40.00	Set a post for temporary 1/4 Sec cor
57.30	Ravine runs N. E
66.00	Ravine runs E of N
80.36	Intersected the N and S line 34 lks North of the corner to Sections 11, 12, 13 & 14 from which corner I run N 89° 45 W on a true line between sections 11 and 14 Va 14° 36' E
40.18	Set a post - deposited a marked a Stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.36	The corner to sections 10 11 14 15
	Land Surface broken
	Soil gravelly 3rd rate

T12 N R 41 W of 6th P.M.

Chs	North between sections 10 and 11 Var 14° 30' E
40.00	Set a post - deposited a marked Stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
59.00	Ravine running W of N and loses or spreads out on the level
80.00	Set a post - deposited a marked Stone and raised a mound of earth with pits as per instructions for corner to sections 2 3 10 and 11.
	Land Sloping North
	Soil Poor 2d rate

T12 N R41 W of 6th P M

Chs	East on a random line between Sections 2 and 11 Va 14° 30' E
40.00	Set a post for temporary 1/4 Sec cor in a large barr running North
80.18	Intersected the N and S line 20 lks North of the corner to Sections 1, 2, 11 and 12 from which corner I run N 89° 35' W on a true line between Sections 2 and 11 Va 14° 30' E
40.09	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.18	The corner to sections 2, 3, 10 and 11 Land rolling Soil poor 2d rate

T12 N R41 W of 6th P M

Chs	North on a true line between Sections 2 and 3 Va 14° 30' E
40.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
83.12	Intersected the 3d Standard parallel 5.02 chs East of the corner to Sections 35 and 36 T13 N R41 W Where I set a post deposited a marked stone and raised a mound of earth with pits as per instructions for closing corner to Sections 2 and 3 Land smooth. Sloping North Soil Sandy 2d rate Sept 24th 1870

T12N R41 W of 6th P M

Chs	
	North between sections 33 and 34
	va 14°36'E
40.00	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
80.00	Set a post-deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 27, 28, 33 and 34
	Land surface level soil 2d rate

East on a random line between sections 27 & 34

	va 14°36'E
40.00	Set a post for temporary 1/4 Sec Cor
80.00	Intersected the N and S line 42 lks North of the corner to sections 26 27 34 and 35 from which corner I run N 89 42' W on a true line between sections 27 and 34
	va 14°36'E
40.00	Set a post-deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
80.00	The corner to sections 27 28 33 and 34
	Land level soil 2d rate

T12N R41 W of 6th P M

Chs	
	North between sections 27 and 28
	va 14°40'E
40.00	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
44.50	Raisin running N E
56.00	Same running N W
62.10	Same running N E
80.00	Set a post-deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 21, 22, 27 and 28
	Land broken
	Soil poor 2d rate

T 12 N R 41 W of 6th P.M.

Chs	East on a random line between Sections 22 and 27 Va 14°40' E
16.50	Ravine running S.E.
40.00	Set a post for temporary 1/4 Sec-Cor-
47.67	Ravine running north
50.45	Ravine running N of N
80.25	Intersected the N and S line 51 lks North of the corner to Sections 22, 23, 26 and 27 From this corner I run N 89° 38' W on a true line between Sections 22 and 27 Va 14°40' E
40.12½	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.25	The corner to Sections 21 22 27 and 28 Land some broken Soil poor 2d rate

T 12 N. R 41 W of 6th P.M.

Chs	North between Sections 21 and 22 Va 14°40' E
6.00	Ravine running east
17.50	ravine running S E
40.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
54.10	Ravine running N E
62.50	Ravine running East
80.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for corner to Sections 15 16 21 and 22, Land broken Soil poor 2d rate

T12 N of R 41 W of 6th P.M.

Chs	East on a random line between Sections 15 and 22 Va 14°40'E
40.00	Set a post for temporary 1/4 Sec Cor
55.50	Ravine trend North
70.80	Ravine running North W
80.17	Intersected the N and S line 40 lks North of the corner to Sections 14, 15, 22 and 23 from which corner I run S 89°43' W on a true line between Sections 15 and 22 Va 14°40'E
400 8/10	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
80.17	The corner to Sections 15 16 21 and 22 Land rolling Soil 2d rate

T12 N of R 41 W of 6th P.M.

Chs	North between Sections 15 and 16 Va 14°40'E
36.00	Ravine running N E
40.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
80.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for corner to Sections 9, 10 15 and 16 Land broken Soil poor 2d rate

T 12 N. R 41 W of 6th P.M.

Chs	
	East on a random line between sections 10 and 15
	Va 14°40'E
2680	Ravine running N W
4000	Set a post for temporary 1/4 Sec Cor
80,05	Intersected the N and S line 17 lks North of the Corner to Sections 10 11, 14 and 15 from which corner I run N 89°53' W on a true line between sections 10 and 15
	Va 14°40'E
4002½	Set a post deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
80,05	The corner to sections 9 10 15 and 16
	Land Surface broken
	Soil poor 2d rate

T 12 N R 41 W of 6th P.M.

Chs	
	North between sections 9 and 10
	Va 14°36'E
13.50	Ravine running N W and spreads or loses itself in the bottom
40,00	Set a post-deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80,00	Set a post-deposited a charred stake and raised a mound of earth with pits as per instructions for corner to sections 3, 4, 9 and 10
	Land rolling
	Soil 2d rate

T12N R41W of 6th PM

Chs	East on a random line between sections 3 and 10.
	Va 14°36' E
40.00	Set a post for temporary 1/4 Sec Cor
79.88	Intersected the N and S line 47 lks north of the corner to Sections 2 3 10 and 11 from which corner I run N89°46' W on a true line between sections 3 and 10
	Va 14°36' E
39.94	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
79.88	The corner to sections 3 4 9 and 10
	Land rolling
	Soil Gravelly poor 2d rate

T12N R41W of 6th PM

Chs	North on a true line between sections 3 and 4
	Va 14°36' E
40.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
83.34	Intersected the 3d standard parallel N 11.70 lks east of the corner to sections 34 and 35 T13N R41W. Where I set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for closing corner to sections 3 and 4
	Land surface smooth - Quality sloping towards the North West
	Soil Sandy poor 2d rate
	Sept 25th 1870

T12 N R 41 W 6th P.M.

Chs	North between Sections 32 and 33 Va 14°36' E
34.25	Dry lake extending about 4 chs Each side of line, bears N.E. & S.W.
40.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
41.30	Leave dry basin bears S.E. & S.W.
80.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for corner to sections 28, 29, 32, and 33 Land surface level Soil 2d rate

T12 N R41 W of 6th P.M.

Chs	East on a random line between sections 28 and 33 Va 14°36' E
40.00	Set a post for temporary 1/4 Sec cor.
79.80	Intersected the N and S line 41 lks north of the corner to sections 27, 28, 33 and 34 from which corner I run N 89° 48' W on a true line between sections 28 and 33 Va 14°36' E
39.90	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
79.80	The corner to sections 28, 29, 32 and 33 Land level Soil 2d rate.
	North between sections 28 and 29 Va 14°36' E
40.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
80.00	Set a post - deposited a charred stake and raised a mound of earth with pits as per instructions for corner to sections 20, 21, 28, and 29 Land level Soil 2d rate

T 12 N R 41 W of 6th P M

Chs	
	East on a random line between Sections 21 and 28
~~40,00~~	~~Set~~ Va 14°36' E
~~40,00~~	~~Set a post deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor~~
40,00	Set a post for temporary 1/4 Sec cor
79,60	Intersected the N and S line 33 lks North of the corner to Sections 21 22 27 and 28 from which corner I run S 89°46' W on a true line between Sections 21 and 28 Va 14°36' E
39,80	Set a post deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
79,80	The corner to Sections 20 21 28 and 29
	Land level soil 2d rate

T 12 N R 41 W of 6th P M.

Chs	
	North between sections 20 and 21 Va 14°36' E
40,00	Set a post deposited a charred stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
86,00	Set a post deposited a charred stake and raised a mound of earth with pits as per instructions for corner to Sections 16 17 20 and 21
	Land level soil 2d rate

T12 N R41 W of 6th P M

Chs	East on a random line between sections 16 and 21 Va 14°36' E.
14.85	Ravine running N E
40.00	Set a post for temporary 1/4 Sec cor
40.55	Ravine running North
53.15	Ravine runs. W of N
79.16	Intersected the N and S line 28 lks north of the Corner to sections 15, 16, 21, 22 from which corner I run N 89°48' W on a true line between sections 16 and 21 Va 14°36' E
39.58	Set a post deposited a chaired stake and raised a mound of earth with pits as per instructions for 1/4 Sec cor
79.16	The Corner to sections 16, 17, 20 and 21 Land Rolling Soil 2d rate

T12 N R41 W 6th P M

Chs	North between sections 16 and 17 Va 14°45' E
11.00	Enter head of ravine running north
39.40	Leave ravine running E of N
40.00	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.00	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 8, 9, 16 and 17 Land surface broken Soil Sand & gravel 3d rate

T12 N R41 W of 6 P.M.

chs	
	East on a random line between sections 9 and 16 Va 14°45' E
8.00	Main Ravine running North
10.00	Set a post for temporary 1/4 Sec cor
19.52	Intersected the N and S line 69 lks north of the corner to sections 9, 10, 15, and 16 from which corner I run N 89°30' W on a true line between section 9 and 16 Va 14°45' E
39.76	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
79.52	The corner to sections 8, 9, 16, and 17
	Land surface broken hilly Soil gravelly 3rd rate

T12 N. R41 W. of 6th P.M.

chs	
	North between sections 8 and 9 Va 14°45' E
44.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
54.00	To the middle of outspread of ravine coming from the S.E.
84.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 4, 5, 8 and 9
	Land sloping north Soil sandy poor 2nd rate

T12 N R41 W of 5th PM

Chs	East on a random line between sections 4 and 9 Va 14°45' E
40.00	Set a post for temporary 1/4 Sec cor
79.69	Intersected the N and S line 35 lks North of the corner to sections 3, 4, 9 and 10 from which corner I run N 89°45' W on a true line between sections 4 and 9 Va 14°45' E
39.84½	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
79.69	The corner to sections 4, 5 8 and 9 Land, Surface Smooth Sloping north Soil Sandy 2d rate

T12 N R41 W of 5th PM

Chs	North on a true line between sections 4 and 5 Va 14°45' E
40.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
83.39	Intersected the 3d Standard parallel 11.63 chs East of the corner to sections 33 and 34 T13 N R41 W Where I set a post deposited a marked stone and raised a mound of earth with pits as per instructions for closing corner to sections 4 and 5 Land Smooth - Sloping North Soil 2d rate Sept 26th 1870

T 12 N R 41 W 6th P M

Chs	
6	North between sections 31 and 32 Va 14°40' E
40.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 29, 30, 31, 32 Land Surface level Soil 2d rate
	East on a random line between sections 29 and 32 Va 14°40' E
40.00	Set a post for temporary 1/4 Sec cor
79.87	Intersected the N and S line 40 lks north of the corner to sections 28, 29, 32 and 33 from which corner I run N 87°43' W on a true line between sections 29 and 32 Va 14°40' E
399 1/2	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
79.87	The corner to sections 29, 30, 31 & 32 Land Surface level Soil 2d rate

T 12 N R 41 W of 6th P M

Chs	
	West on a true line between sections 30 and 31 Va 14°24' E
40.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
77.52	Intersected the State line 4.21 chs north of the 67th mile post Where I set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for closing corner to fractional sections 30 and 31 Land Surface level Soil 2d rate
	North between sections 29 and 30 Va 14°36' E
40.00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
80.00	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 19, 20, 29 and 30 Land level Soil 2d rate

T12 N R41 W of 6th P.M.

Chs	East on a random line between Sections 20 and 29 Va 11° 36
40.00	Set a post for temporary 1/4 Sec cor
79.76	Intersected the N and S line 2 chs North of the corner to sections 20, 21, 28 and 29, from which corner I run N 89° 50 W on a true line between Sections 20 and 29 Va 11° 36
39.88	Set a post - deposited a marked Stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
79.76	The Corner to Secs. 19, 20, 29 & 30 Land level Soil 2d rate

T12 N R41 W of 6th P.M.

Chs	West on a true line between sections 19 & 30 Va 14° 27' E
40.00	Set a post deposited a marked Stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
76.68	Intersected the State line 3.93 chs North of the 68th Mile Post where I set a post - deposited a marked Stone and raised a mound of earth with pits as per instructions for Closing corner to sections 19 and 30 Land level soil 2d rate
	North between Sections 19 and 20 Va 11° 40' E
27.00	Ravine running W of N
40.00	Set a 5 ft. sandstone Stone 10 x 8 x 5 inches for 1/4 Sec cor
80.00	Set a post - deposited a marked Stone and raised a mound of earth with pits as per instructions for corner to sections 17, 18, 19 and 20 Land Broken gravelly points Soil 3d rate

T12N R41W of 6th P.M.

Chs	
	East on a random line between sections 17 and 20 va 14°40'E
7.00	Ravine running North
24.00	Main ravine running W of N
40.00	Set a post for temporary 1/4 Sec cor
48.40	Ravine running N W
79.27	Intersected the N and S line 35 lks North of the corner to Sections 16, 17, 20 and 21 from which corner I run N 89°45' W on a true line between Sections 17 and 20 va 14°40'E
39.63½	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
79.27	The corner to Sections 17, 18, 19 and 20 Land broken Soil 3rd rate

T12N R41W of 6th P.M.

Chs	
	N 87°36' W on a random line between Sections 18 and 19 va 14°40'E
10.00	Ravine with a small running stream running North - a nice spring of good water about 12 rods ~~lks~~ South of this line in the ravine
40.00	Set a post for temporary 1/4 Sec cor
71.25	Ravine runs North
77.67	Intersected the West boundary of the township 54 lks South of the corner to Sections 18, 19 and 19 from which corner I run S 87°45' E on a true line between Sections 18 and 19 va 14°40'E
37.67	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
77.67	The corner to Sections 17, 18, 19 and 20 Land broken Soil poor 2nd rate

T. 12 N R 41 W of 6th P.M.

Chs	North between sections 17 and 18 Va 14°40'E
4000	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
5430	Ravine running N.W.
8000	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 7, 8, 17 and 18 Land somewhat broken Soil poor 2d rate

T. 12 N R 41 W of 6th P.M.

Chs	East on a random line between sections 8 and 17 Va 14°40'E
2400	Ravine running north
3600	Ravine runs N.
7942	Intersected the N and S. line 52 lks north of the corner to sections 8, 9, 16 and 17 from which corner I run N 89°35' W on a true line between sections 8 and 17 Va 14°40'E
3971	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
7942	The corner to sections 7, 8, 17 and 18 Land broken Soil poor 2d rate Sept 27th 1870

T 12 N R 41 W of 6th P M

Chs	N 87° 30' W on a random line between sections 7 and 18 va 14° 40' E
4,00	Set a post for temporary 1/4 Sec Cor
4,60	Drain descending North.
77,28	Intersected the West boundary of the township 32 lks South of the corner to Sections 7 and 18 from which corner I run S 87° 16' E on a true line between sections 7 and 18 va 14° 40' E
37,28	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
77,28	The corner to Sections 7, 8, 17 and 18
	Land rolling
	Soil poor 2d rate

T 12 N R 41 W of 6th P M

Chs	North between sections 7 and 8 va 14° 40' E
4,00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor
8,00	Set a post - deposited a marked stone and raised a mound of earth with pits as per instructions for corner to sections 5, 6, 7 and 8
	Land sloping north
	Soil 2d rate

	Chs	East on a random line between sections 5 and 8 Va 14°46' E
40	40.00	Set a post for temporary 1/4 Sec cor
49 77	79.40	Intersected the N and S line 58 lks north of the corner to sections 4, 5, 8 and 9 from which corner I run N 89°35' W on a true line between sections 5 and 8 Va 14°46' E
37	39.70	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec Cor.
77	79.40	The corner to sections 5, 6, 7 and 8 Land Smooth-Sloping North Soil 2d rate

T12N R11W of 5th P.M.

	Chs	N 87°36' W on a random line between sections 6 and 7 Va 14°46' E
	7.83	Ravine running north
	40.00	Set a post for temporary 1/4 Sec cor
	76.23	Intersected the West boundary of the township 21 lks ~~north~~ of the corner to sections 6 and 7 from which corner I run S 87°37'40" East on a true line between sections 6 and 7 Va 14°46' E
	36.23	Set a post - deposited a marked stake and raised a mound of earth with pits as per instructions for 1/4 Sec Cor
	76.23	The corner to sections 5, 6, 7 and 8 Land Smooth - Sloping gently to the north Soil mixed with gravel 2d rate

		T 12 N R 41 W of 6th P.M.	General Discription
Ch	Chs	North on a true line between Sections 5 and 6 Va 14° 40' E	This township is mostly 2d rate; is some what cut up by ravines, but is mostly smooth and level. The soil is mixed with gravel; but the soil looks good and rich except on the points along the ravines. Would grow wheat, oats, corn and potatoes if sufficient moisture could be furnished. Would raise wheat better than any other crop; as the shaly limestone & small pieces of limestone partly dissolved or decomposed and mixed with the soil indicate a proper soil for that crop. The surface of the land presents good facilities for irrigation by canals or ditches. The water would have to be furnished by wells. The presence of springs in the ravines in the North part show that wells would not have to be very deep up on the table lands. The tranition from table lands to North Slope & thence to River bottom can not be defined well enough to note in field notes
40.0	40.00	Set a post deposited a marked stone and raised a mound of earth with pits as per instructions for 1/4 Sec cor	
49.			
77.	83.39	Intersected the 3d Standard parallel 12.00 chs East of the corner to Sections 32 and 33 T 13 N R 41 W	
		Where I set a post deposited a marked stone and raised a mound of earth with pits as per instructions for closing corner to Sections 5 and 6	
77.		Land level with some Alkali water holes Soil 2d rate Sept 28th 1870	

We hereby Certify that we assisted William Hardin deputy Surveyor in Sub dividing Township Number Twelve (12) north of the base line of Range number forty one west of the Sixth Principal Meridian in the State of Nebraska and that said township has been in all respects to the best of our knowledge and belief well and faithfully surveyed and the boundary Monuments planted according to the instructions furnished by the Surveyor General

John Glen Chamman
Charles Hardin Chamman
Fred. Wiske Mound builder
S. G. Seger Mound builder

Subscribed and sworn to before me a Clerk of the District Court in and for the County of Lincoln in the State of Nebraska this 6th day of October 1870

R C Dougherty
Clerk of the District Court within and for Lincoln County Nebraska

I William Hardin deputy Surveyor do solemnly swear that in pursuance of a contract with R. R. Livingston, Surveyor of public lands in the state of Nebraska bearing date the 6th day of August 1840 and in strict conformity to the laws of the United States and the instructions furnished by the said Surveyor General I have faithfully surveyed the Sub-divisions of Township No 12 North of the base line, of Range No 41 West of the 6th Principal Meridian in the State aforesaid and do further solemnly swear that the foregoing are the true and original field notes of such Survey

William Hardin Deputy Surveyor

Subscribed by said William Hardin deputy Surveyor and sworn to before me A B Fuller a Notary Public for Saunders County Nebraska this 21 day of November 1870

A B Fuller
Notary Public

Surveyor General's Office

Plattsmouth Neb. Mch. 21. 1871

The foregoing field Notes of the Survey of the Subdivision lines of Township No. 12 North of the Base Line, of Range No. 41 West of the Sixth Principal Meridian in the State of Nebraska, Executed by William Harden under his Contract of the Sixth day of August 1870, in the Month of September 1870, having been critically Examined, the necessary Corrections and Explanations made, the said field Notes and the Survey they describe are hereby Approved.

Robt. W. Livingston
Surveyor General.

General Land Office • Original Field Notes

Book Number

631

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.
