General Land Office • Original Field Notes

Book Number

699

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.

124

T. 33-35 N.
R. 51 W.
✓
124.

Tow

Frank S. Wood

T. 33 N. R. 51 W.

6th Principal Meridian.

FIELD NOTES

OF

THE SUBDIVISION LINES OF

Township 33 North Range 51 West

6th Principal Meridian.

BY

Frank S. Wood Deputy Surveyor.

Under his Contract of Nov. 14th 1881

Survey Commenced May 19 - 1882

Survey Completed May 26 - 1882

ted,
pied for Washington,
pied for Register,

rd Denny & Co., Stationers & Printers, S. F., Cal.

Township..... Range.....

.....6th Principal Meridia

6	60	5	44	4	33	3	22	2	11	1
59		58		43		32		21		10
7	57	8	42	9	31	10	20	11	9	12
56		55		41		30		19		8
18	54	17	40	16	29	15	18	14	7	13
53		52		39		28		17		6
19	51	20	38	21	27	22	16	23	5	24
50		49		37		26		15		4
30	48	29	36	28	25	27	14	26	3	25
47		46		35		24		13		2
31	45	32	34	33	23	34	12	35	1	36

Edward Denny & Co., Stationers & Printers, S. F., Cal.
Copyright Secured,
Entered according to Act of Congress, in the Clerk's Office of the Librarian of Congress at Washington, D. C., in the year 1880.

Township..... North Range..... West

.....6th Principal Meridian.

Township ..... North Range ..... West

..... 6th Principal Meridian.

Survey made with Burts Patent Improved Solar Compass nearly new and in first rate order made by W & L E Gurley of Troy N. Y. in 1881

Township 33 North Range 57 West

6th Principal Meridian.

see previous page

Chains	From the corner to Sections 35, 36, 1 and 2 on the South boundary, I run, North, between Sections 35 and 36. Variation. 15° 45' East.
40.00	Set post 3 ft. long 3 ins diam 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face. dug pits - 18×18×12 ins E and W. of post. 5 1/2 ft dist and raised a mound of earth - 1 1/2 ft high 3 1/2 ft. base around post.
80.00	Set post 4 ft. long 4 ins square 12 ins in the ground for corner to Secs. 25-26-35 & 36 marked with - 1 notch on S. and 1 on E. edges. dug pits - 18×18×12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth - 2 ft. high 4 1/2 ft. base
	Land level
	Soil 2nd rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

Chains	East, on a random line between Sections 25 and 36. Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.61	Intersect E. Bdy. of Tp. 16 lks. N. of corner to Secs. 30-31-25-36 from which corner I run N 89°. 53' W. on a true line between Secs. 25 and 36 & 36 from which Va. 15° 45' East
40.31	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits - 18×18×12 ins N. and S. of stone 5 1/2 ft. dist. and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base. around post.
80.61	The corner to Secs. 25-26-35 & 36
	Land Level
	Soil 2nd. rate
	Bunchgrass.

Township 33 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 25 and 26. Variation. 15° 45' East.
40.00	Set post 3 ft. long 3 ins diam 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 on W. face dug pits 18 x 18 x 12 ins E and W. of post 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base. around post.
55.00	Cottonwood Creek 25 lks. wide runs S.E. Scattering timber along this Creek.
80.00	Set post 4 ft. long 4 ins square 12 ins. in the ground for corner to 23-24-25 & 26 marked with - 2 notches on S. and 1 on E. edges, dug pits - 18 x 18 x 12 ins. in each Sec. 5 1/2 ft. dist. and raised a mound of earth 1 ft. high 4 1/2 ft. base
	Land rolling
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 24 and 25. Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
73.00	Drain 20 lks wide runs South-E.
80.70	Intersect E. Bdy. of Tp. 3 lks. S. of the corner to Secs. 24-25-19 & 30 from which corner I run
	S 89° 59' W on a true line between Secs. 24 and 25
	Va. 15° 45' East
40.35	Set post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 on W. face dug pits - 18 x 18 x 12 ins W. and S. of stone 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
80.70	The corner to Secs. 23-24-25 & 26
	Land Level
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

Chains	North, between Sections 23 and 24. Variation 15° 40' East.
40.00	Set post 3 ft. long 3 ins diam 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits - 18 x 18 x 12 ins E and W. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base.
55.00	Drain 20 lks. wide cons. S. E.
80.00	Set post 4 ft. long 4 ins square 12 ins in the ground for corner to Secs. 13 - 14 - 23 - & 24. marked with 3 notches on S. and 1 on E. edges dug pits - 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth - 2 ft. high 4 1/2 ft. base. Around post
	Land. Level
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

Chains	East, on a random line between Sections 13 and 24. Variation 15° 40' East.
40.00	Set temporary 1/4 Sec. Cor.
80.60	Intersect E. Bdy. of Tp. 38 lks. N. of corner to Secs 13 & 24 - 18 & 19 from which corner I run N 89° 44' W. on a true line between Secs 13 and 24
	Va. 15° 40' East.
40.30	Set post 3 ft. long 3 ins. diam 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 on N. face dug pits 18 x 18 x 12 ins N. and S. of stone & raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post.
80.60	The corner to secs. 13 - 14 - 23 & 24
	Land Level
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

Chains	North, between Sections 13 and 14 Variation 15° 40' East.
40.00	Set post 3 ft. long 3 ins. diam. 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits 18 x 18 x 12 ins E. and W. of post 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base, around post
80.00	Set post 4 ft. long 4 ins. square 12 ins in the ground for corner to Secs. 11-12-13 & 14 marked with 4 notches on S. and 1 on E edges dug pits 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth 2 ft. high. 4 1/2 ft. base.
	Land rolling
	Soil 2nd. rate
	Vegetation Bunchgrass.
	I carefully examined the adjustments of my solar compass today particularly the latitude and reversing apparatus and found them correct
	May 19 - 1882

Township 33 North Range 57 West

6th Principal Meridian.

Chains	East, on a random line between Sections 12 and 13. Variation 15° 40' East.
40.00	Set temporary 1/4 Sec. Cor.
80.48	Intersect E. Bdy. of Tp. 8 lks. S. of the corner to Secs 12 - 13 - 7 - 18 from which corner bears S 89° 57' W on a true line between Secs. 12 and 13
	Va. 15° 40' East.
40.24	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S on W. face dug pits 18 x 18 x 12 ins. N. and S. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post
80.48	The corner to Sections 11-12-13 & 14
	Land Rolling
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

Chains	North, between Sections 11 and 12. Variation. 15° 40' East.
40.00	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W face dug pits 18×18×12 ins E. and W. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base.
80.00	Set post 4 ft. long 4 ins. square 12 ins. in the ground for corner to Secs. 1-2-11-& 12 marked with 5 notches on S. and 1 on E edges dug pits 18×18×12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth 2 ft. high 4 1/2 ft base around post Land Rolling Soil 2nd. rate Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

Chains	East, on a random line between Sections 1 and 12. Variation 15° 40' East.
40.00	Set temporary 1/4 Sec. Cor.
80.42	Intersect E. Bdy. of Tp 10 lks. N. of the corner to Secs. 1-12-6-7 from which corner I run N 89° 56' W on a true line between Secs. 1 and 12 Va. 15° 40' East
40.21	Set post 3 ft long 3 ins diam 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits 18×18×12 ins N. & S of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
80.42	The corner to sections 1-2-11-12 Land Rolling Soil 2nd. rate Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

Chains	North, on a random line between Sections 1 and 2. Variation. 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.47	Intersect N. Bdy. of Tp. 1 chs. W. of corner to Secs. 1-2-35 & 36 from which cor. I run S. 3 W. on a true line between Secs. 1 and 2. Va. 16° 45' East
40.47	Set pine post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits - 18 x 18 x 12 ins E. and W. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft high 3 1/2 ft. base. around post.
80.47	The corner to sections 1-2-11 & 12
	Land rolling
	Soil 2nd. rate
	Vegetation Bunchgrass.

6th Principal Meridian.

Chains	North, between Sections 34 and 35. Variation 16° 45' East.
40.00	Set a post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W face dug pits - 18 x 18 x 12 ins E and W. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base. around post.
80.00	Set a post 4 ft. long 4 ins square 12 ins. in the ground for cor. to Secs. 26-27-34 and 35 & marked T. 33 N. Sec. 26 on N.E. R. 51 W. S. 35 on S.E. S. 34 on S.W. and S. 27 on N.W. faces with - 1 notch on S. and 2 on E. edges dug pits - 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth - 2 ft. high 4 1/2 ft. base around post.
	Land rolling
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

Chains	East, on a random line between Sections 26 and 35
	Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.57	Intersect North and South line 9 lks. North of corner to Secs. 25-26 35 & 36 from which corner I run N 89°56' W. on a true line between Secs. 26 and 35.
	Va. 15° 45' East
40.26	Set post 3 ft. long 3 ins. diam 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits - 18 x 18 x 12 ins E. and S. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post
80.57	The corner to Secs. 26-27-34 & 35
	Land level
	Soil 2nd. and 3rd. rate
	Vegetation Bunchgrass.

6th Principal Meridian.

Chains	North, between Sections 26 and 27.
	Variation 15° 45' East.
40.00	Set post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits - 18 x 18 x 12 ins E and W. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft high 3 1/2 ft. base around post
79.00	Cottonwood Creek 30 lks. wide runs East.
80.00	Set a post 4 ft. long 4 ins square 12 ins. in the ground for Cor. to Secs. 22-23-26 and 27 marked on S. 33 N. Sec. 23 on N.E. R 57 W. S. 26 on S.E. S. 27 on S.W. and S. 22 on N.W. faces with - 2 notches on S. and 2 on E. edges dug pits - 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth - 2 ft. high 4 1/2 ft base around post
	Land rolling
	Soil 2nd. rate
	Vegetation Bunchgrass.

Chains	East, on a random line between Sections 23 and 26. Variation. 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.48	Intersect North and South line 6 lks. N. of corner to Secs 23-24-25 and 26 from which corner I run N 89°. 57' W. on a true line between Secs. 23 and 26
	Va. 15° 45' East
40.24	Set post 4 ft. long 4 ins. square 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits - 18 x 18 x 12 ins N. and S. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft high 3 1/2 ft. base around post
80.48	The corner to sections 22-23-26 & 27
	Land level
	Soil 2nd. rate
	Vegetation Bunchgrass.

Chains	North, between Sections 22 and 23. Variation 15° 45' East.
40.00	Set a post 3 ft long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits - 18 x 18 x 12 ins E and W. of post 5 1/2 ft. dist. and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post.
80.00	Set a post 4 ft. long 4 ins square 12 ins in the ground for cor to Secs. 14-15-22 and 23 marked T. 33 N. S. 14 on N.E. R. 57 W. S. 23 on S.E. S 22 on S.W. and S. 15 on N.W. faces with - 3 notches on S. and 2 on E edges - dug pits - 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth - 2 ft. high 2 1/2 ft. base around post.
	Land rolling
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West
6th Principal Meridian.

Chains	East, on a random line between Sections 14 and 23
	Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
60.00	Drain 20 lks. wide course S. E.
80.23	Intersect North and South line 20 lks. N. of corner to Secs. 13-14-23 and 24 from which corner I run N 89° 57' W on a true line between Secs. 14 and 23
	Va. 15° 45' East.
40.12	Set post 2 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face. dug pits - 18 x 18 x 12 ins N. and S. of post 5 1/2 ft. dist. and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base. around post.
80.23	The corner to sections 14-15-22-& 23
	Land rolling
	Soil 2nd. rate
	Vegetation Bunchgrass.
	May 20 - 1882

Township 33 North Range 57 West
6th Principal Meridian.

Chains	North, between Sections 14 and 15.
	Variation 15° 45' East.
40.00	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits - 18 x 18 x 12 ins E and W. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post.
56.00	Drain 20 lks. wide course S. E.
80.00	Set post 4 ft. long 4 ins. square 12 ins. in the ground for cor. to Secs 10-11-14 and 15 marked S. 33 N. S. 11 on N.E. R 57 W. S. 14 on S.E. S. 15 on S.W. and S. 10 on N.W. faces with - 4 notches on S and 2 on E. edges dug pits - 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist. and raised a mound of earth - 2 ft. high 4 1/2 ft base around post.
	Land rolling
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West
6th Principal Meridian.

Chains	East, on a random line between Sections 11 and 14 Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.19	Intersect North and South line 4 lks. N. of corner to Secs 11-12-13 & 14 from which corner I run N 89° 58' W. on a true line between Secs. 11 and 14 Vg. 15° 45' East.
40.10	Set post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits 18 x 18 x 12 ins N. and S of post 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
80.19	The corner to Secs 10-11-14 & 15 Land level Soil 2nd. rate Vegetation Bunchgrass.

Township 33 North Range 57 West
6th Principal Meridian.

Chains	North, between Sections 10 and 11. Variation 15° 45' East.
40.00	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4. Sec. Cor. marked 1/4 S. on W. face dug pits 18 x 18 x 12 ins E. and W. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
80.00	Set post 4 ft. long 4 ins. square 12 ins. in the ground for corner to Secs 2-3-10-11 marked S. 33 N. S. 2 on N.E. R. 57 W. S. 11 on S.E. S. 10 on S.W and S. 3 on N.W. faces with 5 notches on S. and 2 on E. edges dug pits 18 x 18 x 12 ins. in each Sec. 5 1/2 ft. dist and raised a mound of earth 2 ft. high 4 1/2 ft. base around post. Land rolling Soil 2nd. rate Vegetation Bunchgrass.

Chains	East, on a random line between Sections 2 and 11. Variation. 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
79.98	Intersect North and South line 3 lks. N. of corner to Secs 1-2-11 & 12 from which corner I run S 89° 59' W. on a true line between Secs. 2 and 11
	Va. 15° 45' East.
39.99	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits - 18 x 18 x 12 ins N. and S. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post.
79.98	The corner to Secs 2-3-10 & 11 Land rolling Soil 2nd. plate Vegetation Bunchgrass.

Chains	North, on a random line between Sections 2 and 3. Variation 15° 45' East.
40.00	Set post for temporary 1/4 Sec. Cor.
80.65	Intersect North Bdy of Tp. 15 lks. E. of corner to Secs 2 and 3 - 34 & 35 from which corner I run S 6' E. on a true line between Secs 2 and 3
	Va. 15° 45' East
40.65	Set post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits - 18 x 18 x 12 ins E. and W. of post 5 1/2 ft dist and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post.
80.65	The corner to Secs 2-3-10 & 11 Land level Soil 2nd. rate Bunchgrass. Vegetation.

Township 33 North Range 57 West

6th Principal Meridian.

North, between Sections 33 and 34.

Variation. 15° 45' East.

Chains	
40.00	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits - 18 x 18 x 12 ins E. and W. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
80.00	Set post 4 ft. long 4 ins square 12 ins: in the ground for corner to Secs. 27-28-33 and 34 marked S. 33 N. S. 27 on N. E. R. 57 W. S. 34 on S E. S. 33 on S W. and S. 28 on N W. faces with - 1 notch on S and 3 on E sides. dug pits - 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist. and raised a mound of earth - 2 ft. high. 4 1/2 ft. base around post.

Land level

Soil 2nd. rate

Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

East, on a random line between Sections 27 and 34.

Variation 15° 45' East.

Chains	
40.00	Set temporary 1/4 Sec. Cor.
80.30	Intersect North - and South - line 4 lks. S. of corner to Secs. 27-28-33 and 34 & from which corner I run S 89° 58' W on a true line between Secs. 27 and 34

V/a. 15° 45' East

Chains	
40.15	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N face dug pits - 18 x 18 x 12 ins N. and S of post 5 1/2 ft. dist. and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base. around post.
80.30	The corner to Secs. 27-28-33 & 34

Land level

Soil 2nd. rate

Vegetation Bunchgrass.

Chains	North, between Sections 27 and 28. Variation 15° 45' East.
40.00	Set post 3 ft. long 3 ins. diam. 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits - 18 x 18 x 12 ins E. and W. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft base around post.
80.00	Set a post 4 ft. long 4 ins square 12 ins. in the ground for cor. to Secs. 21 - 22 - 27 and 28 marked S. 33 N. S. 22 on N E. R 57 W. S 27 on S. E. S. 28 on S W. and S. 21 on N W. faces with - 2 notches on S. and 3 on E edges dug pits - 18 x 18 x 12 ins. in each Sec. 5 1/2 ft. dist and raised a mound of earth - 2 ft. high 4 1/2 ft. base. around post.
	Land level
	Soil 2nd. rate
	Vegetation Bunchgrass.
	May 22 - 1882

Chains	East, on a random line between Sections 22 and 27. Variation 15° 45° East.
37.00	Big Cottonwood Creek 30 lks. wide course S. E
40.00	Set temporary 1/4 Sec. Cor.
80.40	Intersect North and South line 10 lks. N. of corner to Secs 22-23-26 & 27 from which corner I run N 89°. 56' W. on a true line between Secs. 22 & 27.
	Va. 15° 45' East.
40.20	Set post 8 ft. long 3 ins. diam 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits - 18 x 18 x 12 ins ~~in each~~ ~~1/4 Sec.~~ 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
80.40	The corner to Secs 21-22-27 & 28
	Land level
	Soil 2nd. rate
	Vegetation Bunchgrass.

North, between Sections 21 and 22.

Variation. 15° 45' East.

Chains	
16.00	Big Cottonwood Creek 30 lks. wide course E. Water in pools
40.00	Set post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 on W. face dug pits - 18 x 18 x 12 ins E and W. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post.
80.00	Set post 4 ft. long 4 ins square 12 ins. in the ground for Cor to Secs. 15-16-21 & 22 marked S. 33 N. S. 15 on S.E. R 57 W. 22 on S.E. S. 21 on S.W. and S. 16 on N.W faces. with - 3 notches on S. and 3 on E edges dug pits - 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth - 2 ft. high 4 1/2 ft. base around post.
	Land level
	Soil 2nd. rate
	Vegetation Bunchgrass.

East, on a random line between Sections 15 and 22.

Variation 15° 45' East.

Chains	
40.00	Set temporary 1/4 Sec. Cor.
80.66	Intersect N. and S. line 26 lks. N. of corner to Secs. 14-15-22 & 23 from which corner I run N 89° 49' W on a true line between Secs 15 & 22
	Va. 15° 45 East
40.33	Set post 3 ft. long 3 ins diam. 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits - 18 x 18 x 12 ins N. and S. of post 5 1/2 ft. dist. and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post.
80.66	The corner to Secs 15-16-21 & 22
	Land level
	Soil 2nd. rate
	Vegetation. Bunchgrass.

North, between Sections 15 and 16.

Variation 15° 45' East.

Chains	
40.00	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W face dug pits - 18 x 18 x 12 ins E. and W. of post 5 1/2 ft. dist. and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post.
80.00	Set post 4 ft. long 4 ins. square 12 ins. in the ground for corner to Secs. 9-10-15 & 16 marked S. 33 N. S. 10 N.E. R 57 W. S. 15 on S.E. S. 16 on S.W. & S. 9 on N.W. faces with - 4 notches on S. and 3 on E. edges dug pits - 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth - 2 ft. high 4 1/2 ft. base around post.
	Land level
	Soil 2nd. rate
	Vegetation Bunchgrass.

East, on a random line between Sections 10 and 15.

Variation 15° 45' East.

Chains	
14.00	Drain 20 lks. wide course S.E.
40.00	Set temporary 1/4 Sec. Cor.
80.65	Intersect N. & S. line 32 lks. N. of corner to Secs 10-11-14 & 15 from which corner Dmn N 89° 46' W. on a true line between Secs. 10 & 15.
	Va. 15° 45' East.
40.33	Set post 3 ft. long 3 ins. diam 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits - 18 x 18 x 12 ins N. & S of post 5 1/2 ft. dist. and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post.
80.65	The corner to Secs. 9-10-15 & 16
	Land level
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

North, between Sections 9 and 10.

Variation 15° 45' East.

Chains	
16.00	Drain 20 lks. wide course S. E.
40.00	Set post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits - 18 x 18 x 12 ins. E. & W. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft base. around post.
80.00	Set post 4 ft. long 4 ins. square 12 ins. in the ground for cor. to Secs. 3 - 4 - 9 - 10 marked S. 33 N. S. 3 on N. E. R. 57 W. S. 10 on S. E. S. 9 on S. W. and S. 4 on N. W. faces with - 5 notches on S. and 3 on E. edges. dug pits - 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth - 2 ft. high 4 1/2 ft. base around post.

Land gently rolling
Soil 2nd. rate
Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

East, on a random line between Sections 3 and 10.

Variation 15° 30' East.

Chains	
40.00	Set temporary 1/4 Sec. Cor.
80.78	Intersect N. and S. line 5 lks. N. of corner to Secs 2 - 3 - 10 & 11 from which corner I run N 89° 58' W. on a true line between Secs. 3 and 10

Va. 15° 30' East

Chains	
40.39	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits - 18 x 18 x 12 ins N. & S. of post 5 1/2 ft. dist. and raised a mound of earth - 1 1/2 ft. high 3 1/2 ft. base around post.
80.78	The corner to Secs 3 - 4 - 9 & 10

Land level
Soil 2nd. rate
Vegetation Bunchgrass.

Chains	North, on a random line between Sections 3 and 4. Variation 15°. 45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.94	Intersect North Bdy. of Tp. 36 lks. N° of corner to Secs 3-4-33 and 34 from which corner I run S. 83' W. on a true line between Secs. 3 and 4
	Va. 15° 45' East.
40.94	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits 18 x 18 x 12 ins E. & W. of post 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post
80.94	The corner to Secs. 3-4-9 & 10
	Land level
	Soil 2nd. rate
	Vegetation Bunchgrass.

Chains	North, between Sections 32 and 33. Variation 15. 45' East.
40.00	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits 18 x 18 x 12 ins E and W. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post
80.00	Set charred post 4 ft. long 4 ins square 12 ins. in the ground for corner to Secs. 28-29 32 and 33 marked S. 33 N. S. 28 on A E. R 57 W. S. 33 on S. E S. 32 on S. W. and S. 29 on N W. faces with 1 notch on S. and 4 on E edges dug pits 18 x 18 x 12 ins. in each Sec. 5 1/2 ft. dist and raised a mound of earth 2 ft. high 4 1/2 ft. base around post
	Land level
	Soil 2nd. rate
	Vegetation Bunchgrass.
	May 23 - 1882

Township 33 North Range 57 West

6th Principal Meridian.

Chains	East, on a random line between Sections 28 and 33. Variation 15° 45' East.
40.00	Set temporary 1/4 Sec: Cor.
79.80	Intersect North and South line 30 lks. S. of corner to Secs. 28-27-34 and 33 from which corner I run S. 89° 47' W. on a true line between Secs. 28 and 33
	Va. 15° 45' East.
39.90	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits 18 x 18 x 12 ins. N. and S. of post 5 1/2 ft. dist. and raised a mound earth - 1 1/2 ft. high 3 1/2 ft. base around post.
79.80	The corner to sections 28-29-32 & 33
	Land rolling
	Soil 2nd. and 3rd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West

6th Principal Meridian.

Chains	North, between Sections 28 and 29. Variation 15° 45' East.
40.00	Set post 8 ft. long 3 ins. diam 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits - 18 x 18 x 12 ins. E and W. of post 5 1/2 ft. dist and raised a mound of earth - 1 1/2 ft high 3 1/2 ft. base around post.
80.00	Set post 4 ft. long 4 ins. square 12 ins in the ground for corner to Secs. 20-21-28 and 29 marked T. 33 N. R. 57 W. S. 21 on N.E. S. 28 on S.E. S. 29 on S.W. and S. 20 N.W. faces with - 2 notches on S. and 4 on E. edges. dug pits - 18 x 18 x 12 ins in Each Sec. 5 1/2 ft. dist and raised a mound of earth - 2 ft high 4 1/2 ft. base around post.
	Land level
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West
6th Principal Meridian.

Chains	East, on a random line between Sections 21 and 28. Variation 15° 45' East.
17.00	Big Cottonwood Creek 40 lks. wide course S. E. dry
40.00	Set post 3 for temporary 1/4 Sec. Cor.
44.00	Big Cottonwood Creek 40 lks wide course N. E. water in pools
80.18	Intersect N. and S. line 48 lks. S. of corner to Secs. 21-22-27 & 28 from which corner I run S. 89°. 42' W. on a true line between Secs 21 and 28 Va. 15° 45' East.
40.09	Set post 3 ft. long 3 ins. diam 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits 18 x 18 x 12 ins N. and S. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft high 3 1/2 ft. base around post
80.18	The corner to Secs. 20-21-28 & 29 Land level Soil 2nd. rate Vegetation Bunchgrass.

Township 33 North Range 57 West
6th Principal Meridian.

Chains	North, between Sections 20 and 21. Variation 15° 45' East.
21.00	Big Cottonwood Creek 40 lks. wide course S. E. water in pools.
40.00	Set post 3 ft. long 3 ins diam. 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits 18 x 18 x 12 ins E. and W. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
80.00	Set post 4 ft. long 4 ins square 12 ins. in the ground for corner to Secs. 16-17-20 and 21 marked T. 33 N. 33 N. S. 16 on N. E. R 51 W. S. 21 on S. E. S. 20 on S. W. and S. 17 on N. W. faces with 3 notches on S. and 4 on E. edges dug pits 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth 2 ft. high 4 1/2 ft base around post Land level Soil 2nd. rate Vegetation Bunchgrass.

Township 33 North Range 57 West
6th Principal Meridian.

Chains	East, on a random line between Sections 16 and 21. Variation. 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.20	Intersect N. and S. line 50 lks. S. of corner to Secs. 15-16-21 & 22 from which corner Trees S. 89° 39' W. on a true line between Secs. 16 and 21
	Va. 15° 45' East.
40.10	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits 18 x 18 x 12 ins. N. and S. of post 5 1/2 ft dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft base around post.
80.20	The corner to Secs. 16-17-20 & 21 Land level Soil 2nd. rate Vegetation Bunchgrass.

Township 33 North Range 57 West
6th Principal Meridian.

Chains	North, between Sections 16 and 17. Variation 15°. 45' East.
40.00	Set post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits 18 x 18 x 12 ins E. and W. of post and 5 1/2 ft. dist raised a mound of earth 1 1/2 ft high 3 1/2 ft base around post.
80.00	Set post 4 ft long 4 ins square 12 ins in the ground for corner to Secs. 8-9-16-17 marked T. 33 N. S. 9 on N.E. R. 57 W. S. 16 on S.E. S. 17 on S.W. and S. 8 on N.W. faces with 4 notches on S. and 4 on E. edges dug pits 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth 2 ft. high 4 1/2 ft. base around post. Land level Soil 2nd. rate Vegetation Bunchgrass.

Chains	East, on a random line between Sections 9 and 16. Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
79.96	Intersect N. and S. line 57 lks. S. of corner to Secs. 9-10-15 & 16 from which corner I run S. 89°. 37' W. on a true line between Secs. 9 and 16
	Va. 15°. 45 East
39.98	Set post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits 18 x 18 x 12 ins N. and S. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft high 3 1/2 ft base around post.
79.96	The corner to Secs. 8-9-16 & 17 Land level Soil 2nd. rate Vegetation Bunchgrass.

Chains	North, between Sections 8 and 9. Variation 15° 45' East.
40.00	Set post 3 ft long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits 18 x 18 x 12 ins E. and W. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft high 3 1/2 ft base around post.
72.00	Drain 15 lks. wide course S. E.
80.00	Set charred post 4 ft. long 4 ins. square 12 ins in the ground for corner to Secs. 4-5-8-9 ft. marked T. 33 N. R. 57 W. S. 9 on S. E. S. 8 on S. W. and S. 4 on N. W. faces with 5 notches on S. and 4 on E. edges dug pits 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth 2 ft. high 4 1/2 ft. base around post. Land level Soil 2nd. rate Vegetation Bunchgrass.

Chains	East, on a random line between Sections 4 and 9 Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.13	Intersect N. and S. line 58 lks. S. of the corner to Secs. 3-4-9 and 10 from which corner I run S. 89°. 35' W. on a true line between Secs. 4 and 9.
	Va. 15° 45 East
40.07	Set post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits 18x18x12 ins N. and S. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
80.13	The corner to Secs. 4-5-8 & 9 Land level Soil 2nd. rate Vegetation Bunchgrass.

Chains	North, on a random line between Sections 4 and 5. Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
81.61	Intersect North Boundary of Tp. 10 lks. W. of corner to Secs. 4. 5. 32 and 33 from which corner I run S. 4' W. on a true line between Secs. 4 and 5.
	Va. 15°. 45' East.
41.61	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits 18x18x12 ins. E. and W. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
81.61	The corner to Secs. 4-5-8 and 9 Land rolling Soil 2nd. rate Vegetation Bunchgrass. I carefully examined the adjustments of my solar compass today particularly the latitude and reversing apparatus and found them correct May 24-1882

North, between Sections 31 and 32.

Variation. 15°. 45' East.

Chains	
40.00	Set post 3 ft. long 3 ins diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on W face dug pits 18 x 18 x 12 ins E and W of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
80.00	Set post 4 ft. long 4 ins. square 12 ins in the ground for corner to Secs. 30-31-29 and 32 marked S. 33 N. S. 29 on N. E. R. 57 W. S. 32 on S. E. S. 31 on S. W. and S. 30 on N. W. faces with 1 notch on S. and 5 on E edges dug pits 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth 2 ft high 4 1/2 ft base around post. Land rolling Soil 2nd. rate Bunchgrass vegetation.

East, on a random line between Sections 29 and 32.

Variation 15°. 45' East.

Chains	
40.00	Set temporary 1/4 Sec. Cor.
80.62	Intersect N. and S. line 12 lks. N. of corner to Secs. 28-29-32 and 33 from which corner I run N 89°. 55' W. on a true line between Secs. 29 and 32
	V/a. 15°. 45' East
40.31	Set post 3 ft. long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits 18 x 18 x 12 ins N. and S. of post 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high 3 1/2 ft base around post.
80.62	The corner to sects. 29-30-31 & 32 Land rolling Soil 2nd. rate Vegetation Bunchgrass.

Township 33 North Range 57 West 6th Principal Meridian.

West, on a random line between Sections 30 and 31

Variation 15° 45' East.

Chains	
40.00	Set temporary 1/4 Sec. Cor.
80.66	Intersect W. boundary of Tp. 40 lks. S. of corner to Secs 30-31-25 & 36 from which corner I run S. 89°, 43' E on a true line between Secs 30 & 31
	Va. 15° 45' East.
40.66	Set post 3 ft. long 3 ins diam. 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits 18 x 18 x 12 ins N. and S. of post 5 1/2 ft dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base around post.
80.66	The corner to sections 29-30-31 and 32
	Land rolling
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West 6th Principal Meridian.

North, between Sections 29 and 30.

Variation 15° 45' East.

Chains	
40.00	Set post 3 ft. long 3 ins diam. 12 ins in the ground for 1/4 Sec. Cor. marked 1/4 S. on W. face dug pits 18 x 18 x 12 ins E. and W. of post 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high 3 1/2 ft base around post.
80.00	Set post 4 ft. long 4 ins. square 12 ins. in the ground for corner to Secs. 19-20-29 & 30 marked T. 33 N. S. 20 on N.E. R. 57 W. S. 29 on S.E. S. 30 on S.W. and S. 19 on N.W. faces with 2 notches on S. and 5 on E edges. dug pits 18 x 18 x 12 ins in each Sec. 5 1/2 ft. dist and raised a mound of earth 2 ft. high 4 1/2 ft. base around post.
	Land level
	Soil 2nd. rate
	Vegetation Bunchgrass.

Township 33 North Range 57 West
6th Principal Meridian.

Chains	East, on a random line between Sections 20 and 29. Variation. 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
58.00	Big Cottonwood Creek 25 lks wide course S.E. dry
73.00	Big Cottonwood Creek 25 lks. wide course N.E. dry
80.51	Intersect N. and S. line 16 lks. N. of corner to Secs. 20-21-28 & 29 from which corner I run N. 89° 53' W on a true line between Secs 20 and 29 Va. 15° 45' East
40.26	Set post 3 ft long 3 ins. diam. 12 ins. in the ground for 1/4 Sec. Cor. marked 1/4 S. on N. face dug pits 18x18x12 ins N. and S. of post 5 1/2 ft. dist and raised a mound of earth 1 1/2 ft. high 3 1/2 ft base around post.
80.51	The corner to Secs. 19-20-29-30 Land rolling Soil 1st & 2nd rate Vegetation Bunchgrass

Township 33 North Range 57 West
6th Principal Meridian.

Chains	West, on a random line between Sections 19 and 30. Variation 15° 40' East.
40.00	Set post for temporary 1/4 Sec Cor
80.27	Intersect West Bd of Tp 19 lks South of Cor to Secs 24-25-19 & 30 from which Cor I run S 89° 52' E on a true line between Secs 19 & 30 Var 15° 40' E
40.27	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on N face dug pits 18x18x12 ins N & S of post 5 1/2 ft dist and raised a mound of earth 1 1/2 ft high 3 1/2 ft base around post.
80.27	The Cor to Secs 19-20-29 & 30 Land rolling Soil 1st & 2nd rate Vegetation Bunchgrass

Township 33 North Range 51 West

6th Principal Meridian.

North, between Sections 19 and 20.

Variation. 15° 40′ East.

Chains	
40.00	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on W face dug pits 18×18×12 ins E + W of post 5½ ft dist and raised mound of earth 1½ ft high 3½ ft bike around post
48.00	Big Cottonwood Creek 25 lks wide Course East
67.00	Big Cottonwood Creek 25 lks wide Course S. W.
80.00	Set a post 4 ft long 4 ins square 12 ins in the ground for Cor to Secs 17-18-19 + 20 marked T33 N. S 17 on N. E. R 51 W. S 20 on S. E. S 19 on S. W. and S 18 on N. W. faces with 3 notches on S and 5 on E edges dug pits 18×18×12 ins in each Sec 5½ ft dist and raised mound of earth 2 ft high 4½ ft base around post. Land level and gently rolling Soil 1st + 2nd rate Vegetation Bunchgrass

Township 33 North Range 51 West

6th Principal Meridian.

East, on a random line between Sections 17 and 20.

Variation 15° 45′ East.

Chains	
9.00	Big Cottonwood Creek 25 lks wide Course S.
40.00	Set temporary 1/4 Sec. Cor.
80.60	Intersect N + S line 8 lks N. of Cor to Secs 16-17-20 and 21 from which Cor S run S 89° 57′ W on a true line between Secs 17 + 12 Var 15° 45′ E.
40.30	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on W face dug pits 18×18×12 ins N + S of post 5½ ft dist and raised mound of earth 1½ ft high 3½ ft bike around post
80.60	The Cor to Secs 17-18-19 + 20 Land level and rolling Soil 2nd rate Vegetation Bunchgrass.

Township 33 North Range 51 West

6th Principal Meridian.

Chains	West, on a random line between Sections 18 and 19. Variation 15° 45' East.
17.00	Big Cottonwood Creek 25 lks wide Course N. E.
37.00	Same Creek 25 lks wide Course S. E.
40.00	Set temporary 1/4 Sec. Cor.
79.51	Intersect W. By of Tp 23 lks N. of Cor. to Secs 24-13-18 + 19 from which Cor I run N. 89° 50' E on a true line between Secs 18 + 19 Var 15° 45' E.
39.51	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on N face dug pits 18×18×12 ins N + S. of post 5½ ft dist and raised mound of earth 1½ ft high 3½ ft base around post.
79.51	The Cor to Secs 17-18-19 + 20 Land level and rolling Soil 1st + 2nd rate Vegetation Bunchgrass

I carefully examined the adjustments of my solar compass today particularly the latitude and reversing apparatus & forma thereof correct May 25-1882

Township 33 North Range 51 West

6th Principal Meridian.

Chains	North, between Sections 17 and 18. Variation 15° 45' East.
13.00	Big Cottonwood Creek 25 lks wide Course East.
40.00	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on W face dug pits 18×18×12 ins E + W of post 5½ ft dist and raised mound of earth 1½ ft high 3½ ft base around post
80.00	Set post 4 ft long 4 ins square 12 ins in the ground for Cor to Secs 7-8-17 + 18 marked T33 N. S8 on N. E. R51 W. S17 on S. E. S18 on S. W. and S7 on N W faces with 4 notches on S and 5 on E edges dug pits 18×18×12 ins in each Sec 5½ ft dist and raised mound of earth 2 ft high 4½ ft base around post Land level Soil 2nd rate Vegetation Bunchgrass

Township 33 North Range 51 West

6th Principal Meridian.

Chains	East, on a random line between Sections 8 and 17. Variation 15° 40' East.
40.00	Set temporary 1/4 Sec. Cor.
80.15	Intersect N + S line 38 lks South of Cor to Secs 8-9-16 + 17 from which Cor I run S 89° 44' W. on a true line between Secs 8 + 17 Var. 15° 40' E.
40.08	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on N face dug pits 18 x 18 x 12 ins N. + S. of post 5½ ft dist and raised mound of earth 1½ ft high 3½ ft base
80.15	The Cor to Secs 7-8-17 + 18 Land level Soil 2nd rate Vegetation Bunchgrass

Township 33 North Range 51 West

6th Principal Meridian.

Chains	West, on a random line between Sections 7 and 18. Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
79.40	Intersect West Boundary of Tp. 2 lks S of Cor to Secs 7-12-13 + 18 from which Cor I run S 89° 59' E on a true line between Secs 7 + 18 Var 15° 45' E.
39.40	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on N face dug pits 18 x 18 x 12 ins N + S of post 5½ ft dist and raised mound of earth 1½ ft high 3½ ft base around post
79.40	The Cor to Secs 7-8-17 + 18 Land level Soil 2nd rate Vegetation Bunchgrass

Township 33 North Range 51 West

6th Principal Meridian.

Chains	North, between Sections 7 and 8. Variation. 15° 40′ East.
40.00	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on W face dug pits 18 x 18 x 12 ins E. & W. of post 5 1/2 ft dist and raised mound of earth 1 1/2 ft high 3 1/2 ft base around post
80.00	Set a post 4 ft long 4 ins square 12 ins in the ground for Cor to Secs 5-6-7 & 8 marked with 5 notches on S and 5 on E edges, dug pits 18 x 18 x 12 ins in each Sec 5 1/2 ft dist and raised a mound of earth 2 ft high 4 1/2 ft base
	Land level
	Soil 2nd rate
	Vegetation Bunchgrass

Township 33 North Range 51 West

6th Principal Meridian.

Chains	East, on a random line between Sections 5 and 8. Variation 15° 45′ East.
40.00	Set temporary 1/4 Sec. Cor.
69.00	Cross wash 15 lks wide Course S.E.
79.79	Intersect N & S line 3 lks N of Cor to Secs 4-5-8 & 9 from which Cor I run N 89. 59 W on a true line between Secs 5 & 8
	Var 15° 45′ E.
39.90	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on W face dug pits 18 x 18 x 12 ins N & S of post 5 1/2 ft dist and raised mound of earth 1 1/2 ft high 3 1/2 ft base around post
79.79	The Cor to Secs 5-6-7 & 8
	Land level
	Soil 2nd rate
	Vegetation Bunchgrass

Township 33 North Range 51 West

6th Principal Meridian.

Chains	West, on a random line between Sections 6 and 7. Variation 15° 45' East.
40.00	Set temporary 1/4 Sec Cor
45.00	Enter rolling prairie
79.64	Intersect West Boundary of Tp 5 lks South of Cor to Secs 6-7-1 + 12 from which Cor I run S 89° 58' E on a true line between Secs 6 + 7 Var 15° 45' E.
89.64	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on N face aug pits 18 x 18 x 12 ins N + S of stone 5½ ft dist and raised a mound of earth 1½ ft high 3½ ft base
79.64	The Cor to Secs 5-6-7 + 8 Land level + rolling Soil 2nd rate Vegetation Bunchgrass

Township 33 North Range 51 West

6th Principal Meridian.

Chains	North, on a random line between Sections 5 and 6. Variation 15° 40' East.
6.00	Drain 10 lks wide Course E.
40.00	Set temporary 1/4 Sec. Cor.
80.35	Intersect North By of Tp 71 lks East of Cor to Secs 5-6 31 + 32 from which Cor I run S 30' E on a true line between Secs 5 + 6 Var 15° 40' East.
40.35	Set a post 3 ft long 3 ins diam 12 ins in the ground for 1/4 Sec Cor marked 1/4 S on W face aug pits 18 x 18 x 12 ins E + W of post 5½ ft dist and raised mound of earth 1½ ft high 3½ ft base around post.
80.35	The Cor to Secs 5-6-7 + 8 Land level Soil 2nd rate Vegetation Bunchgrass. May 26 - 1882

GENERAL DESCRIPTION.

This Township is composed of fine gently rolling prairie land
The greater portion of the soil is 2nd rate and is well adapted to Agriculture
It is well watered by numerous Creeks the principal one is Big Cottonwood Creek which flows through the Township. The township has a gentle drainage to the S.E. suitable for farming. The soil does not need irrigation to insure agricultural crops and the luxuriant growth of Bunch grass renders it desirable for grazing purposes

U. S. Surveyor-General's Office.

Plattsmouth Neb.

November 6th 1882

The foregoing Field Notes of the surveys of

Subdivision lines of Tp. 33 North Range 51 West of the Principal Base and

Meridian

in the state of Neb. *executed by*

Frank S. Ward *in the month of* May 1882

U. S. Deputy Surveyor, under his contract, dated

Nov. 14th 1881

having been critically examined, the necessary corrections and explanations made, the said Field Notes and the surveys they describe are hereby approved.

Geo. Spencer

U. S. Surveyor-General for Ia & Neb.

Frank S. Wood, Deputy Surveyor.

T. 34 N. R. 51 W.

6th Principal Meridian.

FIELD NOTES

OF

THE SUBDIVISION LINES OF

Township 34 North Range 51 West

6th Principal Meridian.

Frank S. Wood Deputy Surveyor.

Under his Contract of Nov. 14, 1881,

Survey Commenced Apr. 6, 1882,

Survey Completed Apr. 14, 1882,

Platted,

Copied for Washington,

Copied for Register,

Edward Denny & Co., Stationers & Printers, S. F., Cal.

Township..... Range.....

.....6th Principal Meridi

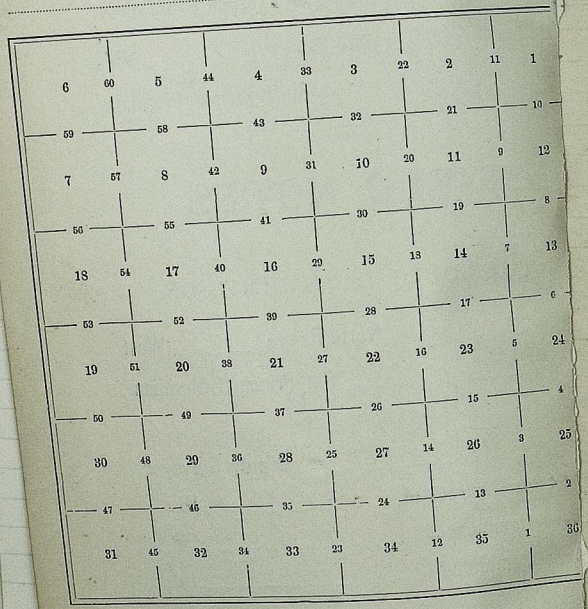

Edward Denny & Co., Stationers & Printers, S. F., Cal.
Copyright Secured,
Entered according to Act of Congress, in the Clerk's Office of the Librarian of Congress at Washington, D. C., in the year 1880.

wnship..... North Range..... West

.....6th Principal Meridian.

Township ..... North Range ..... West
..... 6th Principal Meridian.

Township ..... North Range ..... West
..... 6th Principal Meridian.

Survey made with Burt's Patent
Improved Solar compass, nearly new
and in first rate order.
Made by W. & L. E. Gurley of
Troy N.Y. in 1881.

Township 34 North Range 51 West

(See previous page) 6th Principal Meridian.

Chains	From the corner to Sections 35, 36, 1 and 2 on the South boundary, I run, North, between Sections 35 and 36. Variation. 15°45' East.
	Ascend,
6.00	Top of Divide, bears N.W. & East,
30.00	Descend,
40.00	Set post, 3ft. long, 3ins. dia., 12ins. in the ground, for 1/4 Sec. Cor., marked 1/4 S. on W. face, dug pits, 18x18x12ins. E. & W. of post, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base around post,
80.00	Set post, 4ft. long, 4ins. square, 12ins. in the ground, for Cor. to Secs. 25-26-35-36, marked T. 34 N. S. 25 on N.E., R. 51 W. S. 36 on S.E., S. 35 on S.W. and S. 26 on N.W. faces, with 1 notch on S. & E. edges, dug pits, 18x18x12ins. in each Sec., 5½ft. dist., and raised a mound of earth, 2ft. high, 4½ft. base around post,
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian.

Chains	East, on a random line between Sections 25 and 36. Variation 15°45' East.
	Descend gradually.
40.00	Set temporary 1/4 sec. cor.
66.00	Cross Lone Tree Creek, 20lks. wide, Course S.E.
69.00	Cross same Creek, Course N.E.
73.00	Cross same Creek, Course S.E.
79.52	Intersect East Boundary of Tp., 2lks. South of cor. to secs. 25-30-31-36, from which corner I run S. 89°59' W., on a true line bet. secs. 25-36. Va. 15°45' E.
39.76	Set post, 3ft. long, 3ins. dia., 12ins. in the ground, for 1/4 Sec. Cor., marked 1/4 S. on N. face, dug pits, 18x18x12ins. N. & S. of post, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base around post,
79.52	The cor. to secs. 25-26-35-36.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 25 and 26.
	Variation. 15° 45' East.
	Descends gradually.
10.00	Cross Lone Tree Creek, 20 lks. wide, course N.E.
18.00	Cross same creek course N.W.
21.00	Cross same creek, course S.E.
40.00	Set post, 3ft. long, 3ins. dia., 12ins. in the ground for 1/4 Sec. Cor., marked 1/4 S. on W. face, dug pits 18x18x12ins. E. & W. of post 5½ft. dist. and raised a mound of earth 1½ft. high, 3½ft. base around post.
80.00	Set post, 4ft. long, 4ins. square, 12ins. in the ground for Cor. to Secs. 23-24-25-26, marked T. 34 N. S. 24 on N.E. R. 51 W. S. 25 on S.E. S. 26 on S.W. and S. 23 on N.W. faces with 2 notches on S. and 1 notch on E. edges, dug pits 18x18x12ins. in each Sec., 5½ft. dist., and raised a mound of earth 2ft. high, 4½ft. base around post.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 24 and 25.
	Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
79.54	Intersect East Boundary of Tp., 12 lks. South of Cor. to Secs. 19-24-25-30, from which corner Sun S. 59° 55' W., on a true line bet. Secs. 24-25. Va. 15° 45' E.
39.77	Set post, 3ft. long, 3ins. dia., 12ins. in the ground for 1/4 Sec. Cor., marked 1/4 S. on N. face, dug pits, 18x18x12ins. N. & S. of post, 5½ft. dist. and raised a mound of earth, 1½ft. high, 3½ft. base around post.
79.54	The Cor. to Secs. 23-24-25-26.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Chains	North, between Sections 23 and 24. Variation 15° 45′ East.
	Ascend gradually.
40.00	Set post, 3ft. long, 3ins. dia., 12ins. in the ground, for 1/4 Sec. Cor., marked 1/4 S. on W. face, dug pits 18x18x12ins., E. & W. of post, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base around post.
41.00	Top of Divide bro. N.W. & S.E., and descend gradually.
80.00	Set post, 4ft. long, 4ins. square, 12ins. in the ground, for Cor. to Secs. 13-14-23-24 marked T.34 N. R.51 W. S.13 on N.E., S.24 on S.E., S.23 on S.W. and S.14 on N.W. faces, with 3 notches on S. and notch on E. edges, dug pits, 18x18x12ins. in each Sec., 5½ft. dist., and raised a mound of earth, 2ft. high, 4½ft. base around post.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Chains	East, on a random line between Sections 13 and 24. Variation 15° 45′ East.
	Descend gradually.
12.00	Cross Creek, 15lks. wide, course S.E.
40.00	Set temporary 1/4 Sec. Cor.
80.12	Intersect E. B. of Tp., 47lks. North of Cor. to Secs. 13-18-19-24 from which corner, Azm N.89° 40′ W., on a true line bet. Secs. 13-24, Va. 15° 45′ E.
40.06	Set post, 3ft. long, 3ins. dia., 12ins. in the ground, for 1/4 Sec. Cor., marked 1/4 S. on N. face, dug pits 18x18x12ins., N. & S. of post, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base around post.
80.12	Sec. Cor. to Secs. 13-14-23-24.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 13 and 14
	Variation 15°45' East.
	Descend gradually
7.00	Cross Creek, 15lks. wide, course S.E., and ascend gradually.
40.00	Set post, 3ft. long, 3ins. dia., 12ins. in the ground, for 1/4 Sec. Cor. marked 1/4 S. on W. face, dug pits 18x18x12ins. E. & W. of post, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base around post
80.00	Set post, 4ft. long, 4ins. square, 12ins. in the ground, for Cor. to Secs. 11-12-13-14, marked T. 34 N. S. 12 on N.E., R. 51 W. S. 13 on S.E., S. 14 on S.W. and S. 11 on N.W. faces, with 4 notches on S. and 1 notch on E. edges, dug pits, 18x18x12ins. in each Sec., 5½ft. dist., and raised a mound of earth, 2ft. high, 4½ft. base around post.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.
	April 6, 1882.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 12 and 13.
	Variation 15°45' East.
	Descend gradually.
40.00	Set temporary 1/4 Sec. Cor.
75.00	Cross Creek 20lks. wide, course S.E.
80.21	Intersect E. B. of Sp. 34lks. South of Cor. to Secs. 7-12-13-18 from which Corner, I run S. 89° 45' W., on a true line bet. Secs. 12-13.
	Va. 15°45' E.
40.11	Set post, 3ft. long, 3ins. dia., 12ins. in the ground, for 1/4 Sec. Cor., marked 1/4 S. on N. face, dug pits, 18x18x12 ins. N. & S. of post, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base around post.
80.21	The Cor. to Secs. 11-12-13-14.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 11 and 12.
	Variation. 15° 45' East.
	Descend gradually,
40.00	Set post, 3ft. long 3ins. dia., 12ins. in the ground, for 1/4 Sec. Cor., marked 1/4 S. on W. face dug pits, 18x18x12ins., E. & W. of post, 5 1/2ft. dist., and raised a mound of earth 1 1/2ft. high, 3 1/2ft. base around post.
79.00	Cross creek, 20lks. wide, course S.E. and ascend gradually,
80.00	Set post, 4ft. long, 4ins. square, 12ins. in the ground, for Cor. to Secs. 1-2-11-12, marked T. 34 N. S. 1 on N.E., R. 51 W. S. 12 on S.E., S. 11 on S.W. and S. 2 on N.W. faces with 5 notches on S. and 1 notch on E. edges, dug pits, 18x18x12ins. in each Sec., 5 1/2ft. dist., and raised a mound of earth, 2ft. high, 4 1/2ft. base around post.
	Land rolling.
	Soil 2nd class.
	Vegetation, Bunchgrass.

Chains	East, on a random line between Sections 1 and 12.
	Variation 15° 45' East.
	Descend
20.00	Cross Drain, 50lks. wide, course South and descend,
40.00	Set temporary 1/4 sec. cor.
70.00	Top of Ridge, bro. N.W. & S. and descend,
80.50	Intersect E.B. of Tp., 18lks. South of cor. to secs. 1-6-7-12, from which course bears S. 89° 52' W., on a true line bet. secs. 1-12. Va. 15° 45' E.
40.25	Set post, 3ft. long, 3ins. dia., 12ins. in the ground, for 1/4 Sec. Cor., marked 1/4 S. on N. face dug pits, 18x18x12ins. N. & S. of post, 5 1/2ft. dist., and raised a mound of earth, 1 1/2ft. high, 3 1/2ft. base around post,
80.50	The cor. to secs. 1-2-11-12,
	Land mountainous,
	Soil 2nd & 3rd class,
	Vegetation, Bunchgrass.

Township 34 North Range 51 West 6th Principal Meridian.

Chains	North, on a random line between Sections 1 and 2. Variation. 15° 45' East.
40.00	Set temporary 1/4 Sec. cor.
45.00	Ascend,
61.00	Top of Divide and descend,
80.41	Intersect North Boundary of Tp, 50 lks. West of cor. to secs. 1-2-35-36, from which corner I run S. 21' W., on a true line bet. secs. 1-2.
	Va. 15° 45' E.
40.41	Set post, 3 ft. long 3 ins. dia., 12 ins. in the ground for 1/4 Sec. Cor., marked 1/4 S. on W. face dug pits 18 x 18 x 12 ins. E. & W. of post, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base around post,
80.41	The cor. to secs. 1-2-11-12,
	Land mountainous,
	Soil 2nd & 3rd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 51 West 6th Principal Meridian.

Chains	North, between Sections 34 and 35. Variation 15° 45' East.
	Ascend,
34.00	Top of Divide bet. E. and W. & descend,
40.00	Set Sandstone, 12 x 10 x 4 ins., 8 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face dug pits 18 x 18 x 12 ins. E. & W. of Stone, 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base,
80.00	Set Sandstone 16 x 12 x 4 ins., 11 ins. in the ground for Cor. to Secs. 26-27-34-35 marked with 1 notch on S. and 2 notches on E. edges, dug pits 18 x 18 x 12 ins. in each Sec. 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base,
	Land mountainous,
	Soil 2nd & 3rd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian.

Chains	East, on a random line between Sections 26 and 35
	Variation 15° 45' East.
	Along North slope.
40.00	Set temporary 1/4 sec. cor.
80.44	Intersect N. & S. line, 4 lks. North of cor. to secs. 25-26-35-36 from which corner I run N. 89° 58' W., on a true line bet. secs. 26-35.
	Va. 15° 45' E.
40.22	Set post, 3 ft. long, 3 ins. dia., 12 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 S. on N. face, dug pits, 18 x 18 x 12 ins. N. & S. of post, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base around post.
80.44	The cor. to secs. 26-27-34-35.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian.

Chains	North, between Sections 26 and 27.
	Variation 15° 45' East.
40.00	Set Sandstone, 14 x 9 x 5 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits, 18 x 18 x 12 ins. E. & W. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
56.00	Cross S. Fork of Lone Tree Creek, 20 lks. wide, Course East.
80.00	Set Sandstone, 16 x 10 x 4 ins., 11 ins. in the ground, for Cor. to Secs. 22-23-26-27 marked with 2 notches on S. & E. edges, dug pits, 18 x 18 x 12 ins. in each Sec., 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base.
	Land level.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 23 and 26.
	Variation 15°45' East.
16.00	Cross N. Fork of Lone Tree Creek, 15lks. wide, Course S.E.
36.00	Cross Same Creek, Course N.E.
40.00	Set temporary 1/4 Sec. Cor.
44.00	Cross Same Creek, Course S.E.
80.30	Intersect N. & S. line, 10lks. N. of Cor. to Secs. 23-24-25-26 from which corner, Sun N.89°56' W. on a true line bet. Secs. 23-26, Va. 15°45' E.
40.15	Set Sandstone, 12x12x4 ins., 8 ins. in the ground, for 1/4 Sec. Cor. marked 1/4 on N. face, dug pits 18x18x12 ins., N. & S. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
80.30	The Cor. to Secs. 22-23-26-27, Land level, Soil 2nd rate, Vegetation, Bunchgrass. Carefully examined the adjustments of my Solar compass today, particularly the latitude and reversing apparatus, and found them correct. Apr. 7, 1882.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 22 and 23.
	Variation 15°45' East.
	Descend gradually
32.00	Cross N. Fork of Lone Tree Creek, 20lks. wide, Course East and ascend gradually.
40.00	Set Sandstone, 12x8x6 ins., 8 ins. in the ground, for 1/4 Sec. Cor. marked 1/4 on W. face, dug pits 18x18x12 ins. E. & W. of stone 5 1/2 ft. dist. and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
80.00	Set Sandstone, 13x10x6 ins., 9 ins. in the ground, for Cor. to Secs. 14-15-22-23, marked with 3 notches on S. and 2 notches on E. edges, dug pits 18x18x12 ins. in each Sec., 5 1/2 ft. dist. and raised a mound of earth 2 ft. high, 4 1/2 ft. base.
	Land rolling.
	Soil 2nd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

East, on a random line between Sections 14 and 23

Variation 15°45' East.

Chains	
	Ascend,
40.00	Set temporary 1/4 sec. cor.
50.00	Top of Ridge, bro. N.W. & S.E. & descend.
79.80	Intersect N. & S. line, 30 lks. North of cor. to secs. 13-14-23-24 from which corner, I run N.89°47' W. on a true line bet. secs. 14-23. Va. 15°45' E.
39.90	Set Sandstone, 12 x 10 x 6 ins., 8 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18 x 18 x 12 ins., N. & S. of Stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
79.80	The cor. to secs. 14-15-22-23.
	Land mountainous,
	Soil 2nd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

North, between Sections 14 and 15.

Variation 15°45' East.

Chains	
	Ascend,
40.00	Set Sandstone, 14 x 12 x 4 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18 x 18 x 12 ins., E. & W. of Stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
41.00	Top of Ridge, bro. N.W. and S.E. and descend.
58.00	Legges Creek, 20 lks. wide, course S.E. and ascend.
80.00	Set Sandstone, 15 x 10 x 5 ins., 11 ins. in the ground, for cor. to Secs. 10-11-14-15 marked with 4 notches on S. and 2 notches on E. edges, dug pits, 18 x 18 x 12 ins. in each Sec., 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base.
	Land mountainous,
	Soil 2nd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 57 West
6th Principal Meridian.

Chains	East, on a random line between Sections 11 and 14
	Variation 15° 45' East.
	Ascend,
10.00	Top of Ridge, brs. N.W. & S.E. & descend,
40.00	Set temporary 1/4 Sec. Cor.,
51.00	Cross Creek, 20lks. wide, course S.E. and ascend,
79.85	Intersect N. & S. line, 12lks. North of Cor. to Secs. 11-12-13-14 from which corner, Azm N.89° 55' W., on a true line bet. Secs. 11-14. Va. 15° 45' E.
39.93	Set Sandstone, 14x9x5 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits 18x18x12 ins. N. & S. of stone, 5 1/2 ft. dist., and raised a mound of earth 1 1/2 ft. high, 3 1/2 ft. base,
79.85	The Cor. to Secs. 10-11-14-15,
	Land mountainous,
	Soil 2nd & 3rd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 57 West
6th Principal Meridian.

Chains	North, between Sections 10 and 11.
	Variation 15° 45' East.
	Ascend,
6.00	Top of Ridge, brs. N.W. & S.E. & descend,
31.00	Cross Creek, 20lks. wide, course S.E.
40.00	Set Sandstone, 12x10x5 ins., 8 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits 18x18x12 ins. E. & W. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base,
42.00	Ascend,
80.00	Set Sandstone, 14x12x4 ins., 9 ins. in the ground, for Cor. to Secs. 2-3-10-11, marked with 5 notches on S. and 2 notches on E. edges, dug pits, 18x18x12 ins. in each Sec., 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base,
	Land mountainous,
	Soil 3rd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 2 and 11. Variation. 15°45' East.
	Ascend,
5.00	Top of Ridge, brs. N.W. & S.E.
	and descend,
40.00	Set temporary 1/4 sec. cor.
65.00	Cross Creek, 15lks. wide, course
	S.E. and ascend,
79.42	Intersect N. & S. line, 8lks. N.
	of cor. to secs. 1-2-11-12, from
	which corner, I run N.89°57' W.,
	on a true line bet. secs. 2-11
	Va. 15°45' E.
39.71	Set Sandstone 12x9x5 ins., 8 ins.
	in the ground, for 1/4 Sec. Cor.,
	marked 1/4 on N. face, dug pits
	18x18x12 ins., N. & S. of stone, 5 1/2 ft.
	dist. and raised a mound of
	earth, 1 1/2 ft. high, 3 1/2 ft. base,
79.42	The cor. to secs. 2-3-10-11,
	Land mountainous.
	Soil 2nd & 3rd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, on a random line between Sections 2 and 3. Variation 15°45' East.
	Ascend,
6.00	Top of Ridge, brs. N.W. & S.E. and
	descend
35.00	Cross Creek, 30lks. wide, course
	S.E. and ascend,
40.00	Set temporary 1/4 sec. cor.
80.30	Intersect N.B. of Jn., 16lks. East
	of cor. to secs. 2-3-34-35 from
	which corner, I run S.7 E.,
	on a true line bet. secs. 2-3.
	Va. 15°45' E.
40.30	Set Sandstone 12x10x4 ins., 8 ins.
	in the ground, for 1/4 Sec. Cor.,
	marked 1/4 on W. face, dug pits
	18x18x12 ins., E. & W. of stone, 5 1/2 ft.
	dist. and raised a mound of
	earth, 1 1/2 ft. high, 3 1/2 ft. base.
80.30	The cor. to secs. 2-3-10-11
	Land mountainous.
	Soil 2nd & 3rd rate,
	Vegetation, Bunchgrass.
	Apr. 8, 1882.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 33 and 34.
	Variation 15° 45' East.
40.00	Set Sandstone, 14x12x4 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits, 18x18x12 ins. E. & W. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base,
80.00	Set Sandstone, 14x10x4 ins., 9 ins. in the ground, for Cor. to Secs. 27-28-33-34, marked with 1 notch on S. and 3 notches on E. edges, dug pits, 18x18x12 ins. in each Sec., 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base,
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 27 and 34.
	Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.40	Intersect N. & S. line, 6 lks. South of Cor. to Secs. 26-27-34-35, from which corner, I run S. 89° 57' W., on a true line bet. Secs. 27-34,
	Va. 15° 45' E.
40.20	Set Sandstone, 12x8x6 ins., 8 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18x18x12 ins. N. & S. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base,
80.40	The Cor. to Secs. 27-28-33-34,
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian.

Chains	North, between Sections 27 and 28. Variation 15° 45' East.
	Descend gradually,
40.00	Set Sandstone, 16 x 10 x 3 ins., 11 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits 18 x 18 x 12 ins., E. & W. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base,
41.00	Cross South Fork of Lone Tree Creek, 20 lks. wide, course E.
80.00	Set Sandstone, 16 x 10 x 4 ins., 11 ins. in the ground, for Cor. to Secs. 21-22-27-28, marked with 2 notches on S. and 3 notches on E. edges, dug pits 18 x 18 x 12 ins. in each Sec., 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base,
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian.

Chains	East, on a random line between Sections 22 and 27. Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.08	Intersect N. & S. line, 18 lks. South of Cor. to Secs. 22-23-26-27 from which corner Impr. S. 89° 52' W., on a true line bet. Secs. 22-27. Va. 15° 45' E.
40.024	Set Sandstone, 12 x 10 x 4 ins., 8 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18 x 18 x 12 ins., N. & S. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base,
80.08	The Cor. to Secs. 21-22-27-28,
	Land level,
	Soil 2nd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 51 West 6th Principal Meridian.

Chains	North, between Sections 21 and 22. Variation 15° 45' East.
40.00	Set Sandstone 14 x 12 x 8 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18 x 18 x 12 ins. E. & W. of stone, 5 1/2 ft. dist., and raised a mound of earth 1 1/2 ft. high, 3 1/2 ft. base,
80.00	Set Sandstone 14 x 10 x 4 ins., 9 ins. in the ground, for Cor. to Secs. 15-16-21-22, marked with 3 notches on S. and E. edges, dug pits, 18 x 18 x 12 ins. in each Sec., 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base,
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West 6th Principal Meridian.

Chains	East, on a random line between Sections 15 and 22. Variation 15° 45' East.
	Descend gradually,
22.00	cross North Fork of Lone Tree Creek, 20 lks. wide, course S.E. and ascend gradually,
40.00	Set temporary 1/4 Sec. Cor.,
80.20	Intersect N. & S. line, 15 lks. South of Cor. to Secs. 14-15-22-23, from which corner, I run S. 89° 54' W., on a true line bet. Secs. 15-22. Va. 15° 45' E.
40.10	Set Sandstone 14 x 14 x 4 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18 x 18 x 12 ins. N. & S. of stone, 5 1/2 ft. dist., and raised a mound of earth 1 1/2 ft. high, 3 1/2 ft. base,
80.20	The Cor. to Secs. 15-16-21-22,
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 15 and 16.
	Variation 15° 45' East.
	Descend gradually;
25.00	cross N. Fork of Long Tree Creek 30 lks. wide, course S.E. ascend gradually.
40.00	Set Sandstone, 12 x 8 x 6 ins., 8 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits 18 x 18 x 12 ins., E. & W. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high 3 1/2 ft. base.
80.00	Set Sandstone, 20 x 12 x 4 ins., 15 ins. in the ground, for Cor. to Secs. 9-10-15-16, marked with 4 notches on S. and 3 notches on E. edges, dug pits 18 x 18 x 12 ins. in each Sec., 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base.
	Land rolling.
	Soil 2nd rate,
	Vegetation, Bunchgrass.
	Apr. 10, 1882.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 10 and 15.
	Variation 15° 45' East.
40.00	Set temporary 1/4 Sec. Cor.
54.00	cross Drain, course S.E. & ascend
80.43	Intersect N. & S. line, 13 lks. South of Cor. to Secs. 10-11-14-15, from which corner, Drum S. 89° 54' W., on a true line bet. Secs. 10-15. Va. 15° 45' E.
40.22	Set Sandstone, 12 x 8 x 4 ins., 8 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18 x 18 x 12 ins. N. & S. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
80.43	The Cor. to Secs. 9-10-15-16.
	Land rolling.
	Soil 2nd rate
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 9 and 10.
	Variation 15° 45' East.
	Descend gradually.
40.00	Set Sandstone, 12 x 8 x 6 ins, 8 ins. in the ground, for ¼ Sec. Cor., marked ¼ on W. face, dug pits, 18 x 18 x 12 ins. E. & W. of Stone 5½ ft. dist., and raised a mound of earth, 1½ ft. high, 3½ ft. base,
56.00	Cross Drain, course S.E.
80.00	Set Sandstone, 14 x 12 x 4 ins, 9 ins. in the ground, for Cor. to Secs. 3-4-9-10, marked with 5 notches on S. and 3 notches on E. edges, dug pits 18 x 18 x 12 ins. in each Sec. 5½ ft. dist., and raised a mound of earth, 2 ft. high, 4½ ft. base.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 3 and 10.
	Variation 15° 45' East.
	Descend gradually.
24.00	Cross Drain, course S.E.
40.00	Set temporary ¼ Sec. Cor.
60.00	Ascend West slope of Bluff, bears N. & S.
80.25	Intersect N. & S. line, 4 lks. South of Cor. to Secs. 2-3-10-11, from which corner, Sun S. 89° 58' W., on a true line bet. Secs. 3 & 10. Va. 15° 45' E.
40.13	Set Sandstone, 14 x 12 x 3 ins., 9 ins. in the ground, for ¼ Sec. Cor., marked ¼ on N. face, dug pits, 18 x 18 x 12 ins. N. & S. of Stone 5½ ft. dist., and raised a mound of earth, 1½ ft. high, 3½ ft. base,
80.25	The Cor. to Secs. 3-4-9-10.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, on a random line between Sections 3 and 4. Variation. 15°45' East.
	Descend gradually.
40.00	Set temporary 1/4 Sec. Cor.
71.00	Cross Drain course S.E.
80.47	Intersect North Boundary of Tp. 6 lks. West of Cor. to Secs. 3-4-33-34, from which corner, Jump S. 3 W., on a true line bet. Secs. 3-4.
	Va. 15°45' E.
40.47	Set Sandstone, 18 x 10 x 3 ins. 12 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits 18 x 18 x 12 ins., E. & W. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
80.47	The Cor. to Secs. 3-4-9-10.
	Land rolling.
	Soil 2nd rate
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 32 and 33. Variation 15°45' East.
	Descend gradually.
40.00	Set Sandstone, 14 x 8 x 4 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits, 18 x 18 x 12 ins., E. & W. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
59.00	Cross South Fork of Lone Tree Creek, 20 lks. wide, course East and ascend gradually.
80.00	Set Sandstone, 20 x 12 x 4 ins., 15 ins. in the ground, for Cor. to Secs. 28-29-32-33 marked with 1 notch on S. and 4 notches on E. edges, dug pits, 18 x 18 x 12 ins. in each Sec., 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base.
	Land rolling.
	Soil 2nd rate
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 28 and 33. Variation 15°45' East.
	Descend gradually.
2.00	Cross South Fork Lone Tree creek, 15lks. wide, runs North,
5.00	Cross same, course S.E.,
38.00	Cross same, course N.E.,
40.00	Set temporary ¼ Sec. Cor.
80.35	Intersect N. & S. line, 20lks. S. of Cor. to Secs. 27-28-33-34, from which corner Trees S. 89°54' W., on a true line bet. Secs. 28-33. Va. 15°45' E.,
40.18	Set Sandstone, 12x10x3ins. 8ins. in the ground, for ¼ Sec. Cor., marked ¼ on N. face, dug pits 18x18x12ins. N. & S. of stone, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base,
80.35	The Cor. to Secs. 28-29-32-33.
	Land rolling.
	Soil 2nd rate
	Vegetation, Bunchgrass.
	I carefully examined the adjustments of my Solar compass today, particularly the latitude & reversing apparatus & found them correct. Apr. 11, 1882.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 28 and 29. Variation 15°45' East.
40.00	Set Sandstone, 10x8x4ins., 7ins. in the ground, for ¼ Sec. Cor., marked ¼ on W. face, dug pits, 18x18x12ins. E. & W. of stone, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base,
80.00	Set Sandstone, 18x16x4ins. 12ins. in the ground, for Cor. to Secs. 20-21-28-29, marked with 2 notches on S. and 4 notches on E. edges, dug pits 18x18x12ins. in each Sec., 5½ft. dist., and raised a mound of earth 2ft. high, 4½ft. base,
	Land rolling.
	Soil 2nd rate
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 21 and 28. Variation. 15°45' East.
19.00	Cross Drain, course S.E.
40.00	Set temporary 1/4 sec. cor.
50.28	Intersect N. & S. line, 10 lks. South of cor. to secs. 21-22-27-28, from which corner, Drum, S 89°56' W, on a true line bet. secs. 21-28. Va. 15°45' E.
40.14	Set Sandstone, 14x12x4 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18x18x12 ins, N. & S. of Stone, 5 1/2 ft. dist, and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base,
80.28	The cor. to secs. 20-21-28-29.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 20 and 21. Variation 15°45' East.
40.00	Cross drain course S.E. and
	Set Sandstone, 10x8x6 ins., 7 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits, 18x18x12 ins. E. & W. of Stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base,
80.00	Set Sandstone, 20x10x3 ins., 15 ins. in the ground, for Cor. to Secs. 16-17-20-21, marked with 3 notches on S. and 4 notches on E. edges, dug pits, 18x18x12 ins. in each Sec. 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

East, on a random line between Sections 16 and 21.

Variation, 15° 45' East.

Chains	
1/0.00	Set temporary 1/4 Sec. Cor.
80.37	Intersect N. & S. line, 8 lks. South of Cor. to Secs. 15-16-21-22 from which corner, Sun S. 89° 57' W., on a true line bet. Secs. 16-21. Va. 15° 45' E.
40.19	Set Sandstone, 18 x 16 x 3 ins. 12 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N face, dug pits, 18 x 18 x 12 ins. N. & S. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
80.37	The Cor. to Secs. 16-17-20-21. Land rolling. Soil 2nd rate, Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

North, between Sections 16 and 17.

Variation 15° 45' E, East.

Chains	
	Descend gradually.
30.00	Cross North Fork of Lone Tree Creek, 20 lks. wide, runs S.E. and ascend gradually.
40.00	Set Sandstone, 10 x 8 x 5 ins., 7 ins. in the ground, for 1/4 Sec. Cor., marked from W. face, dug pits, 18 x 18 x 12 ins. E. & W. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
80.00	Set Sandstone, 15 x 12 x 6 ins., 10 ins. in the ground, for Cor. to Secs. 8-9-16-17, marked with 4 notches on S. and E. edges, dug pits, 18 x 18 x 12 ins. in each Sec., 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base. Land rolling. Soil 2nd rate Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 9 and 16. Variation 15°45' East.
	Descend gradually,
30.00	Cross Drain, course S.E.,
40.00	Set temporary 1/4 sec. cor.
80.23	Intersect N. & S. line 45 lks. South of cor. to secs. 9-10-15-16 from which corner, Trum S.89°41' W., on a true line bet. secs. 9-16, Va. 15°45' E.,
40.12	Set Sandstone, 14 x 8 x 4 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18 x 18 x 12 ins., N. & S. of stone 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high 3 1/2 ft. base,
80.23	The cor. to secs. 8-9-16-17,
	Land rolling,
	Soil 2nd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 8 and 9. Variation 15°45' East.
40.00	Set Sandstone, 12 x 12 x 3 ins., 8 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits, 18 x 18 x 12 ins. E. & W. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base,
80.00	Set Sandstone 16 x 12 x 4 ins., 11 ins. in the ground, for Cor. to Secs. 4-5-8-9, marked with 5 notches on S. and 4 notches on E. edges dug pits, 18 x 18 x 12 ins. in each sec., 5 1/2 ft. dist., and raised a mound of earth, 2 ft. high, 4 1/2 ft. base.
	Land rolling.
	Soil 2nd rate
	Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian.

Chains	East, on a random line between Sections 4 and 9
	Variation 15° 45' East.
	Descend gradually,
40.00	Set temporary ¼ Sec. cor.
71.00	Cross Drain, course S.E.,
80.12	Intersect N. & S. line, 30lks. South of cor. to Secs. 3-4-9-10, from which corner, Sun S. 89° 47' W., on a true line bet. Secs. 4-9.
	Va. 15° 45' E.
40.06	Set Sandstone, 12x10x4ins. 8ins. in the ground, for ¼ Sec. Cor., marked ¼ on N. face, dug pits, 18x18x12ins. N. & S. of stone, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base.
80.12	The corner to Secs. 4-5-8-9.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian.

Chains	North, on a random line between Sections 4 and 5.
	Variation 15° 45' East.
40.00	Set temporary ¼ Sec. cor.
80.70	Intersect N. B. of Sp., 20lks. West of cor. to Secs. 4-5-32-33, from which corner, Sun S. 9' W., on a true line bet. Secs. 4-5.
	Va. 15° 45' E.
40.70	Set Sandstone, 14x14x3ins., 9ins. in the ground, for ¼ Sec. Cor., marked ¼ on W. face, dug pits, 18x18x12ins. E. & W. of stone, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base.
80.70	The cor. to Secs. 4-5-8-9.
	Land rolling
	Soil 2nd rate
	Vegetation, Bunchgrass.
	Apl. 12, 1882.

Chains	North, between Sections 31 and 32. Variation. 15° 45' East.
40.00	Set Sandstone, 14x10x6ins, 9ins, in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits, 18x18x12ins, E. & W. of Stone, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base,
80.00	Set Sandstone, 20x14x4ins., 15ins. in the ground, for Cor. to Secs. 29-30-31-32, marked with 1 notch on S. and 5 notches on E. edges, dug pits, 18x18x12ins. in each Sec., 5½ft. dist., and raised a mound of earth, 2ft. high, 4½ft. base.
	Land rolling.
	Soil 2nd rate,
	Vegetation, Bunchgrass.

Chains	East, on a random line between Sections 29 and 32. Variation 15° 45' East.
4.00	Cross South Fork of Lone Tree Creek, 15lks. wide, Course S.E.,
40.00	Set temporary 1/4 Sec. Cor.
80.52	Intersect N. & S. line, 34lks. South of Cor. to Secs. 28-29-32-33, from which corner, Sun S. 89° 45' W., on a true line bet. Secs. 29-32, Va. 15° 45' E.,
40.26	Set Sandstone, 12x8x6ins, 8ins, in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18x18x12ins, N. & S. of Stone, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base,
80.52	The Cor. to Secs. 29-30-31-32.
	Land rolling,
	Soil 2nd rate,
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	West, on a random line between Sections 30 and 31 Variation 15°45' East.
40.00	Set temporary 1/4 sec. cor.
78.82	Intersect West Boundary of Tp, 41lks. South of cor. to secs. 25-30-31-36 from which corner, Trees S.89°58' E., on a true line bet. secs. 30-31 Va. 15°45' E.
38.82	Set Sandstone 18x12x4ins., 12ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18x18x12ins. N. & S. of stone, 5½ft. dist., and raised a mound of earth, 1½ft. high 3½ft. base,
78.82	The cor. to secs. 29-30-31-32.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 29 and 30. Variation 15°45' East.
2.00	Cross Drain course S.E.
40.00	Set Sandstone 12x10x4ins., 8ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits, 18x18x12ins. E. & W. of stone, 5½ft. dist., and raised a mound of earth, 1½ft. high 3½ft. base,
78.00	Cross Drain course S.E.
80.00	Set Sandstone 18x16x4ins., 12ins. in the ground, for Cor. to Secs. 19-20-29-30, marked with 2 notches on S. and 5 notches on E. edges dug pits, 18x18x12ins. in each Sec., 5½ft. dist., and raised a mound of earth, 2ft. high, 4½ft. base,
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	East, on a random line between Sections 20 and 29. Variation. 15°45' East.
40.00	Set temporary ¼ sec. cor.
76.00	Cross Drain, course S.E.
80.45	Intersect N. & S. line, 26lks. North of cor. to secs. 20-21-28-29, from which corner, Sun N.89°49' W., on a true line bet. secs. 20-29, Va. 15°45' E.
40.23	Set Sandstone 12x12x3 ins., 8 ins. in the ground, for ¼ Sec. Cor., marked ¼ on N. face, dug pits, 18x18x12 ins. N. & S. of stone, 5½ ft. dist. and raised a mound of earth, 1½ ft. high, 3½ ft. base.
80.45	The cor. to secs. 19-20-29-30.

Land rolling.
Soil 2nd rate.
Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	West, on a random line between Sections 19 and 30. Variation 15°45' East.
64.00	Cross Drain, course S.E.
40.00	Set temporary ¼ sec. cor.
78.42	Intersect West Boundary of Tp. 64lks. South of cor. to secs. 19-24-25-30, from which corner, Sun S.89°33' E., on a true line bet. secs. 19-30, Va. 15°45' E.
38.42	Set Sandstone 14x12x3½ ins., 9 ins. in the ground, for ¼ Sec. Cor., marked ¼ on N. face, dug pits, 18x18x12 ins. N. & S. of stone, 5½ ft. dist. and raised a mound of earth, 1½ ft. high, 3½ ft. base.
78.42	The cor. to secs. 19-20-29-30.

Land rolling.
Soil 2nd rate.
Vegetation, Bunchgrass.

Township 34 North Range 57 West
6th Principal Meridian.

Chains	North, between Sections 19 and 20. Variation. 15°45' East.
40.00	Set Sandstone, 14x17x4ins., 9ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits, 18x18x12ins. E. & W. of stone, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base,
80.00	Set Sandstone, 20x18x4ins., 15ins. in the ground, for Cor. to Secs. 17-18-19-20, marked with 3 notches on S. and 5 notches on E. edges, dug pits, 18x18x12ins. in each Sec., 5½ft. dist., and raised a mound of earth, 2ft. high, 4½ft. base,
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 57 West
6th Principal Meridian.

Chains	East, on a random line between Sections 17 and 20. Variation 15°45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.48	Intersect N. & S. line 14 lks. North of Cor. to Secs. 16-17-20-21, from which corner, Drum N. 89°54' W., on a true line bet. Secs. 17-20. Va. 15°45' E.
40.24	Set Sandstone, 12x10x3ins., 8ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits 18x18x12ins. N. & S. of stone, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base,
80.48	The Cor. to Secs. 17-18-19-20.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	West, on a random line between Sections 18 and 19. Variation 15°45' East
40.00	Set temporary ¼ Sec. Cor.
77.75	Intersect West Boundary of Tp. 48lks. South of Cor. to Secs. 13-18-19-24 from which Corner, Sun S.89°39' E., on a true line bet. Secs. 18-19. Va. 15°45' E.
37.75	Set Sandstone, 18x8x4ins. 12ins. in the ground, for ¼ Sec. Cor., marked ¼ on N. face, dug pits 18x18x12ins. S. & N. of stone, 5½ft. dist., and raised a mound of earth 1½ft. high, 3½ft. base.
77.75	The Cor. to Secs. 17-18-19-20. Land rolling. Soil 2nd rate. Vegetation, Bunchgrass. Apl. 13, 1882.

Township 34 North Range 51 West
6th Principal Meridian.

Chains	North, between Sections 17 and 18. Variation 15°45' East
20.00	Cross North Fork of Lone Tree Creek, 20lks. wide, Course East.
40.00	Set Sandstone, 12x10x4ins., 8ins. in the ground, for ¼ Sec. Cor., marked ¼ on W. face, dug pits, 18x18x12ins. E. & W. of stone, 5½ft. dist., and raised a mound of earth, 1½ft. high, 3½ft. base.
80.00	Set Sandstone 18x12x4ins., 12ins. in the ground, for Cor. to Secs. 7-8-17-18, marked with 7 notches on S. and 5 notches on E. edge, dug pits 18x18x12ins. in each Sec., 5½ft. dist., and raised a mound of earth, 2ft. high 4½ft. base. Land rolling. Soil 2nd rate. Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian

East, on a random line between Sections 8 and 17.

Variation 15° 45' East.

Chains	
40.00	Set temporary 1/4 sec. cor.
72.00	Cross Drain, course S.E.
80.54	Intersect N. & S. line, 23 lks. North of cor. to secs. 8-9-16-17 from which corner, Sun S.89° 50' W., on a true line bet. secs. 8-17. Va. 15° 45' E.
40.27	Set Sandstone 12 x 12 x 3 ins. 8 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits 18 x 18 x 12 ins. N. & S. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high 3 1/2 ft. base.
80.54	The cor. to secs. 7-8-17-18.

Land rolling.
Soil 2nd rate
Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian.

West, on a random line between Sections 7 and 18.

Variation 15° 45' East.

Chains	
40.00	Set temporary 1/4 sec. cor.
78.38	Intersect West Boundary of Tp., 75 lks. South of cor. to secs. 7-12-13-18 from which corner, Sun S.89° 28' E., on a true line bet. secs. 7-18. Va. 15° 45' E.
38.38	Set Sandstone 18 x 12 x 4 ins. 12 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits 18 x 18 x 12 ins. N. & S. of stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base.
78.38	The cor. to secs. 7-8-17-18.

Land rolling.
Soil 2nd rate
Vegetation, Bunchgrass.

Chains	North, between Sections 7 and 8.
	Variation. 15°45' East.
	Descend gradually.
40.00	Set Sandstone, 14 x 10 x 5 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits, 18 x 18 x 12 ins. E. & W. of Stone, 5 1/2 ft. dist., and raised a mound of earth 1 1/2 ft. high, 3 1/2 ft. base,
52.00	Cross Drain, course S.E.,
70.00	Cross Drain, course S.E. & ascend gradually.
80.00	Set Sandstone, 20 x 14 x 4 ins., 15 ins. in the ground, for Cor. to Secs. 5-6-7-8, marked with 5 notches on S. & E. edges, dug pits, 18 x 18 x 12 ins. in each Sec., 5 1/2 ft. dist., and raised a mound of Earth, 2 ft. high, 4 1/2 ft. base,
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Chains	East, on a random line between Sections 5 and 8.
	Variation 15°45' East.
40.00	Set temporary 1/4 Sec. Cor.
80.20	Intersect N. & S. line, 22 lks. North of Cor. to Secs. 4-5-8-9 from which Corner, Surv. N.89°51' W., on a true line bet. Secs. 5-8,
	Va. 15°45' E.
40.10	Set Sandstone, 14 x 10 x 4 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18 x 18 x 12 ins. N. & S. of Stone, 5 1/2 ft. dist., and raised a mound of earth, 1 1/2 ft. high, 3 1/2 ft. base,
80.20	The Cor. to Secs. 5-6-7-8.
	Land rolling.
	Soil 2nd rate.
	Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian.

Chains	West, on a random line between Sections 6 and 7. Variation 15°45' East.
15.00	Cross Drain, course S.E.
40.00	Set temporary 1/4 Sec. Cor.
77.80	Intersect West Boundary of Tp., 5 lks. South of Cor. to Secs. 1-6-7-12 from which corner, Run S.89°38' E., on a true line bet. Secs. 6-7. Va. 15°45' E.
37.80	Set Sandstone, 18x12x3 ins., 12 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on N. face, dug pits, 18x18x12 ins. N. & S. of stone, 5½ ft. dist., and raised a mound of earth, 1½ ft. high, 3½ ft. base.
77.80	The Cor. to Secs. 5-6-7-8. Land rolling. Soil 2nd rate. Vegetation, Bunchgrass.

Township 34 North Range 51 West

6th Principal Meridian.

Chains	North, on a random line between Sections 5 and 6. Variation 15°45' East.
	Ascend.
40.00	Set temporary 1/4 Sec. Cor.
51.00	Top of Divide, brs. N.70° E. & S.70° W. and descend.
80.40	Intersect N.B. of Tp., 7 lks. West of Cor. to Secs. 5-6-31-32 from which corner, Run S.30' W., on a true line bet. Secs. 5-6. Va. 15°45' E.
40.40	Set Sandstone, 14x9x4 ins., 9 ins. in the ground, for 1/4 Sec. Cor., marked 1/4 on W. face, dug pits, 18x18x12 ins. E. & W. of stone, 5½ ft. dist., and raised a mound of earth, 1½ ft. high, 3½ ft. base.
80.40	The Cor. to Secs. 5-6-7-8. Land mountainous. Soil 3rd rate. Vegetation, Bunchgrass.

I carefully examined the adjustments of my Gurley compass today, particularly the latitude and reversing apparatus and found them correct.

Apr. 14, 1882.

GENERAL DESCRIPTION.

The general character of the land in this Township is rolling with soil 2nd rate.
It is well watered by Lone Tree Creek and its tributaries.
The fine growth of Bunchgrass throughout the Tp. furnishes good grazing land, and a considerable portion is valuable for agricultural purposes.
Stock raising is at present the principle industry.

U. S. Surveyor-General's Office.

Plattsmouth Neb.

November 6th 1882

The foregoing Field Notes of the surveys of

Subdivision lines of Tp. 34 N. Range 51 W. of the Princial Base and [illegible]

Meridian

in the State of Neb. executed by

Frank S. Wood

in the month of Apr. U. S. Deputy Surveyor, under his contract no. 5 dated

Nov. 14th 1881

having been critically examined, the necessary corrections and explanations made, the said Field Notes and the surveys they describe are hereby approved.

Geo. S. Smith

U. S. Surveyor-General for Neb. & Ia.

Field Notes.
of the Subdivision lines of
Fractional
Township 33 S. Range 51 West.
of the 6th Principal Meridian.
By
Frank S. Wood.
Deputy Surveyor.
Under his Contract of November
14th 1881.

Survey Commenced June 16, 1882.
Survey Completed June 20, 1882.

Township 35 N. R. 51 W. of the 6th P.M.

INDEX.

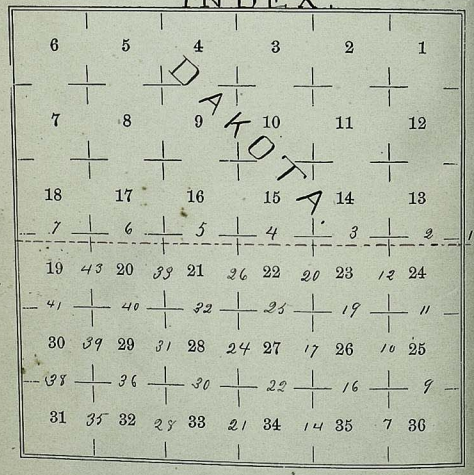

Retracings of the North boundary of Tps. 35 N. R. 51 W. of the 6th P.M.

Chains

Before proceeding to subdivide this Township, I set my compass at the Closing cor. to fractional Tps. 35 N. Ranges 50 & 51 W. on the N. boundary of Nebraska and carefully tested it, particularly the latitude and reversing apparatus and found it to be in perfect adjustment.

I also observed for latitude and obtained 43° North.

Thence I run West on a blank line on the 184th mile.

Variation 15° 20' East.

1.50 To the 184th Mile post. I found the mound nearly obliterated, the pits filled and the post broken off. I set a cottonwood post 4 ft. long, 4 ins. square, charred stake 24 ins. in the grou

Chains. for mile post No 184 marked "N E B." on S. "D A K." on N. and "184 M." on E. sides, dug pits 30 x 30 x 24 ins. E. & W. of post 6 ft. dist. and raised a mound of earth around post.

West on a blank line on the 185th Mile.

Variation 15° 20' E.

79.76 To the 185th Mile post. I found the mound nearly obliterated, the pits partly filled and the post gone. I dug in the mound and found the "marked stone" and set a cottonwood post 5 ft. long. 4 ins. square charred stake, 18 ins. in the ground, for 185th Mile post, marked "N. E. B." on

Chains. S. "D A K." on N. and 185 M. on E. sides, dug pits 30 x 30 x 24 ins. E. & W. of post 6 ft. dist. and raised a mound of earth around post.

West on a blank line on the 186th Mile.

Variation 15° 20' E.

79.03 To a point 24 lks. N. of the 186th Mile post. I found the mound wholly obliterated, the pits nearly filled and the post gone. I dug in the mound and found a portion of the post and the "marked stone", and set an ash post. 4 ft. long. 4 ins. square, charred stake, 18 ins. in the ground, for Mile post No 186, marked

Chains. S.E Bow S. D.A.K.. on N. and 186 M.. on E. sides. dug pits 30 x 30 x 24 ins. E. & W. of post. 6 ft. dist. and raised a mound of earth around post.

West on a blank line on the 187th mile

Variation 15° 20' E.

79.85 To a point 20 lks. N. of Mile post No 187 I found the mound nearly obliterated, the post gone and the pits filled. I dug in the mound and found the "marked stone" and set a pine post 4 ft. long, 4 ins. square, charred stake 18 ins. in the ground for the 187th Mile post marked N.E.B. on

Chains S. D.A.K. on N. and 187 M. on E. sides. dug pits 30 x 30 x 24 ins. E. & W. of post. 6 ft. dist. and raised a mound of earth around post.

West on a blank line on the 188th mile.

Variation 15° 20' E.

79.50 To a point 5 lks. N. of the 188th Mile post. I found the mound nearly obliterated, the post broken off and the pits partly filled. I set a cottonwood post 5 ft. long, 4 ins. square, charred stake 18 ins. in the ground for the 188th Mile post, marked N.E.B. on S. D.A.K. on N. and 188 M. on E. sides dug pits 30 x 30 x 24

Chains. ins. E. & W. of post. 6 ft. dist. and raised a mound of earth around post.

West on a blank line on the 189th Mile

Variation 15° 20' E.

79.90 To the 189th Mile post. I found the mound nearly obliterated, the post gone, and the pits partly filled. I dug in the mound and found a piece of the old post, and set a cottonwood post 4 ft. long, 4 ins. square, charred stake 18 ins. in the ground, for the 189th Mile post, marked N.E.B. on S. D.A.K. on N. 189 M. on E. sides, dug pits 30 x 30 x 24

Chains ins E. & W. of post. 6 ft. dist. and raised a mound of earth around post.

West on a blank line on the 190th Mile.

Variation 15° 20' E.

78.56 To a point 5 lks. S. of the Closing cor. to fractional Tps. 35 N. Ranges 51 & 52 W. recently built and in good condition.

June 16, 1882.

From the corner to sections 12, 35 & 36, on the S. boundary, I run N. between secs. 35 & 36

Variation 15° 30' E.

40.00 Set a pine post 3 ft. long, 3 ins. square, charred stake 12 ins. in

Tp. 35 N. R. 51 W of the 6th P.M.

Chains in the ground for 1/4 sec. cor. marked 1/4 S. on W. face. dug pits 18 x 18 x 12 ins. N. & S. of post. 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high. 3 1/2 ft. base around post.

80.00 Set a pine post 4 ft. long. 4 ins. square. charred stake. 18 ins. in the ground for cor. to secs. 25. 26. 35 & 36. marked.
T. 35. S. 25 on N.E.
R. 51. S. 36 on S.E.
S. 35 on S.W. and
S. 26 on N.W. faces. with 1 notch on S. & E. edges. dug pits 18 x 18 x 12 ins. in each sec. 5 1/2 ft. dist. and raised a mound of earth 2 ft. high. 4 1/2 ft. base. around post.
Sand. rolling.
Soil. 3rd rate. Vegetation. grass.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. East on a random line between sections 25 & 36.
Variation 15° 30' East.

4.00 Dry creek bed. 20 lks. wide. descends S.E. (water in pools.)

12.00 Drain. 25 lks. wide descends S.W.

40.00 Set post for temporary 1/4 sec. cor.

51.00 Dry creek bed. 12 lks. wide. descends S.E. (Water in pools)

79.20 Intersect E. boundary of Tp. 70 lks. N. of cor. to secs. 25. 30. 31 & 36. Thence run N. 89° 30' W. on a true line between secs. 25 & 36 with same variation.

39.60 Set a post 3 ft. long. 3 ins. square. charred stake. 12 ins. in the ground for 1/4 sec. cor. marked 1/4 S. on N. face. dug pits 18 x 18 x 12 ins. E. & W. of post. 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high. 3 1/2 ft. base. around post.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains	
79.20	The cor to secs. 25 26 35 & 36.
	Land, rolling.
	Soil, 3d rate.
	Vegetation, grass.

North between sections 25 & 26.
Variation 15° 30' E.

2.00	Dry creek bed, descends S.E. (Water in pools)
40.00	Set a pine post 3 ft. long, 3 ins. square, charred stake, 12 ins. in the ground for 1/4 sec. cor. marked 1/4 S. on W. face, dug pits 18 x 18 x 12 ins. N. & S. of post 5 1/2 ft. diet. and raised a mound of earth 1 1/2 ft. high, 3 1/2 ft. base around post.
80.00	Set a pine post 4 ft. long, 4 ins. square, charred stake 18 ins. in the ground, for cor. to secs. 23, 24,

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.	
	25 & 26 marked T. 35. S. 24 on N.E. R. 51 S. 25 on S.E. S. 26 on S.W. and S. 23 on N.W. faces, with 2 notches on S. and 1 notch on E. edges, dug pits 18 x 18 x 12 ins. in each sec. 5 1/2 ft. diet. and raised a mound of earth 2 ft. high, 4 1/2 ft. base, around post.
	Land, rolling.
	Soil, 3d rate.
	Vegetation, grass.

East on a random line between sections 24 & 25
Variation 15° 30' East.

40.00	Set post for temporary 1/4 sec. cor.
54.00	Drain, 20 lks. wide, descends S.E.
79.24	Intersect E. boundary of Tp.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.	
	73 lks. N. of cor. to secs. 19, 24, 25 and 30. Thence I run N. 89° 29' W. on a true line between secs. ~~23~~ 25 & 24 with same variation.
39.62	Set a pine post 3 ft. long, 3 ins. square, charred stake, 12 ins. in the ground for 1/4 sec. cor. marked 1/4 S. on N. face, dug pits 18 x 18 x 12 ins. E. & W. of post 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high, 3 1/2 ft. base, around post.
79.24	The cor. to secs. 23, 24, 25 & 26.
	Land, rolling.
	Soil, 3rd rate.
	Vegetation, grass.
	North between sections 23 & 24.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.	
	Variation 15° 30' East.
40.00	Set a pine post 4 ft. long, 3 ins. square, charred stake, 12 ins. in the ground, for 1/4 sec. cor. marked 1/4 S. on W. face, dug pits 18 x 18 x 12 ins. E. & W. of post 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high, 3 1/2 ft. base, around post.
68.97	Intersect North boundary of Neb. 89 lks. E. of the 185th Mile post, and at point of intersection set a pine post, 4 ft. long 4 ins. square, charred stake 18 ins. in the ground for closing cor. to fractional secs. 23 & 24 marked T. 35. R. 51 C.C. on S. S. 24 on E. & S. 23 on W. sides, with 5 notches on W. & 1 notch on E. sides, dug pits 18 x 18 x 12 ins.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.	
	S.E. & W. of post 5½ ft. dist. and raised a mound of earth around post.
	Land, rolling.
	Soil, 3rd rate.
	Vegetation, grass.

Note. I carefully tested my Solar compass to-day, particularly the latitude and reversing apparatus and found it to be in perfect adjustment. I also observed for latitude and obtained 43° N.

From the corner to sections 2, 3, 34 & 35, on the S. boundary, I run North between Secs. 34 & 35

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains	
	Variation 15° 30' E.
23.00	Drain 20 lks. wide, descends S.E.
40.00	Set a pine post 3 ft. long, 3 ins. square, charred stake 12 ins. in the ground, for ¼ sec. cor. marked ¼ S. on W. face, dug pits 18 x 18 x 12 ins. N. & S. of of post, 5½ ft. dist. and raised a mound of earth 1½ ft. high 3½ ft. base, around post.
68.00	Drain, 45 lks. wide, descends S.E.
80.00	Set a pine post, 4 ft. long 4 ins. square, charred stake 18 ins. in the ground, for cor. to secs. 26, 27, 34 & 35 marked T. 35 N. S. 26 on N.E. R. 51 S. 35 on S.E. S. 34 on S.W. and S. 27 on N.W. faces, with 1 notch on S.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. and 2 notches on E. edges. dug pits 18×18×12 ins. in each sec. 5½ ft. dist. and raised a mound of earth 2 ft. high. 4½ ft. base. around post.

Land. rolling.

Soil. 3d rate.

Vegetation. grass.

East on a random line between secs. 26 & 35.

Variation 15° 30' E.

40.00 Set post for temporary ¼ sec. cor.

47.50 Dry creek bed. 10 lks. wide, descends N.E. (Water in pools.)

79.90 Intersect N. & S. line 46 lks. N. of cor. to secs. 25-26 35 & 36. Thence Drum N. 89° 40' W. on a true line between secs. 26 & 35 with same va.

39.95 Set a pine post. 3 ft. long. 3 ins.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. square. charred stake 12 ins. in the ground for ¼ sec. cor. marked ¼ S. on N. face. dug pits 18×18×12 ins. E. & W. of post. 5½ ft. dist. and raised a mound of earth 1½ ft. high. 3½ ft. base. around post.

79.90 The cor. to secs. 26 27 34 & 35.

Land, rolling.

Soil, 3d rate.

Vegetation. grass.

North between secs. 26 & 27.

Variation 15° 30' E.

40.00 Set a pine post. 3 ft. long. 3 ins. square. charred stake. 12 ins. in the ground. for ¼ sec. cor. marked ¼ S. on W. face. dug pits 18×18×12 ins. N. & S. of post. 5½ ft. dist. and raised a mound

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.	
	of earth 1½ ft. high 3½ ft. base. around post.
80.00	Set a pine post 4 ft. long. 4 ins. square. charred stake. 18 ins. in the ground. for. cor. to secs. 22, 23, 26 & 27, marked T. 35 S. 23 on N.E. R. 51 S. 26 on S.E. S. 27 on S.W. and S. 22 on N.W. faces with 2 notches on S. & E. edges. dug pits 18 x 18 x 12 ins in each sec. 5½ ft. dist. and raised a mound of earth 2 ft. high. 4½ ft. base. around post. Land. rolling. Soil. 3rd rate. Vegetation. grass.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.	
	East on a random line between sections 23 & 26. Variation 15° 30' E.
40.00	Set post for temporary 1/4 secs. cor.
79.96	Intersect N. & S. line 40 lks. N. of cor. to secs. 23 24 25 & 26
	Thence I run N. 89° 43' W. on a true line betw. secs. 23 & 26 with same variation.
39.98	Set a pine post. 3 ft. long. 3 ins. square. charred stake 12 ins. in the ground. for 1/4 sec. cor. marked 1/4 S. on N. face. dug pits 18 x 18 x 12 ins. E. & W. of post. 5½ ft. dist. and raised a mound of earth 1½ ft. high. 3½ ft. base. around post.
79.96	The cor. to secs. 22 23 26 & 27 Land. rolling. Soil. 2nd rate Vegetation. grass.

Tp. 35 N. R 51 W. of the 6th P.M.

Chains	
	North between Sections 22 & 23
	Variation 15° 30' E.
140.00	Set a Pine post 3 ft. long, 3 ins. square, charred stake 12 ins. in the ground, for 1/4 sec. cor. marked 1/4 S. on W. face, dug pits 18 x 18 x 12 ins. N. & S. of post, 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base, around post.
41.00	Dry creek bed, 15 lks. wide, descends N.W. Water in pools.
68.21	Intersect North boundary of Nebraska 60 lks. W. of the 186th mile post and at point of intersection set a pine post 5 ft. long, 4 ins. square, charred stake 18 ins. in the ground, for closing corner to fractional sections 22 & 23, marked

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains	
	C.C. T. 35 R. 51 on S. S 23 on E. S. 22 on W. sides, with 4 notches on W. & 2 on E. edges, dug pits 18 x 18 x 12 ins. S. E. & W. of post 5 1/2 ft. dist. and raised a mound of earth around post.
	Land: rolling. Soil: 2nd rate. Veg. grass.
	June 17, 1882.
	From the corner to sections 3, 4, 33 & 34 on the South boundary, I run North between sections 33 & 34.
	Variation 15° 30' E.
40.00	Set a limestone 14 x 8 x 8 ins. 10 ins. in the ground for 1/4 sec. cor. marked 1/4 on W. face, dug pits 18 x 18 x 12 ins. N. & S. of stone, 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high,

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.	
	3½ ft. base alongside.
80.00	Set a pine post 4 ft. long, 4 ins. square, charred stake, 18 ins. in the ground, for cor. to secs. 27, 28, 33 & 34 marked. T. 35. S. 27 on N.E. R. 51 S. 34 on S.E. S. 33 on S.W. and. S. 28 on N.W. faces, with 1 notch on S. & 3 notches on E. edges: dug pits 18x18x12 ins. in each sec. 5½ ft. dist. and raised a mound of earth 2 ft. high, 4½ ft. base, around post. Land, rolling. Soil, 2d rate. Vegetation, grass.
	East on a random line between Sections 27 & 34.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.	
	Variation 15° 30' East.
26.00	Drain 35 lks. wide, descends S.E.
40.00	Set post for temporary ¼ sec. cor.
70.00	Drain, 15 lks. wide, descends S.E.
79.96	Intersect N. & S. line 30 lks. N. of cor. to secs. 26, 27, 34 & 35. Thence I run N. 89° 47' W. on a true line between secs. 27 & 34 with same variation.
37.98	Set a pine post, 3 ft. long, 4 ins. square charred stake 12 ins. in the ground, for ¼ sec. cor. marked ¼ S. on N. face, dug pits 18x18x12 ins. E. & W. of post, 5½ ft. dist. and raised a mound of earth 1½ ft. high, 3½ ft. base, around post.
79.96	The cor. to secs. 27, 28, 33 & 34. Land rolling.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains	
	Soil. 3rd rate.
	Vegetation. grass.
	North between sections 27 & 28. Variation 15° 30' E.
40.00	Set a limestone 13 x 8 x 7 ins. 10 ins. in the ground, for 1/4 sec. cor. marked 1/4 on W. face. dug pits 18 x 18 x 12 ins. N. & S. of stone 5 1/2 ft dist. and raised a mound of earth 1 1/2 ft. high. 3 1/2 ft. base. alongside.
80.00	Set a pine post. 4 ft. long. 4 ins. square. charred stake. 18 ins. in the ground. for cor. to secs. 21. 22 27 & 28. marked. T. 35 S. 22. on N.E. R. 51. S. 27 on S.E. S. 28 on S.W. and S. 21 on N.W. faces. with 2 notches

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains	
	on S. and 3 notches on E. edges. dug pits 18 x 18 x 12 ins. in each sec. 5 1/2 ft. dist. and raised a mound of earth 2 ft. high, 4 1/2 ft. base. around post.
	Land. rolling.
	Soil. 2nd rate.
	Vegetation. grass.
	East on a random line between Sections 22 & 27. Variation 15° 30' E.
17.00	Drain. 35 lks. wide descends N.W.
40.00	Set post for temporary 1/4 sec. cor.
41.00	Drain. 25 lks. wide descends N.W.
79.98	Intersect N. & S. line 8 lks. N. of cor. to secs. 22. 23. 26 & 27.
	Thence Lrun
	N. 89° 57' W. on a true line between secs. 22 & 27 with same variation.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.	
39.99	Set a pine post 3 ft. long 3 ins. square charred stake 12 ins. in the ground for 1/4 sec. cor. marked 1/4 S. on N. face. dug pits 18 x 18 x 12 ins. E. & W. of post. 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high. 3 1/2 ft. base. around post.
79.98	The cor. to secs. 21, 22, 27 & 28.
	Land. rolling.
	Soil. 3d rate.
	Vegetation. grass.
	North between secs. 21 & 22
	Variation 15° 30' E.
40.00	Set a pine post. 3 ft. long. 3 ins. square charred stake 12 ins in the ground for 1/4 sec. cor. marked 1/4 S. on W. face. dug pits 18 x 18 x 12 ins. N. & S. of post. 5 1/2 ft. dist.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.	
	and raised a mound of earth 1 1/2 ft. high. 3 1/2 ft. base. around post.
68.00	Intersect N. boundary of Nebraska. 130 lks. W. of the 187th Mile post. and at point of intersection set a pine post 3 ft. long. 4 ins. square charred stake 12 ins. in the ground. for closing cor. to fractional secs. 21 & 22. marked C.C. T. 35 R. 51 on S. S. 22 on E. and S. 21 on W. sides. with 8 notches on E. & W. sides. dug pits 18 x 18 x 12 ins. S., E. & W. of post 5 1/2 ft. dist. and raised a mound of earth around post.
	Land. rolling.
	Soil. 2d rate.
	Vegetation. grass.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.

Note.- I carefully tested my Solar Compass to-day, particularly the latitude and reversing apparatus, and found it to be in perfect adjustment.
I also observed for latitude and obtained 43° N.

From the corner to sections 4, 5, 32 & 33, on the S. boundary I run N. orth between secs. 32 & 33.
Variation 15° 30' East.

40.00 Set a pine post 3 ft. long, 6 ins. square, charred stake 12 ins. in the ground, for 1/4 sec. cor. marked 1/4 S. on W. face, dug pits 18 x 18 x 12 ins. N. & S. of post, 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.

high, 3 1/2 ft. base, around post.

80.00 Set a pine post 4 ft. long 4 ins. square, charred stake 18 ins. in the ground, for cor. to secs. 28, 29, 32 & 33, marked
T. 35. S. 28. on N.E.
R. 51. S. 33 on S.E.
S. 32 on S.W. and
S. 29 on N.W. faces, with 1 notch on S. and 4 notches on E. edges.
dug pits 18 x 18 x 12 ins. in each sec. 5 1/2 ft. dist. and raised a mound of earth 2 ft. high, 4 1/2 ft. base, around post.
Land, rolling
Soil, 2nd rate.
Vegitation, grass.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. East on a random line between sections 28 & 33.

Variation. 15° 80' E.

40.00 Set a pitch pine post for temp. 1/4 sec. cor.

80.30 Intersect N. & S. line. 40 lks. N. of cor. to secs. 27 28 33 & 34.

Thence I run N. 89° 43' W. on a true line between secs. 28 & 33. with same variation

40.15 Set a pitch pine post 3 ft. long, 3 ins square. charred stake. 18 ins. in the ground for 1/4 sec. cor. marked 1/4 S. on N. face. dug pits 18 x 18 x 12 ins. E. & W. of post 5 1/2 ft. dist. and raised a mound of earth. 1 1/2 ft. high. 3 1/2 ft. base, around post.

80.30 The cor. to secs. 28 29 32 & 33.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. Land. gently rolling.

Soil. 2d rate.

Vegetation. grass.

North between Sections 28 & 29

Variation 15° 30' E.

40.00 Set a pine post. 3 ft. long. 3 ins square. charred stake. 12 ins. in the ground, for 1/4 sec. cor. marked 1/4 S. on W. face. dug pits 18 x 18 x 12 ins. N. & S. of post 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base. around post.

80.00 Set. pine post. 4 ft. long. 4 ins. square. charred stake. 18 ins in the ground for cor. to secs. 20. 21. 28 & 29. marked T. 35. S. 21 on N.E. R. 51. S. 28 on S.E.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. S. 29 on S.W. and S. 26 on N.W. sides with 2 notches on S. and 4 notches on E. sides. dug pits 18×18×12 ins. in each sec. 5½ ft. dist. and raised a mound of earth 2 ft. high. 4½ ft. base. around post.
Land, rolling.
Soil, 2d rate.
Vegetation, grass.

East on a random line between secs. 21 & 28.
Variation 15° 30' E.

40.00 Set post for temporary ¼ sec. cor.
42.00 Ravine, 60 lks. wide descends N.W.
79.75 Intersect N. & S. line 40 lks. N. of cor. to secs. 21, 22, 27 & 28.
Thence I run.
N. 89° 43' W. on a true line between

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. secs. 21 & 28 with same va.
39.87 Set a pine post, 3 ft. long, 3 ins. square charred stake, 12 ins. in the ground; for ¼ sec. cor. marked ¼ S. on N. face. dug pits 18×18×12 ins. E. & W. of post. 5½ ft. dist. and raised a mound of earth 1½ ft. high. 3½ ft. base, around post.
79.75 The cor. to secs. 20, 21, 28 & 29.
Land, rolling.
Soil, 2d rate.
Vegetation, grass.

North between sections 20 & 21.
Variation 15° 30' E.

39.75 Dry creek bed, 18 lks. wide descends N.W. (water in pools)
40.00 Set a pine post 3 ft. long, 3 ins. square, charred stake 12 ins. in

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. the ground for 1/4 sec. cor. marked 1/4 S. on W. face, dug pits 18 x 18 x 12 ins. N. & S. of post. 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high, 3 1/2 ft. base, around post.

68.26 Intersect N. boundary of Nebraska, 152 lks. W. of the 188th Mile post. and at point of intersection set a pitch pine post. 4 ft. long 4 ins. square, charred stake, 18 ins. in the ground, for closing cor. to fractional secs. 20 & 21 marked T. 35 R. 51 & C.C. on S. S. 21 on E. & S. 20 on W. sides, with 4 notches on E & 2 on W. sides, dug pits 18 x 18 x 12 ins. S. E. & W. of post. 5 1/2 ft. dist. & raised a mound of earth around post.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. Land, level.
Soil, 2d rate.
Vegetation, grass.
June 19. 1882.

From the corner to sections 5, 6, 31 & 32 on the S. boundary Run. North between secs. 31 & 32.
Variation 15° 30' E.

20.00 Creek, 20 lks. wide, runs N.E.

40.00 Set a pitch pine post. 3 ft. long, 3 ins. square, charred stake, 12 ins. in the ground for 1/4 sec. cor. marked 1/4 S. on W. face, dug pits 18 x 18 x 12 ins. N. & S. of post 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high, 3 1/2 ft. base, around post.

76.00 Ravine, 50 lks. wide descends N.E.

80.00 Set a pine post 4 ft. long 4 ins. square, charred stake 12 ins. in the

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. ground for cor. to secs. 29, 30, 31 and 32 marked
T. 35. S. 29 on N.E.
R. 51. S. 32 on S.E.
S. 31 on S.W. and
S. 30 on N.W. faces, with 1 notch on S. & 5 notches on E. edges. dug pits 18×18×12 ins. in each sec. 5½ ft. dist. and raised a mound of earth 2 ft. high, 4½ ft. base around post.
Land, gently rolling.
Soil, 2d rate.
Vegetation, grass.

East on a random line between sections 29 & 32.
Variation 15° 30' E.

12,00 Creek, 18 lks. wide, runs N.W.
40,00 Set post for temporary ¼ sec. cor.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains.
79,60 Intersect N. & S. line 50 lks. S. of cor. to secs. 28, 29, 32 & 33. Thence Run S. 89° 39' W. on a true line between secs. 29 & 32 with same variation.
39,80 Set a pine post 3 ft. long, 3 ins. square, charred state, 12 ins. in the ground for ¼ sec. cor. marked ¼ S. on N. face. dug pits 18×18×12 ins. E. & W. of post. 5½ ft. dist., and raised a mound of earth 1½ ft. high. 3½ ft. base around post.
79,60 The cor. to secs. 29, 30, 31 & 32.
Land, rolling.
Soil, 2d rate.
Vegetation, grass.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains	
	West on a random line between Sections 30 & 31.
	Variation 15° 30' E.
37.00	Dry creek bed. 20 lks. wide. descends S.E. (water in pools.)
40.00	Set a post for temporary 1/4 sec. cor.
77.90	Intersect W. boundary of Tp. 84 lks. S. of cor. to secs. 25, 30. 31 & 36. Thence I run S. 89° 23' E. on a true line between secs. 30 & 31 with same variation.
37.90	Set a pine post 8 ft. long, 3 ins. square, charred stake 12 ins. in the ground, for 1/4 sec. cor. marked 1/4 S. on N. face. dug pits 18 x 18 x 12 ins. E. & W. of post. 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high. 3 1/2 ft. base. around post.
77.90	The cor. to secs. 29 30 31 & 32.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains	
	Land. gently rolling.
	Soil. 2d rate
	Vegetation. grass.
	North between sections 29 & 30.
	Variation 15° 30' E.
13.00	Creek. 15 lks. wide runs N.W.
27.00	Same creek 2 chs. wide, runs N.E.
40.00	Set a pitch pine post. 3 ft. long. 3 ins. square charred stake. 12 ins. in the ground. for 1/4 sec. cor. marked 1/4 S. on W. face. dug pits 18 x 18 x 12 ins. W. & S. of post. 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high. 3 1/2 ft. base. around post.
80.00	Set a pine post. 4 ft. long. 4 ins. square. charred stake 12 ins. in the ground. for cor. to secs. 19 20 29 & 30 marked.

Tp. 35 N. R. 51 W. of the 6th P.M.

Chains. T. 35 S. 20 on N.E.
R. 51. S. 29 on S.E.
S. 30 on S.W. and
S. 19 on N.W. faces. with 2
notches on S. & 5 notches on
E. edges. dug pits 18 x 18 x 12 ins.
in each sec. 5½ ft. dist. and
raised a mound of earth
2 ft. high. 4½ ft. base,
around post.
Land. level.
Soil. 2d rate.
Vegetation. grass.

East on a random line between
Sections 20 & 29.
Variation 15° 30' E.

25.00 Creek, 25 lks. wide runs N.
40.00 Set post for temporary ¼ sec. cor.
79.86 Intersect N. & S. line. at cor.

Tp. 35 N. R. 51 W. of the 6th P.M.

to secs. 20, 21, 28 & 29.
Thence I run West on a true
line between sections 20 & 29
with same variation.

39.93 Set a pine post. 3 ft. long. 3 ins.
square. charred stake 12 ins. in the
ground for ¼ sec. cor. marked
¼ S. on N. face. dug pits 18 x 18
x 12 ins. E. & W. of post. 5½ ft.
dist. and raised a mound of
earth. 1½ ft. high. 3½ ft. base.
around post.

79.86 The cor. to secs. 19, 20, 29 & 30.
Land. gently rolling.
Soil. 2d rate.
Vegetation. grass.

West on a random line between
Sections 19 & 30.
Variation 15° 30' East.

Tp. 35 N. R 51 W. of the 6th P.M.

Chains	
40.00	Set post for temporary 1/4 sec. cor.
77.55	Intersect W. boundary of Tp. 40 lks. S. of cor. to secs. 19, 24, 25 & 30. Thence I run S. 89° 42' E. on a true line between secs. 19 & 30 with same variation.
37.55	Set a pine post 3 ft. long 3 ins. square, charred stake 12 ins. in the ground for 1/4 sec. cor. marked 1/4 S. on N. face. dug pits 18 x 18 x 12 ins. E. & W. of post. 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high. 3 1/2 ft. base. around post.
71.55	The cor. to secs. 19, 20, 29 & 30.
	Land. level.
	Soil. 2d rate.
	Vegetation. grass.

Tp. 35 N. R. 5 W. of the 6th P.M.

Chains	
	North between sections 19 & 20. Variation. 15° 30' E.
40.00	Set a pitch pine post 3 ft. long. 3 ins. square. charred stake 12 ins. in the ground. for 1/4 sec. cor. marked 1/4 S. on W. face. dug pits 18 x 18 x 12 ins. N. & S. of post. 5 1/2 ft. dist. and raised a mound of earth 1 1/2 ft. high 3 1/2 ft. base. around post.
68.20	Intersect North boundary of Nebraska. 187 lks. W. of the 189th Mile post. and at point of intersection set a pine post. 4 ft. long. 3 ins. square charred stake 12 ins. in the ground for closing corner to fractional secs. 19 & 20 marked C.C. T. 35 R. 51 on S. S. 20 on E & S. 19 on W. sides with 1 notch on W. &

Tp. 35 N. R. 51 W. of the 6th P.M.

5 notches on E. edges; dug pits 18 x 18 x 12 ins. S., E. and W. of post 5½-ft. dist. and raised a mound of earth 2 ft. high. 4½ ft. base. around post.

Land, level.

Soil. 2d rate.

Vegetation. grass.

June 20. 1882.

General Description.

The land in this Township is gently rolling. the soil is 2d and 3d rate. and there is a good growth of grass.

There is a small stream flowing through the western part. and nearly all the ravines contain pools of good water.

The land in the valleys will produce good crops without irrigation. and the whole township is an excellent stock range.

U. S. Surveyor Gen'l's Office
Plattsmouth Neb.

The foregoing Field Notes of the Resurvey of the N. boundary and Survey of the subdivision lines of Twp. No. 35 North Range No. 5 West, of the Principal Base and Meridian in the State of Neb., executed by Frank S. Wood, U. S. Dep. Surveyor, under his Contract No. 5. Dated Nov. 14th 1881, in the month of June 1882. having been critically examined, the necessary corrections & explanations made. the said Field Notes & the Surveys they describe are hereby approved.

Geo. Smith
Surveyor General

General Land Office • Original Field Notes

Book Number

699

The images in this file are photographs of the notes of the original surveys of the State of Nebraska on file in the Office of the Nebraska State Surveyor located in Lincoln, Nebraska.

The original surveys in Nebraska began in the mid 1850's and were completed in the mid 1880's. The Nebraska office of the Surveyor General was closed June 30, 1886.
